



APPENDIX 4-4

**CONSTRUCTION AND
ENVIRONMENTAL
MANAGEMENT PLAN (2019)**

Construction and Environmental Management Plan

**Meenbog Wind Farm Development at
Meenbog & Adjacent Townlands, Co.
Donegal**



Planning & Environmental Consultants

DOCUMENT DETAILS

Client: Planree Ltd.

Project title: Meenbog Wind Farm

Project Number: 160502

Document Title: Construction and Environmental Management Plan

Doc. File Name: CEMP F- 2019.02.01- 160502-b

Prepared By: McCarthy Keville O'Sullivan Ltd.
Planning & Environmental Consultants
Block 1, G.F.S.C.
Moneenageisha Road, Galway



Document Issue:

Rev	Status	Issue Date	Document File Name	Author(s)	Approved By:
01	Draft	21/11/2017	CEMP D1-2017.11.21-160502	OC	MW
02	Final	13/12/2017	CEMP F-2017.12.13-160502	OC	MW
03	Draft	18/12/2018	CEMP D1-2018.12.18-160502-b	OC	MW
04	Final	01/02/2019	CEMP D1-2018.12.18-160502-b	OC	MW

Table of Contents

1	Introduction.....	1
1.1	Scope of Construction and Environmental Management Plan.....	1
2	Site and Project Details	3
2.1	Site Location and Description	3
2.2	Description of the Development	3
2.3	Targets and Objectives.....	4
2.4	Construction Methodologies Overview	5
2.4.1	Introduction	5
2.4.2	Overview of Proposed Construction Methodology.....	5
2.4.2.1	Temporary Construction Compound	5
2.4.2.2	Borrow Pit.....	6
2.4.2.3	Drainage System.....	7
2.4.2.4	Upgrade of Existing Roads	8
2.4.2.5	New Site Access Roads	8
2.4.2.6	Watercourse/Culvert Crossing on the Wind Farm Site	9
2.4.2.7	Crane Hardstands.....	11
2.4.2.8	Turbine and Anemometry Mast Foundations.....	11
2.4.2.9	Electricity Substation and Control Buildings	13
2.4.2.10	Cable Trenching	13
2.4.2.11	Grid Connection.....	14
2.4.2.11.1	Parallel Road Excavations inroad & in Grass margin.....	14
2.4.2.11.2	Existing Underground Services	16
2.4.2.11.3	Joint Bays.....	16
2.4.2.11.4	Watercourse/Culvert Crossing – Grid Connection Cable Route.....	17
2.4.2.11.5	General Construction Measures.....	20
2.4.2.12	Recreation and Amenity Areas	20
2.4.2.13	Decommissioning.....	20
3	Environmental Management	22
3.1	Introduction.....	22
3.2	Protecting Water Quality.....	22
3.2.1	Environmental Management in the Construction Phase	22
3.2.2	Site Drainage Design.....	22
3.2.3	Legislation and Best Practice Guidance.....	22
3.2.4	Site Drainage and Management	23
3.2.4.1	Preparative Site Drainage Management.....	23
3.2.4.2	Pre-emptive Site Drainage Management.....	24
3.2.4.3	Reactive Site Drainage.....	24
3.2.4.4	Operational Phase Drainage.....	24
3.3	Refuelling, Fuel and Hazardous Materials Storage.....	25
3.4	Cement Based Products Control Measures	25
3.5	Peat Stability Management.....	26
3.5.1	General Recommendations for Good Construction Practice.....	26
3.6	Traffic Management.....	27

3.6.1	Turbine and Materials Transport Route	27
3.7	Ecological Management.....	28
3.8	Dust Control	29
3.9	Noise Control	29
3.10	Invasive Species Management.....	30
3.10.1	General Best Practice Control Methods	30
3.10.2	Site Management.....	30
3.10.3	Establishing Good Site Hygiene	30
3.11	Waste Management	31
3.11.1	Legislation	31
3.11.2	Waste Management Hierarchy.....	31
3.11.3	Construction Phase Waste Management Plan	32
3.11.3.1	Description of the Works.....	32
3.11.3.2	Waste Arisings and Proposals for Minimisation, Reuse and Recycling of Construction Waste.....	33
3.11.3.3	Waste Arising from Construction Activities.....	33
3.11.3.4	Waste Arising from Decommissioning	34
3.11.4	Reuse	34
3.11.5	Recycling	34
3.11.6	Implementation	34
3.11.6.1	Roles and Responsibilities for Waste Management.....	34
3.11.6.2	Training.....	34
3.11.6.3	Record Keeping	35
3.11.7	Waste Management Plan Conclusion	35
4	Drainage Management Plan	36
4.1	Wind Farm Drainage	36
4.1.1	Introduction	36
4.1.2	Existing Drainage Features	36
4.1.3	Drainage Design Principles	37
4.1.4	Site Management & Pollution Prevention	37
4.1.5	Pre-Construction Drainage Management	38
4.1.6	Construction Phase Drainage Management Plan	39
4.1.6.1	Drainage Design	39
4.1.6.1.1	Interceptor Drains.....	39
4.1.6.1.2	Swales.....	40
4.1.6.1.3	Check Dams	41
4.1.6.1.4	Level Spreaders.....	41
4.1.6.1.5	Piped Slope Drains.....	42
4.1.6.1.6	Vegetation Filters.....	43
4.1.6.1.7	Settlement Ponds	43
4.1.6.1.8	Dewatering Silt Bags	44
4.1.6.1.9	Siltbuster.....	44
4.1.6.1.10	Culverts.....	45
4.1.6.1.11	Silt Fences.....	46
4.1.6.2	Construction Compound Drainage	47
4.1.6.3	Borrow Pit Drainage	47
4.1.6.4	Tree Felling Drainage Controls.....	48
4.1.6.5	Cable Trench Drainage	49
4.1.7	Drainage Maintenance	49
4.1.8	Operational Phase Drainage Management	50

5	Environmental Management Implementation	52
5.1	Roles and Responsibilities	52
5.1.1	Wind Farm Construction Manager/Site Supervisor	52
5.1.2	Site Environmental Clerk of Works	53
5.1.3	Project Ecologist	54
5.1.4	Project Hydrologist	54
5.1.5	Project Geotechnical Engineer / Geologist.....	54
5.2	Monitoring of Surface Water Quality	55
5.2.1	Pre-Construction Drainage Inspection and Monitoring	56
5.2.2	Construction Phase Drainage Inspection and Monitoring:	56
5.2.2.1	In-situ field monitoring:.....	57
5.2.2.2	Monthly Laboratory Analysis Sampling.....	57
5.2.2.3	Continuous Turbidity Monitoring.....	57
5.2.2.4	Monitoring Parameters	57
5.2.3	Surface Water Monitoring Reporting.....	58
5.2.4	Post-Construction Monitoring	58
5.3	Environmental Awareness and Training	58
5.3.1	Environmental Induction.....	58
5.3.2	Toolbox Talks	59
6	Emergency Response Plan.....	60
6.1	Emergency Response	60
6.1.1	Roles and Responsibilities	60
6.1.2	Initial Steps.....	61
6.1.3	Site Evacuation/Fire Drill.....	62
6.1.4	Excessive Peat Movement.....	62
6.1.5	Onset of Peat Slide.....	62
6.1.6	Spill Control Measures	63
6.2	Contacting the Emergency Services	64
6.2.1	Emergency Communications Procedure.....	64
6.2.2	Contact Details.....	64
6.2.3	Procedure for Personnel Tracking	65
6.3	Induction Checklist	65
7	Mitigation Proposals	66
8	Monitoring Proposals.....	83
9	Programme of Works	92
10	Compliance and Review.....	93
10.1	Site Inspections and Environmental Audits	93
10.2	Auditing	93
10.3	Environmental Compliance.....	93
10.4	Corrective Action Procedure.....	94
10.5	Construction Phase Plan Review.....	94

1 INTRODUCTION

This Construction and Environmental Management Plan (CEMP) has been developed by McCarthy Keville O' Sullivan Ltd. on behalf of Planree Ltd. The CEMP provides the environmental management framework to be adhered to during the pre-commencement, construction and operational phases of the development and it incorporates the mitigating principles to ensure that the work is carried out in a way that minimises the potential for any environmental impacts to occur. This CEMP has been prepared in conjunction with the Environmental Impact Assessment Report (EIAR), Natura Impact Statement (NIS) and the Condition Compliance Statement (CCS) of the permitted Meenbog Wind Farm.

This CEMP identifies the key planning and environmental considerations that must be adhered to and delivered during site construction and operation. This report is intended as a single, amalgamated document that can be used during the future phases of the project, as a single consolidated point of reference relating to all construction, environmental and drainage requirements for the planning authority, developer and contractors alike.

The CEMP has been prepared in accordance with the planning permission conditions set by An Bord Pleanála under ABP-300460-17 which relates to the development of Meenbog Wind Farm including junction accommodation works along the turbine delivery route and connection to the national grid

1.1 Scope of Construction and Environmental Management Plan

This report is presented as a guidance document for the construction phase of the Meenbog Wind Farm. It outlines clearly the mitigation measures and monitoring proposals that are required to be adhered to in order to construct the wind farm in an appropriate manner. The report is divided into ten sections, as outlined below.

Section 1 provides a brief introduction as to the scope of the report

Section 2 outlines the site and project details, detailing the targets and objectives of this plan along with providing an overview of anticipated construction methodologies that will be adopted throughout the project.

Section 3 sets out details of the environmental controls on site which looks at noise and dust controls. Site drainage measures, peat management and a waste management plan are also included in this section.

Section 4 sets out the development drainage management plan which provides details of the various drainage infrastructure that will be installed to manage and control the quality of surface water runoff from the site.

Section 5 sets out a fully detailed implementation plan for the environmental management of the project outlining the roles and responsibilities of the project team

Section 6 outlines the Emergency Response Plan to be adopted in the event of an emergency in terms of site health and safety and environmental protection

Section 7 consists of a summary table of all mitigation proposals to be adhered to during the implementation of the project, categorised into three separate headings, 1) pre-commencement measures; 2) construction-phase measures and 3) operational-phase measures.

Section 8 consists of a summary table of all monitoring requirements and proposals to be adhered to during the implementation of the project, categorised into three separate headings, 1) pre-commencement measures; 2) construction-phase measures and 3) operational-phase measures.

Section 9 sets out an anticipated programme for the timing of the works.

Section 10 outlines the proposals for reviewing compliance with the provisions of this report.

2 SITE AND PROJECT DETAILS

2.1 Site Location and Description

The site of the Permitted Development is located in the townlands of Meenbog and Croaghonagh and adjacent townlands associated with the underground electrical cabling, listed in Table 2.1, in County Donegal. The Permitted Development will comprise of the provision of a total of 19 No. wind turbines, with a maximum ground to top blade tip height of up to 156.5m and all associated infrastructure.

The wind farm site measures approximately 990 hectares or 2,446 acres. The Grid Reference co-ordinates for the approximate centre of the site are (E207,963 N385,970). The Permitted Development is located approximately eight kilometres south west of the towns of Ballybofey and Stranorlor and approximately 15 kilometres northwest of the town of Castlederg, Co. Tyrone.

The electrical connection from the Permitted Development to the national grid will be completed by underground cabling which will run within the public road corridor to the existing Clogher 110 kV Electricity Substation.

Table 2.1 Townlands containing infrastructure

Development Infrastructure	Townland
Current Wind Farm Site & Amenity Area Development	Meenbog
	Croaghonagh
	Cashelnavan
Grid Connection Route	
	Tawnawully Mountains
	Keadew Upper
	Friarbush
	Ardinawark
	Keadew Lower
	Cullionbuoy

2.2 Description of the Development

During the construction phase of the project, civil works will include constructing the reinforced concrete foundations; access road construction and upgrade of existing access roads; construction of temporary compounds; construction of substation; upgrading existing watercourse crossings, construction of underground cabling; and a permanent meteorological mast.

The design life of the project is expected to be 30 years.

The key components of the wind farm include the following:

- 19 no. Wind Turbines with a maximum blade tip height of 156.5 metres;
- 19 no. Hardstand Areas to facilitate cranes for turbine erection and to act as construction material storage compounds;
- 1 no. Permanent Meteorological Mast;

- 1 no. 110kV Electricity substation and control building with 2 no. control buildings with welfare facilities, associated electrical plant and equipment, security fencing and waste water holding tank;
- 110kV underground grid connection cabling;
- Upgrade of access junctions;
- Upgrade of existing tracks, roads and provision of new site access roads and hardstand areas;
- 3 no. borrow pits;
- 2 no. temporary construction compounds;
- Recreation and amenity works, including marked trails (upgrade of existing tracks and provision of new tracks), picnic, amenity and play areas, car parking and vehicular access;
- Site drainage
- Forestry felling
- Permanent signage;
- All associated site development and ancillary works

The permitted site layout showing individual elements of the development is shown in Figure 2.1 & 2.2 and in the Site Layout Drawings included in Appendix 1.

2.3 Targets and Objectives

In so far as they have been completed to date, or are to be further completed in future, the construction phase works are designed to approved standards, which include specified materials, standards, specifications and codes of practice. The design of the project has considered environmental issues and this is enhanced by the works proposals.

The key site targets are as follows;

- Adopt a sustainable approach to construction and, ensure sustainable sources for materials supply where possible;
- Keeping all watercourses free from obstruction and debris;
- Avoidance of any pollution incident or near miss as a result of working around or close to existing watercourses and having emergency measures in place;
- Correct fuel storage and refuelling procedures to be followed;
- Air and noise pollution prevention to be implemented;
- Construction Methods and designs will be altered where it is found there is an adverse effect on the environment;
- Good waste management and house-keeping to be implemented;
- Using recycled materials if possible, *e.g.* excavated stone, soil and subsoil material;
- Avoidance of vandalism;
- Monitoring of the works and any adverse effects that it may have on the environment and,
- Provide adequate environmental training and awareness for all project personnel.

The key site objectives are as follows;

- Keep impact of construction to a minimum on the local environment, watercourses and wildlife;
- Comply with all relevant water quality legislation;

Map Legend

EIAR Study Area

Proposed Turbine Location

Proposed Met Mast Location

Proposed Substation Compound

Proposed Borrow Pit Areas

Proposed Temporary Construction Compound

Proposed Temporary Construction Compound/
Proposed Amenity Area

Existing Roads - Upgrade Proposed

Existing Tracks - Upgrade Proposed

Proposed New Roads

Grid Connection Cabling Route

Proposed Amenity Walkways

A detailed topographic map of the Meenbog Wind Farm site in County Donegal, Ireland. The map features contour lines indicating elevation, with peaks such as Cross Hill (385m) and Carna (452m). Key geographical features include the River Bann, Lough Bann, and the surrounding hills of Croaghmagawna and Croaghconnellagh. The proposed wind farm layout is overlaid on the map, showing 19 numbered turbine locations (blue circles) and a central substation compound (cyan rectangle). Other infrastructure includes borrow pit areas (orange rectangles), temporary construction compounds (yellow and dark green rectangles), and proposed access roads (red lines). The map also shows existing roads (brown lines) and proposed new roads (green lines). A grid connection cabling route is shown as a blue line, and proposed amenity walkways are indicated by light blue lines. The map is oriented with North at the top, as indicated by the compass rose in the bottom right corner. The scale is 1:25,000, and the date of the map is 22-11-2017.

McCarthy
McCarthy Keville O'Sullivan Ltd., Block 1, G.F.S.C. Moreenaghessa Road, Galway, Ireland. Email: info@mcCarthyKeville.co.uk Tel: +353 (0)91 735611 Fax: +353 (0)91 71279

MAP NO:

Figure 2.1

SCALE:

1:25,000

PROJECT TITLE:

160502 - Meenbog Wind Farm, Co. Donegal

DRAWING BY:

Eoin McCarthy

CHECKED BY:

Michael Watson

ISSUE NO.:

160502-2017.11.22-D10

DATE:

22-11-2017

Land & Property Services Intellectual Property is protected by Crown Copyright and is reproduced with the permission of Land & Property Services under Delegated Authority from the Controller of HMSO, © Crown Copyright and database right Licence No. 2892 (2017)

Ordnance Survey Ireland Licence No. AR 0021815 © Ordnance Survey Ireland/Government of Ireland

Map Legend



EIS Study Area



Proposed Meenbog Wind Farm Electricity Substation




Existing Clogher 110kV Substation Location



Bridge Crossing Locations



Meenbog Wind Farm to
Clogher Substation Cabling Route

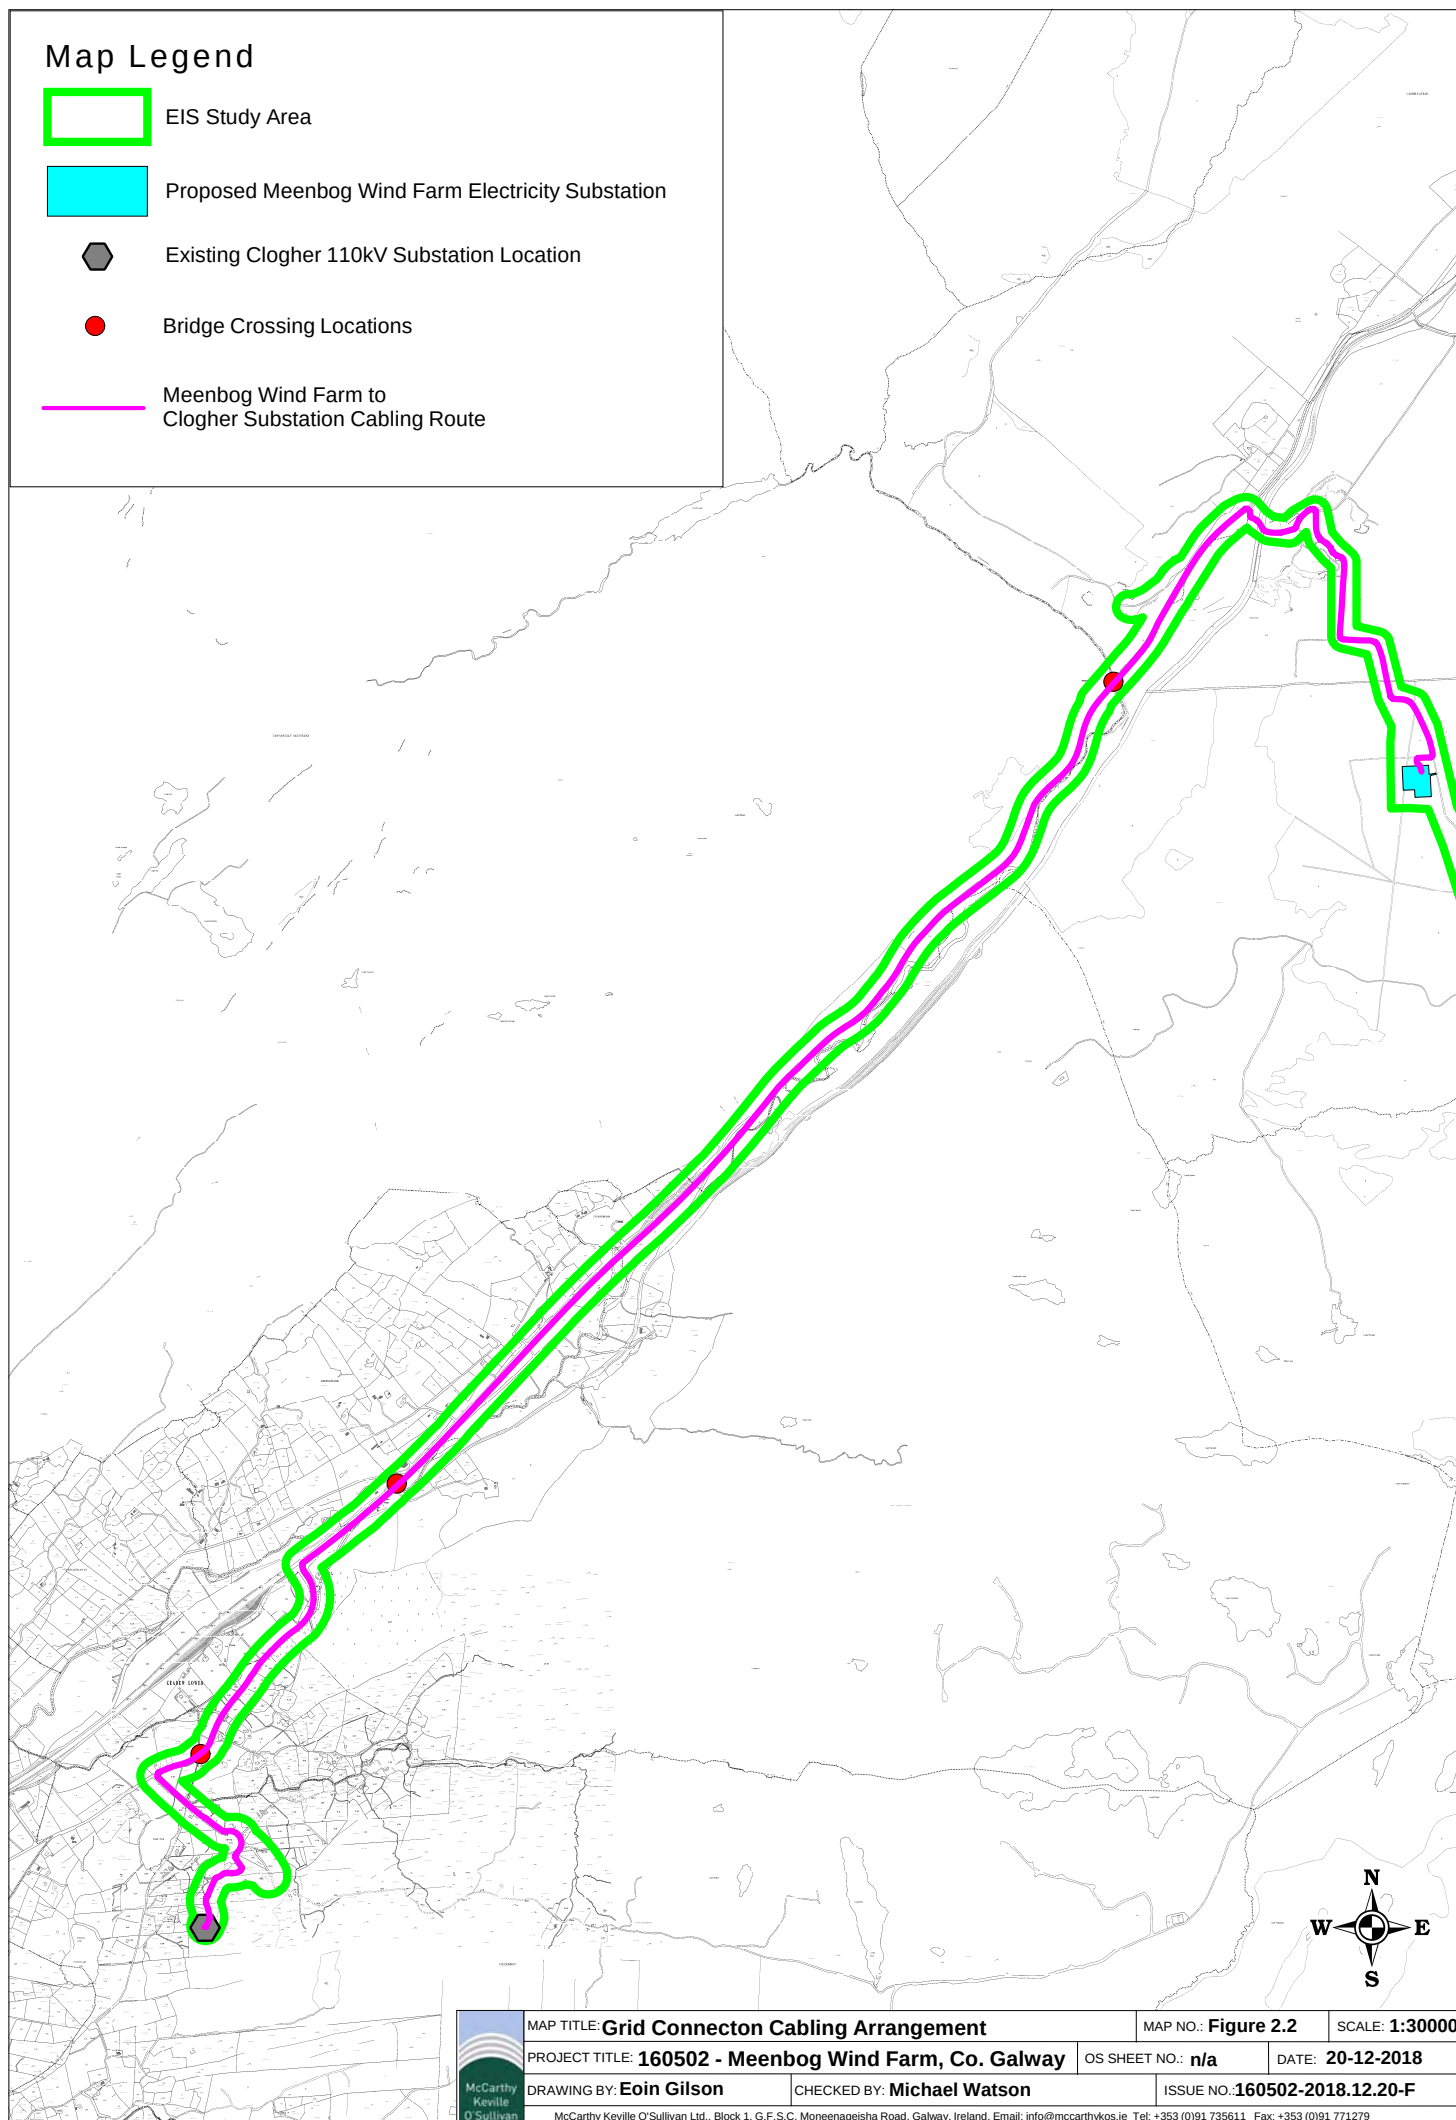

MAP TITLE: **Grid Connecton Cabling Arrangement**

MAP NO.: **Figure 2.2**

SCALE: **1:30000**

PROJECT TITLE: **160502 - Meenbog Wind Farm, Co. Galway**

OS SHEET NO.: **n/a**

DATE: **20-12-2018**

DRAWING BY: **Eoin Gilson**

CHECKED BY: **Michael Watson**

ISSUE NO.: **160502-2018.12.20-F**

McCarthy Keville O'Sullivan Ltd., Block 1, G.F.S.C. Moneenageisha Road, Galway, Ireland. Email: info@mccarthykos.ie Tel: +353 (0)91 735611 Fax: +353 (0)91 771279

- Ensure construction works and activities are completed in accordance with mitigation and best practice approach presented in the Environmental Report and associated planning documentation;
- Ensure construction works and activities are completed in accordance with any planning conditions for the development;
- Ensure construction works and activities have minimal impact/disturbance to local landowners and the local community;
- Ensure construction works and activities have minimal impact on the Natural Environment;

2.4 Construction Methodologies Overview

2.4.1 Introduction

Mid Cork Electrical Ltd. have been appointed as the contractor for the civil works for the construction phase of the Permitted Development. The appointed contractor for the works will be required to comply with this CEMP and any revisions made to this document in the preparation of method statements for the various elements of the construction phase of the Permitted Development. An overview of the proposed Construction Methodologies is provided below.

2.4.2 Overview of Proposed Construction Methodology

The proposed anticipated construction methodology is summarised under the following main headings:

- Temporary Construction Compounds;
- Borrow Pits;
- Site Drainage;
- Upgrade of Existing Roads;
- New Site Access Roads;
- Crane Hardstands;
- Turbine and Anemometry Mast Foundations;
- Electricity Substation and Control Buildings;
- Peat Repositories (cells within borrow pits);
- Cable Trenching;
- Grid Connection Cabling; and,
- Recreation and Amenity Areas
- Decommissioning

2.4.2.1 Temporary Construction Compound

There are two temporary construction compounds permitted for the site. One will be located in the northwest of the site, just north of the substation location. The second temporary construction compound is located north of the site, northwest of Turbine no. 17 which will become an amenity area on completion on the construction of the wind farm. The location of the construction compound is shown on the site layout drawings in Figure 2.1. The compound will typically be constructed as follows:

- The area to be used as the compound will be marked out at the corners using ranging rods or timber posts. Drainage runs and associated settlement ponds (refer to Section 3.1.1 below) will be installed around the perimeter;
- The compound will be established using a similar technique as the construction of the excavated site tracks as discussed below;

- Where required, a layer of geogrid will be installed and compacted layers of well graded granular material will be spread and lightly compacted to provide a hard area for site offices and storage containers;
- Areas within the compound will be constructed as site roads and used as vehicle hardstandings during deliveries and for parking;
- A bunded containment area will be provided within the compound for the storage of lubricants, oils and site generators etc.;
- If necessary the compound will be fenced and secured with locked gates, although fencing would only be utilised where significant risk of danger to third parties or vandalism is envisaged; and,
- Upon completion of the project the compound will be decommissioned by backfilling the area with the material arising during excavation, landscaping with topsoil as required. (North-eastern compound will be repurposed as an amenity area as described in Section 4.6 of the EIAR)
- During the construction phase, a self-contained port-a-loo with an integrated waste holding tank will be used on site for toilet facilities. This will be maintained by the service contractor as required and will be removed from the site on completion of the construction phase.
- The water supply to the site will be from a temporary water storage tank which will be filled using a mobile water tank which will source water locally as required.

2.4.2.2 Borrow Pit

The development will comprise three borrow pits one of which is located in the southern section of the site, north of turbine no. 5. The other borrow pits are located in north of the site, south of turbine no. 15 and east of turbine no. 13 as shown in Figure 2.1. The borrow pits will typically be excavated as follows:

- The areas to be used for both borrow pit will be marked out at the corners using ranging rods or timber posts. Drainage runs and associated settlement ponds will be installed around the perimeter;
- The initial borrow pit excavation will involve removal of peat and overburden from the top of bedrock. These materials will be used to form a berm on the downhill side of the borrow pit to provide screening of the borrow pit operations;
- Interceptor drainage ditches will be excavated on all sides of the borrow pit to catch surface water runoff, and direct it to downstream re-distribution locations;
- The bedrock material will be extracted from the borrow pit and stockpiled or used as required;
- The use of material won from the borrow pit will be sequential with new road construction or turbine base formations;
- Temporary stockpiling of aggregates will be required to accommodate the cut and fill operations within the borrow pit, and the progression of access roads and turbine excavations;
- As the borrow pit excavations progress and become deeper, surface water and groundwater ingress will be removed via pumping to settlement ponds, and re-distribution locally across natural vegetated areas. Where required, additional specialist treatment will be employed to ensure no deterioration in downstream water quality occurs;
- When extraction ceases within the borrow pit, the uphill face of the rock will be stepped and deposits of soil will be placed which will assist in the re-vegetation of the rock face.

- The extraction area of the borrow pit will have to be permanently secured and a stock-proof fence will be erected around the borrow pit to prevent access to these areas as well as the installation of appropriate health and safety signage.

Once the required volume of rock has been extracted from the borrow pit areas, it is intended to reinstate these areas with peat and overburden excavated from the works areas of the Permitted Development.

The total estimated volume of peat and spoil to be excavated and managed during the construction phase of the Permitted Development is 330,820m³. The borrow pit areas, within the site of the Permitted Development will undergo restoration with this peat and spoil material after all rock has been excavated from the borrow pit. The volume of excavated peat and overburden will be managed as outlined below:

- Excavators will remove the peat from the permanent development footprint areas i.e. excavated roads, hardstanding areas and turbine foundation areas.
- Temporary, sealed stockpiling areas, located adjacent to the hardstanding areas and turbine foundation areas, will be chosen following onsite discussions between the construction site manager, an ecologist, a geotechnical engineer and hydrologist.
- The excavators will move the excavated peat to the designated temporary stockpiling areas within the construction and soft levelled areas.
- The temporary stockpiling areas will be surrounded by silt fences to ensure sediment-laden run-off does not occur.
- The excavated peat will remain in these areas over a period of time until the volume of the peat has reduced as the water drains out of the mounded peat.
- The excavators will then load the peat directly into dump trucks, to transport the peat to the nearest borrow pit area.
- The material will be backfilled into the borrow areas and will be spread evenly across the area.
- The peat and subsoil will also as part of landscaping and reinstatement along access roads and turbine excavations.

This method of managing the volume of surplus peat and other overburden material will ensure that no excavated material will be left on-site, or stockpiled adjacent to access roads and turbine locations, following the completion of the construction works.

2.4.2.3 Drainage System

The early establishment of temporary drainage facilities will manage the risk of impacts on watercourses on and adjacent to the site during construction. In addition, construction operations will adopt best working practices. The development of the site will need to be phased accordingly. The construction of the drainage will start from the downstream sections and progress upstream, connecting conveyance systems with other drainage features as each development phase progresses. They will therefore need to be designed with sufficient flexibility to respond to an early phase incoming flow during the construction phase.

The implementation of a Scheduling of Works Operating Record (SOWOR) prior to commencement will provide a series of pre-commencement triggers which set out specific conditions which will be met before the commencement of works particularly sensitive areas. These pre-commencement triggers will apply to the installation of any drainage infrastructure. An example of an SOWOR is included in Appendix 2.

Detailed measures to address surface water management based upon the design criteria and philosophy will be implemented. The drainage system will be excavated and constructed in conjunction with the road and hard standing construction. Drains will be excavated, and settlement ponds constructed to eliminate any suspended solids within surface water running off the site. Surface drainage design and management is summarised with in Section 3.2 and 4 below.

2.4.2.4 Upgrade of Existing Roads

It is proposed to utilise the existing road network as much as possible (approximately 14.5 km will be used). These roads will require upgrading which will entail widening of the roadway to a total running width of approximately six metres, with wider sections at corners and on the approaches to turbine locations, and the laying of a new surface dressing on the existing section of roadway where necessary. The road widening will be undertaken as follows:

- If it is considered that the current road formation level is adequate to support required bearing, then no upgrade or widening works will be completed;
- Otherwise, where required, the subsoil in the existing road verge will be excavated down to a suitable formation layer and the spoil used for the restoration of borrow pits or in reinstatement areas;
- Well-graded imported granular fill will be spread and compacted in layers with an overall thickness of up to 300mm to provide a homogeneous running surface. The thickness of layers and amount of compaction required will be decided by the Construction Manager based on the characteristics of the material and the compaction plant to be used. These layers of granular fill will be brought to the same level as the top of the existing road surface;
- A layer of geogrid will be installed directly onto the top of the granular fill layer and the existing road surface where required; and,
- A layer of finer well graded stone for the running surface will be laid on the geogrid and compacted.
- Prior to any works commencing on the upgrade of existing roads, the requirement for additional roadside drainage will be considered by the Project Hydrologist in line with the proposals outlined in Section 4
- Where road widening is required in an area where the peat depth is greater than c1.5m, it will be necessary to complete the road upgrade using a floating road methodology as summarised in the section that follows.

2.4.2.5 New Site Access Roads

There is approximately 7.7 km of new access roads to be installed at the site. In a number of areas across the site, floating roads will be required where peat depths exceed c1.5m. Floating roads will be constructed using either a lightweight construction methodology which includes the use of layers of brash and lumber either side of a geogrid membrane where required and capped with suitable stone material or the use of geogrid capped with a stone material. The new access roads will be constructed as follows:

- Establish alignment of the new site roads from the construction drawings and mark out the centrelines with ranging rods or timber posts;
- The road layout has been designed to avoid crossings of natural watercourses where possible;
- Where existing culverts are to be upgraded or extended, the works will be carried out to follow a method statement to be agreed with Inland Fisheries Ireland.

- The access tracks will be of single-track design with an overall width of 6m. There will be some local widening on the bends, junctions and around turbine bases for the safe passage of large vehicles;
- Any excavated road section's will, where it is considered beneficial have turf stripped over the area of the excavation and stored growing side up for reuse. This area will be oversized to facilitate the excavated subsoil material. The subsoil material will subsequently be capped with topsoil to form an earth bund around the excavated material;
- Where the Geotechnical Engineer confirms it is more suitable, a non-excavated ground bearing road will be employed. In this case a reinforced sub-base will be placed directly on the existing ground using geotextile separation layer and layers of geogrid reinforcing as designed by the Geotechnical Engineer to achieve the bearing capacity required for the road running surface.
- All peat excavated will be used as part of the borrow pit restoration or in reinstatement areas. Topsoil will be temporarily stockpiled locally for reuse for landscaping the backfill placed above the foundations. A bund constructed of the excavated subsoil covered with a layer of Geogrid and capped with the peat topsoil for landscaping purposes will form the down-gradient boundary to the reinstatement areas;
- The subsoil will be excavated down to a suitable formation layer of either firm clay or bedrock;
- Where floating roads are to be constructed, the subsoil will not be excavated but a layer of geo-grid or layers of brash and lumber will be laid directly on to the peat surface.
- Well-graded granular fill will be spread and compacted in layers with an overall thickness of up to 750mm and a suitable capping layer to provide a homogeneous running surface. The thickness of layers and amount of compaction required will be decided by the Construction Manager based on the characteristics of the material and the compaction plant to be used;
- All new roadways will be constructed with a camber to aid drainage of surface water;
- Batters will generally be sloped to between 1:1 and 1:2 (depending on depth and type of material) and will be left as cut to re-vegetate naturally with local species. Design slopes will be informed by the Geotechnical Engineer;
- At bends or steep inclines from the roads, reflective snow poles will be erected to warn traffic on dark mornings and evenings that there is a turn in the road or a sharp incline beyond the site road.
- The granular fill use to complete the final running surface of the roads on site will be tested to BS812-111:1990 "Ten percent fines value".

2.4.2.6 Watercourse/Culvert Crossing on the Wind Farm Site

A survey of all existing stream culverts and stream crossings along existing roads (for upgrade) and access roads was undertaken as part of the drainage mapping. There are a total of 19 no. existing watercourse crossings and 5 no. new watercourse crossings. The locations of existing and new crossings are shown on Figure 2.3. The minimum required culvert dimensions of new culverts are shown in Appendix 3 which has informed the selection of both piped culvert and clear span bridge methodologies for the watercourse crossings.

It is proposed to construct c. 5m wide clear-span bridge over the Bunadaowen River within the Permitted Development site to provide access to Turbine No. 18 in the eastern half of the site. The crossing will comprise a pre-cast concrete clear span bridge as shown in Drawing 0502 - 47 in Appendix 1.

The typical construction methodology for the installation of a pre-cast concrete clear-span bridge is presented below:

- The access road on the approach to the watercourse will be completed to a formation level which is suitable for the passing of plant and equipment required for the installation of the watercourse crossing.
- All drainage measures along the site road will be installed in advance of the works.
- The abutment will consist of concrete panels which will be installed on a concrete lean mix foundation to provide a suitable base. The base will be excavated to rock or competent ground with a mechanical excavator with the foundation formed in-situ using a semi-dry concrete lean mix. The base will be excavated along the stream bank with no instream works required.
- Access to the opposite side of the river for excavation and foundation installation will require the installation of pre-cast concrete slab across the river to provide temporary access for the excavator.
- All pre-cast concrete panels and slabs/beams will be installed using a crane which will be set up on the southern side of the stream and will be lifted into place from the stream back with no contact with the watercourse.
- A concrete deck will be poured over the beams/slabs which span across the river. This will be shuttered, sealed and water tested before concrete pouring can commence. The deck will be leak tested before concrete pouring can commence.
- Once the culvert is in position stone backfill will be placed and compacted against the culvert up to the required level above the foundations.

When the concrete beams are cured the filling and compaction of the road will be completed. The road finish level will be decided by the Project Engineer.

All other new crossings will be completed using piped culvert, the crossings will be installed as follows:

- The access road on the approach watercourse will be completed to a formation level which is suitable for the passing of plant and equipment required for the installation of the watercourse crossing.
- The installation of the culvert will take place in low flow conditions.
- Where a flow exists, the water running through the watercourse channel will be pumped around the water crossing location and back into the watercourse channel downstream of the works area.
- Where over pumping is required, measures will be taken to ensure that the pumped water discharge does not disturb the stream bed with the force of water from the discharge. A steel plate to reduce the force of the flow will be used where appropriate.
- The project engineer will determine the required gradient of the culvert. The pipe must be laid at a gradient that will ensure water is contained within the pipe at all times. Where necessary a rock armour dam will be installed within the stream to reduce flow and ensure an acceptable depth of water remains within the pipe. Where a gradient of 1 – 1.5% is identified, the use of a baffle has been recommended.
- The bed of the watercourse channel will be excavated, if necessary, to achieve the correct line and to allow the pipe to be embedded 300mm into the base of the existing drain.

- The embedded section will be allowed to fill naturally with existing material within the base of the drain or with suitable drainage material such as gravel or round shingle where deemed applicable.
- The culvert will be lowered into place using an excavator with a lifting mechanism.
- Large stone boulders (approx. 400mm), sourced from the on-site borrow pits, will be placed over the culvert to create a headwall for the culvert and a suitable sub-base for road construction.
- Smaller 50mm stone, sourced on site will be placed upon the sub-base to construct the road over the water crossing.

Any watercourse crossings required will be installed outside of the salmonid spawning season, October to June in any year, in accordance with Inland Fisheries Ireland best practice (IFI, 2016). This will ensure no potential impacts on salmonid spawning habitat.

All of the above works will be supervised by the Environmental Clerk of Works and the project hydrologist.

2.4.2.7 Crane Hardstands

All crane pads will be designed taking account of the loadings provided by the turbine manufacturer and will consist of a compacted stone structure. The crane hardstands will be constructed in a similar manner to the excavated site roads and will measure approximately to the turbine manufacturer's requirements. Where an excavated crane hardstand cannot be used due to the depth of peat, the hardstand will be supported by using reinforced concrete piles as per the methodology outlined for piled foundations summarised below. The position of the crane pads varies between turbine locations depending on topography, position of the site access road, and the turbine position.

2.4.2.8 Turbine and Anemometry Mast Foundations

The wind turbines and anemometry mast foundations will be a reinforced concrete base designed to Eurocode 2/BS8110. Foundation loads will be provided by wind turbine and mast supplier, and factors of safety will be applied to these in accordance with European design regulations. The turbine will be anchored to the foundation using a bolt assembly which shall be cast into the concrete. The anemometry mast is a free-standing structure which is also anchored to the reinforced concrete foundation. It is anticipated that the foundations for both the turbines and the anemometry mast will be either ground bearing or piled foundations and that the formation level of the turbine foundations will be on the lower mineral subsoil or bedrock. Bases will measure approximately 20 metres in diameter. They will likely be formed one metre below the base of the peat layer on stiff subsoil material or bedrock, or at a suitable level directed by the Geotechnical Engineer/Designer. The foundations will be constructed as follows:

- The extent of the excavation will be marked out and will include an allowance for trimming the sides of the excavation to provide a safe working area and slope batter;
- Where practical, the peat will be stripped over the area of the excavation and stored growing side up for reuse, the subsoil will be excavated and stored to one side for reuse during the landscaping around the finished turbine;
- No material will be removed from site and storage areas will be stripped of vegetation prior to stockpiling in line with best working practices;
- All groundwater and surface water arising from turbine base excavation will be pumped to the dirty water system prior to discharge from the works area;

- Soil excavation shall be observed by a qualified archaeologist in accordance with a scheme of archaeological monitoring to identify any significant remains as they come to light and,
- The foundations excavation will be raised to formation level by compacted layers of well graded granular material will be spread and compacted to provide a hard area for the turbine foundation.

Standard excavated reinforced concrete bases will be completed as follows:

- A layer of concrete blinding will be laid approximately 75mm thick directly on top of the newly exposed formation, tamped and finished with a screed board to leave a flat level surface. The concrete should be protected from rainfall during curing and all surface water runoff from the curing concrete should be prevented from entering surface water drainage directly;
- High tensile steel reinforcement will be fixed in accordance with the designer's drawings & schedules. The foundation anchorage system will be installed, levelled and secured to the blinding using steel box section stools;
- Ductwork will be installed as required, and formwork erected around the steel cage and propped from the backside as required;
- The foundation anchorage system will be checked both for level and line prior to the concrete being installed in the base. These checks will be passed to turbine manufacturer for their approval;
- Concrete will be placed using a concrete pump and compacted when in the forms using vibrating pokers to the levels and profile indicated on the drawings. Upon completion of the concreting works the foundation base will be covered and allowed to cure;
- Steel shutters will be used to pour the circular chimney section;
- Earth wires will be placed around the base; and,
- The foundation will be backfilled with a cohesive material, where possible using the material arising during the excavation and landscaped using the vegetable soil set aside during the excavation.
- Soil, rock and other materials excavated during construction shall not be left stockpiled on site following completion of works. Excavated areas shall be appropriately restored within three months of the date of commissioning of the wind farm

Reinforced concrete piled foundations will be completed as follows:

- The extent of the excavation will be marked out and will include an allowance for trimming the sides of the excavation to provide a safe working area and slope batter;
- No material will be removed from site and placement areas will be stripped of vegetation prior to stockpiling in line with best working practices;
- A piling platform for the piling rig will be constructed. This can be done in two ways depending on the bearing capacity of the underlying soil.
 - o The first method is to lay geo-textile on the existing surface and a stone layer will then be placed on top of the geo-textile by an excavator and compacted in order to give the platform sufficient bearing capacity for the piling rig.
 - o The second method is to excavate the soils to a suitable intermediate mineral subsoil and backfill to the formation level.
- The piling rig, fitted with an auger, will then bore through the soft material with a sleeve fitted around the auger to prevent the sidewalls of the peat from

collapsing. The borehole is then extended to a suitable depth into the subsoil/bedrock.

- When the auger and the sleeve are removed high tensile steel cages will be lowered into the boreholes. These steel cages will extrude above the level of the top of the concrete pile.
- As the auger is removed concrete is pumped into the borehole.
- Reinforcing steel on the top of the pile will tie to the foundation base steel.

The procedure for standard excavated reinforced concrete bases as outlined above can be applied from here.

2.4.2.9 Electricity Substation and Control Buildings

The electricity substation and control buildings will be constructed within the site, adjacent to the existing access road, as shown in Figure 2.1. The dimensions of the substation area will be set to meet the requirements and specifications of ESB/Eirgrid and the necessary equipment to safely and efficiently operate the wind farm;

The substation will be constructed by the following methodology:

- The area of the substation will be marked out using ranging rods or wooden posts and the soil stripped and removed to a temporary placement area for later use in landscaping. No material will be removed from site and the temporary placement areas will be stripped of vegetation prior to stockpiling in line with best working practises;
- Wind farm control buildings will also be built within the substation compound;
- All groundwater and surface water arising from turbine base excavation will be pumped to the dirty water system and treated in settlement ponds, and/or specialist treatment systems, prior to discharge from site; and,
- The foundations will be excavated down to the level indicated by the project engineer. The foundations will be shuttered and poured with reinforced concrete. An anti-bleeding admixture will be included in the concrete mix;
- The substation will be constructed with masonry blockwork. The block work walls will be built up from the footings to DPC level and the floor slab constructed, having first located any ducts or trenches required by the follow on mechanical and electrical contractors;
- The block work will then be raised to wall plate level and the gables & internal partition walls formed. Scaffold will be erected around the outside of the building for this operation;
- Concrete roof slabs will be lifted into position using an adequately sized mobile crane;
- The timber roof trusses will then be lifted into position using a telescopic load all or mobile crane depending on site conditions. The roof trusses will then be felted, battened, tiled and sealed against the weather.
- A rainwater harvesting system will be installed to provide the small volume of water required for the operation of the substation and control building.
- The electrical equipment will be installed and commissioned.
- Perimeter fencing will be erected around the substation and control building compound area.
- All wastewater from the staff welfare facilities in the control buildings by means of a sealed storage tank which will be fitted with an automated alarm system that will provide sufficient notice that the tank requires emptying.

2.4.2.10 Cable Trenching

The transformer in each turbine is connected to the substation through a network of buried electrical cables. The ground is trenched typically using a mechanical

excavator. The top layer of soil is removed and saved so that it is replaced on completion. The cables will be laid within 3 no. 160mm diameter HDPE ducting laid in a trefoil formation with 2 no. 125mm HDPE comms ducts laid above within the same trench.

The cabling ducts are bedded with suitable material unless the ground conditions are such that no bedding is required. The cables will be laid at a depth that meets all national and international requirements and will generally be approximately 1.3m below ground level; a suitable marking tape is installed between the cables and the surface. On completion, the ground will be reinstated as previously described above. The route of the cable ducts will follow the access track to each turbine location and are visible on the site layout drawings included as Appendix 1.

2.4.2.11 Grid Connection

A connection to the national electricity grid will be made by underground electricity cabling originating from the Meenbog Wind Farm substation and will run south connecting to the existing electricity Clogher 110kV electricity substation. The installation methodology for the underground electrical cable is summarised in the following sections. Should Eirgrid require the provision of any additional ducting at the time of completing the wind farm grid connection works, this can be accommodated within the same works programme using the methodologies as set out below for cabling works and watercourses crossings.

2.4.2.11.1 Parallel Road Excavations inroad & in Grass margin

The grid connection route generally follows the existing road corridor except for a section of approximately 300m southeast of the N15 and 230m northwest of the N15 that will cross cut over bog, grassland and scrub habitats to facilitate directional drilling, under the N15 and a tributary of the Lowerymore River as set out in Figure 2.2 and Appendix 1. The grid connection cabling is summarised as follows:

- The area where excavations are planned will be surveyed and all existing services will be identified.
- All relevant bodies i.e. ESB, Donegal County Council etc. will be contacted and all drawings for all existing services sought.
- A traffic management plan for the grid connection cabling works will be prepared in advance of any works commencing.
- A road opening licence will be obtained where required and all plant operators and general operatives will be inducted and informed as to the location of any services.
- Excavation permit will be completed and all plant operators and general operatives will be inducted and informed as to the location of any services.
- A 13 tonne rubber tracked 360-degree excavator will be used to excavate the trench to the dimensions specified in the ESB Networks manuals. The 110kV trench material build-up is designed to the "Functional Specification for the Installation of Ducts and Ancillary Structures for 110kV Underground Power Cables and Associated Communications Cables for Contestable Projects" No. 18150.
- All excavated material not used for backfilling will be removed to the on-site borrow pit areas or to an approved tip or if suitable stock piled and reused where appropriate.
- The trench depth is specified at c. 1250mm therefore trench support will be installed with the trench sides benched or battered back where appropriate.
- Any ingress of ground water will be removed from the trench using submersible pumps.

- A silt filtration system will be used to prevent contamination of any watercourse.
- Once the trench has been excavated a base layer of 15 N CBM4 concrete will be installed and compacted. All concrete will be offloaded directly from the concrete truck directly into the trench.
- Ducting will then be placed in the trench as per specification, approved cable ties will be used where required to secure the trefoil ducts together (at 3 metre centres).
- Once the trefoil ducts have been installed couplers will be fitted and capped to prevent any dirt etc. entering the duct. In poor ground conditions, the end of the trefoil ducts will be shimmed up off of the bed of the trench to prevent any possible ingress of water dirt. The shims will be removed again once the next length has been connected.
- Extreme care will be taken to ensure that all duct collars (both ends) are clean and in good condition prior to ducts being joined.
- The as built location of the ducting will be surveyed using a total station/GPS.
- 15 N CBM4 concrete will be carefully installed so as not to displace the ducting to the underside of the communications duct and compacted as per approved detail. See Plate 2.1.
- Spacers will be used to ensure that the correct cover is achieved at both sides of the trefoil ducting.
- ESB marker board will be fitted above the trefoil ducting.
- The Communication duct will be fitted and kept to one side of the trench ensuring that the minimum cover is achieved and 15N CBM4 concrete will be placed to the specified cover and compacted, see Plate 2.1.
- ESB red marker board will be installed and the remainder of trench will be backfilled in two compacted layers with approved material (lean mix concrete/clause 804).
- Yellow marker tape will be installed as per approved detail specifications, 300 mm maximum below finished road/ground level.
- The finished surface will be reinstated as per original specification or to the requirements of the land owner/Local Authority as appropriate.
- Marker Posts will denote all changes of direction, road crossings, etc.



Plate 2.1 Typical Trench Views

2.4.2.11.2 Existing Underground Services

Any underground services encountered along the route will be surveyed for level and the ducting will pass over the service provided adequate cover is available. A minimum clearance of 300mm will be required between the bottom of the ducts and the service in question. If the clearance cannot be achieved the ducting will pass under the service and again 300 mm clearance between the top of the communications duct and bottom of the service will be achieved. In deeper excavations, an additional layer of marker tape will be installed between the communications layer and yellow top-level marker tape. If the required separation distances cannot be achieved then a number of alternative options are available such as using steel plates laid across the width of the trench and using 35N concrete surrounding the ESB ducts where adjacent services are within 600mm, with marker tape on the side of the trench. Back fill around any utility services will be with dead sand/pea shingle where appropriate. All excavations will be kept within the roadway boundaries, i.e. in road or grass margin.

2.4.2.11.3 Joint Bays

Joint bays are pre-cast concrete chambers where lengths of cable ducting will be connected. They will be located at various points along the ducting route approximately every 600-1000 meters. Where possible joint bays will be located in areas where there is a natural widening/wide grass margin on the road in order to accommodate easier construction, cable installation and create less traffic congestion. During construction, the joint bay locations will be completely fenced off and will be incorporated into the traffic management system. Once they have been constructed they will be backfilled temporarily until cables are being installed.

2.4.2.11.4 Watercourse/Culvert Crossing – Grid Connection Cable Route

The underground cable route crosses a number of minor culverts throughout its length and 3 no. bridge crossings. The construction methodology has been designed to eliminate the requirement for in-stream works. A general description of the various construction methods employed at culvert and bridge crossings are described in the following paragraphs below. A list of the bridge crossings and the proposed crossing method at each location is provided in Table 2.1 below. The crossing methodologies employed at the remaining 25 No. culvert crossings, along the grid connection cable route, will be selected from the suite of watercourse crossing options outlined below, as appropriate, depending on culvert type, depth, size and local ground conditions.

The bridge crossing locations are shown in Figure 2.2. The culvert crossing and bridge crossing locations are also shown on the underground cable route drawings included as Appendix 1.

Piped Culvert Crossings over Culvert – Option 1

Watercourses will not be directly impacted upon since no instream works or bridge/culvert alterations are proposed. Where sufficient cover exists above the culvert, the trench will be excavated above the culvert and the ducts will be installed in the trefoil arrangement passing over the sealed pipe where no contact will be made with the watercourse. This method of duct installation is further detailed in Figure 2.4

Piped Culvert Crossings under Culvert – Option 2

Watercourses will not be directly impacted upon since no instream works or bridge/culvert alterations are planned. Where the culvert consists of a socketed concrete or sealed plastic pipe, a trench will then be excavated beneath the culvert and cable ducts will be passed under the sealed pipe as outlined in Figure 2.5.

If this duct installation method cannot be achieved due to the invert level of the existing culvert or due to the composition of the culvert e.g. stone culverts, the ducts will be installed by alternative means as set out in the following sections.

Flatbed Formation over Culverts or at Road Level – Option 3

Where cable ducts are to be installed over an existing culvert where sufficient cover cannot be achieved by installing the ducts in a trefoil arrangement, the ducts will be laid in a much shallower trench the depth of which will be determined by the location of the top of the culvert. The ducts will be laid in this trench in a flatbed formation over the existing culvert and will be encased in 6mm thick steel galvanized plate with a 30N concrete surround as per ESB Networks specification. This method of duct installation is further detailed in Figure 2.6.

Where a bridge or culvert has insufficient deck cover to fully accommodate the required ducts, the ducts can be laid in a flatbed formation partially within the existing road surface. Where this option is to be employed, the ducts will also be encased in steel with a concrete surround as per Eirgrid and/or ESB Networks specifications. In order to achieve cover over these ducts and restore the carriageway of the road, it may be necessary to locally raise the pavement level to fully cover the ducts. The increase road level will be achieved by overlaying the existing pavement with a new wearing course as required. Any addition of a new pavement will be tied back into the existing road pavement at grade. After the crossing over the culvert has been achieved, the ducts will resume to the trefoil arrangement within a standard trench. This method of duct installation is further detailed in Figure 2.7.

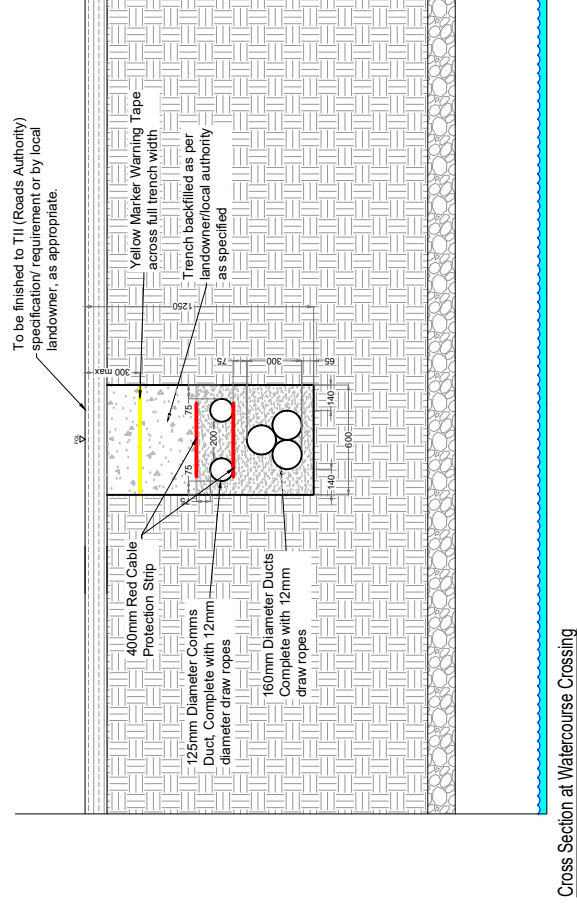
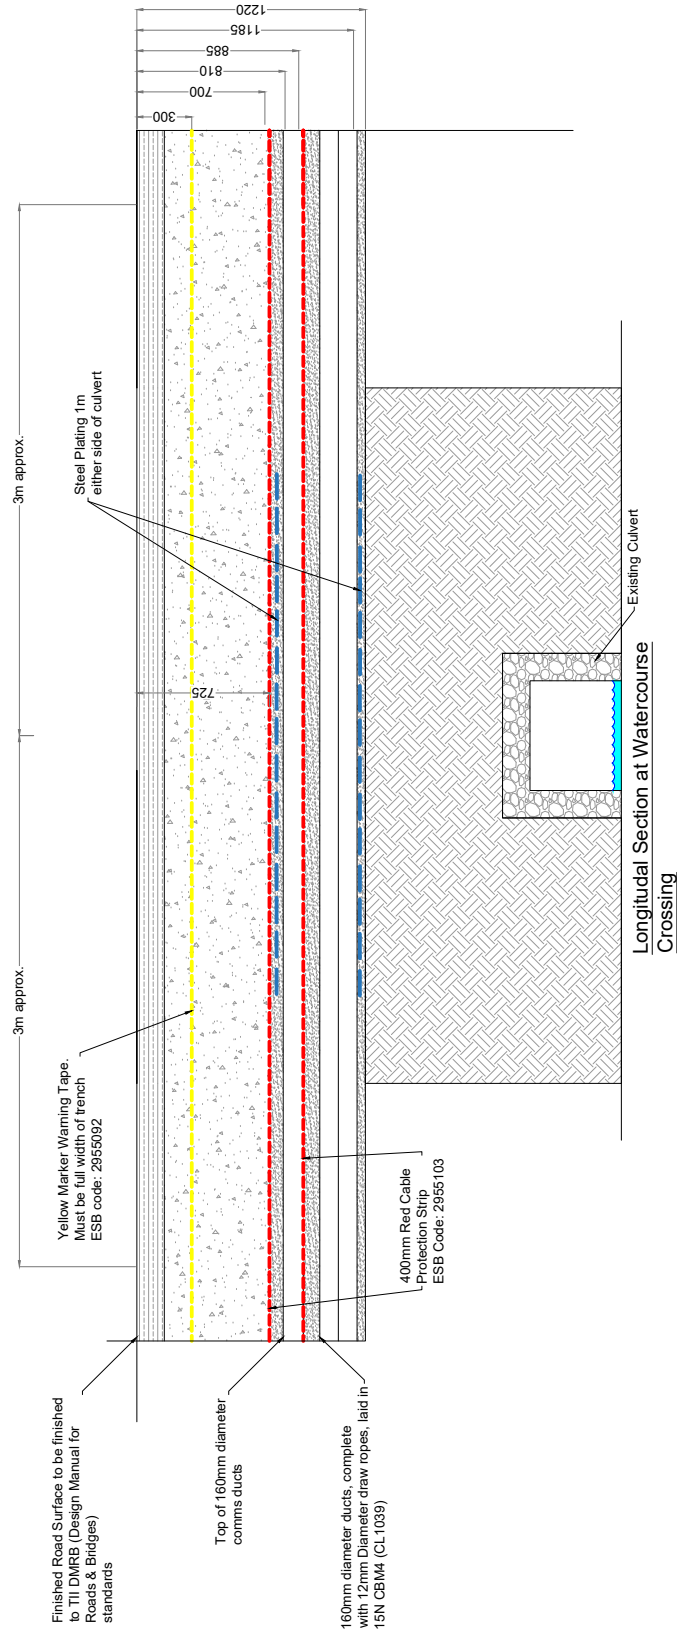


Figure 2.4

Cable Trench Over Culvert

PROJECT TITLE	Meenbog Wind Farm, Co. Donegal			
DRAWINGS	Joseph O'Brien	ENGINEER	Michael Watson	
PROJECT NO.	160602	DRAWING NO.	0502 - 53	
SCALE	1:30 @ A3	CASE	20.12.2018	

McCarthy Kevinite
 Kevinite
 O'Sullivan

Block 1,
 Planning & Environmental Consultants
 100, Springfield Services Centre,
 Monaghan Road,
 Galway, Ireland.
 email: info@mcCarthyKevinite.ie
 Tel: +353 (0)1 353 911 500
 Fax: +353 (0)1 717 729

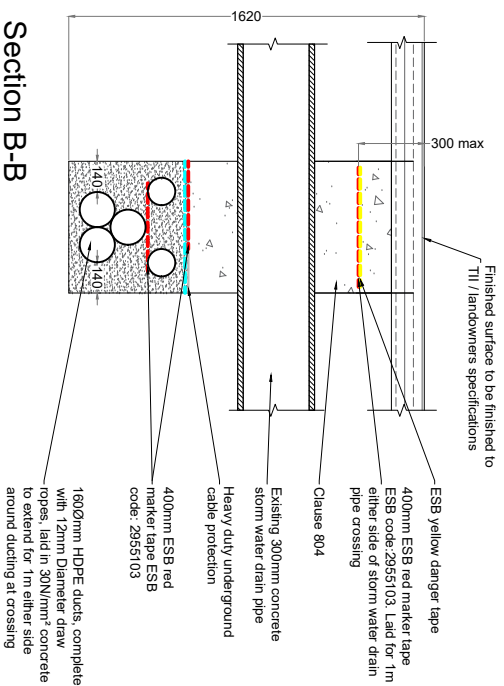
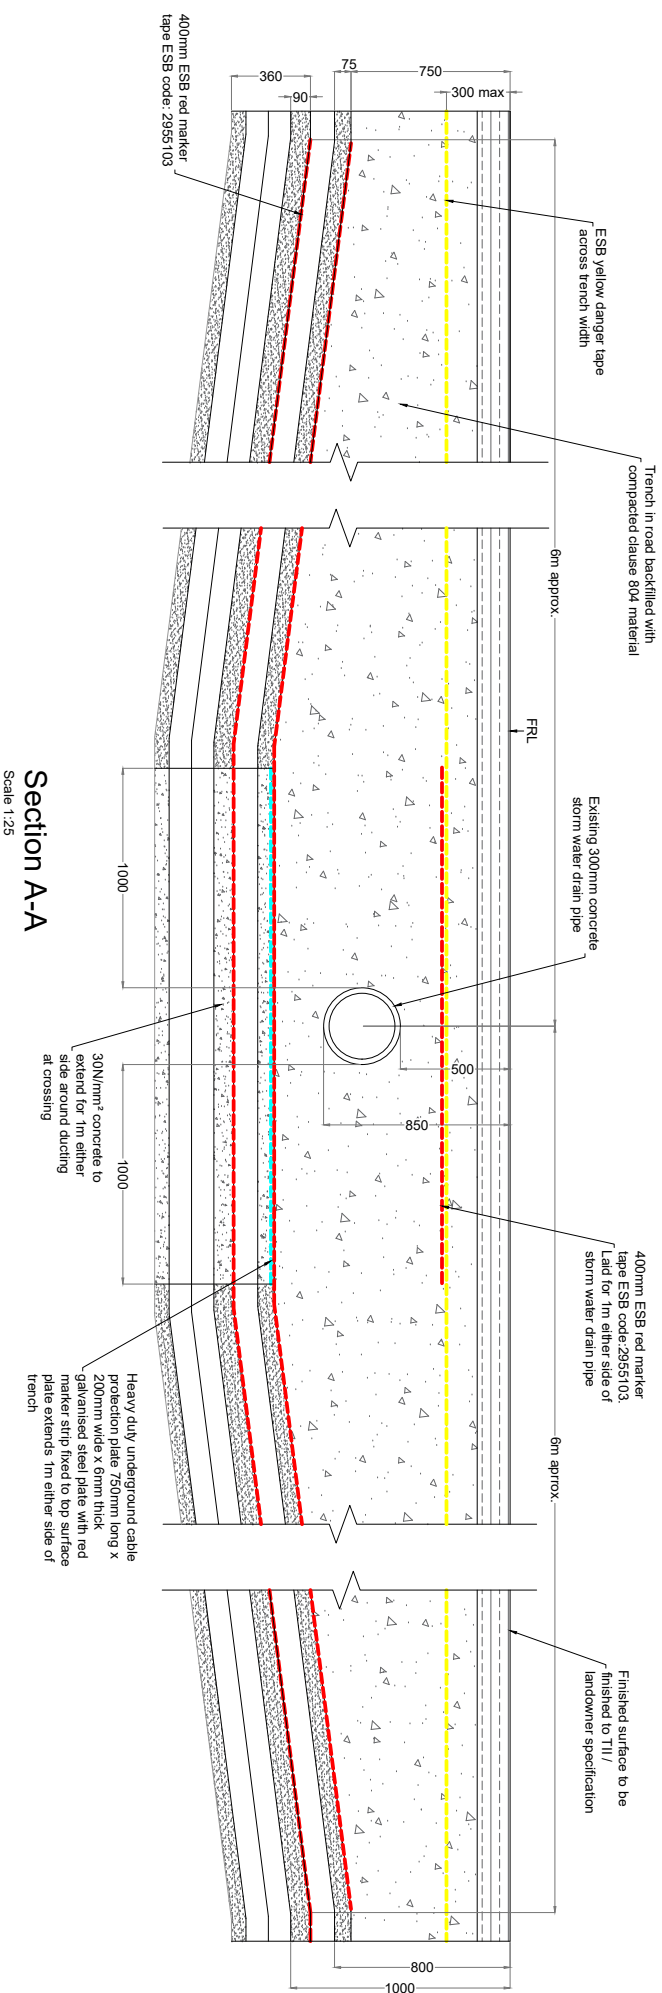


Figure 2.5

Cable Trench Under Piped Culvert

PROJECT FILE	
Meenbog Wind Farm, Co. Donegal	
DRAWING BY:	CHECKED BY:
PROJECT NO:	DRAWING NO:
160502	0502 - 54
SCALE	DATE:
1:25 @ A3	20.12.2018

McCarthy Keyville O'Sullivan Ltd
Planning & Environmental Consultants
Block 1,
Galway Financial Services Centre,
Moreenageisha Road,
Galway, Ireland.
email: info@mcCarthyKos.ie
website: www.mccarthykos.ie
Tel: +353 91 735611
Fax: +353 91 771279


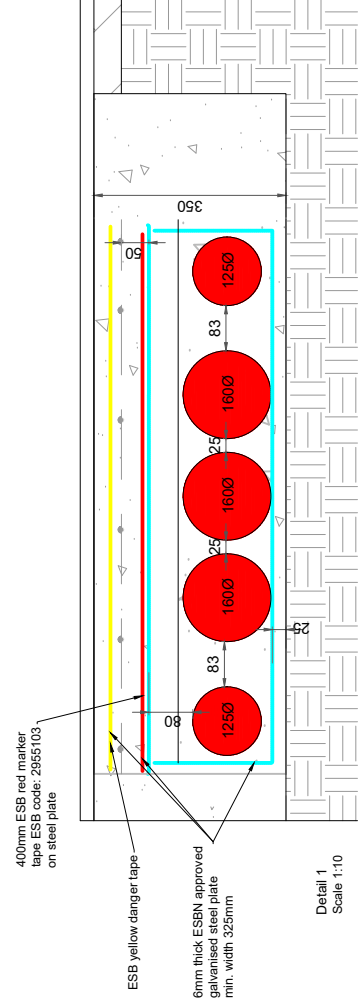


Figure 2.6

Cable Trench Flatbed Formation Over Culvert

Meenbog Wind Farm, Co. Donegal

DRAWN BY	CHECKED BY
Joseph O'Brien	Michael Watson
PROJECT NO	EXAMINATION NO
160502	0502 - 55
SCALE	DATE
As Shown @ A3	20.12.2018

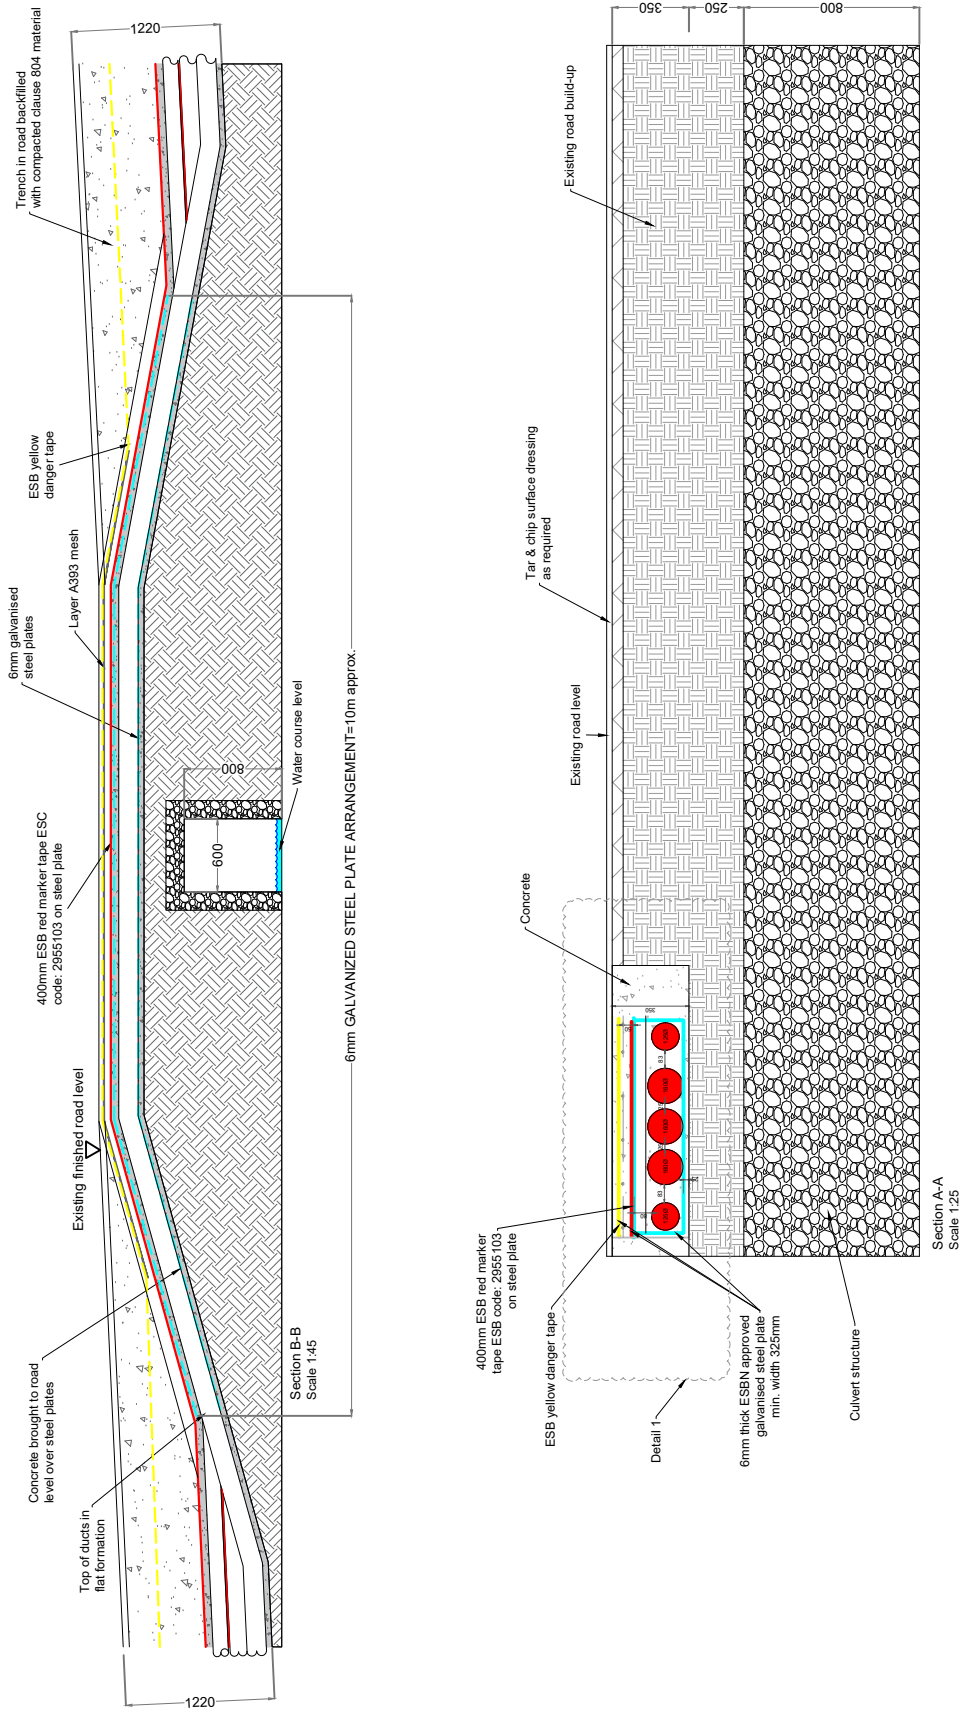

McCarthy Keville O'Sullivan Ltd.
Planning & Environmental Consultants
Block 1, The Industrial Estate, Carrigrohane,
Galway, Ireland.
www.mccarthyks.ie
email: info@mccarthyks.ie
Tel: +353 91 771277
Fax: +353 91 771279

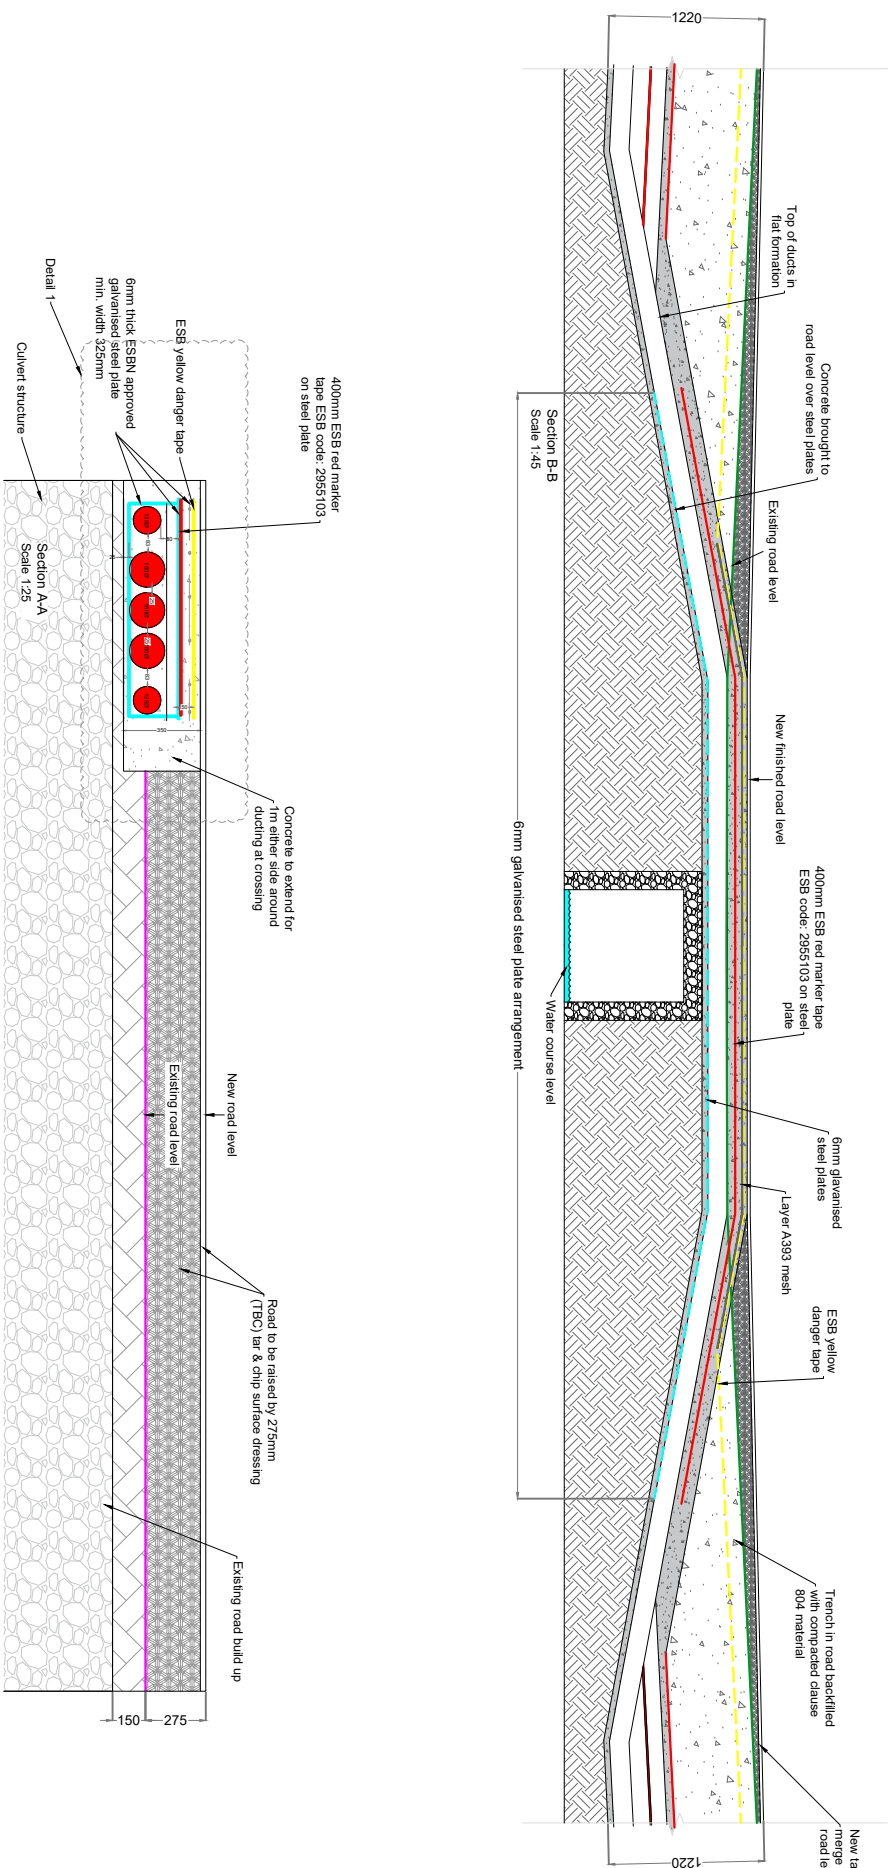


Figure 2.7

DRAWING TITLE	
Cable Trench Flatbed at Road Surface Level	
PROJECT TITLE	
Meenbog Wind Farm, Co. Donegal	
DRAWING NO.	
160902	
SCALE	
As Shown @ A3	
DATE	
20.12.2016	
CHECKED BY	
Michael Watson	
DRAWN BY	
Joseph O'Brien	
PROJECT NO.	
160902	
SCALE	
As Shown @ A3	
DATE	
20.12.2016	

The flatbed formation methodology will also be used at bridge structures where there is an existing footpath. The cables will be installed in the same flatbed arrangement where the existing footpath will be excavated to allow for the installation of the cables. The footpath will be reinstated after cable ducts have been installed. Where there is no existing footpath, it is proposed to install a footpath to encase the cable ducts after they have been laid in the flatbed formation.

Directional Drilling – Option 4

In the event that none of the above methods are appropriate, directional drilling will be utilised.

The directional drilling method of duct installation will be carried out using Vermeer D36 x 50 Directional Drill (approximately 22 tonnes), or similar plant, will be utilised for the horizontal directional drilling at watercourse/culvert crossings listed above. The launch and reception pits will be approximately 0.55m wide, 2.5m long and 1.5m deep. The pits will be excavated with a suitably sized excavator. The drilling rig will be securely anchored to the ground by means of anchor pins which will be attached to the front of the machine. The drill head will then be secured to the first drill rod and the operator shall commence to drill into the launch pit to a suitable angle which will enable him to obtain the depths and pitch required to the line and level of the required profile. Drilling of the pilot bore shall continue with the addition of 3.0m long drill rods, mechanically loaded and connected into position.

During the drilling process, a mixture of a natural, inert and fully biodegradable drilling fluid such as *Clear Bore™* and water is pumped through the centre of the drill rods to the reamer head and is forced in to void and enables the annulus which has been created to support the surrounding subsoil and thus prevent collapse of the reamed length. Depending on the prevalent ground conditions, it may be necessary to repeat the drilling process by incrementally increasing the size of the reamers. When the reamer enters the launch pit, it is removed from the drill rods which are then passed back up the bore to the reception pit and the next size reamer is attached to the drill rods and the process is repeated until the required bore with the allowable tolerance is achieved.

The use of a natural, inert and biodegradable drilling fluid such as *Clear Bore™* is intended to negate any adverse impacts arising from the use of other, traditional polymer-based drilling fluids and will be used sparingly as part of the drilling operations. It will be appropriately stored prior to use and deployed in the required amounts to avoid surplus. Should any excess drilling fluid accumulate in the reception or drilling pits, it will be contained and removed from the site in the same manner as other subsoil materials associated with the drilling process to a licensed recovery facility.

Backfilling of launch & reception pits will be conducted in accordance with the normal specification for backfilling excavated trenches. The directional drilling methodology is further detailed in Figure 2.8.

Horizontal Drilling – Option 5

The process of horizontal drilling is carried out by an auger boring machine. The methods employed are similar to directional drilling (a launch and reception pit are required). The drilling pit for horizontal drilling is excavated to a depth greater than that required for directional drilling. This is necessary as the drilling process is horizontal only and cannot drill in a downward direction to get under a watercourse as in the case of directional drilling. Therefore, the drilling pit is excavated to a base level

at which the drilling will take place which will be a minimum of 3 metres below the bed of the watercourse. The auger boring machine is mobilised within the drilling pit where an air driven auger cutting head bores through the ground horizontally. The drilled bore is supported by a steel sleeve which is hammered through the opening by air compressors during drilling to avoid collapse. The spoil material passes back through the auger within the steel sleeve and out of the bored channel. The process is continued until the crossing reaches the opposing reception pit on the other side of the watercourse. Electrical ducts will be passed through the sleeves and the steel sleeves will then be removed. The entire excavation will be backfilled as necessary. The horizontal drilling methodology is illustrated in Figure 2.9.

Table 2.1 Grid Connection Route Bridge Crossings Methodology

Bridge Crossing no.	Name	Description	Watercourse Crossing Option	Extent of In-stream Works
1	Lowerymore Bridge	The existing bridge consists of a concrete deck which cannot be excavated for a cable trench therefore the cable will be installed under the watercourse by means of directional or horizontal drilling which will ensure that no contact will be made with the watercourse during the works.	Option 4	None. No in-stream works required.
2	Lower Keadew Bridge	The existing bridge consists of a concrete deck which cannot be excavated for a cable trench therefore the cable will be installed under the watercourse by means of directional or horizontal drilling which will ensure that no contact will be made with the watercourse during the works.	Option 4	None. No in-stream works required.
3	Barnesmore Bridge	Stone arch bridge which cannot be excavated for a cable trench therefore the cable will be installed under the watercourse by means of directional or horizontal drilling which will ensure that no contact will be made with the watercourse during the works.	Option 4	None. No in-stream works required.

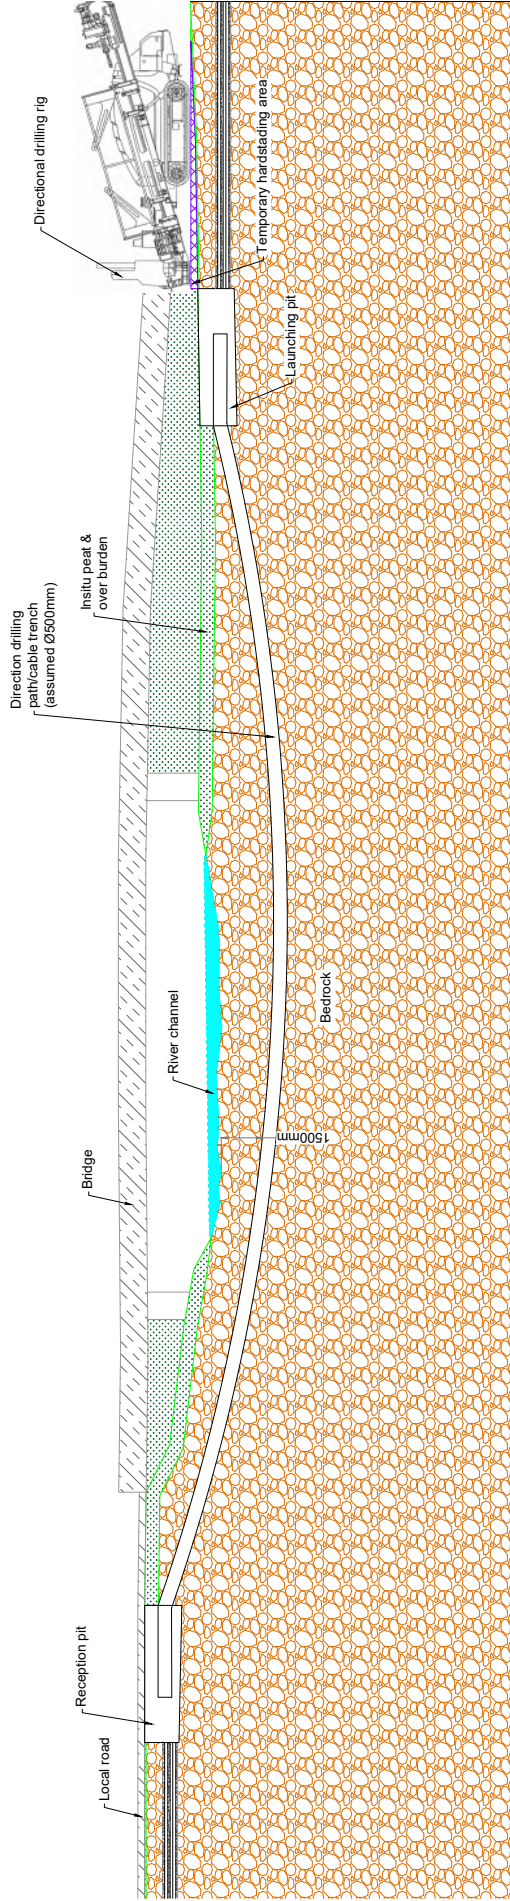


Figure 2.8

Directional Drilling

DRAWING TITLE	
PROJECT TITLE	
Meenbog Wind Farm, Co. Donegal	
DRAWN BY	CHECKED BY
Joseph O'Brien	Michael Watson
PROJECT NO.	EXAMINATION NO.
160502	0502 - 57
SCALE	DATE
1:200 @ A3	20.12.2018



McCarthy Keville O'Sullivan Ltd.
Planning & Environmental Consultants
Block 1, Lifford Industrial Estate, Carrinagh,
Galway, Ireland.
email: info@mcCarthyKos.ie
website: www.mcCarthyKos.ie
Fax: +353 91 771279

McCarthy Keville O'Sullivan Ltd.
Planning & Environmental Consultants
Block 1, Lifford Industrial Estate, Carrinagh,
Galway, Ireland.
email: info@mcCarthyKos.ie
website: www.mcCarthyKos.ie
Fax: +353 91 771279

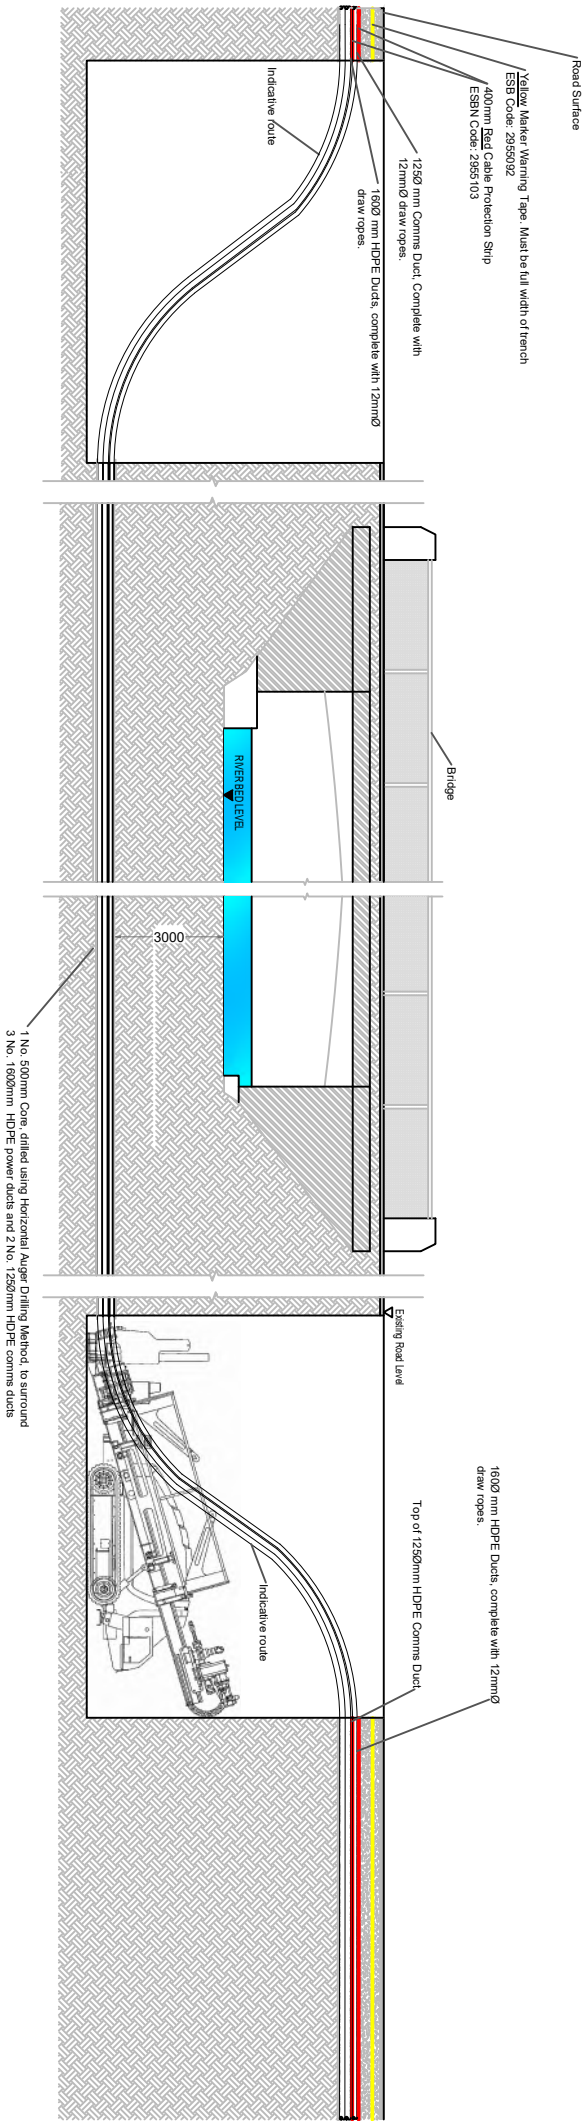


Figure 2.9

DRAWING TITLE			
Horizontal Auger Drilling			
PROJECT TITLE			
Meenbrog Wind Farm, Co. Donegal			
DRAWN BY		CHECKED BY	
Joseph O'Brien		Michael Watson	
PROJECT NO.		DRAWING NO.	
160602		0602 - 58	
SCALE		DATE	
1: 100 @ A3		20.12.2016	

2.4.2.11.5 General Construction Measures

Prior to any works commencing a dilapidation survey will be conducted of the entire grid connection route, photographing and noting any existing damage or defects to structure or road surfaces. A copy of this survey will be submitted to Donegal County Council prior to works commencing.

Communication with the public, local residences and businesses along the route will be an important responsibility of the project supervisor. Keeping all affected parties up to date and informed both shortly prior and during the construction period at all times. Two to three weeks before any work commencing reasonable efforts will be made to inform all affected parties of the oncoming works.

Signage will be erected in the weeks prior to any works commencing along and on adjacent roads to the cable route notifying the public of the forthcoming construction. Contact details for the contractor and details of license will also be posted along the cable route during construction.

Every effort will be made to minimise the impact of the above works on local residences and traffic. Consideration will also be given to the agricultural community and works will be organised and sequenced so as not to inconvenience any such activities.

- All personnel will be inducted and made familiar with the method statements, risk assessments and traffic management plans involved.
- All site-specific safety rules will be adhered to.
- All plant operators will have appropriate CSCS training.
- All personnel will have SOLAS Safe Pass training
- Fire extinguishers and first aid supplies will be available in the work area.
- The road way will be maintained in clean condition at all times.
- Helmets, high visibility clothing and safety footwear will be worn at all times.
- A competent foreman will be on site at all times.
- Excavations are back filled at the end of each working day.
- The trench will not be over crowded.
- Unauthorised access will be monitored and prevented.
- Pipe work will be lifted into position manually.
- Hand dig will be used to expose any services detected during the survey.

2.4.2.12 Recreation and Amenity Areas

The recreation and amenity facilities consist of a series of marked walkways, complimented by waypoint signage, and visitor facilities in the form of a car park, play areas, barbeque area, picnic area and community garden. The walkways will be constructed with the same methodology for site access roads. The temporary construction compound located in the north of the site will provide an amenity area within the site once the Permitted Development has been commissioned. This area will be developed as a compound initially so it will be well established requiring only minor works to accommodate the facilities.

Waypoint signage will be installed throughout the recreation and amenity area to provide information and location reference point for facility users. The signage will be installed as part of the amenity walkway construction where the signage poles will be erected in concrete footings.

2.4.2.13 Decommissioning

The design life of the wind farm is 30 years after which time decommissioning will occur. At the end of the design life of the wind farm, or if the operations at the wind farm cease for a period of greater than one year, the turbines, met mast and all their

associated above ground components will be removed from site. The turbine foundations will be covered with soil to facilitate re-vegetation. The management of waste materials arising from the decommissioning of the development is outlined in the Waste Management Plan (Section 4 below).

Site roadways could be in use for other purposes other than the wind operation of the wind farm by the time the decommissioning of the project is to be considered, and therefore it may be more appropriate to leave the site roads in situ for future use. If it were to be confirmed that the roads were not required in the future for any other useful purpose, they could be removed

The substation will remain in place as it will be under the ownership of the ESB/EirGrid. Underground cables will be removed and the ducting left in place.

A full reinstatement plan will be submitted to Donegal County Council three months prior to decommissioning.

3 ENVIRONMENTAL MANAGEMENT

3.1 Introduction

This CEMP has been prepared and presented as a standalone document and includes all drainage measures required to construct the wind farm. The drainage proposals will be developed further prior to the commencement of construction however, any such improvements will be in line with the principles and mitigation presented in the EIAR. The following sections give an overview of the drainage design, dust and noise control measures and a waste management plan for the site.

3.2 Protecting Water Quality

3.2.1 Environmental Management in the Construction Phase

Timing of road works can strongly influence the potential for damaging the freshwater environment. Operations during wetter periods of the year pose a significantly greater risk of causing erosion and siltation, which can be particularly severe following major rainfall or snowmelt events. Traditionally, wind farm construction undertaken during the drier summer months would result in significantly less erosion and siltation. Construction activities in the hydrological buffer zones shall be avoided during or after prolonged rainfall or an intense rainfall event and work will cease entirely near watercourses when it is evident that water quality is being impacted. Given that this site has an established road network and existing watercourse crossing points, there will be minimal impacts on watercourses.

3.2.2 Site Drainage Design

The site drainage features for this site have previously been outlined in Section 4.7 of the EIAR and are again further developed in Section 4 of this CEMP. The protection of the watercourses within and surrounding the site, and downstream catchments that they feed is of utmost importance in considering the most appropriate drainage proposals for the site of the Permitted Development. No routes of any natural drainage features will be altered as part of the Permitted Development as new watercourse crossings are kept to a minimum to facilitate the Permitted Development. Turbine locations and associated roadways were originally selected to avoid natural watercourses and existing roads are to be used wherever possible. The Permitted Development has where possible, been kept a minimum of 50 metres from natural watercourses. There will be no direct discharges to any natural watercourses, with all drainage waters being dispersed as overland flows. Buffer zones around the existing natural drainage features have informed the layout of the Permitted Development.

Existing artificial drains in the vicinity of existing site roads will be maintained in their present location where possible. If it is expected that these artificial drains will receive drainage water from works areas, check dams will be added (as specified below) to control flows and sediment loads in these existing artificial drains. If road widening or improvement works are necessary along the existing roads, where possible, the works will take place on the opposite side of the road to the drain.

3.2.3 Legislation and Best Practice Guidance

The drainage design has been prepared based on experience of the project team of other wind farm sites in peat-dominated environments, and the number of best practice guidance documents.

There is no one guidance document that deals with drainage management and water quality controls for wind farm developments. However, a selection of good practice approaches have been adopted in preparation of this CEMP, and these are taken from the various best practice guidance documents listed below. These relate to infrastructure and operational works on forested sites, forest road design, water quality controls for linear projects, forestry road drainage and management of geotechnical risks. To achieve best practice in terms of water protection through construction management all drainage management is prepared in accordance with guidance contained in the following:

- Forestry Commission (2004): Forests and Water Guidelines, Fourth Edition. Publ. Forestry Commission, Edinburgh;
- Coillte (2009): Forest Operations & Water Protection Guidelines;
- Forest Service (Draft): Forestry and Freshwater Pearl Mussel Requirements – Site Assessment and Mitigation Measures;
- Forest Service (2000): Forestry and Water Quality Guidelines. Forest Service, DAF, Johnstown Castle Estate, Co. Wexford;
- Forest Service, (2000): Code of Best Forest Practice – Ireland. Forest Service, DAF, Johnstown Castle Estate, Co. Wexford;
- COFORD (2004): Forest Road Manual – Guidelines for the design, construction and management of forest roads;
- MacCulloch (2006): Guidelines for risk management of peat slips on the construction of low volume low cost roads over peat (Frank MacCulloch Forestry Civil Engineering Forestry Commission, Scotland);
- Authority (2005): Guidelines on Procedures for Assessment and Treatment of Geology, Hydrology and Hydrogeology for National Road Schemes;
- Wind Farm Development Guidelines for Planning Authorities (September 1996);
- Requirements for the Protection of Fisheries Habitat during Construction and Development Works at River Sites. Eastern Regional Fisheries Board;
- Guidelines on Protection of Fisheries During Construction Works Adjacent to Waters, Inland Fisheries Ireland (2016);
- Good Practice During Wind Farm Construction (Scottish Natural Heritage, 2010);
- PPG1 - General Guide to Prevention of Pollution (UK Guidance Note);
- PPG5 – Works or Maintenance in or Near Water Courses (UK Guidance Note);
- CIRIA (Construction Industry Research and Information Association) guidance on 'Control of Water Pollution from Linear Construction Projects' (CIRIA Report No. C648, 2006);
- Control of water pollution from construction sites - Guidance for consultants and contractors. CIRIA C532. London, 2001; and,
- Control of water pollution from linear construction projects -Technical guidance. CIRIA C648 London, 2006.

3.2.4 Site Drainage and Management

3.2.4.1 Preparative Site Drainage Management

The materials and equipment necessary to implement the drainage measures outlined above will be brought on-site in advance of any works commencing.

An adequate quantity of straw bales, clean stone, terram, stakes, etc. will be kept on site at all times to implement the drainage design measures as necessary. The drainage measures outlined in the above will be installed prior to, or at the same time as the works they are intended to drain.

3.2.4.2 Pre-emptive Site Drainage Management

The works programme for the groundworks element of the construction phase will take account of weather forecasts and predicted rainfall in particular. Large excavations, large movements of overburden or large-scale overburden or soil stripping will be suspended or scaled back if heavy rain is forecast. The extent to which works will be scaled back or suspended will relate directly to the amount of rainfall forecast.

3.2.4.3 Reactive Site Drainage

The final drainage design prepared for the site has provided for reactive management of drainage measures. The effectiveness of drainage measures designed to minimise runoff entering works areas and capture and treat silt-laden water from the works areas, will be monitored continuously by the Environmental Clerk of Works (ECoW) on-site. The ECOW or supervising hydrologist will respond to changing weather, ground or drainage conditions on the ground as the project proceeds, to ensure the effectiveness of the drainage design is maintained in so far as is possible. This may require the installation of additional check dams, interceptor drains, or swales as deemed necessary on-site. The drainage design may have to be modified on the ground as necessary, and the modifications will draw on the various features outlined above in whatever combinations are deemed to be most appropriate to situation on the ground at a particular time.

In the event that works are giving rise to siltation of watercourses, the ECOW or supervising hydrologist will stop all works in the immediate area around where the siltation is evident. The source of the siltation will be identified and additional drainage measures such as those outlined above will be installed in advance of works recommencing.

3.2.4.4 Operational Phase Drainage

The project hydrologist will inspect and review the drainage system after construction has been completed to provide guidance on the requirements of an operational phase drainage system. This operational phase drainage system will have been installed during the construction phase in conjunction with the road and hardstanding construction work as described below:

- Interceptor drains will be maintained up-gradient of all infrastructure to collect clean surface runoff, in order to minimise the amount of runoff reaching areas where suspended sediment could become entrained. It will then be directed to areas where it can be re-distributed over the ground by means of a level spreader.
- Swales/road side drains will be maintained to intercept and collect runoff from access roads and hardstanding areas of the site, likely to have entrained suspended sediment, and channel it to stilling ponds for sediment settling;
- Check dams will be maintained at regular intervals along interceptor drains and swales/roadside drains in order to reduce flow velocities and therefore minimise erosion within the system during storm rainfall events; and,
- Stilling ponds/settlement ponds, emplaced downstream of swales and roadside drains, will buffer volumes of runoff discharging from the drainage system during periods of high rainfall, by retaining water until the storm hydrograph has receded, thus reducing the hydraulic loading to watercourses. The stilling ponds will be sized according to the size of the area they will be receiving water from but will be sufficiently large to accommodate peak flows storm events. Inspection and maintenance of all settlement ponds will be ongoing through the construction period.

3.3 Refuelling, Fuel and Hazardous Materials Storage

The following mitigation measures are proposed to avoid release of hydrocarbons at the site:

- Minimal refuelling or maintenance of construction vehicles or plant will take place on site. Off-site refuelling should occur at a controlled fuelling station;
- On-site refuelling will take place using a mobile double skinned fuel bowser. The fuel bowser, a double-axel custom-built refuelling trailer will be re-filled off site and will be towed around the site by a 4x4 jeep to where machinery is located. It is not practical for all vehicles to travel back to a single refuelling point, given the size of the cranes, excavators, etc. that will be used during the construction of the wind farm. The 4x4 jeep will also carry fuel absorbent material and pads in the event of any accidental spillages. The fuel bowser will be parked on a level area in the construction compound when not in use. Only designated trained and competent operatives will be authorised to refuel plant on site. Mobile measures such as drip trays and fuel absorbent mats will be used during all refuelling operations.
- Fuels volumes stored on site should be minimised. Any fuel storage areas will be bunded appropriately for the fuel storage volume for the time period of the construction and fitted with a storm drainage system and an appropriate oil interceptor;
- The electrical substation building will be bunded appropriately to the volume of oils likely to be stored, and to prevent leakage of any associated chemicals and to groundwater or surface water. The bunded area will be fitted with a storm drainage system and an appropriate oil interceptor;
- The plant used should be regularly inspected for leaks and fitness for purpose; and,
- An emergency plan for the construction phase to deal with accidental spillages will be contained within Environmental Management Plan. Spill kits will be available to deal with and accidental spillage in and outside the refuelling area.

3.4 Cement Based Products Control Measures

The following mitigation measures are proposed to avoid release of cement leachate from the site:

- No batching of wet-cement products will occur on site;
- Ready-mixed supply of wet concrete products and where possible, emplacement of pre-cast elements, will take place. Where possible pre-cast elements for culverts and concrete works will be used;
- No washing out of any plant used in concrete transport or concreting operations will be allowed on-site;
- Where concrete is delivered on site, only chute cleaning will be permitted, using the smallest volume of water possible. No discharge of cement contaminated waters to the construction phase drainage system or directly to any artificial drain or watercourse will be allowed.
- Use weather forecasting to plan dry days for pouring concrete;
- Ensure pour site is free of standing water and plastic covers will be ready in case of sudden rainfall event;
- The small volume of water that will be generated from washing of the concrete lorry's chute will be directed into a concrete washout area, typically built using straw bales and lined with an impermeable membrane. Two examples are shown in Plates 3.1 and 3.2 below. The areas are generally covered when not in use to prevent rainwater collecting. In periods of dry weather, the areas can be

uncovered to allow much of the water to be lost to evaporation. At the end of the concrete pours, any of the remaining liquid contents is tankered off-site. Any solid contents that will have been cleaned down from the chute will have solidified and can be broken up and disposed of along with other construction waste.

The 50m wide river buffer zone and 20 m existing artificial drainage buffer will be emplaced for the duration of the construction phase. No construction activity will occur within the buffer zone with the exception of bridge and culvert construction. The buffer zone will:

- Prevent any cement based products accidentally entrained in the construction phase drainage system entering directly into watercourses, achieved in part by ending drain discharge outside the 50m buffer zone and allowing percolation across the vegetation of the buffer zone;
- Provide a buffer against accidental direct run-off to surface waters by any pollutants, or by pollutants entrained in surface water run-off.



Plate 3.1 Concrete washout area



Plate 3.2 Concrete washout area

3.5 Peat Stability Management

The management of the peat volumes summarised in Section 2.4.2.2 in terms of peat stability is summarised in this section. Peat instability or failure refers to a significant mass movement of a body of peat that would have an adverse impact on wind farm development and the surrounding environment. Peat failure excludes localised movement of peat that could occur below an access road, creep movement or erosion type events. In the absence of appropriate mitigation, the consequence of peat failure at the study area may result in:

- Death or injury to site personnel;
- Damage to machinery;
- Damage or loss of access tracks;
- Drainage disrupted;
- Site works damaged or unstable;
- Contamination of watercourses, water supplies by sediment particulates; and,
- Degradation of the environment.

3.5.1 General Recommendations for Good Construction Practice

The peat stability assessment indicates that there is insignificant risk of peat failure, although drainage mitigation measures would be required to prevent the build-up of water in the peat and reduce the risk of failure (AGEC, 2017).

The following issues incorporated into the construction phase of the project will assist in the management of the risks for this site (AGEC, 2017):

- Appointment of experienced and competent contractors;
- The site should be supervised by experienced and qualified personnel;
- Allocate sufficient time for the project (be aware that decreasing the construction time has the potential to increase the risk of initiating a peat movement);
- Prevent undercutting of slopes and unsupported excavations;
- Maintain a managed robust drainage system;
- Prevent placement of loads/overburden on marginal ground;
- Set up, maintain and report readings from peat stability monitoring systems;
- Ensure construction method statements are followed or where agreed modified/ developed; and,
- Revise and amend the Geotechnical Risk Register as construction progresses.

3.6 Traffic Management

Traffic Management Plans for the construction phase of the wind farm and grid connection are included in Appendix 4. The Traffic Management Plans have been prepared to consider both the wind farm and the grid connection works as standalone projects.


Where grid connection works relating to the Meenbog Wind Farm are ongoing, the contractor will schedule and phase these works accordingly to ensure that these works do not coincide with intensive periods of construction on the wind farm development and thus reduce the impact of concurrent construction specific to the wind farm.

3.6.1 Turbine and Materials Transport Route

Material such as concrete will be sourced from a local quarry and will access the site using the N15 as the primary haul route to access the site as outlined in Figure 3.1. All deliveries will access the site via the western or northern entrance using this haul route. All deliveries of construction materials to the site will take place within the defined working hours of 7am – 7pm. It may be necessary on occasion, to commence works before 7am where concrete pours will be required to start earlier due to the volume of concrete required and the location of the concrete pour relative to the concrete supplier's batching plant. Main pours will be planned days and weeks in advance and will ensure disruption to work and school related traffic is avoided. The locations of all turbine foundations where large concrete pours will take place are off the public road and will be accessed by the internal site roads and will therefore eliminate the potential for queuing of trucks on the adjoining public road network. The typical vehicle type for delivery of construction materials to site with the exception of the wind turbines will be with standard heavy goods vehicles (HGV).

A detailed traffic and transport management plan for turbine delivery will be prepared by the haulage company, when appointed and will be submitted to Donegal County Council for approval. The plan will include:

- A delivery schedule.
- A schedule of control measures for exceptional wide and heavy loads.
- Details of temporary works or any other minor alteration identified.
- A dry run of the route using vehicles with similar dimensions.

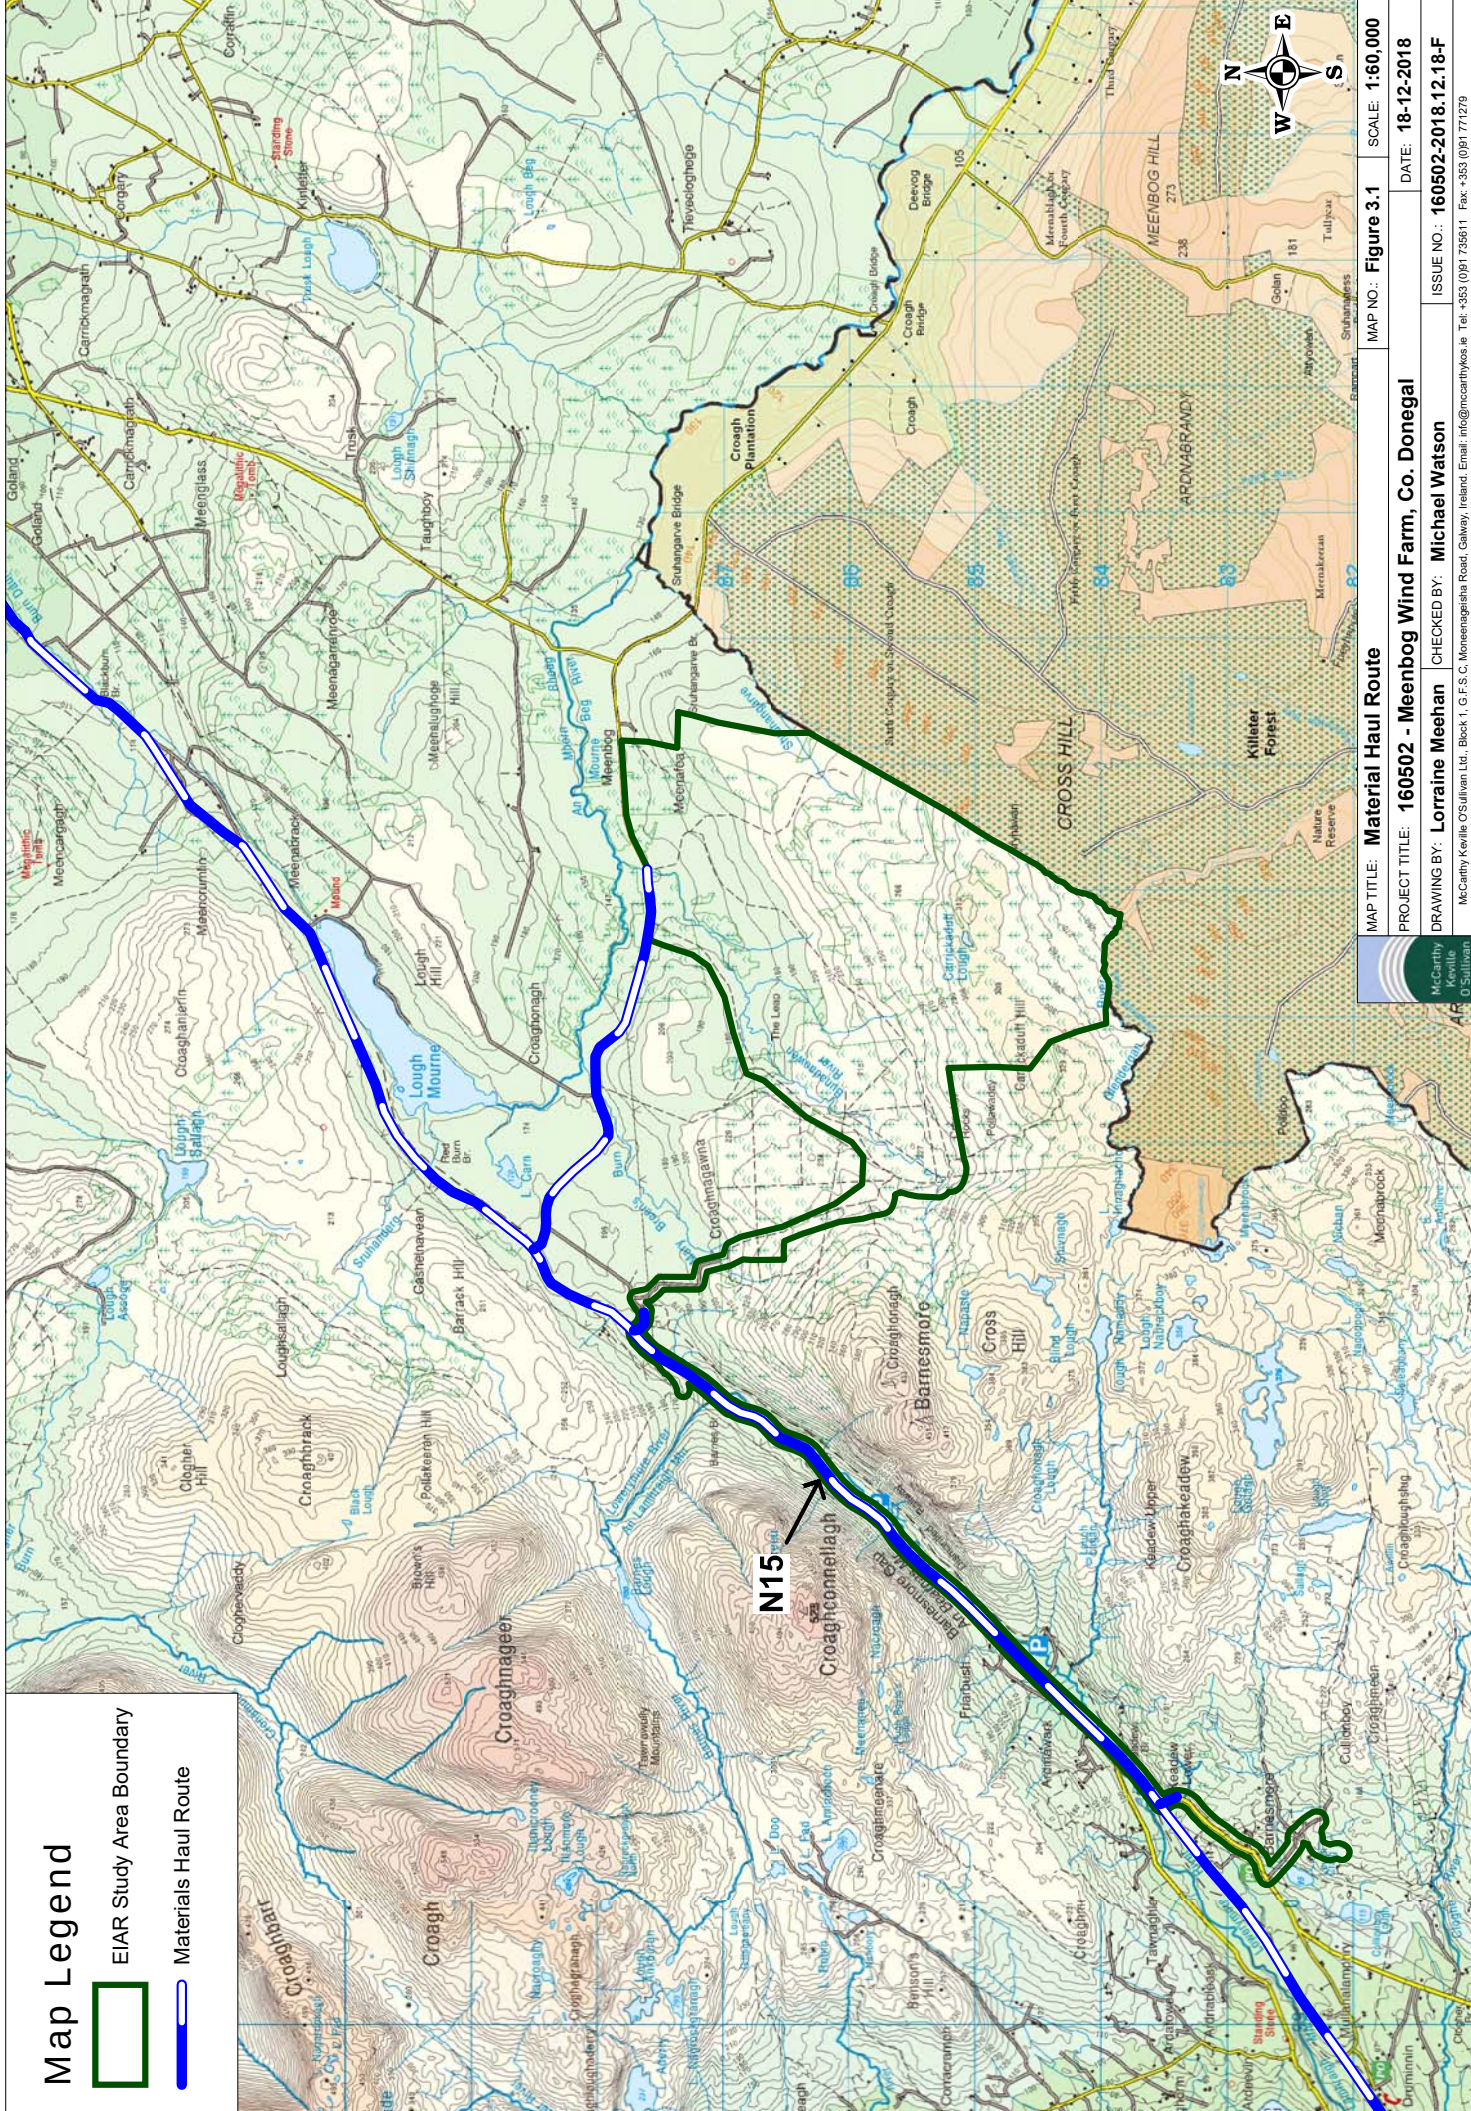

Map Legend

-  EIAR Study Area Boundary
-  Materials Haul Route



McCarthy Keville O'Sullivan

MAP TITLE: **Material Haul Route**

PROJECT TITLE: **160502 - Meenbog Wind Farm, Co. Donegal**

DRAWING BY: **Lorraine Meehan** CHECKED BY: **Michael Watson**

McCarthy Keville O'Sullivan Ltd, Block 1, G.F.S.C. Morenagarra Road, Galway, Ireland. Email: info@mcCarthyKeville.ie Tel: +353 (0)91 735611 Fax: +353 (0)91 771279


MAP NO.: **Figure 3.1**

SCALE: **1:60,000**


DATE: **18-12-2018**

ISSUE NO.: **160502-2018.12.18-F**

Map Legend

 EIA/R Study Area Boundary

 Turbine Delivery Route

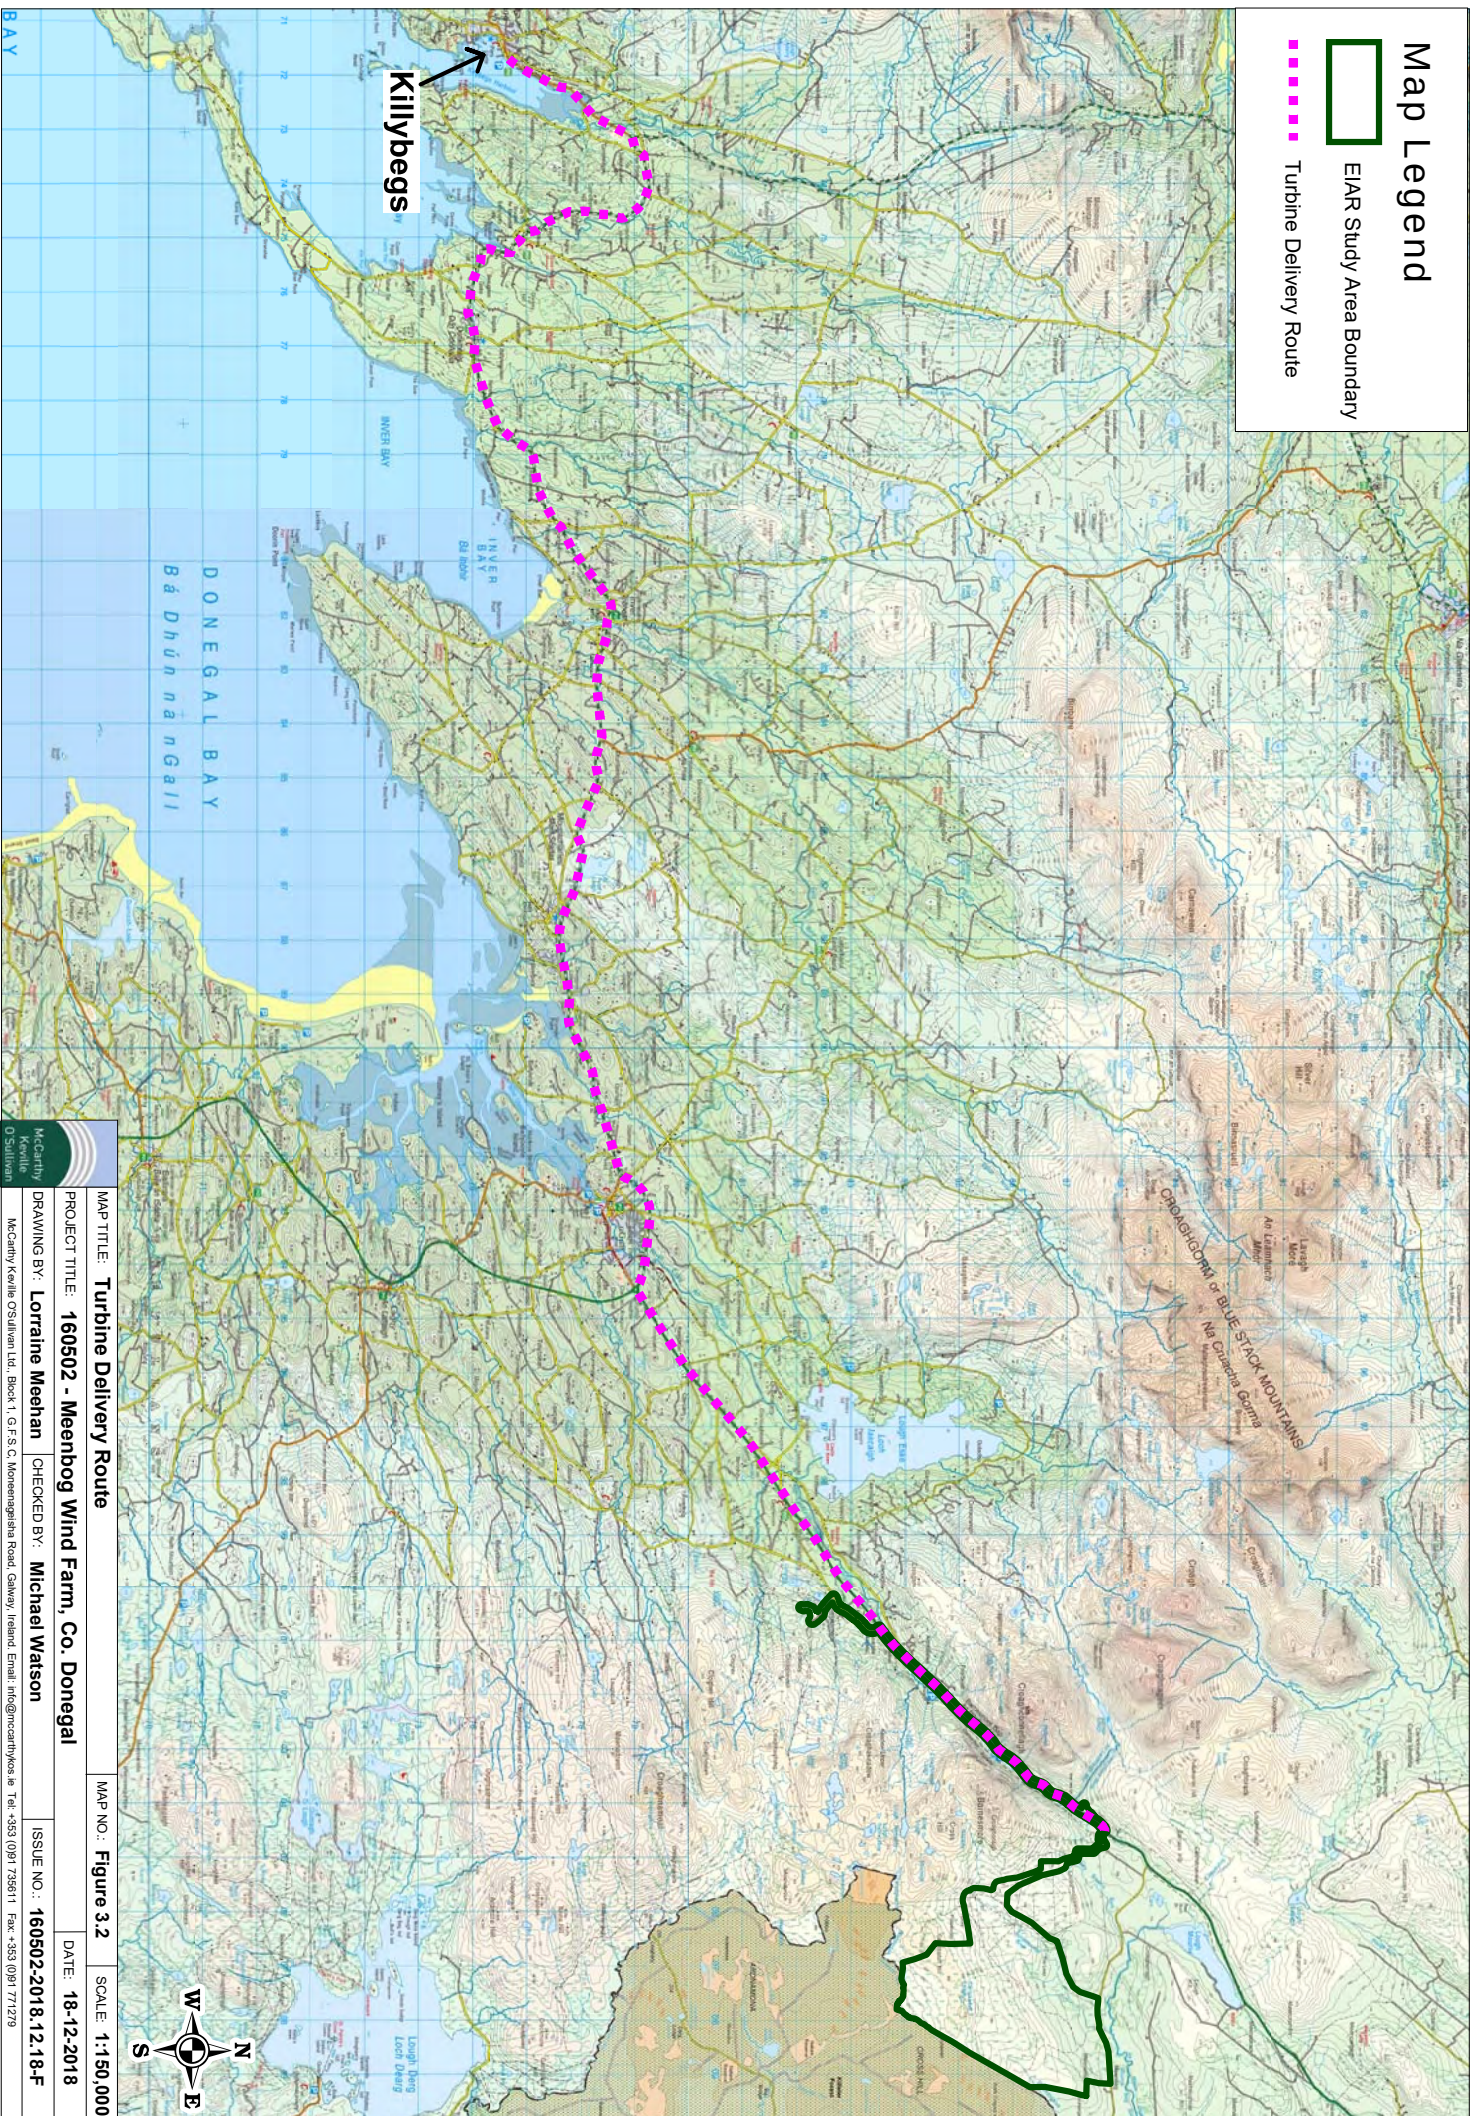

The turbine transport route from the N15 National Secondary Road to the development sites are shown on Figure 3.2 also. The deliveries of turbine components to the site will be made in convoys of three to four vehicles at a time, and mostly at night when roads are quietest. Convoys will be accompanied by escorts at the front and rear operating a "stop and go" system. Although the turbine delivery vehicles are large, they will not prevent other road users or emergency vehicles passing, should the need arise. The delivery escort vehicles will ensure the turbine transport is carried out in a safe and efficient manner with minimal delay or inconvenience for other road users. It is not anticipated that any section of the local road network will be closed during transport of turbines, although there will be some delays to local traffic at pinch points. During these periods it may be necessary to operate local diversions for through traffic. All deliveries comprising abnormally large loads will be made outside the normal peak traffic periods to avoid disruption to work and school-related traffic.

Prior to the Traffic Management Plan for turbine delivery being finalised, a full dry run of the transport operation along the proposed route will be completed using vehicles with attachments to simulate the dimensions of the wind turbine transportation vehicles. This dry run will inform the final traffic management plan. All turbine deliveries will be provided for in a transport management plan which will have to be prepared in advance of the turbine delivery stage, when the exact transport arrangements are known, delivery dates confirmed and escort proposals in place. Such a transport management plan is typically submitted to the Planning Authority for agreement in advance of any abnormal loads using the local roads, and will provide for all necessary safety measures, including a convoy and Garda escort as required, off-peak turning/reversing movements and any necessary safety controls.

The roads and bridges all haul route will be subject to a condition survey by a suitably qualified engineer both before and after construction. Protection measures for such infrastructure as specified by the appointed engineers report will be implemented in full prior to construction.

In the event of construction damage arising on any roads or bridges along the haul route it will be rectified immediately by the developer under consultation with the relevant roads engineer.


Prior to the delivery of oversized loads, the developer will engage with the local community to provided information on the scale, time and duration of such deliveries. This information will be informed by pre-delivery surveys which will be completed by the suppliers. This information will be relayed to the local community by information leaflet and a website if deemed necessary.

The proposed construction will run from February 2019 – July 2020 as summarised in Section 9 below. This is the timescale within which it is intended to use the public road network as outlined in Figures 3.1 & 3.2 to facilitate construction of the development.

3.7 Ecological Management

The construction works associated with the upgrade of the existing access track adjacent to the Croaghonagh Bog Special Area of Conservation (site code: 000129) shall not encroach upon the Special Area of Conservation. Figure 3.3 set out the location of Croaghonagh Bog relative to the development site.

Surveys for Irish Ladies tresses can only be conducted will be carried out prior to works in applicable areas between **early August and early September** (NRA 2009). Surveys

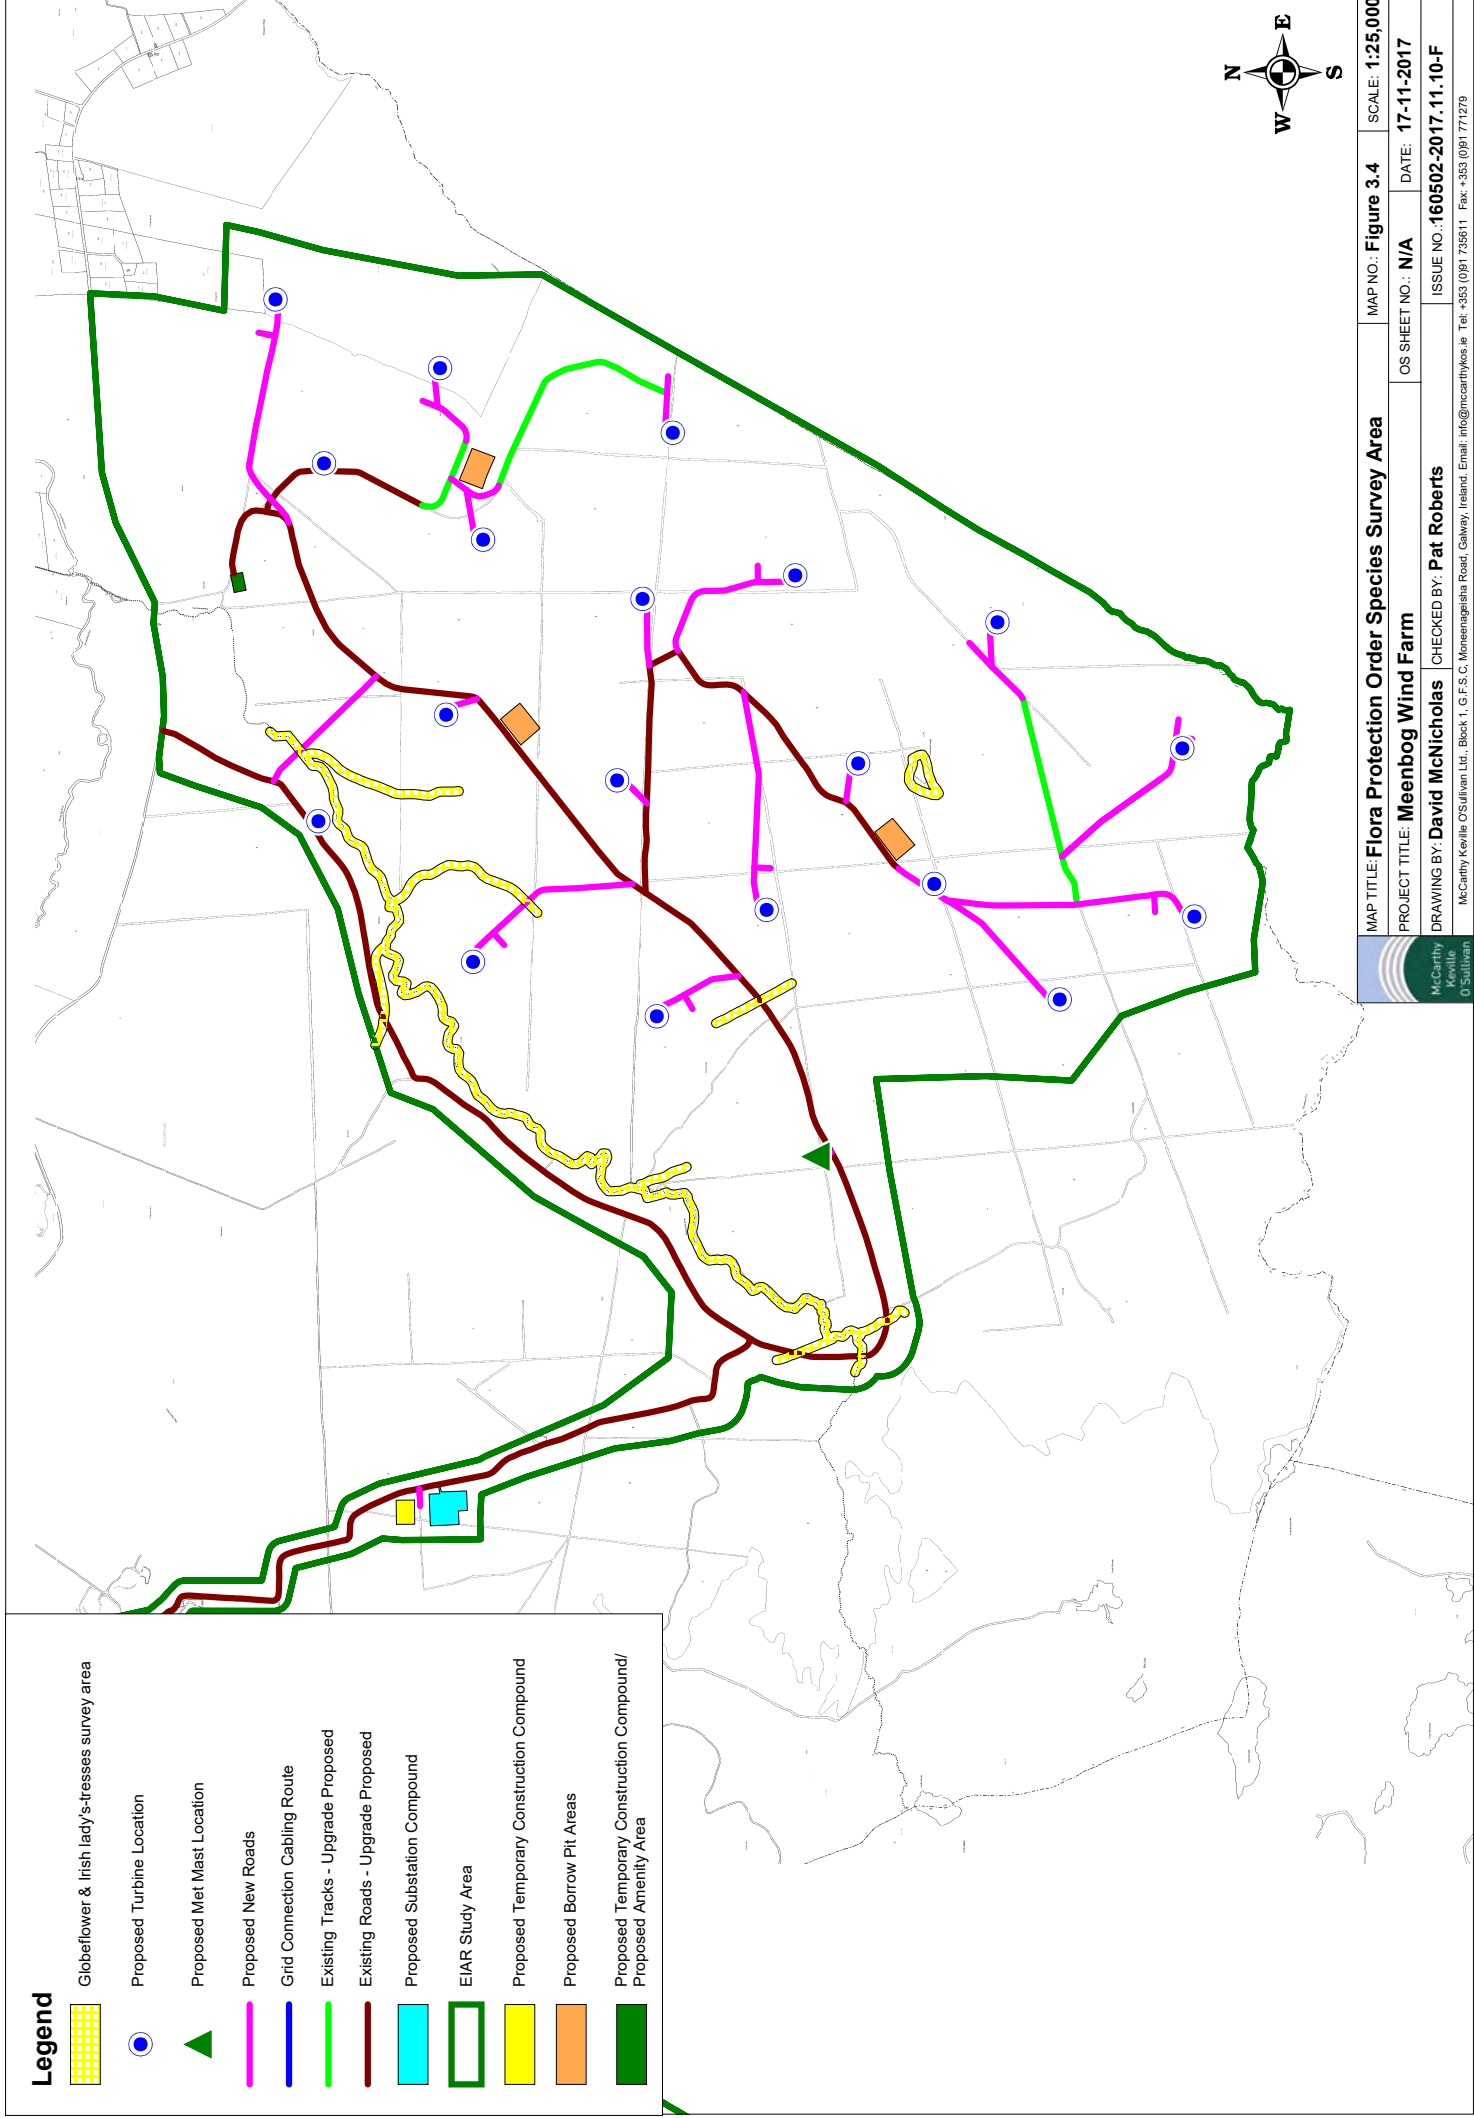

for Globeflower will be conducted between **June and August**. Surveys will only be required where works traverse potential suitable habitat as identified in Figure 3.4. Works can proceed outside the identified areas.

3.8 Dust Control

Construction dust can be generated from many on-site activities such as excavation and backfilling. The extent of dust generation will depend on the type of activity undertaken, the location, the nature of the dust, *i.e.* soil, sand, peat, etc. and the weather. In addition, dust dispersion is influenced by external factors such as wind speed and direction and/or, periods of dry weather. Construction traffic movements also have the potential to generate dust as they travel along the haul route.

Proposed measures to control dust include:

- Any site roads with the potential to give rise to dust will be regularly watered, as appropriate, during dry and/or windy conditions;
- The designated public roads outside the site and along the main transport routes to the site will be regularly inspected by the ECoW for cleanliness, and cleaned as necessary;
- Material handling systems and material storage areas will be designed and laid out to minimise exposure to wind;
- Water misting or sprays will be used as required if particularly dusty activities are necessary during dry or windy periods;
- Water misting or bowzers will operate on-site as required to mitigate dust in dry weather conditions;
- The transport of soils or other material, which has significant potential to generate dust, will be undertaken in tarpaulin-covered vehicles where necessary;
- All construction related traffic will have speed restrictions on un-surfaced roads to 20 kph;
- Daily inspection of construction sites to examine dust measures and their effectiveness.
- When necessary, sections of the haul route will be swept using a truck mounted vacuum sweeper; and,
- All vehicles leaving the construction areas of the site will pass through a wheel cleansing area prior to entering the local road network.

3.9 Noise Control

The operation of plant and machinery, including construction vehicles, is a source of potential impact that will require mitigation at all locations within the site. Proposed measures to control noise include:

- Diesel generators will be enclosed in sound proofed containers to minimise the potential for noise impacts;
- Plant and machinery with low inherent potential for generation of noise and/or vibration will be selected. All construction plant and equipment to be used on-site will be modern equipment and will comply with the European Communities (Construction Plant and Equipment) (Permissible Noise Levels) Regulations;
- Regular maintenance of plant will be carried out in order to minimise noise emissions. Particular attention will be paid to the lubrication of bearings and the integrity of silencers;
- All vehicles and mechanical plant will be fitted with effective exhaust silencers and maintained in good working order for the duration of the works;

- Compressors will be of the “sound reduced” models fitted with properly lined and sealed acoustic covers which will be kept closed whenever the machines are in use and all ancillary pneumatic tools shall be fitted with suitable silencers;
- Machines, which are used intermittently, will be shut down during those periods when they are not in use;
- Training will be provided by the ECoW to drivers to ensure smooth machinery operation/driving, and to minimise unnecessary noise generation; and,
- Local areas of the haul route will be condition monitored and maintained if necessary.

3.10 Invasive Species Management

A baseline invasive species survey will be carried out at the site to identify the presence and location of any invasive species (listed under the Third Schedule of the European Communities (Birds and Natural Habitats) Regulations 2011 (S.I. 477 of 2011) by a suitably qualified ecologist. If the presence of such species is found at or adjacent to the site, particularly in areas where its excavation may be required, an invasive species management plan will be prepared for the site to prevent the introduction or spread of any invasive species within the footprint of the works. An invasive species management plan, if required, will set out best practice control methods as summarised in the following sections.

3.10.1 General Best Practice Control Methods

The following general best practice guidelines in the treatment and control of invasive species during construction works are outlined below having regard to guidance documents outlined in Section 2.5 particularly those issued by the National Roads Authority (2010).

3.10.2 Site Management

Careful preparation of the site and planning of the works is crucial to successful treatment of invasive species. The following list of guidelines, which is not exhaustive, shall be followed by all on-site personnel. Only those who have been inducted into biosecurity measures on-site may enter the contaminated zones within the works areas. Should any risk of contaminated material escaping be observed by the site supervisor, the management plan for the site must be amended by an appropriately qualified person to mitigate against the risk.

3.10.3 Establishing Good Site Hygiene

- A risk assessment and method statement must be provided by the Contractor prior to commencing works.
- Fences will be erected around areas of infestation, as confirmed by test pits, and warning signs shall be erected.
- A designated wash-down area will be created, where power-washed material from machinery can be contained, collected and disposed of with other contaminated material. This area will contain a washable membrane or hard surface.
- Stockpile areas will be chosen to minimise movement of contaminated soil.
- Stockpiles will be marked and isolated.
- Contaminated areas which will not be excavated will be protected by a root barrier membrane if they are likely to be disturbed by machinery. Root barrier membranes will be protected by a layer of sand above and below and topped with a layer of hardcore.

- The use of vehicles with caterpillar tracks within contaminated areas will be avoided to minimise the risk of spreading contaminated material.
- An ECoW/suitably qualified ecologist will be on site to monitor and oversee the implementation of invasive species management plans.

Plant and equipment which is operated within an area for the management of materials in contaminated areas should be decontaminated prior to relocating to a different works area. The decontamination procedures should take account of the following:

- Personnel may only clean down if they are familiar with the plant and rhizome material and can readily identify it.
- Decontamination will only occur within designated wash-down areas.
- Vehicles will be cleaned using stiff-haired brush and pressure washers, paying special attention to any areas that might retain rhizomes e.g. wheel treads and arches.
- All run-off will be isolated and treated as contaminated material. This will be disposed of in already contaminated areas.

3.11 Waste Management

This section of the CEMP provides a waste management plan (WMP) which outlines the best practice procedures during the excavation and construction phases of the project. The WMP will outline the methods of waste prevention and minimisation by recycling, recovery and reuse at each stage. Disposal of waste will be seen as a last resort.

3.11.1 Legislation

The Waste Management Act 1996 to 2011 and its subsequent amendments provide for measures to improve performance in relation to waste management, recycling and recovery. The Act also provides a regulatory framework for meeting higher environmental standards set out by other national and EU legislation.

The Act requires that any waste related activity has to have all necessary licenses and authorisations. It will be the duty of the Waste Manager on the site of the development to ensure that all contractors hired to remove waste from the site have valid Waste Collection Permits. It will then be necessary to ensure that the waste is delivered to a licensed or permitted waste facility. The hired waste contractors and subsequent receiving facilities must adhere to the conditions set out in their respective permits and authorisations.

The Department of the Environment provides a document entitled, 'Best Practice Guidelines on the Preparation of Waste Management Plans for Construction and Demolition Projects' (2006). It is important to emphasise that no demolition will take place at this site however, this document was referred to throughout the process of completing this WMP.

3.11.2 Waste Management Hierarchy

The waste management hierarchy sets out the most efficient way of managing waste in the following order:

Prevention and Minimisation:

The primary aim of the WMP will be to prevent and thereby reduce the amount of waste generated at each stage of the project.

Reuse of Waste:

Reusing as much of the waste generated on site as possible will reduce the quantities of waste that will have to be transported off site to recovery facilities or landfill.

Recycling of Waste:

There are a number of established markets available for the beneficial use of Construction and Demolition waste such as using waste concrete as fill for new roads.

At all times during the implementation of the WMP, disposal of waste to landfill will be considered only as a last resort.

3.11.3 Construction Phase Waste Management Plan

3.11.3.1 Description of the Works

The Permitted Development will involve the construction of turbines, associated new site roads and upgrade of some existing roads, a substation & control building and an anemometry mast.

The turbines will be manufactured off site and delivered to site where on-site assembly will occur.

The turbine and anemometry mast foundations will consist of stone excavated from the onsite borrow pit and a concrete base which will contain reinforcing steel. These concrete foundations will be shuttered with steel formwork specifically designed for the works and re-usable off site on similar projects.

The substation and control buildings will be constructed on a concrete foundation with the buildings constructed with concrete masonry blocks with a timber roof structure and roof tile or slate covering. The roof structure will be made up of prefabricated roof trusses manufactured off site to minimise timber cutting on site.

The site roads will be constructed with rock won from the onsite borrow pit.

The waste types arising from the construction phase of the Permitted Development are outlined in Table 3.2 below.

Table 3.2 Expected waste types arising during the Construction Phase

Materials type	Example	EW Code
Cables	Electrical wiring	17 04 11
Cardboard	Boxes, cartons	15 01 01
Composite packaging	Containers	15 01 05
Metals	Copper, aluminium, lead, iron and steel	17 04 07
Inert materials	Sand, stones, plaster, rock, blocks	17 01 07
Mixed municipal waste	Daily canteen waste from construction workers, miscellaneous	20 03 01
Plastic	PVC frames, electrical fittings	17 02 03
Plastic packaging	Packaging with new materials	15 01 02
Tiles and ceramics	Slates and tiles	17 01 03
Wooden packaging	Boxes, pallets	15 01 03

Hazardous wastes that may occur on site during the construction phase of the Permitted Development may include oil, diesel fuel, chemicals, paints, preservatives

etc. All hazardous wastes will be stored in bunded containers/areas before being collected by an authorised waste contractor and brought to an EPA licensed waste facility. As mentioned above, hazardous wastes will be kept separate from non-hazardous wastes to ensure that contamination does not occur.

3.11.3.2 Waste Arisings and Proposals for Minimisation, Reuse and Recycling of Construction Waste

Construction waste will arise on the project mainly from excavation and unavoidable construction waste including material surpluses and damaged materials and packaging waste.

Appropriate measures should be taken to ensure excess waste is not generated during construction, including;

- Ordering of materials should be on an 'as needed' basis to prevent over supply to site. Co-ordination is required with suppliers enabling them to take/buy back surplus stock.
- Purchase of materials pre-cut to length to avoid excess scrap waste generated on site.
- Request that suppliers use least amount of packaging possible on materials delivered to the site.
- Ensuring correct storage and handling of goods to avoid unnecessary damage that would result in their disposal
- Ensuring correct sequencing of operations.
- Use reclaimed materials in the construction works.

Hazardous waste will be kept separate from all other construction waste to prevent contamination and removed appropriately.

3.11.3.3 Waste Arising from Construction Activities

All waste generated on site will be contained in waste skips at a waste storage area on site. This waste storage area will be kept relatively tidy with the various waste skip clearly labelled to indicate the allowable material to be disposed of therein.

The expected waste volumes generated on site are unlikely to be large enough to warrant source segregation. Therefore, all wastes streams generated on site will be deposited into a single skip. This waste material will be transferred to a Materials Recovery Facility (MRF) by a fully licensed waste contractor where the waste will be sorted into individual waste streams for recycling, recovery or disposal.

The waste generated from the turbine erection will be limited to the associated protective covers which are generally reusable. Considering the specialist nature of this packaging material the majority will be taken back by suppliers for their own reuse. Any other packaging waste generated from the turbine supply will be deposited in the on-site skip and subsequently transferred to the MRF

It is not envisaged that there will be any waste material arising from the materials used to construct the road as only the quantity of stone necessary will be excavated from the borrow pit on an 'as needed' basis.

Site personnel will be instructed at induction that no under no circumstances can waste be brought to site for disposal in the on-site waste skip. It must also be made clear that the burning of waste material on site is forbidden.

3.11.3.4 Waste Arising from Decommissioning

The lengthy time frame between the completion of the construction phase and decommissioning will result in the only materials remaining on site at that time are likely to be turbines and associated cabling and crushed stone used in construction of roads, hardstand, foundations etc.

The waste types arising from the decommissioning of the development are outlined in Table 3.3 below.

Table 3.3 Expected waste types arising during Decommissioning

Materials type	Example	EWC Code
Cables	Electrical wiring	17 04 11
Metals	Copper, aluminium, lead, iron and rebar	17 04 07
Inert materials	Crushed stone,	17 01 07

3.11.4 Reuse

Many construction materials can be reused a number of times before they have to be disposed of:

- Concrete can be reused as aggregate for roads cable trench backfilling material.
- Plastic packaging etc. can be used to cover materials on site or reused for the delivery of other materials.
- Excavated peat will be can be reused for reinstatement of the areas around turbine foundations and adjacent to site roads.

3.11.5 Recycling

If a certain type of construction material cannot be reused on site, then recycling is the most suitable option. The opportunity for recycling on site will be restricted to the associated packaging from the wind turbines.

All waste that is produced during the construction phase including dry recyclables will be deposited in the on-site skip initially and sent for subsequent segregation at a remote facility. The low volume of such material that is anticipated to be generated at the Permitted Development is the justification for adopting this method of waste management.

3.11.6 Implementation

3.11.6.1 Roles and Responsibilities for Waste Management

Prior to the commencement of the Permitted Development a member of the on-site construction management staff will be assigned the role of Construction Waste Manager. The Construction Waste Manager will be in charge of the implementation of the objectives of the WMP, ensuring that all hired waste contractors have the necessary authorisations and that the waste management hierarchy is adhered to. The person nominated must have sufficient authority so that they can ensure everyone working on the Permitted Development adheres to the WMP.

3.11.6.2 Training

It is important for the Construction Waste Manager to communicate effectively with colleagues in relation to the aims and objectives of the WMP. All employees working on site during the construction phases of the project will be trained in materials management and thereby, should be able to:

- Distinguish reusable materials from those suitable for recycling;
- Ensure maximum segregation at source;
- Co-operate with site manager on the best locations for stockpiling reusable materials;
- Separate materials for recovery; and
- Identify and liaise with waste contractors and waste facility operators.

3.11.6.3 Record Keeping

The WMP will provide systems that will enable all arising, movements and treatments of construction waste to be recorded. This system will enable the contractor to measure and record the quantity of waste being generated. It will highlight the areas from which most waste occurs and allows the measurement of arising against performance targets. The WMP can then be adapted with changes that are seen through record keeping.

The fully licensed waste contractor employed to remove waste from the site will be required to provide documented records for all waste dispatches leaving the site of the Permitted Development. Each record will contain the following:

- Consignment Reference Number
- Material Type(s) and EWC Code(s)
- Company Name and Address of Site of Origin
- Trade Name and Collection Permit Ref. of Waste Carrier
- Trade Name and Licence Ref. of Destination Facility
- Date and Time of Waste Dispatch
- Registration no. of Waste Carrier vehicle
- Weight of Material
- Signature of Confirmation of Dispatch detail
- Date and Time of Waste Arrival at Destination
- Weight of Material
- Site Address of Destination Facility

3.11.7 Waste Management Plan Conclusion

The WMP will be properly adhered to by all staff involved in the project which will be outlined within the induction process for all site personnel. The waste hierarchy should always be employed when designing the plan to ensure that the least possible amount of waste is produced during the construction phase. Reuse of certain types of construction wastes will cut down on the cost and requirement of raw materials therefore further minimising waste levels.

This preliminary WMP has been prepared to outline the main objectives that are to be adhered to for the preparation of a more detailed WMP to be completed after the planning phase of the Permitted Development.

4 DRAINAGE MANAGEMENT PLAN

The drainage management plan is essential to ensure that the details submitted as part of the environmental impact statement are fully implemented on site during the construction of the development. This report incorporates a detailed silt management plan and pollution prevention plan and including appropriately drainage infrastructure including interceptor & collector drains, check dams and settlement ponds as required. A programme for drainage maintenance has been provided to ensure the drainage system operates effectively and within its capacity.

4.1 Wind Farm Drainage

4.1.1 Introduction

The drainage management plan is essential to ensure that the details submitted as part of the environmental impact statement and as part of the further information response are fully implemented on site during the construction of the development. This report incorporates a detailed silt management plan and pollution prevention plan and including appropriately-sized silt traps and/or settlement ponds as required. Detailed Drainage Design Drawings for the permitted development as prepared by Hydro Environmental Services are included in Appendix 1 of this document. The drainage design employs the various measures further described below.

The protection of the watercourses within and surrounding the site, and downstream catchments that they feed is of utmost importance in considering the most appropriate drainage proposals for the site of the development. The development's drainage design has therefore been designed specifically with the intention of having no negative impact on the water quality of the site and its associated natural watercourses, and consequently no impact on downstream catchments and ecological ecosystems. There will be no direct discharges to any natural watercourses, with all drainage waters being dispersed as overland flows or directly into artificial drainage ditches following the installation of silt traps, check dams and/or settlement ponds to these ditches. Any discharges over land, from the works areas will be made over vegetation filters maintaining a 50 metre distance from natural watercourses. Buffer zones around the existing natural drainage features have informed, wherever possible, the layout of the permitted development.

4.1.2 Existing Drainage Features

The routes of natural drainage features will not be altered as part of the development. Turbine locations have been selected to avoid natural watercourses. The wind farm development has also been designed to require only 5 no. new watercourse crossings. Some extensions to existing culverts may be required under existing roadways to manage drainage waters where road widening and upgrade is required. These will be sufficiently sized to accommodate peak flows from storm events.

There will be no direct discharges to natural watercourses. Discharges from the works areas or from interceptor drains will be made over vegetated ground at a minimum of 50 metres distance from natural watercourses in the majority of cases. There are exceptions to this where existing or new roadways traverse, or run alongside, natural watercourses and it is necessary to provide drainage measures along such sections of roadway. Discharges will be made at a minimum distance of 20 metres from artificial drainage ditches unless otherwise specified in future revisions of the drainage design.

Buffer zones around the existing natural drainage features have informed the layout of the development and are indicated on the drainage design drawings.

Where artificial drains are currently in place in the vicinity of works areas, these drains may have to be diverted around the works areas to minimise the amount of water in the vicinity of works areas. Where it may not be possible to divert artificial drains around work areas, the drains will be blocked to ensure sediment laden water from the works areas has no direct route to other watercourses. Where drains have to be blocked, the blocking will only take place after an alternative drainage system to handle the same water has been put in place.

Existing artificial drains in the vicinity of existing site roads will be maintained in their present location where possible. If it is expected that these artificial drains will receive drainage water from works areas, check dams will be added (as specified below) to control flows and sediment loads in these existing artificial drains. If road widening or improvement works are necessary along the existing roads, where possible, the works will take place on the opposite side of the road to the drain.

4.1.3 Drainage Design Principles

Drainage water from any works areas of the site will not be directed to any natural watercourses within the site. Two distinct methods will be employed to manage drainage water within the site. The first method involves keeping clean water clean by avoiding disturbance to natural drainage features, minimising any works in or around artificial drainage features, and diverting clean surface water flow around excavations and construction areas. The second method involves collecting any drainage waters from works areas within the site that might carry silt or sediment, to allow attenuation and settlement prior to controlled diffuse release.

The drainage design is intended to maximise erosion control, which is more effective than having to control sediment during high rainfall. Such a system also requires less maintenance. The area of exposed ground will be minimised. The drainage measures will prevent runoff from entering the works areas of the site from adjacent ground, to minimise the volume of sediment-laden water that has to be managed. Discoloured run-off from any construction area will be isolated from natural clean run-off.

A schematic line drawing of the drainage design is presented in Figure 4.1 below.

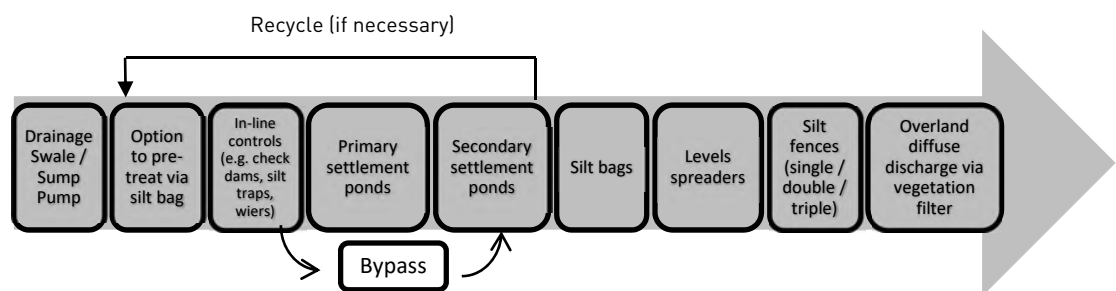


Figure 4.1 Schematic drawing of drainage design

4.1.4 Site Management & Pollution Prevention

The drainage management plan takes into account the principles of erosion and sediment control. Erosion control where runoff is prevented from flowing across exposed ground and sediment control where runoff is slowed to allow suspended sediment to settle are important elements in a drainage management plan. The drainage management plan has been prepared to provide erosion and sediment control

to prevent sediment and potentially pollutant runoff entering watercourses during the construction phase. The drainage management plan will ensure the following:

- Implement erosion control to prevent runoff flowing across exposed ground and become polluted by sediments;
- Intercept and divert clean water runoff away from construction site runoff to avoid cross contamination of clean water with soiled water;
- Implement sediment control to slow down runoff allowing suspended sediments to settle in situ particularly on roads and hardstanding areas;
- Implement the erosion and sediment controls before starting site clearance works;
- Minimise area of exposed ground by maintaining existing vegetation that would otherwise be subject to erosion in the vicinity of the wind park infrastructure and keeping excavated areas to a minimum;
- Delay clearing of peat before construction begins rather than stripping the entire site months in advance particularly during road construction;
- Designate temporary stockpiling areas located away from drains and watercourses that are protected by silt trapping apparatus such as a geotextile silt fence to prevent contaminated runoff where necessary; it is not envisaged that the stock piling areas will affect the drainage measures on site.
- Avoid working near watercourses during or after prolonged rainfall or an intense rainfall event and cease work entirely near watercourses when it is evident that pollution is occurring;
- Install a series of silt fences or other appropriate silt retention measure where there is a risk of erosion runoff to watercourses from construction related activity particularly if working during prolonged wet weather period or if working during intense rainfall event;
- Implement sediment control measures that includes for the prevention of runoff from adjacent intact ground that is for the separation of clean and 'dirty' water;
- Install appropriate silt control measures such as silt-traps, check dams and settlement ponds;
- Provide recommendations for road cleaning where needed particularly in the vicinity of watercourses; and
- Controls need to be regularly inspected and maintained otherwise a failure may result, such as a build-up of silt or tear in a fence, which could lead to water pollution. Controls must work effectively until the vegetation has re-established; inspection and maintenance is critical after prolonged or intense rainfall.

4.1.5 Pre-Construction Drainage Management

There are existing drainage features across the site, and due to the agricultural nature of the area as well as the ongoing commercial forestry operations, runoff drains relatively freely to local drains. This existing drainage system will continue to function as it is during the pre-construction phase. Prior to commencement of works in sub-catchments across the site main drain inspections will be completed to ensure ditches and streams are free from debris and blockages that may impede drainage.

The Project Hydrologist/Design Engineer will attend the site before construction commences and will assist with micro siting of drainage controls as per the mechanisms for interaction outlined in Section 5 of this CEMP. The drainage system will be excavated and constructed in conjunction with the road and hard standing construction. Drains will be excavated, and settlement ponds constructed to eliminate any suspended solids within surface water running off the site.

4.1.6 Construction Phase Drainage Management Plan

A drainage management plan is presented in this section of the CEMP to provide an overview for planning compliance and tendering purposes. This includes descriptions of the various drainage controls to be employed during the construction phase and operational phase of the wind farm development.

The early establishment of temporary drainage facilities will reduce the risk of pollution problems during construction. In addition, construction operations will adopt best working practices for drainage controls. The construction of the drainage system will start from the downstream sections and progress upstream, connecting conveyance systems with other drainage features as each development phase of the site progresses. They will therefore need to be designed with sufficient flexibility to respond to an early phase of limited incoming flow during the construction phase when sediment or other pollution may be a problem if upstream controls perform poorly, and the final phase of maximum incoming flows within the various catchments.

The implementation of a Schedule of Works Operation Record (SOWOR) will continue through the construction phase of the project. The SOWOR provides number of abandonment triggers which will ensure that site management are well informed as to the level of incident that will require the abandonment of works. The various triggers both pre-commencement and abandonment ensure best practice in terms of water quality management is maintained prior to commencement and during the various felling and construction phases.

Best practice and practical experience on other similar projects suggests that in addition to the drainage plans that are included in this CEMP, there are additional site based decisions and plans that can only be made in the field through interaction between the Site Construction Manager, the Project Hydrologist and the Project Geotechnical Engineers as per Section 5 of this CEMP.

In relation to decisions that are made on site it is important to stress that these will be implemented in line with the associated drainage controls and mitigation measures outlined in Section 7 below, and to ensure protection of all watercourses.

4.1.6.1 Drainage Design

Detailed drainage design measures are included in the site layout drawings of the development included in Appendix 1 of this report. The drainage design employs the various measures further described below.

4.1.6.1.1 Interceptor Drains

Interceptor drains will be installed upgradient of any works areas to collect surface flow runoff and prevent it reaching excavations and construction areas of the site where it might otherwise have come into contact with exposed surfaces and picked up silt and sediment. The drains will be used to divert upslope runoff around the works area to a location where it can be redistributed over the ground surface as sheet flow. This will minimise the volume of potentially silty runoff to be managed within the construction area.

The interceptor drains will be installed in advance of any main construction works commencing. The material excavated to make the drain will be compacted on the downslope edge of the drain to form a diversion dike. On completion of the construction phase works, it is envisaged that the majority of the interceptor drains could be removed. At that stage, there will be no open excavations or large areas of exposed

ground that are likely to give rise to large volumes of potentially silt-laden run off. Any areas in which works were carried out to construct roads, turbine bases or hardstands, will have been built up with large grade hardcore, which even when compacted in place, will retain sufficient void space to allow water to infiltrate the subsurface of these constructed areas. It is not anticipated that roadways or other installed site infrastructure will intercept ground-conveyed surface water runoff to any significant extent that would result in scouring or over-topping or spill over. Where the drains are to be removed, they will be backfilled with the material from the diversion dike. Interceptor drains may have to be retained in certain locations, for example where roadways are to be installed on slopes, to prevent the roadways acting as conduits for water that might infiltrate the roadway sub-base. In these cases, interceptor drains would be maintained in localised areas along the roadway with culverts under the roadway, which would allow the intercepted water to be discharged to vegetation filters downgradient of the roadway. Similarly, in localised hollows where water is likely to be funnelled at greater concentrations than on broader slopes, interceptor drains and culverts may be left in situ following construction.

Figure 4.2 shows an illustrative drawing of an interceptor drain.

The velocity of flow in the interceptor will be controlled by check dams (see Section 4.2.6.1.3 below), which will be installed at regular intervals along the drains to ensure flow in the channel is non-erosive. On steeper sections where erosion risks are greater, a geotextile membrane will be added to the channel.




Interceptor drains will be installed horizontally across slopes to run in parallel with the natural contour line of the slope. Intercepted water will travel along the interceptor drains to areas downgradient of works areas, where the drain will terminate at a level spreader (see Section 4.2.6.1.4 below). Across the entire length of the interceptor drains, the design elevation of the water surface along the route of the drains will not be lower than the design elevation of the water surface in the outlet at the level spreader.

4.1.6.1.2 Swales




Drainage swales are shallow drains that will be used to intercept and collect run off from construction areas of the site during the construction phase. Drainage swales will remain in place to collect runoff from roads and hardstanding areas of the development during the operational phase. A swale is an excavated drainage channel located along the downgradient perimeter of construction areas, used to collect and carry any sediment-laden runoff to a sediment-trapping facility and stabilised outlet. Swales are proven to be most effective when a dike is installed on the downhill side. They are similar in design to interceptor drains and collector drains described above. Figure 4.2 shows an illustrative example of a drainage swale.

Drainage swales will be installed downgradient of any works areas to collect surface flow runoff where it might have come into contact with exposed surfaces and picked up silt and sediment. Swales will intercept the potentially silt-laden water from the excavations and construction areas of the site and prevent it reaching natural watercourses.

Drainage swales will be installed in advance of any main construction works commencing. The material excavated to make the swale will be compacted on the downslope edge of the drain to form a diversion dike.

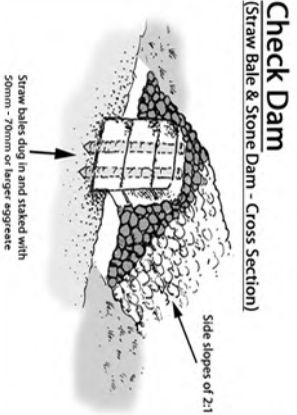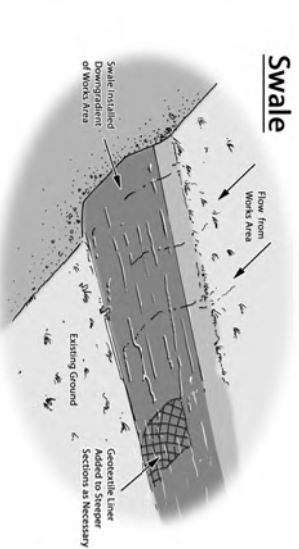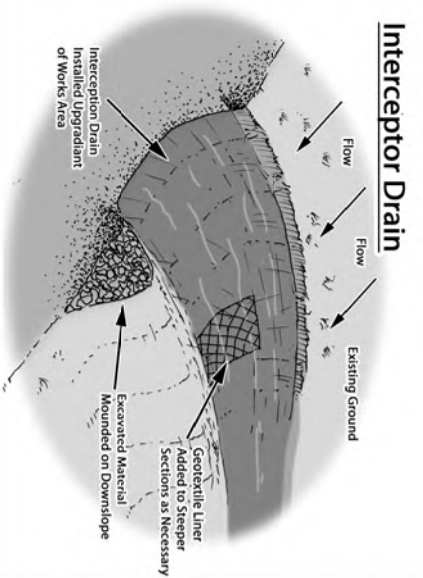

Drainage Design Measures

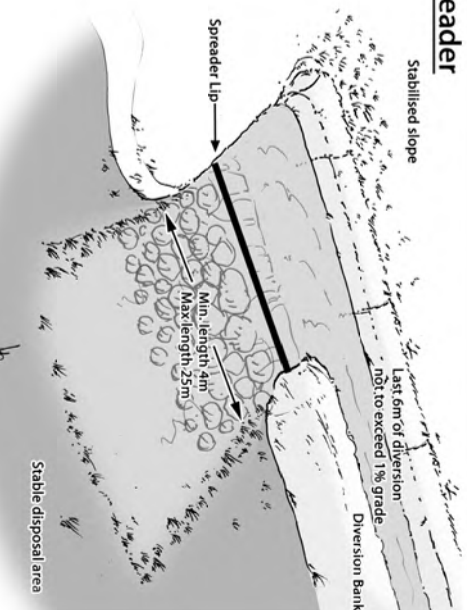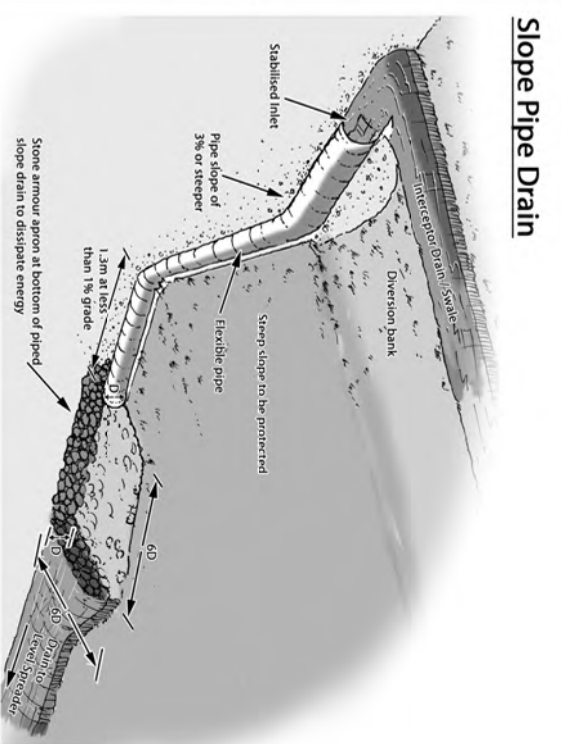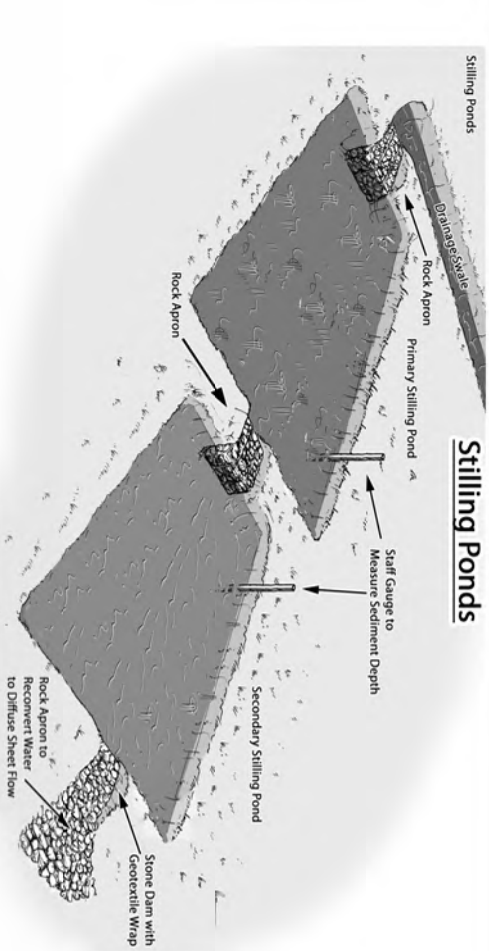

MAP TITLE: Drainage Design Measures				MAP NO.: Figure 4.2	SCALE: n/a
PROJECT TITLE: Meenbog Wind Farm				DATE: 18-12-2018	
DRAWING BY: Owen Cahill				ISSUE NO. 160502-2018.12.18-F	
CHECKED BY: Michael Watson				DATE: 18-12-2018	
McCarthy Kenille O'Sullivan Ltd, Block 1, G.F.S.C. Moorenagallia Road, Galway, Ireland. Email: info@mcCarthyKenille.ie Tel: +353 (0)91 7736611 Fax: +353 (0)91 771279					

4.1.6.1.3 Check Dams

The velocity of flow in the interceptor drains and drainage swales, particularly on sloped sections of the channel, will be controlled by check dams, which will be installed at regular intervals along the drains to ensure flow in the swale is non-erosive. Check dams will also be installed in some existing artificial drainage channels that will receive waters from works areas of the site.

Check dams will restrict flow velocity, minimise channel erosion and promote sedimentation behind the dam. The check dams will be installed as the interceptor drains are being excavated. Check dams may also be installed in some of the existing artificial drainage channels on the site, downstream of where drainage swales connect in.

The check dams will be made up of straw bales or stone, or a combination of both depending on the size of the drainage swale it is being installed in. Where straw bales are to be used, they will be secured to the bottom of the drainage swale with stakes. Clean 4-6 inch stone will be built up on either side and over the straw bale to a maximum height of 600mm over the bottom of the interceptor drain. In smaller channels, a stone check dam will be installed and pressed down into place in the bottom of the drainage swale with the bucket of an excavator.

The check dams will be installed at regular intervals along the interceptor drains to ensure the bottom elevation of the upper check dam is at the same level as the top elevation of the next down-gradient check dam in the drain. The centre of the check dam will be approximately 150mm lower than the edges to allow excess water to overtop the dam in flood conditions rather than cause upstream flooding or scouring around the dams.

Check dams will not be used in any natural watercourses, only artificial drainage channels and interceptor drains. The check dams will be left in place at the end of the construction phase to limit erosive linear flow in the drainage swales during extreme rainfall events.

Check dams are designed to reduce velocity and control erosion and are not specifically designed or intended to trap sediment, although sediment is likely to build up. If necessary, any excess sediment build up behind the dams will be removed. For this reason, check dams will be inspected and maintained regularly to insure adequate performance. Maintenance checks will also ensure the centre elevation of the dam remains lower than the sides of the dam.

4.1.6.1.4 Level Spreaders

A level spreader will be constructed at the end of each interceptor drain to convert concentrated flows in the drain, into diffuse sheet flow on areas of vegetated ground. The level spreaders will be located downgradient of any works areas in locations where they are not likely to contribute further to water ingress to construction areas of the site.

The water carried in interceptor drains will not have come in contact with works areas of the site, and therefore should be free of silt and sediment. The level spreaders will distribute clean drainage water onto vegetated areas where the water will not be re-concentrated into a flow channel immediately below the point of discharge. The discharge point will be on level or only very gently sloping ground rather than on a steep slope so as to prevent erosion. Figure 4.2 shows an illustrative example of a level spreader.

The slope in the channel leading into the spreader will be less than or equal to 1%. The slope downgradient of the spreader onto which the water will dissipate will have a grade of less than 6%. The availability of slopes with a grade of 6% or less will determine the locations of level spreaders. If a slope grade of less than 6% is not available in the immediate area downgradient of a works area at the end of a diversion drain, a piped slope drain (see Section 4.2.6.1.5 below) will be used to transfer the water to a suitable location.

The spreader lip over which the water will spill will be made of a concrete kerb, wooden board, pipe, or other similar piece of material that can create a level edge similar in effect to a weir. The spreader will be level across the top and bottom to prevent channelised flow leaving the spreader or ponding occurring behind the spreader. The top of the spreader lip will be 150mm above the ground behind it. The length of the spreader will be a minimum of four metres and a maximum length of 25 metres, with the actual length of each spreader to be determined by the size of the contributing catchment, slope and ground conditions.

Clean four-inch stone can be placed on the outside of the spreader lip and pressed into the ground mechanically to further dissipate the flow leaving the level spreader over a larger area.

4.1.6.1.5 Piped Slope Drains

Piped slope drains will be used to convey surface runoff from diversion drains safely down slopes to flat areas without causing erosion. Once the runoff reaches the flat areas it will be reconverted to diffuse sheet flow. Level spreaders will only be established on slopes of less than 6% in grade. Piped slope drains will be used to transfer water away from areas where slopes are too steep to use level spreaders.

The piped slope drains will be semi-rigid corrugated pipes with a stabilised entrance and a rock apron at the outlet to trap sediment and dissipate the energy of the water. The base of drains leading into the top of the piped slope drain will be compacted and concavely formed to channel the water into the corrugated pipe. The entrance at the top of the pipe will be stabilised with sandbags if necessary. The pipe will be anchored in place by staking at approximately 3-4 metre intervals or by weighing down with compacted soil. The bottom of the pipe will be placed on a slope with a grade of less than 1% for a length of 1.5 metres, before outflowing onto a rock apron.

The rock apron at the outlet will consist of 6-inch stone to a depth equal to the diameter of the pipe, a length six times the diameter of the pipe. The width of the rock apron will be three times the diameter of the pipe where the pipe opens onto the apron and will fan out to six times the diameter of the pipe over its length. Figure 4.2 shows a diagrammatic example of a piped slope drain and rock apron.

Piped slope drains will only remain in place for the duration of the construction phase of the project. On completion of the works, the pipes and rock aprons will be removed and all channels backfilled with the material that was originally excavated from them.

Piped slope drains will be inspected weekly and following rainfall events. Inlet and outlets will be checked for sediment accumulation and blockages. Stake anchors or fill over the pipe will be checked for settlement, cracking and stability. Any seepage holes where pipe emerges from drain at the top of the pipe will be repaired promptly.

4.1.6.1.6 Vegetation Filters

Vegetation filters are the existing vegetated areas of land that will be used to accept surface water runoff from upgradient areas. The selection of suitable areas to use as vegetation filters will be determined by the size of the contributing catchment, slope and ground conditions.

Vegetation filters will carry outflow from the level spreaders as overland sheet flow, removing any suspended solids and discharging to the groundwater system by diffuse infiltration.

Vegetation filters will not be used in isolation for waters that are likely to have higher silt loadings. In such cases, silt-bearing water will already have passed through settlement ponds prior to diffuse discharge to the vegetation filters via a level spreader.

4.1.6.1.7 Settlement Ponds

Settlement ponds will be used to attenuate runoff from works areas of the site during the construction phase and will remain in place to handle runoff from roads and hardstanding areas of the development during the operational phase. The purpose of the settlement ponds is to intercept runoff potentially laden with sediment and to reduce the amount of sediment leaving the disturbed area by reducing runoff velocity. Reducing runoff velocity will allow larger particles to settle out in the settlement ponds, before the run-off water is redistributed as diffuse sheet flow in filter strips downgradient of any works areas.

Settlement ponds will be excavated/constructed at each required location as two separate ponds in sequence, a primary pond and a secondary pond. The points at which water enters and exits the settlement ponds will be stabilised with rock aprons, which will trap sediment, dissipate the energy of the water flowing through the settlement pond system, and prevent erosion. The primary settlement pond will reduce the velocity of flows to less than 0.5 metres per second to allow settlement of silt to occur. Water will then pass from the primary pond to the secondary pond via another rock apron. The secondary settlement pond will reduce the velocity of flows to less than 0.3 metres per second. Water will flow out of the secondary settlement pond through a stone dam, partially wrapped in geo-textile membrane, which will control flow velocities and trap any sediment that has not settled out. Figure 4.2 shows an illustrative example of a settlement pond system.

Water will flow by gravity through the settlement pond system. The settlement ponds will be sized according to the size of the area they will be receiving water from but will be sufficiently large to accommodate peak flows storm events. The settlement ponds will be dimensioned so that the length to width ratio will be greater than 2:1, where the length is the distance between the inlet and the outlet. Where ground conditions allow, settlement ponds will be constructed in a wedge shape, with the inlet located at the narrow end of the wedge. Each settlement pond will be a minimum of 1-1.5 metres in depth. Deeper ponds will be used to minimise the excavation area needed for the required volume.

The embankment that forms the sloped sides of the settlement ponds will be stabilised with vegetated turves, which will have been removed during the excavation of the settlement ponds area or will be seeded after installation.

Settlement ponds will be located towards the end of swales, close to where the water will be reconverted to diffuse sheet flow. Upon exiting the settlement pond system,

water will be immediately reconverted to diffuse flow via a fan-shaped rock apron if there is adequate space and ground conditions allow. Otherwise, a swale will be used to carry water exiting the settlement pond system to a level spreader to reconvert the flow to diffuse sheet flow.

A water level indicator such as a staff gauge will be installed in each settlement pond with marks to identify when sediment is at 10% of the settlement pond capacity. Sediment will be cleaned out of the still pond when it exceeds 10% of pond capacity. Settlement ponds will be inspected weekly and following rainfall events. Inlet and outlets will be checked for sediment accumulation and anything else that might interfere with flows.

4.1.6.1.8 Dewatering Silt Bags

Dewatering silt bags are made of a high quality geotextile fabric which allow the flow of water through them while trapping any silt or sediment suspended in the water. The silt bags provide a passive non-mechanical method of removing any remaining silt contained in the potentially silt-laden water collected from works areas within the site.

Dewatering silt bags are an additional drainage measure that can be used downgradient of the settlement ponds at the end of the drainage swale channels and will be located, wherever it is deemed appropriate, throughout the site. The water will flow, via a pipe, from the settlement ponds into the silt bag. The silt bag will allow the water to flow through the geotextile fabric and will trap any of the finer silt and sediment remaining in the water after it has gone through the previous drainage measures. The dewatering silt bags will ensure that there will be no loss of peaty silt into any watercourse.

The dewatering silt bags that will be used will be approximately three metres in width by 4.5 metres (see Plate 4.1 and Plate 4.2 below) in length and will be capable of trapping approximately four tonnes of silt.



Plate 4.1 Silt Bag with water being pumped through



Plate 4.2 Silt Bag under inspection

4.1.6.1.9 Siltbuster

A "siltbuster" or similar equivalent piece of equipment will be available to filter any water pumped out of excavation areas if necessary, prior to its discharge to settlement ponds or swales.

Siltbusters are mobile silt traps that can remove fine particles from water using a proven technology and hydraulic design in a rugged unit. The mobile units are specifically designed for use on construction sites.

The unit stills the incoming water/solids mix and routes it upwards between a set of inclined plates for separation. Fine particles settle onto the plates and slide down to the base for collection, whilst treated water flows to an outlet weir after passing below a scum board to retain any floating material. The inclined plates dramatically increase the effective settling area of the unit giving it a very small footprint on site and making it highly mobile. Figure 4.3 below shows an illustrative diagram of the Siltbuster.

The Siltbuster units are now considered best practice for the management of dirty water pumped from construction sites. The UK Environment Agency and the Scottish Environmental Protection Agency have all recommended/specified the use of *Siltbuster* units on construction projects.

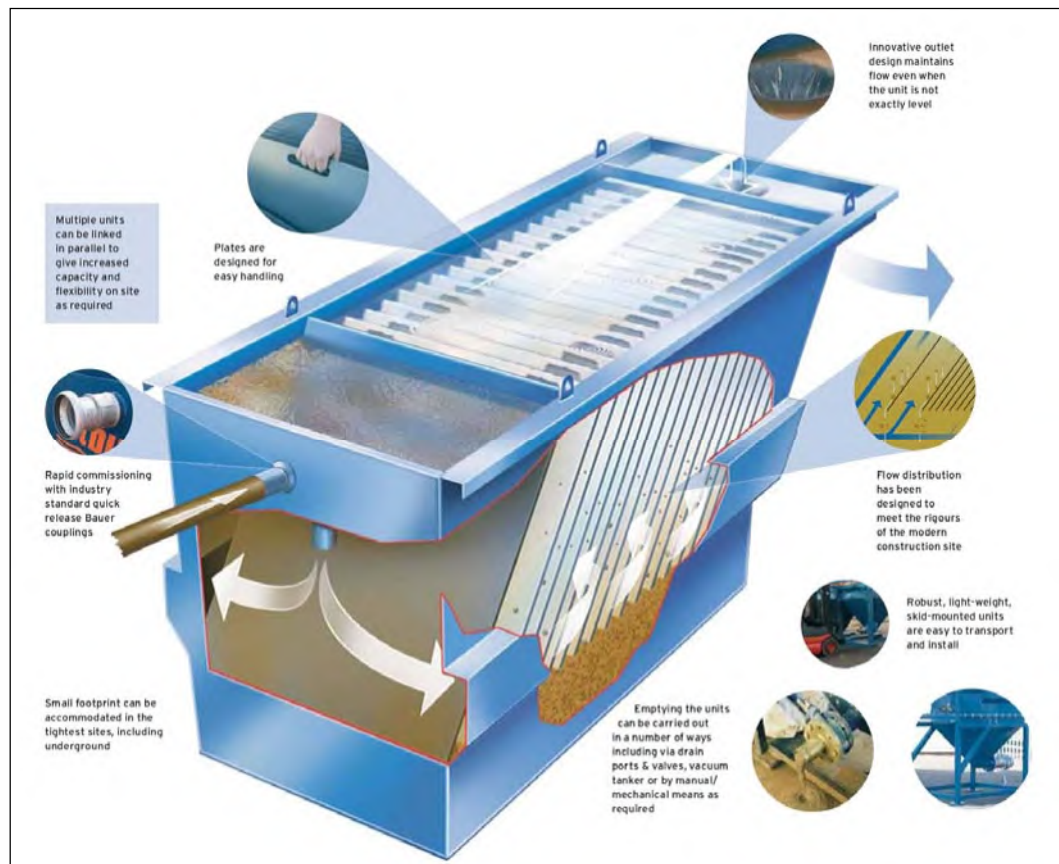


Figure 4.3 Siltbuster

4.1.6.1.10 Culverts

Where any new culverts of existing watercourses crossing are to be installed, they will be the subject of consent applications to the Office of Public Works under Section 50 of the Arterial Drainage Act, 1945. Some culverts may be installed to manage drainage waters from works areas of the development, particularly where the waters have to be taken from one side of an existing roadway to the other for discharge. The size of culverts will be influenced by the depth of the track or road sub-base. In some cases, two, or more, smaller diameter culverts may be used where this depth is limited, though this will be avoided as they will have a higher associated risk of blockage than a single, larger pipe. In all cases, culverts will be oversized to allow mammals to pass through the culvert.

Culverts will be installed with a minimum internal gradient of 1% (1 in 100). Smaller culverts will have a smooth internal surface. Larger culverts may have corrugated

surfaces which will trap silt and contribute to the stream ecosystem. Depending on the management of water on the downstream side of the culvert, large stone may be used to interrupt the flow of water. This will help dissipate its energy and help prevent problems of erosion. Smaller water crossings will simply consist of an appropriately sized pipe buried in the sub-base of the road at the necessary invert level to ensure ponding or pooling doesn't occur above or below the culvert and water can continue to flow as necessary.

All culverts will be inspected regularly to ensure they are not blocked by debris, vegetation or any other material that may impede conveyance.

4.1.6.1.11 Silt Fences

Silt fences will be installed as an additional water protection measure around existing watercourses in certain locations, particularly where works are proposed within the 50-metre buffer zone from natural watercourses, which is inevitable where existing roads in proximity to watercourses are to be upgraded as part of the development. These areas include around existing culverts, around the headwaters of watercourses, and the proposed locations are indicated on the site layout drawings included in Appendix 1.

Silt fences will be installed as single, double or a series of triple silt fences, depending on the space available and the anticipated sediment loading. The silt fence designs follow the technical guidance document '*Control of Water Pollution from Linear Construction Projects*' published by CIRIA [Ciria, No. C648, 1996]. Up to three silt fences may be deployed in series as outlined in Figure 4.4.

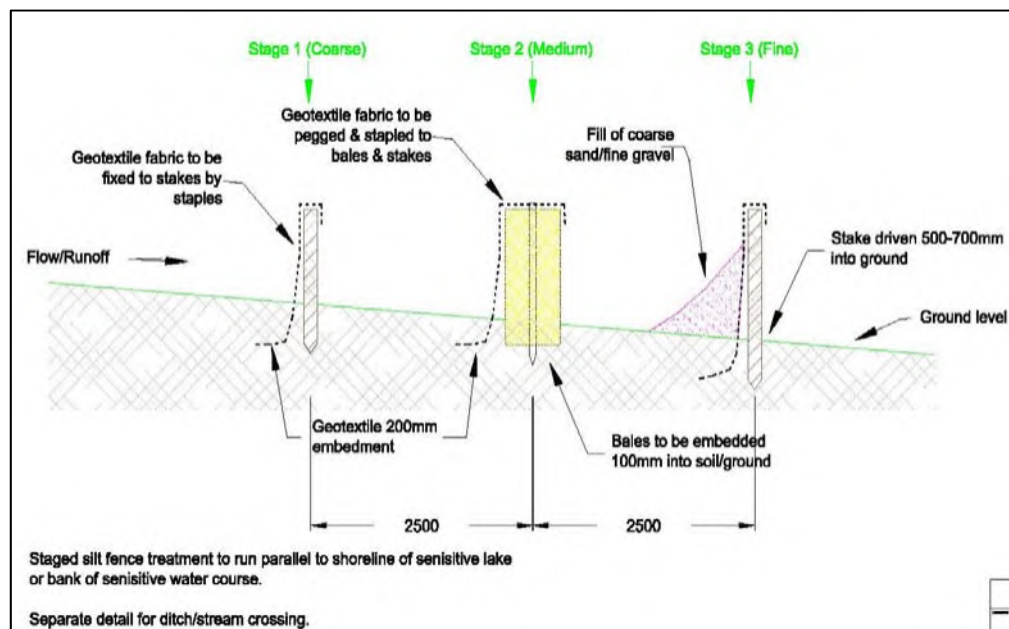


Figure 4.4 Silt Fence Detail

The Stage 1 (Coarse) silt fence will consist of a geotextile fabric such as Terram 1000 attached by staples to fixed stakes. The Terram sheets will be folded in an L shape with one metre extending horizontally in towards the works area. This horizontal section will be buried at a distance of approximately 150mm beneath a clean stone surface. Terram 1000 is a permeable fabric through which water can pass, but through which

sediment particles cannot. It does however, impede water flow and can lead to the backing up of water and sediment, which reduce its effectiveness.

The Stage 2 (Medium) silt fence will consist of straw bales, embedded 100mm into the soil/ground and fixed in place with stakes. A geotextile fabric will be pegged and stapled to the straw bales and stakes.

The Stage 3 (Fine) silt fence will be similar to the Stage 1 fence, with the addition of a course sand and/or fine gravel at the base of the geotextile.

In the case of all three types of fence, the geotextile fabric will be embedded at least 150mm below the ground surface.

In a small number of locations around the site where space between the works areas and watercourses may be limited, silt fence designs will be combined to increase their effectiveness. For example, a straw bale silt fence (Stage 2) may be double wrapped with geotextile fabric (Stage 1) and course sand/fine gravel added on the upgradient side (Stage 3). See Figure 4.4. The most suitable type, number or combination of silt fences will be determined on a location specific basis for the various parts of the site. Site fences will be inspected regularly to ensure water is continuing to flow through the Terram, and the fence is not coming under strain from water backing up behind it.

4.1.6.2 Construction Compound Drainage

Surface water run-off from the construction compound will be controlled via a single outlet that will be installed at the edge of the compound. The single outfall point will be constructed to handle runoff from the compound and its immediate surrounds. Interceptor drains will already have been installed upgradient of the compound area before any excavation begins.

Run off from the single outlet point will be diverted via a drainage swale and on to a settlement pond prior to discharge over an area of vegetated ground.

4.1.6.3 Borrow Pit Drainage

While surface water will be contained in the borrow pit area, the design proposal is to control the level of water in the borrow pit area by creating a single point outlet from the basin-like area that will ensure the water does not overtop the pit area. Run-off from the borrow pit areas will be controlled via a single outlet that will be installed at the edge of the borrow pit. The single outfall point will be constructed to handle runoff from the borrow pit and its immediate surrounds. Interceptor drains will already have been installed upgradient of the borrow pit area before any extraction begins.

Run off from the single outlet point will be diverted via a drainage swale to a series of settlement ponds and onwards to a level spreader, which will convert concentrated flows in the drain, into diffuse sheet flow on areas of vegetated ground. The management of surface runoff from the peat disposal area by converting it to diffuse sheet flow removes the risk of contamination of surface water drains and removes the requirement for silt traps leading from this particular area.

During the construction phase of the project, it will be necessary to keep the borrow pit area free of standing water while rock is still being extracted. This will be achieved by using a mobile pump, which will pump water into the same series of drains, settlement ponds and level spreader, which will receive the water from the single outlet.

4.1.6.4 Tree Felling Drainage Controls

Mitigation measures which will reduce the risk of entrainment of suspended solids and nutrient release in surface watercourses comprise best practice methods which are set out as follows:

- Machine combinations will be chosen which are most suitable for ground conditions at the time of felling and to minimise soils disturbance;
- Use of buffer zones for aquatic zones (see Table 4.1 below);
- Checking and maintenance of roads and culverts will be on-going through any felling operation. No tracking of vehicles through watercourses will occur, as vehicles will use road infrastructure and existing watercourse crossing points. Where possible, existing drains will not be disturbed during felling works;
- Ditches which drain from the area to be felled towards existing surface watercourses will be blocked, and temporary silt traps will be constructed. No direct discharge of such ditches to watercourses will occur. Drains and sediment traps should be installed during ground preparation. Collector drains will be excavated at an acute angle to the contour (~0.3%-3% gradient), to minimise flow velocities. Main drains to take the discharge from collector drains will include water drops and rock armour, as required, where there are steep gradients, and should avoid being placed at right angles to the contour;
- Sediment traps will be sited outside of buffer zones and will have no direct outflow into the aquatic zone. Machine access will be maintained to enable the accumulated sediment to be excavated. Sediment will be carefully disposed of away from all aquatic zones. Where possible, all new silt traps will be constructed on even ground and not on sloping ground;
- In areas, particularly sensitive to erosion, it may be necessary to install double or triple sediment traps. This measure will be reviewed on site during construction;
- All drainage channels will taper out before entering the aquatic buffer zone. This ensures that discharged water gently fans out over the buffer zone before entering the aquatic zone, with sediment filtered out from the flow by ground vegetation within the zone. On erodible soils, silt traps will be installed at the end of the drainage channels, to the outside of the buffer zone;
- Drains and silt traps will be maintained throughout all felling works, ensuring that they are clear of sediment build-up and are not severely eroded. Correct drain alignment, spacing and depth will ensure that erosion and sediment build-up are minimised and controlled;
- Brash mats will be used to support vehicles on soft ground, reducing peat and mineral soils erosion and avoiding the formation of rutted areas, in which surface water ponding can occur. Brash mat renewal should take place when they become heavily used and worn. Provision should be made for brash mats along all off-road routes, to protect the soil from compaction and rutting. Where there is risk of severe erosion occurring, extraction should be suspended during periods of high rainfall;
- Timber should be stacked in dry areas, and outside a local 50m stream buffer zone. Straw bales and check dams to be emplaced on the down gradient side of timber storage/processing sites;
- Works should be carried out during periods of no, or low rainfall, in order to minimise entrainment of exposed sediment in surface water run-off;
- Checking and maintenance of roads and culverts will be on-going through the felling operation;
- Refuelling or maintenance of machinery will not occur within 50m of an aquatic zone. Dedicated refuelling areas will be used during the felling works; and,

- Branches, logs or debris will not be allowed to build up in aquatic zones. All such material will be removed when harvesting operations have been completed, but care will be taken to avoid removing natural debris deflectors.

Table 4.1 Minimum Buffer Zone Widths (Forest Service, 2000)

Average slope leading to the aquatic zone		Buffer zone width on either side of the aquatic zone	Buffer zone width for highly erodible soils
Moderate	(0 – 15%)	10 m	15 m
Steep	(15 – 30%)	15 m	20 m
Very steep	(>30%)	20 m	25 m

The majority of the felling will be within and around the development footprint of turbine bases and access roads.

Best practice methods related to water incorporated into the forestry management and water quality protection measures will be derived from:

- Forestry Commission (2011): Forests and Water Guidelines, Fifth Edition. Publ. Forestry Commission, Edinburgh;
- Coillte (2013) Forest Operations & Water Protection Guidelines;
- DAFM (2017). Felling and Reforestation Policy;
- Coillte (2009) Methodology for Clear Felling Harvesting Operations;
- Forest Service (2000): Forestry and Water Quality Guidelines. Forest Service, DAF, Johnstown Castle Estate, Co. Wexford; and,
- Forest Service, (2000): Code of Best Forest Practice – Ireland. Forest Service, DAF, Johnstown Castle Estate, Co. Wexford.

4.1.6.5 Cable Trench Drainage

Cable trenches are typically developed in short sections, thereby minimising the amount of ground disturbed at any one time and minimising the potential for drainage runoff to pick up silt or suspended solids. Each short section of trench is excavated, ducting installed and bedded, and backfilled with the appropriate materials, before work on the next section commences.

To efficiently control drainage runoff from cable trench works areas, excavated material is stored on the upgradient side of the trench. Should any rainfall cause runoff from the excavated material, the material is contained in the downgradient cable trench. Excess subsoil is removed from the cable trench works area immediately upon excavation, and in the case of the development, would be transported to one of the on-site borrow pit disposal areas or used for landscaping and reinstatements of other areas elsewhere on site.

On steeper slopes, silt fences, as detailed in Section 4.2.6.1.11 above will be installed temporarily downgradient of the cable trench works area, or on the downhill slope below where excavated material is being temporarily stored to control run-off.

4.1.7 Drainage Maintenance

Drainage performance will form part of the civil works contract requirements. During the construction phase the effectiveness of drainage measures designed to minimise runoff entering works areas and capture and treatment of potentially silt-laden water from the works areas will be monitored periodically (daily, weekly, and event based monitoring, *i.e.* after heavy rainfall events as summarised in Section 5.2 below) by the

ECoW and/or the Project Hydrologist. The ECoW will respond to changing weather and drainage conditions on the ground as the project proceeds, to ensure the effectiveness of the drainage design is maintained.

The abandonment triggers as set out in the SOWOR will be adopted as part of drainage inspections to ensure that any of the conditions prescribed under any abandonment trigger does not exist at the locations under inspection.

Regular inspections of all existing and installed drainage systems will be undertaken, especially after heavy rainfall, to check for blockages, and ensure there is no build-up of standing water within the system. Any excess build-up of silt levels at check dams, the settlement ponds, or any other drainage features that may decrease the effectiveness of the drainage feature, will be removed. For this reason, check dams will be inspected and maintained weekly during the construction phase of the project to insure adequate performance. Maintenance checks will also ensure the centre elevation of the dam remains lower than the sides of the dam.

Check dams will also be inspected weekly during the construction phase of the project and following rainfall events to ensure the structure of the dam is still effective in controlling flow. Any scouring around the edges of the check dams or overtopping of the dam in normal flow conditions will be rectified by reinforcement of the check dam. Drainage swales will be regularly inspected for evidence of erosion along the length of the swale. If any evidence of erosion is detected, additional check dams will be installed to limit the velocity of flow in the channel and reduce the likelihood of erosion occurring in the future.

A water level indicator such as a simple staff gauge or level marker will be installed in each settlement pond with marks to identify when sediment is at 50% of the pond's capacity. Sediment will be cleaned out of the settlement pond when it exceeds 50% of capacity. Settlement ponds will be inspected weekly during the construction phase of the project and following rainfall events. Inlet and outlets will be checked for sediment accumulation and anything else that might interfere with flows.

On completion of the civil and excavations works at the site, the frequency of inspections and monitoring of the drainage infrastructure will reduce to monthly as deemed appropriate by the ECoW.

4.1.8 Operational Phase Drainage Management

The project hydrologist will inspect and review the drainage system after construction has been completed to provide guidance on the requirements of an operational phase drainage system. This operational phase drainage system will have been installed during the construction phase in conjunction with the road and hardstanding construction work as described below:

- Interceptor drains will be maintained up-gradient of all infrastructure to collect clean surface runoff, in order to minimise the amount of runoff reaching areas where suspended sediment could become entrained. It will then be directed through a series of in-line treatments prior to discharge;
- Swales/road side drains will be maintained to intercept and collect runoff from access roads and hardstanding areas of the site, likely to have entrained suspended sediment, and channel it to settlement ponds for sediment settling;
- Check dams will be maintained at regular intervals along interceptor drains and swales/roadside drains in order to reduce flow velocities and therefore minimise erosion within the system during storm rainfall events; and,

- Settlement ponds, emplaced downstream of swales and roadside drains, will buffer volumes of runoff discharging from the drainage system during periods of high rainfall, by retaining water until the storm hydrograph has receded, thus reducing the hydraulic loading to watercourses.

In operational phase of the wind farm, the reliance on the drainage system summarised above will become reduced as areas naturally revegetate. Once areas revegetate, this will result in a resumption of the natural drainage management that will have existed prior to any construction.


5 ENVIRONMENTAL MANAGEMENT IMPLEMENTATION

5.1 Roles and Responsibilities

The Site Supervisor/Construction Manager and/or Environmental Clerk of Works (ECoW) are the project focal point relating to construction-related environmental issues.

In general, the ECoW will maintain responsibility for monitoring the works and Contractors/Sub-contractors from an environmental perspective. The ECoW will act as the regulatory interface on environmental matters by reporting to and liaising with Donegal County Council and other statutory bodies as required.

The ECoW will report directly to the Site Supervisor/Wind Farm Construction Manager. A Project Ecologist, Project Hydrologist and Project Geotechnical engineer will visit the site regularly and report to site management. This structure provides a “triple lock” review/interaction by external specialists. An organogram structure for the construction stage is as follows:

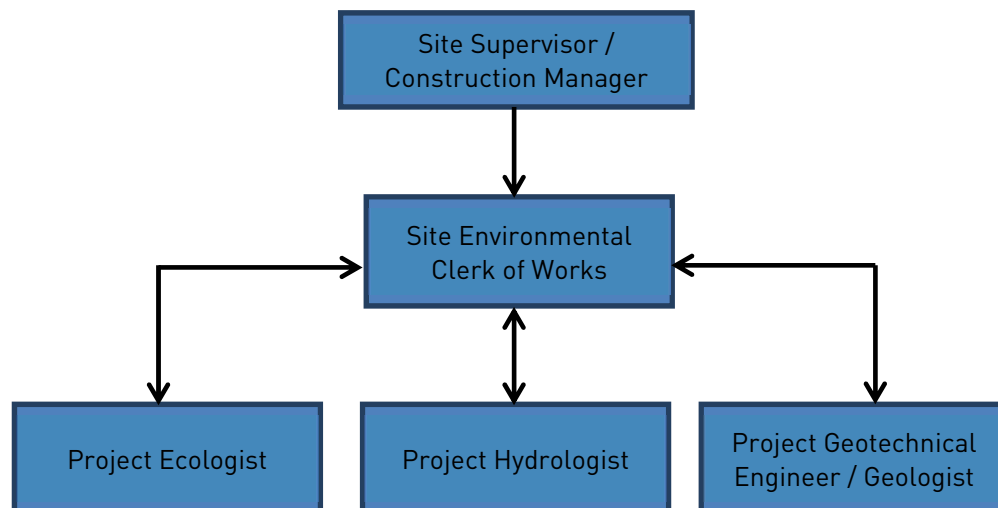

Any requirement of favourable planning permission decision, for the works to be supervised by an engineer with professional indemnity insurance, who upon completion of the works, including site stability, shall certify the said works, will be adhered to. Such an engineer will be appointed to oversee and supervise the construction phase of the project.

5.1.1 Wind Farm Construction Manager/Site Supervisor

The Site Supervisor/Construction Manager will have overall responsibility for the organisation and execution of all related environmental activities as appropriate, in accordance with regulatory and project environmental requirements. The duties and responsibilities of the Site Supervisor/Construction Manager will include:

- Ensure that all works are completed safely and with minimal environmental risk;
- Approve and implement the Project CEMP and supporting environmental documentation, and ensure that all environmental standards are achieved during the construction phase of the project;

- Take advice from the ECoW on legislation, codes of practice, guidance notes and good environmental working practice relevant to their work;
- Ensure compliance through audits and management site visits;
- Ensure timely notification of environmental incidents; and,
- Ensure that all construction activities are planned and performed such that minimal risk to the environment is introduced.

5.1.2 Site Environmental Clerk of Works

The main contractor will be required to engage a qualified Environmental Engineer, Environmental Scientist, or equivalent, with experience in wind farm construction to fulfil the role of Site Environmental Clerk of Works (ECoW), and to monitor all site works and to ensure that methodologies and mitigation are followed throughout construction to avoid negatively impacting on the receiving environment.

The ECoW will report to the Construction Manager. The responsibilities and duties of the ECoW will include the following:

- Preparation of the CEMP and supporting environmental documentation and review/approval of contractor method statements;
- Undertake inspections and reviews to ensure the works are carried out in compliance with the CEMP;
- Monitor the implementation of the CEMP, particularly all proposed/required Environmental Monitoring;
- Generate environmental reports as required to show environmental data trends and incidents and ensure environmental records are maintained throughout the construction period;
- Advise site management/contractor/sub-contractors on:
 - o Prevention of environmental pollution and improvement to existing working methods;
 - o Changes in legislation and legal requirements affecting the environment;
 - o Suitability and use of plant, equipment and materials to prevent pollution;
 - o Environmentally sound methods of working and systems to identify environmental hazards;
- Ensure proper mitigation measures are initiated and adhered to during the construction phase;
- Liaise with Project Ecologist, Project Hydrologist and Project Geotechnical Engineer to ensure regular site visits and audits/inspections are completed;
- Ensure adequate arrangements are in place for site personnel to identify potential environmental incidents;
- Ensure that details of environmental incidents are communicated in a timely manner to the relevant regulatory authorities, initially by phone and followed up as soon as is practicable by e-mail;
- Support the investigation of incidents of significant, potential or actual environmental damage, and ensure corrective actions are carried out, recommend means to prevent recurrence and communicate incident findings to relevant parties; and,
- Identify environmental training requirements and arrange relevant training for all levels of site-based staff/workers.
- The level, detail and frequency of reporting expected from the ECoW for the Construction Manager, developer's project manager, and any Authorities or other Agencies, will be agreed by all parties prior to commencement of

construction, and may be further adjusted as required during the course of the project.

5.1.3 Project Ecologist

The Project Ecologist will report to the ECoW and is responsible for the protection of sensitive habitats and species encountered during the construction phase of the wind farm. The Project Ecologist will not be full time on site but will visit the site at least once a month during construction.

The responsibilities and duties of the Project Ecologist will include the following:

- Review and input to the final construction phase CEMP in respect of ecological matters;
- In liaison with ECoW, oversee and provide advice on all relevant ecology mitigation measures set out in EIAR;
- Regular inspection and monitoring of the development, through all phases of construction/operation and provide ecological advice as required;
- Carry out ecological monitoring and survey work as may be required by the planning authority.
- Complete a pre-commencement invasive species survey at the site

5.1.4 Project Hydrologist

The Project Hydrologist will report to the ECoW and is responsible for inspection and review of drainage and water quality aspects associated with construction of the wind farm. The Project Hydrologist will not be full time on site but will visit the site at least once a month during construction.

The responsibilities and duties of the Project Hydrologist will include the following:

- Assist in compiling a detailed drainage design before construction commences and attend the site to set out and assist with micro siting of drainage controls. This will be completed over several site visits at the start of the construction phase;
- Review and input to the final construction phase CEMP in respect of drainage and water quality management;
- Following the initial stage of drainage construction regular site visits will be required, at least once a month, to complete hydrological and water quality audits and reviews and report any issues noted to the Site Supervisor/Construction Manager; and,
- Complete ongoing inspection and monitoring of the development, particularly in areas of drainage control, through all phases of construction (including pre, during and post construction) and ensure construction is carried out as specified in the EIAR.

5.1.5 Project Geotechnical Engineer / Geologist

The Geotechnical Engineer or Project Geologist will report to the ECoW and is responsible for inspection and review of geotechnical aspects associated with construction of the wind farm. The Geotechnical Engineer will not be full time on site but will visit site at least once a month during construction phase.

The responsibilities and duties of the Geotechnical Engineer or Geologist will include the following:

- Visit site regularly, or at least once a month during the construction phase, to complete geotechnical audits and reviews and report any issues to the Site Supervisor/Construction Manager;
- Ensuring that identified hazards are listed in the Geotechnical Risk Register and that these are subject to ongoing monitoring;
- Set up and review the readings of the peat stability monitoring system and,
- Ongoing inspection and monitoring of the development, particularly in areas of peatland and at the borrow pit areas through all phases of construction (including pre, during and post construction) and ensure construction is carried out as specified in the EIAR.

5.2 Monitoring of Surface Water Quality

The surface water quality monitoring programme combines the use of laboratory analysis, water quality monitoring instrumentation and visual inspection to develop a comprehensive schedule of monitoring of all watercourse that exist both at the site and the surrounding area. The information collected by this schedule of water monitoring, particularly the continuous turbidity monitoring will inform the pre-commencement triggers in the SOWOR before works commence in an area. The turbidity monitors both upstream and downstream of the site will provide instant data on the quality of water in which they are deployed and will be equipped with an alarm system to alert site management if a peak in turbidity occurs as set out in the SOWOR.

The water monitoring programme was prepared in accordance with the following legislation:

- Planning and Development Acts 2000-2017;
- Planning and Development Regulations, 2001 (as amended);
- S.I. No. 94 of 1997: European Communities (Natural Habitats) Regulations, resulting from EU Directives 92/43/EEC on the conservation of natural habitats and of wild fauna and flora (the Habitats Directive) and 79/409/EEC on the conservation of wild birds (the Birds Directive);
- S.I. No. 293 of 1988: Quality of Salmon Water Regulations, resulting from EU Directive 78/659/EEC on the Quality of Fresh Waters Needing Protection or Improvement in order to Support Fish Life;
- S.I. No. 272 of 2009: European Communities Environmental Objectives (Surface Waters) Regulations 2009 and S.I. No. 722 of 2003 European Communities (Water Policy) Regulations which implement EU Water Framework Directive (2000/60/EC) and provide for implementation of 'daughter' Groundwater Directive (2006/118/EC). Since 2000 water management in the EU has been directed by the Water Framework Directive (WFD). The key objectives of the WFD are that all water bodies in member states achieve (or retain) at least 'good' status by 2015. Water bodies comprise both surface and groundwater bodies, and the achievement of 'Good' status for these depends also on the achievement of 'good' status by dependent ecosystems. Phases of characterisation, risk assessment, monitoring and the design of programmes of measures to achieve the objectives of the WFD have either been completed or are ongoing. In 2015 it will fully replace a number of existing water related directives, which are successively being repealed, while implementation of other Directives (such as the Habitats Directive 92/43/EEC) will form part of the achievement of implementation of the objectives of the WFD;
- S.I. No. 41 of 1999: Protection of Groundwater Regulations, resulting from EU Directive 80/68/EEC on the protection of groundwater against pollution caused by certain dangerous substances (the Groundwater Directive);

- S.I. No. 249 of 1989: Quality of Surface Water Intended for Abstraction (Drinking Water), resulting from EU Directive 75/440/EEC concerning the quality required of surface water intended for the abstraction of drinking water in the Member States (repealed by 2000/60/EC in 2007);
- S.I. No. 439 of 2000: Quality of Water intended for Human Consumption Regulations and S.I. No. 278 of 2007 European Communities (Drinking Water No. 2) Regulations, arising from EU Directive 98/83/EC on the quality of water intended for human consumption (the Drinking Water Directive) and WFD 2000/60/EC (the Water Framework Directive);
- S.I. No. 272 of 2009: European Communities Environmental Objectives (Surface Waters) Regulations 2009;
- S.I. No. 9 of 2010: European Communities Environmental Objectives (Groundwater) Regulations 2010; and,
- S.I. No. 296 of 2009: European Communities Environmental Objectives (Freshwater Pearl Mussel) Regulations 2009.

Relevant Northern Irish legislation were also reviewed and considered during the assessment of trans-border hydrological impacts.

This water monitoring programme will be the subject of independent review by the supervising hydrologist who will provide the necessary guidance on the monitoring requirements. The water monitoring programme is outlined in the following sections.

5.2.1 Pre-Construction Drainage Inspection and Monitoring

There is an existing drainage network across the site and runoff drains relatively freely to local watercourses and streams. This existing drainage system will continue to function as it is during the pre-construction phase.


However, prior to commencement of works in sub-catchments across the site main drain inspections will be completed to ensure ditches and streams are free from debris and blockages that may impede drainage. These inspections will be done on a catchment by catchment basis as the construction works develop across the site, as works in all areas will not commence simultaneously.

Monthly Laboratory Analysis Sampling: Baseline laboratory analysis for the parameters listed below with relevant regulatory limits and Environmental Quality Standards (EQSs) will be undertaken for each watercourse *e.g.* at SW1 – SW3 as outlined in Figure 5.1. This will not be restricted to just these three locations and further sampling points will be added as deemed necessary by the ECoW in consultation with the project hydrologist.

5.2.2 Construction Phase Drainage Inspection and Monitoring:

Inspection sheets and photographic records will be kept on site. Inspection points will include the in-situ field monitoring point locations and the laboratory analysis sampling points. Inspection points will depend on works being completed within the catchment upstream of the identified monitoring locations. Visual inspections will also be completed after major rainfall events, *i.e.* after events of >25mm rainfall in any 24-hour period and data including photographs will be collected by visual inspections and independently assessed by the supervising hydrologist who will monitor and advise on the records being received.

The following periodic inspection regime will be implemented:

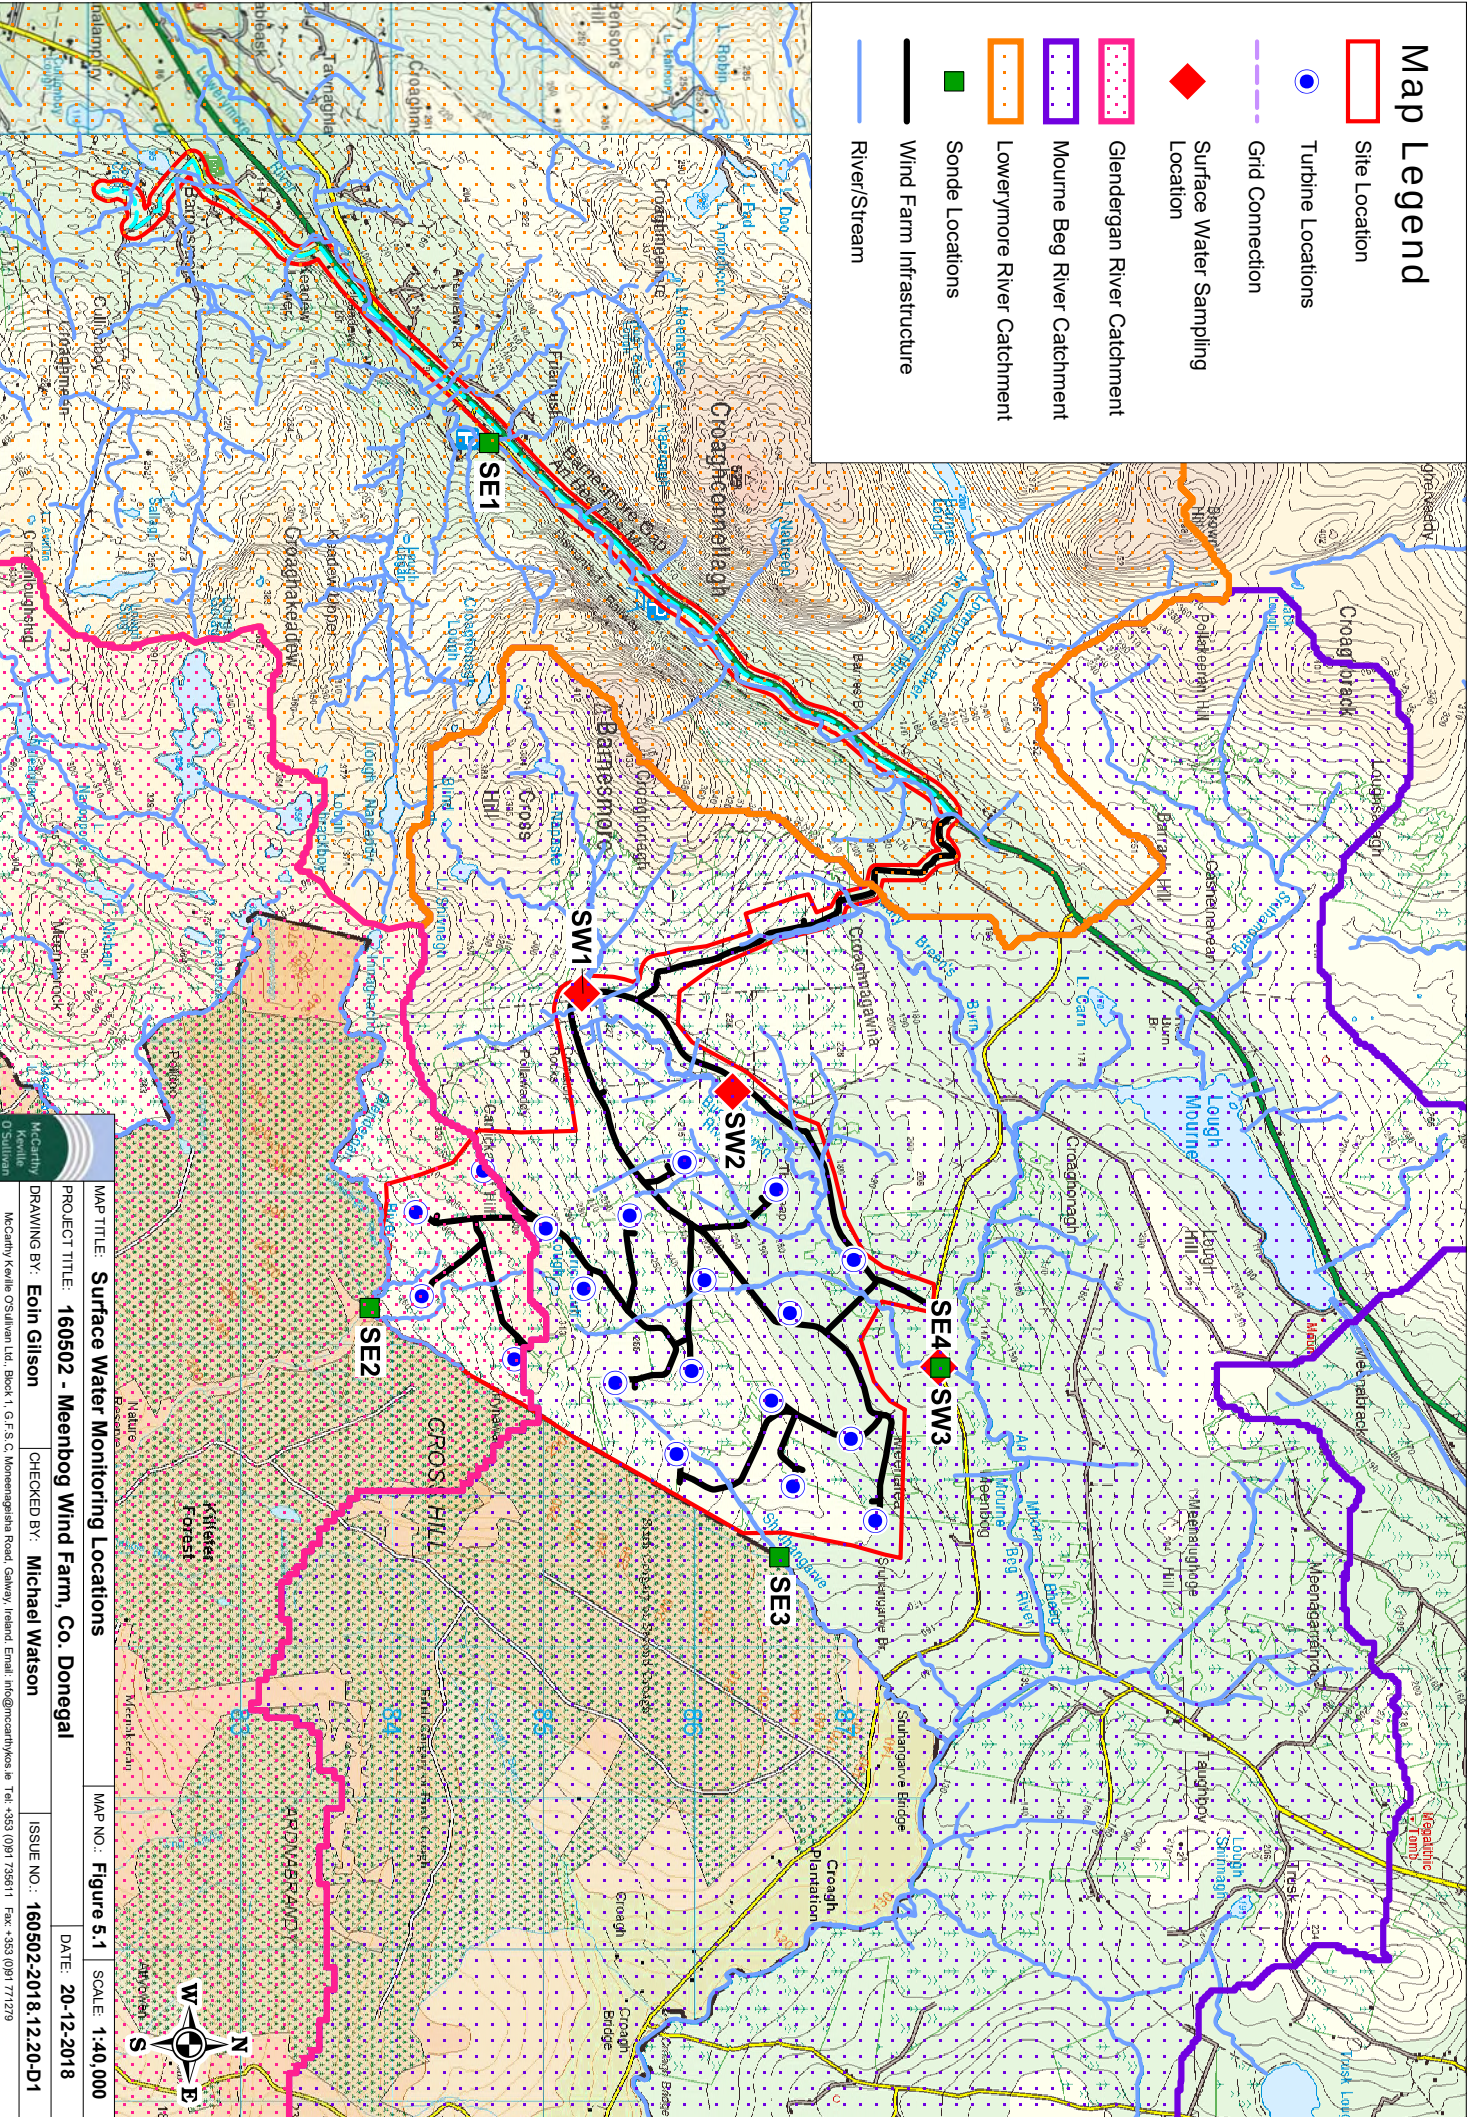

- Daily general visual inspections of site operations and inspections of all watercourses within the site and in the surrounding area by the ECoW or a suitably qualified and competent person as delegated by the ECoW;
- Inspections to include all elements of drainage infrastructure to ensure the system is operating correctly and to identify and maintenance that is required. Any changes, such as discolouration, odour, oily sheen or litter should be noted and corrective action should be implemented. High risk locations such as settlement ponds will be inspected daily. Daily inspections checks will be completed on plant and equipment, and whether materials such as straw bales or oil absorbent materials need replacement;
- Event based inspections by the ECoW as follows:
 - o >10 mm/hr (*i.e.* high intensity localised rainfall event);
 - o >25 mm in a 24-hour period (heavy frontal rainfall lasting most of the day); or,
 - o Rainfall depth greater than monthly average in 7 days (prolonged heavy rainfall over a week).
- Monthly site inspections by the Project Hydrologist/ ECoW during construction phase;
- Quarterly site inspections by the Project Hydrologist/ ECoW after construction for a period of one year following the construction phase; and,
- A written record will be maintained or available on-site within this Construction Environmental Management Plan (CEMP) which will be maintained on-site during the construction phase.

5.2.2.1 In-situ field monitoring:

Field chemistry measurements of unstable parameters, (pH, conductivity, dissolved oxygen and temperature) will be taken at all monitoring locations outlined in Figure 5.1. These analyses will be carried out by either the ECoW or the Project Hydrologist. In-situ field monitoring will be completed on a weekly basis. In-situ field monitoring will also be completed after major rainfall events, *i.e.* after events of >25mm rainfall in any 24-hour period. The supervising hydrologist will monitor and advise on the readings collected by in-situ field monitoring.

5.2.2.2 Monthly Laboratory Analysis Sampling

Laboratory analysis of a range of parameters with relevant regulatory limits and EQSs will continue throughout the construction phase for each monitoring location as outlined in Figure 5.1. All samples will be sent for analysis to an independent laboratory. This sampling will also be completed on an event based basis, *i.e.* after major rainfall events (>25mm rainfall in any 24-hour period). The supervising hydrologist will monitor and advise on the readings being received from the testing laboratory.

5.2.2.3 Continuous Turbidity Monitoring

Turbidity monitors or sondes will be installed at locations surrounding the wind farm site as outlined in Figure 5.1. The sondes will provide continuous readings for turbidity levels in the watercourse. This equipment will be supplemented by daily visual monitoring at their locations as outlined in the sections below.

5.2.2.4 Monitoring Parameters

The analytical determinants of the monitoring programme (including limits of detection and frequency of analysis) will be as per S.I. No. 272 of 2009 European Communities Environmental Objectives (Surface Waters) Regulations, S.I. No. 722 of 2003 European Communities (Water Policy) Regulations and European Communities Environmental

Objectives (Freshwater Pearl Mussel) Regulations 2009. The likely suite of parameters will include:

- pH (field measured)
- Electrical Conductivity (field measured)
- Temperature (field measured)
- Dissolved Oxygen (field measured)
- Turbidity (NTU) (sonde measured)
- Total Suspended Solids (mg/l)
- Ammoniacal Nitrogen as NH₃ (mg/l)
- Ammoniacal Nitrogen as NH₄ (mg/l)
- Nitrite (NO₂) (mg/l)
- Ortho-Phosphate (P) (mg/l)
- Nitrate (NO₃) (mg/l)
- Phosphorus (unfiltered) (mg/l)
- Chloride (mg/l)
- Biochemical Oxygen Demand (BOD) (mg/l)

5.2.3 Surface Water Monitoring Reporting

Visual inspection and laboratory analysis results of water quality monitoring shall assist in determining requirements for any necessary improvements in drainage controls and pollution prevention measures implemented on site.

It will be the responsibility of the Environmental Clerk of Works to present the ongoing results of water quality and weather monitoring at or in advance of regular site meetings.

Reports on water quality will consider all field monitoring and visual inspections, and results of laboratory analysis completed for that period. Reports will describe how the results compare with baseline data as well as previous reports on water quality. The reports will also describe whether any deterioration or improvement in water quality that has been observed, whether any effects are attributable to construction activities and what remedial measures or corrective actions have been implemented.

All water monitoring reports will be available to Donegal County Council on request at any stage during the construction phase

5.2.4 Post-Construction Monitoring

Monthly sampling for laboratory analysis for a range of parameters as adopted during pre-commencement and construction phases will continue for six months after construction is complete. The supervising hydrologist will monitor and advise on the readings being received from the testing laboratory.

5.3 Environmental Awareness and Training

5.3.1 Environmental Induction

The Environmental Induction will be integrated into the general site induction on a case by case basis for each member of staff employed on-site depending on their assigned roles and responsibilities on site. Where necessary, the Environmental Induction will as a minimum include:

- A copy of the Environmental Management Site Plans and discussion of the key environmental risks and constraints;

- An outline of the CEMP structure;
- A discussion of the applicable Works Method Statement;
- The roles and responsibilities of staff, including contractors, in relation to environmental management; and,
- An outline of the Environmental Incident Management Procedure.

5.3.2 Toolbox Talks

Tool box talks would be held by the ECoW or Construction Manager at the commencement of each day, or at the commencement of new activities. The aims of the tool box talks are to identify the specific work activities that are scheduled for that day or phase of work. In addition, the necessary work method statements and sub plans would be identified and discussed prior to the commencement of the day's activities.

Site meetings would be held on a regular basis involving all site personnel. The objectives of site meetings is to discuss the coming weeks activities and identify the relevant work method statements and sub plans that will be relevant to that weeks activities. Additionally, any non-compliance identified during the previous week would also be discussed with the aim to reduce the potential of the same non-compliance reoccurring.

6 EMERGENCY RESPONSE PLAN

An Emergency Response Plan is presented in this section of the CEMP. It provides details of procedures to be adopted in the event of an emergency in terms of site health and safety and environmental protection.

6.1 Emergency Response

The Emergency Response Plan (ERP) is presented in this section of the CEMP. It provides details of procedures to be adopted in the event of an emergency. The site ERP includes details on the response required and the responsibilities of all personnel in the event of an emergency. The ERP will require updating and submissions from the contractor/PSCS and suppliers as the project progresses. Where sub-contractors that are contracted on site are governed by their own emergency response procedure a bridging arrangement will be adopted to allow for inclusion of the sub-contractor's ERP within this within this document.

This is a working document that requires updating throughout the various stages of the project.

6.1.1 Roles and Responsibilities

The chain of command during an emergency response sets out who is responsible for coordinating the response. The Site Manager will lead the emergency response which makes him responsible for activating and coordinating the emergency response procedure. The other site personnel who can be identified at this time who will be delegated responsibilities during the emergency response are presented in Figure 6.1. In a situation where the Site Manager is unavailable or incapable of coordinating the emergency response, the responsibility will be transferred to the next person in the chain of command outlined in Figure 6.1. This will be updated throughout the various stages of the project.

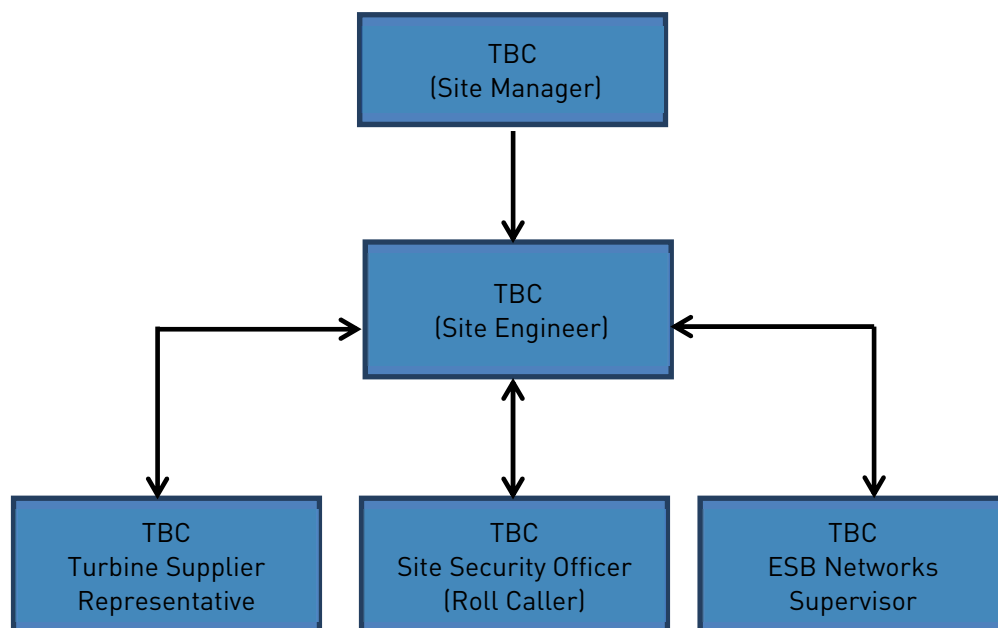


Figure 6.1 Emergency Response Procedure Chain of Command

6.1.2 Initial Steps

In order to establish the type and scale of potential emergencies that may occur, the following hazards have been identified as being potential situations that may require an emergency response in the event of an occurrence.

Table 6.1 Hazards associated with potential emergency situations

Hazard	Emergency Situation
Construction Vehicles: Dump trucks, tractors, excavators, cranes etc.	Collision or overturn which has resulted in operator or third-party injury.
Abrasive wheels/Portable Tools	Entanglement, amputation or electrical shock associated with portable tools
Contact with services	Electrical shock or gas leak associated with an accidental breach of underground services
Fire	Injury to operative through exposure to fire
Falls from heights including falls from scaffold towers, scissor lifts, and ladders	Injury to operative after a fall from a height
Sickness	Illness unrelated to site activities of an operative e.g. heart attack, loss of consciousness, seizure

In the event of an emergency situation associated with, but not restricted to, the hazards outlined in Table 6.1 the Site Manager will carry out the following:

- Establish the scale of the emergency situation and identify the number of personnel, if any, have been injured or are at risk of injury.
- Where necessary, sound the emergency siren/fog horn that activates an emergency evacuation on the site. The Site Manager must proceed to the assembly point if the emergency poses any significant threat to their welfare **and if there are no injured personnel at the scene that require assistance.** The Site Manager will be required to use his own discretion at that point. In the case of fire, the emergency evacuation of the site should proceed, without exception. The site evacuation procedure is outlined in Section 6.1.3.
- Make safe the area if possible and ensure that there is no identifiable risk exists with regard to dealing with the situation e.g. if a machine has turned over, ensure that it is in a safe position so as not to endanger others before assisting the injured.
- Contact the required emergency services or delegate the task to someone if he is unable to do so. If delegating the task, ensure that they follow the procedures for contacting the emergency services as set out in Section 6.3.
- Take any further steps that are deemed necessary to make safe or contain the emergency incident e.g. cordon off an area where an incident associated with electrical issues has occurred.
- Contact any regulatory body or service provider as required e.g. ESB Networks the numbers for which as provided in Section 6.3.2.
- Contact the next of kin of any injured personnel where appropriate. The procedure for this is outlined in Section 6.3.3.

6.1.3 Site Evacuation/Fire Drill

A site evacuation/fire drill procedure will provide basis for carrying out the immediate evacuation of all site personnel in the event of an emergency. The following steps will be taken:

- Notification of the emergency situation. Provision of a siren or fog horn to notify all personnel of an emergency situation.
- An assembly point will be designated in the construction compound area and will be marked with a sign. All site personnel will assemble at this point.
- A roll call will be carried out by the Site Security Officer to account for all personnel on site.
- The Site Security Officer will inform the Site Manager when all personnel have been accounted for. At this time, the Site Manager will decide the next course of action which be determined by the situation that exists at that time. The Site Manager will advise all personnel accordingly.

All personnel will be made aware of the evacuation procedure during site induction. The Fire Services Acts of 1981 and 2003 require the holding of fire safety evacuation drills at specified intervals and the keeping of records of such drills.

6.1.4 Excessive Peat Movement

Where there is excessive peat movement or continuing peat movement recorded at a monitoring location or identified at any location within the site but no apparent signs of distress to the peat (e.g. cracking, surface rippling) then the following shall be carried out.

1. All construction activities shall cease within the affected area.
2. Increased monitoring at the location shall be carried out. The area will be monitored, as appropriate, until such time as movements have ceased.
3. Re-commencement of limited construction activity shall only start following a cessation of movement and the completion of a geotechnical risk assessment by a geotechnical engineer.

6.1.5 Onset of Peat Slide

Where there is the onset or actual detachment of peat (e.g. cracking, surface rippling) then the following shall be carried out.

1. On alert of a peat slide incident, all construction activities will cease and all available resources will be diverted to assist in the required mitigation procedures.
2. Where considered possible, action will be taken to prevent a peat slide reaching any watercourse. This will take the form of the construction of check barrages on land. Due to the terrain, the possible short run-out length to watercourses, speed of movement and the inability to predict locations it may not be possible to implement any on-land prevention measures, in this case a watercourse check barrage will be implemented.
3. For localised peat slides that do not represent a risk to a watercourse and have essentially come to rest, the area will be stabilised initially by rock infill, if required. The failed area and surrounding area will then be assessed by the engineering staff and stabilisation procedures implemented. The area will be monitored, as appropriate, until such time as movements have ceased.

6.1.6 Spill Control Measures

Every effort will be made to prevent an environmental incident during the construction and operational phase of the project. Oil/Fuel spillages are one of the main environmental risks that will exist at the site which will require an emergency response procedure. The importance of a swift and effective response in the event of such an incident occurring cannot be over emphasised. The following steps provide the procedure to be followed in the event of such an incident.

- Stop the source of the spill and raise the alarm to alert people working in the vicinity of any potential dangers.
- If applicable, eliminate any sources of ignition in the immediate vicinity of the incident
- Contain the spill using the spill control materials, track mats or other material as required. Do not spread or flush away the spill.
- If possible, cover or bund off any vulnerable areas where appropriate such as drains, watercourses or sensitive habitats.
- If possible, clean up as much as possible using the spill control materials.
- Contain any used spill control material and dispose of used materials appropriately using a fully licensed waste contractor with the appropriate permits so that further contamination is limited.
- Notify the ECoW immediately giving information on the location, type and extent of the spill so that they can take appropriate action.
- The ECoW will inspect the site and ensure the necessary measures are in place to contain and clean up the spill and prevent further spillage from occurring.
- The ECoW will notify the appropriate regulatory body such as Donegal County Council, Department of Communications, Climate Action and Environment (DCCAE), if deemed necessary.

Environmental incidents are not limited to just fuel spillages. Therefore, any environmental incident must be investigated in accordance with the following steps.

- The ECoW must be immediately notified.
- If necessary, the ECoW will inform the appropriate regulatory authority. The appropriate regulatory authority will depend on the nature of the incident.
- The details of the incident will be recorded on an Environmental Incident Form which will provide information such as the cause, extent, actions and remedial measures used following the incident. The form will also include any recommendations made to avoid reoccurrence of the incident.
- If the incident has impacted on an ecologically sensitive receptor, such as a sensitive habitat, protected species or designated conservation site (pSPA or cSAC), the ECoW will liaise with the Project Ecologist.
- If the incident has impacted on a sensitive receptor such as an archaeological feature the ECoW will liaise with the Project Archaeologist.
- A record of all environmental incidents will be kept on file by the ECoW and the Main Contractor. These records will be made available to the relevant authorities such as Donegal County Council and DCCAE, if required.

The ECoW will be responsible for any corrective actions required as a result of the incident e.g. an investigative report, formulation of alternative construction methods or environmental sampling, and will advise the Main Contractor as appropriate.

6.2 Contacting the Emergency Services

6.2.1 Emergency Communications Procedure

In the event of requiring the assistance of the emergency services the following steps should be taken:

Stay calm. It's important to take a deep breath and not get excited. Any situation that requires 999/112 is, by definition, is an emergency. The dispatcher or call-taker knows that and will try to move things along quickly, but under control.

Know the location of the emergency and the number you are calling from. This may be asked and answered a couple of times but don't get frustrated. Even though many emergency call centres have enhanced capabilities meaning they are able to see your location on the computer screen they are still required to confirm the information. If for any reason you are disconnected, at least emergency crews will know where to go and how to call you back.

Wait for the call-taker to ask questions, then answer clearly and calmly. If you are in danger of assault, the dispatcher or call-taker will still need you to answer quietly, mostly "yes" and "no" questions.

If you reach a recording, listen to what it says. If the recording says your call cannot be completed, hang up and try again. If the recording says all call takers are busy, *WAI/T*. When the next call-taker or dispatcher is available to take the call, it will transfer you.

Let the call-taker guide the conversation. He or she is typing the information into a computer and may seem to be taking forever. There's a good chance, however, that emergency services are already being sent while you are still on the line.

Follow all directions. In some cases, the call-taker will give you directions. Listen carefully, follow each step exactly, and *ask for clarification* if you don't understand.

Keep your eyes open. You may be asked to describe victims, suspects, vehicles, or other parts of the scene.

Do not hang up the call until directed to do so by the call taker.

Due to the remoteness of the site it may be necessary to liaise with the emergency services on the ground in terms of locating the site. This may involve providing an escort from a designated meeting point that may be located more easily by the emergency services. This should form part of the site induction to make new personnel and sub-contractors aware of any such arrangement or requirement if applicable.

6.2.2 Contact Details

A list of emergency contacts is presented in Table 5.2. A copy of these contacts will be included in the Site Safety Manual and in the site offices and the various site welfare facilities.

Table 5.2 Emergency Contacts

Contact	Telephone no.
Emergency Services – Ambulance, Fire, Gardaí	999/112
Doctor – Milbrae Surgery Ballybofey	074 913 1023
Hospital – Letterkenny University Hospital	074 912 5888
ESB Emergency Services	1850 372 999
Bord Gáis Emergency	1850 20 50 50
Gardaí –Local Garda Station TBC	TBC
Health and Safety Co-ordinator - Health & Safety Services	TBC
Health and Safety Authority	1890 289 389
Project Supervisor Construction Stage (PSCS): TBC	TBC
Project Supervisor Design Stage (PSDS):	TBC
Client –	Planree Ltd

6.2.3 Procedure for Personnel Tracking

All operatives on site without any exception will have undergone a site induction where they will be required to provide personal contact details which will include contact information for the next of kin.

In the event of a site operative becoming in an emergency situation where serious injury has occurred and hospitalisation has taken place, it will be the responsibility of the Site Manager or next in command if unavailable to contact the next of kin to inform them of the situation that exists.

6.3 Induction Checklist

Table 5.3 provides a list of items highlighted in this ERP which must be included or obtained during the mandatory site induction of all personnel that will work on the site. This will be updated throughout the various stages of the project.

Table 5.3 Emergency Response Plan Items Applicable to the Site Induction Process

ERP Items to be included in Site Induction	Status
All personnel will be made aware of the evacuation procedure during site induction	
Due to the remoteness of the site it may be necessary to liaise with and assist the emergency services on the ground in terms of locating the site. This may involve providing an escort from a designated meeting point that may be located more easily by the emergency services. This should form part of the site induction to make new personnel and sub-contractors aware of any such arrangement or requirement if applicable.	
All operatives on site without any exception will have undergone a site induction where they will be required to provide personal contact details which will include contact information for the next of kin.	

7 MITIGATION PROPOSALS

All mitigation measures relating to the pre-commencement, construction and operational phases of the Permitted Development were set out in the various sections of the Environmental Impact Assessment Report (EIAR) prepared as part of the planning permission application to An Bord Pleanála.

This section of the CEMP groups together all of the mitigation measures presented in the EIAR. The Mitigation Measures are presented in the following pages.

By presenting the mitigation proposals in the below format, it is intended to provide an easy to audit list that can be reviewed and reported on during the future phases of the project. The tabular format in which the below information is presented, can be further expanded upon during the course of future project phases to provide a reporting template for site compliance audits.

Table 7.1 Site preparation and Mitigation Measures

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
Pre-Commencement Phase				
MM1	EIAR Section 7	It is proposed that construction works will commence outside the bird nesting season (1 st of April to 31 st of July inclusive).		
MM2	EIAR Section 4	The removal and disposal of wastewater from the site will be carried out by a fully permitted waste collector holding valid Waste Collection Permits as issued under the Waste Management (Collection Permit) Regulations, 2007. Information on the appointed permitted contractor and evidence of a maintenance contract will be submitted to the Planning Authority prior to any construction works taking place.		
MM3	EIAR Section 4	All site activities will be provided for in a Construction Environmental Management Plan, prepared prior to the commencement of any operations onsite. The CEMP will set out all measures necessary to ensure works are carried out in accordance with the mitigation measures set out in the EIAR and will set out the monitoring and inspections procedures and frequencies.		
MM4	EIAR Section 4 CEMP Section 4	An ECoW will oversee the site works and implementation of the Environmental Management Plan and provide on-site advice on the mitigation measures as necessary to ensure the project proceeds as intended. The level, detail and frequency of reporting expected from the ECoW for the Construction Manager, developer's project manager, and any Authorities or other Agencies, will be agreed by all parties prior to commencement of construction, and may be further adjusted as required during the course of the project.		
MM5	EIAR Section 4	The arrangements for concrete deliveries to the site will be discussed with suppliers before work starts, agreeing routes, prohibiting on-site washout and discussing emergency procedures.		
MM6	EIAR Section 4	Drainage swales will be installed in advance of any construction works commencing.		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
	CEMP Section 3			
MM7	EIAR Section 4 CEMP Section 2	Borrow pits will be secured with stock proof fencing to prevent access to these areas. Appropriate health and safety signage will be erected on the fencing prior to construction works commencing.		
MM8	EIAR Section 4 CEMP Section 2	Culverts will be installed at locations where streams or natural drainage channels cross the new access track route. All works involving culverts, whether they are new, upgraded or extended, will be carried out to follow a method statement to be agreed with Inland Fisheries Ireland.		
MM9	EIAR Section 4 CEMP Section 3	All materials and equipment necessary to implement the drainage mitigation measures will be brought on-site in advance of any works commencing. The drainage measures outlined in the EIAR will be installed prior to, or at the same time as the works they are intended to drain. An adequate amount of straw bales, clean stone, terram, stakes, etc. will be kept on site at all times to implement the drainage design measures as necessary. The works programme for the ground works part of the construction phase of the project will also take account of weather forecasts and predicted rainfall in particular.		
MM10	EIAR Section 4 CEMP Section 3			
MM11	EIAR Section 4 CEMP Section 3, 7	The effectiveness of drainage measures designed to minimise runoff entering works areas and capture and treat silt-laden water from the works areas, will be monitored as part of the water quality and monitoring programme set out in Section 7 of the CEMP. The ECoW or supervising hydrologist will respond to changing weather, ground or drainage conditions on the ground as the project proceeds, to ensure the effectiveness of the drainage design is maintained in so far as is possible. This may require the installation of additional check dams, interceptor drains or swales as deemed necessary on-site.		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
MM12	EIAR Section 4 CEMP Section 7	An inspection and maintenance plan for the drainage system on site will be prepared in advance of commencement of any works. Regular inspections of all installed drainage systems will be necessary, especially after heavy rainfall, to check for blockages, and ensure there is no build-up of standing water at parts of the systems where it is not intended. The inspection of the drainage system will be the responsibility of the ECoW or the supervising hydrologist.		
MM13	EIAR Section 9 CEMP Section 3	A 50-metre buffer zone will be maintained around watercourses during the windfarm construction. With the exception of road crossings of streams and associated culvert construction, no development infrastructure, vehicle or plant movement, construction activity or stock-piling of construction materials or construction waste will take place within this zone, and no vegetation will be removed from within this zone.		
MM14	EIAR Section 9 CEMP Section 3	A 20-metre buffer zone will be maintained around existing artificial drainage points for the duration of the construction phase.		
MM15	EIAR Section 7	No felling of conifers, individual trees or bushes will be carried out during the general bird breeding season. (the 1st of April to the 31st of July inclusive).		
MM16	EIAR Section 6	An Invasive Species Management Plan will be developed following a preconstruction invasive survey. The report will describe the best practice measures that will be followed to ensure that works associated with the permitted wind farm development do not result in the spread or proliferation of invasive species.		
MM17	EIAR Section 6	A pre-construction mammal survey will be undertaken to identify evidence of protected mammals within the works areas associated with the Permitted Development.		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
MM18	EIAR Section 14	A pre-commencement condition survey of roads associated with the Permitted Development will be carried out prior to commencement of construction activities.		
MM19	EIAR Section 4 CEMP Section 9	The procedures for the implementation of the mitigation measures outlined in such an CEMP and their effectiveness and completion is typically audited by way of an Environmental Management Plan Audit Report. The CEMP Audit Report effectively lists all mitigation measures prescribed in any of the planning documentation, all conditions attached to the grant of planning permission and any further mitigation measures proposed during the detailed design stage and allows them to be audited on a systematic and regular basis.		
Construction Phase				
Construction Management				
MM20	EIAR Section 4 CEMP Section 3	On-site refuelling will be carried out at dedicated refuelling locations using a mobile double skinned fuel bowser. The fuel bowser, a double-axel custom-built refuelling trailer will be re-filled off site and will be towed around the site by a 4x4 jeep to where machinery is located. It is not practical for all vehicles to travel back to a single refuelling point, given the size of the cranes, excavators, etc. that will be used during the construction of the permitted wind farm development. The 4x4 jeep will also carry fuel absorbent material and pads in the event of any accidental spillages. The fuel bowser will be parked on a level area in the construction when not in use. Only designated trained and competent operatives will be authorised to refuel plant on site. Mobile measures such as drip trays, spill kits and fuel absorbent mats will be used during all refuelling operations.		
MM21	EIAR Section 4	No batching of wet-cement products will occur on site. Ready-mixed supply of wet concrete products and where possible, emplacement of pre-cast elements, will take place. Only ready-mixed concrete will be used during the construction phase, with all ready-mixed concrete being delivered from local batching plants in sealed concrete delivery trucks.		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
MM22	EIAR Section 4	No washing out of any plant used in concrete transport or concreting operations will be carried out onsite. When concrete is delivered to site, only the chute of the delivery truck will be cleaned, using the smallest volume of water necessary, before leaving the site. Concrete trucks will be directed back to their batching plant for washout.		
MM23	EIAR Section 4	No concrete will be transported around the site in open trailers or dumpers so as to avoid spillage while in transport.		
MM24	EIAR Section 4	Clearly visible signs in prominent locations will be placed close to concrete pour areas specifically stating washout of concrete lorries is not permitted on the site.		
MM25	EIAR Section 4	All concrete used in the construction of turbine bases will be poured directly into the shuttered formwork from the delivery truck. If this is not practical, the concrete will be poured from the delivery truck into a hydraulic concrete pump or into the bucket of an excavator, which will transfer the concrete to the location where it is needed.		
MM26	EIAR Section 4	Main pours will be planned days or weeks in advance. Large pours will be avoided when prolonged periods of heavy rain are forecast.		
MM27	EIAR Section 4	Concrete pumps and machine buckets will be restricted from slewing over watercourses while placing concrete.		
MM28	EIAR Section 4	Excavations will be sufficiently dewatered before concreting begins. Dewatering will continue while concrete sets.		
MM29	EIAR Section 4	Covers will be available for freshly placed concrete to avoid the surface washing away in heavy rain.		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
MM30	EIAR Section 4	Surplus concrete after completion of a pour will be used elsewhere at suitable locations around the site where it is required.		
MM31	EIAR Section 4 CEMP Section 3	If necessary, water will be taken from settlement ponds in the site's drainage system and will be pumped into a bowser or water spreader to dampen down haul roads and site compounds to prevent the generation of dust. Silty or oily water will not be used for dust suppression.		
MM32	CEMP Section 3	All construction related traffic will have speed restrictions on un-surfaced roads to 20 kph.		
MM33	EIAR Section 4	A road sweeper will be available if any section of the public roads were to be dirtied by trucks associated with the Permitted Development.		
MM34	EIAR Section 4	During construction of the Permitted Development, all staff will be made aware of and adhere to the Health & Safety Authority's <i>'Guidelines on the Procurement, Design and Management Requirements of the Safety, Health and Welfare at Work (Construction) Regulations 2006'</i> . This will encompass the use of all necessary Personal Protective Equipment and adherence to the site Health and Safety Plan.		
MM35	EIAR Section 4	Any area where excavations are planned will be surveyed and all existing services will be identified prior to commencement of any works. Liaison will be held with the relevant sections of the Local Authority including all the relevant area engineers to ensure all services are identified. Excavation permits will be completed and all plant operators and general operatives will be inducted and informed as to the location of any services.		
Drainage Design and Management				
MM36	EIAR Section 4	Swales will be used to intercept and collect run off from construction areas of the site during the construction phase, and channel it to stilling ponds for sediment attenuation.		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
	CEMP Section 3			
MM37	EIAR Section 4 CEMP Section 3	Interceptor drains will be installed upgradient of any works areas to collect surface flow runoff and prevent it reaching excavations and construction areas of the site. It will then be directed to areas where it can be re-distributed over the ground as sheet flow.		
MM38	EIAR Section 4 CEMP Section 3	Check dams will not be used in any natural watercourses, only artificial drainage channels and interceptor drains. The check dams will be left in place when the interceptor drains are backfilled at the end of the construction phase to limit linear flow in the backfilled drain. The check dams will be installed at regular intervals along interceptor drains to restrict flow velocity, minimise channel erosion and promote sedimentation behind the dam. The check dams will be installed as the interceptor drains are being excavated. The spacing and frequency of the check dams will be dependent on the gradient of the interceptor drain or swale in which they are being installed.		
MM39	EIAR Section 4 CEMP Section 3	A level spreader will be constructed at the end of each interceptor drain to convert concentrated flows in the drain into diffuse sheet flow on areas of vegetated ground. The levels spreaders will be located downgradient of any works areas in locations where they are not likely to contribute further to water ingress to construction areas of the site. They will also be emplaced at end of swales carrying discharge from settlement ponds. The level spreaders will distribute clean drainage water onto vegetated areas where the water will not be reconcentrated into a flow channel immediately below the point of discharge. The discharge point will be on level or only very gently sloping ground rather than on a steep slope so as to prevent erosion. No drains will discharge directly to surface waters.		
MM40	EIAR Section 4 CEMP Section 3	Piped slope drains will be used to convey surface runoff from diversion drains safely down slopes to flat areas without causing erosion. Once the runoff reaches the flat areas it will be reconverted to diffuse sheet flow. Level spreaders will only be established on slopes of less than 6% in grade. Piped slope drains will be used to transfer water away from areas		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
		where slopes are too steep to use level spreaders. Piped slope drains will only remain in place for the duration of the construction phase of the project. On completion of the works, the pipes and rock aprons will be removed and all channels backfilled with the material that was originally excavated from them.		
MM41	EIAR Section 4 CEMP Section 3	Vegetation filters, that is areas of existing vegetation, accepting drainage water issuing from level spreaders as sheet flow, will remove any suspended sediment from water channelled via interceptor drains or any remaining sediment in waters channelled via swales and stilling ponds.		
MM42	EIAR Section 4 CEMP Section 3	Stilling ponds will be used to attenuate runoff from works areas of the site during the construction phase and will remain in place to handle runoff from roads and hardstanding areas of the Permitted Development during the operational phase. Stilling ponds will be excavated/constructed at each required location as two separate ponds in sequence, a primary pond and a secondary pond. The stilling ponds will be sized according to the size of the area they will be receiving water from but will be sufficiently large to accommodate peak flows storm events. The stilling ponds will be dimensioned so that the length to width ratio will be greater than 2:1, where the length is the distance between the inlet and the outlet. Where ground conditions allow, stilling ponds will be constructed in a wedge shape, with the inlet located at the narrow end of the wedge. Each stilling pond will be a minimum of 1-1.5 metres in depth. Deeper ponds will be used to minimise the excavation area needed for the required volume. The embankment that forms the sloped sides of the stilling ponds will be stabilised with vegetated turves, which will have been removed during the excavation of the stilling ponds area.		
MM43	EIAR Section 4 CEMP Section 3	A siltbuster or similar equivalent piece of equipment will be available if required to filter any water pumped out of excavation areas, prior to its discharge to settlement ponds or swales. This includes turbine base excavations and borrow pit excavations. This water is		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
		likely to have a high sediment load and will be directed via swales to settlement ponds after treatment in the unit.		
MM44	EIAR Section 4 CEMP Section 3	Culverts will be installed at locations where streams or natural drainage channels cross the new access track route. All works involving culverts, whether they are new, upgraded or extended, will be carried out to follow a method statement to be agreed with Inland Fisheries Ireland.		
MM45	EIAR Section 4 EIAR Section 9 CEMP Section 3	Silt fences will be installed along the routes of existing watercourses or drainage ditches where site roads pass over the watercourses, immediately downstream of the construction area. Silt fences will be installed along a level contour so water does not pond more than 400 mm at any point. The silt fence will be trenched at least 100 mm into the ground and will be stretched tight between the posts. The fences will not be allowed to sag or break away from the fence posts. Silt fences will be installed as single, double or a series of triple silt fences, depending on the space available and the anticipated sediment loading. During the near stream construction work double silt fences will be emplaced immediately down-gradient of the construction area for the duration of the construction phase.		
MM46	EIAR Section 9 CEMP Section 3	Mitigation measures which will reduce the risk of entrainment of suspended solids and nutrient release in surface watercourses comprise best practice methods which are set out above in Section 3.4.		
MM47	EIAR Section 4 CEMP Section 3	The works programme for the groundworks part of the construction phase of the project will also take account of weather forecasts and predicted rainfall in particular.		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
MM48	EIAR Section 4 CEMP Section 3, 4 & 7	The effectiveness of drainage measures designed to minimise runoff entering works areas and capture and treat silt-laden water from the works areas, will be monitored continuously by the ECoW or supervising hydrologist on-site. The ECoW or supervising hydrologist will respond to changing weather, ground or drainage conditions on the ground as the project proceeds, to ensure the effectiveness of the drainage design is maintained in so far as is possible. This may require the installation of additional check dams, interceptor drains or swales as deemed necessary on-site.		
MM49	EIAR Section 4	Material excavated to create the working area will be stored locally for later reuse in backfilling the working area around the turbine foundation. The excavated material will be covered with polythene sheets and surrounded by silt fences to ensure sediment-laden run-off does not occur.		
Flora and Fauna				
MM50	EIAR Section 9 CEMP Section 3	Best practice Forestry Service Guideline mitigation measures will reduce the risk of entrainment of suspended solids and nutrient release in surface watercourses as outlined in the EIAR.		
MM51	Condition 16 CCS Section 10 Bird Monitoring Programme	If any hen harrier breeding activity is identified, surveys will focus on establishing the location of the nest site and no works shall be permitted within a 500m buffer of the nest (Forestry Commission Scotland 2006). Works will not be permitted to recommence within the buffer zone until it can be demonstrated that that hen harrier are no longer reliant on the nest site. All site staff and subcontractors will be made aware of any restrictions to be imposed by means of a toolbox talk and a map of the 'no-works zone' will be made available to all construction staff. The restricted area will also be marked off using hazard-tape fencing to alert all persons on site to the suspension of works within that area.		
Peat, Subsoils and Bedrock				

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
MM52	CEMP Section 3	General recommendation for good construction practice to minimise the risk of construction activity causing potential peat instability are outlined in Section 3.6 of the CEMP.		
MM53	EIAR Section 8	Peat removed from turbine locations will be transported to the designated borrow pit areas.		
MM54	EIAR Section 8	Any excess mounded peat in temporary placement areas for long periods will be digger-bucket sealed and covered with polyethylene sheets or reseeded at the earliest opportunity.		
MM55	EIAR Section 8	In order to minimise runoff during the construction phase, stripping of peat should not take place during excessively dry weather (to prevent dust generation) or extremely wet periods (to prevent increased silt rich runoff).		
MM56	EIAR Section 9	Brash mats will be used where necessary to support vehicles on soft ground, reducing peat and mineral soils erosion and avoiding the formation of rutted areas, in which surface water ponding can occur. Brash mat renewal should take place when they become heavily used and worn. Provision should be made for brash mats along all off-road routes, to protect the soil from compaction and rutting.		
MM57	EIAR Section 8 CEMP Section 3	The following issues incorporated into the construction phase of the project will assist in the management of the risks for this site (AGEC, 2017): ▪ Appointment of experienced and competent contractors; ▪ The site should be supervised by experienced and qualified personnel; ▪ Allocate sufficient time for the project (be aware that decreasing the construction time has the potential to increase the risk of initiating a peat movement); ▪ Prevent undercutting of slopes and unsupported excavations; ▪ Maintain a managed robust drainage system; ▪ Prevent placement of loads/overburden on marginal ground; ▪ Set up, maintain and report findings from monitoring systems;		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
		- Ensure construction method statements are followed or where agreed modified/ developed; and, - Revise and amend the Geotechnical Risk Register as construction progresses.		
Air Quality/Dust				
MM58	EIAR Section 4 CEMP Section 3 EIAR Section 10	- Revise and amend the Geotechnical Risk Register as construction progresses. - Truck wheels will be washed to remove mud and dirt before leaving the site. - All plant and materials vehicles shall be stored in the dedicated compound area. - Areas of excavation will be kept to a minimum, and stockpiling will be minimised by coordinating excavation, spreading and compaction. - Construction traffic will be restricted to defined routes and a speed limit will be implemented. - Water misting or bowzers will operate on-site as required to mitigate dust in dry weather conditions. - The transport of soils or other material, which has significant potential to cause dust, will be undertaken in tarpaulin-covered vehicles where necessary. - The agreed haul route roads adjacent to the site will be regularly inspected for cleanliness and cleaned as necessary.		
MM59	EIAR Section 10	All construction machinery will be maintained in good operational order while on-site, minimising any emissions that are likely to arise.		
MM60	EIAR Section 10	In periods of extended dry weather, dust suppression may be necessary along haul roads and around the borrow pit area to ensure dust does not cause a nuisance. If necessary, water will be taken from stilling ponds in the site's drainage system and will be pumped into a bowser or water spreader to dampen down haul roads and site compounds to prevent the generation of dust. Silty or oily water will not be used for dust suppression, because this would transfer the pollutants to the haul roads and generate polluted runoff		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
		or more dust. Water bowser movements will be carefully monitored, as the application of too much water may lead to increased runoff.		
Noise				
MM61	EIAR Section 4 & 11	Equipment will be sensitively located, taking account of local topography and natural screening.		
MM62	EIAR Section 4 & 11	All construction work will be restricted to the specified working hours. Any construction work carried out outside of these hours shall be restricted to activities that will not generate noise of a level that may cause a nuisance.		
MM63	EIAR Section 4 & 11	Plant will be selected taking account of the characteristics of noise emissions from each item. All plant and machinery used on the site shall comply with E.U. and Irish legislation in relation to noise emissions. The timing of on- and off-site movements of plant near occupied properties will be controlled.		
MM64	EIAR Section 11	The contract documents will clearly specify that the Contractor undertaking the construction of the works will be obliged to adhere to the following noise abatement measures: - No plant used on site will be permitted to cause an on-going public nuisance due to noise. - The best means practicable, including proper maintenance of plant, will be employed to minimise the noise produced by on site operations. - All vehicles and mechanical plant will be fitted with effective exhaust silencers and maintained in good working order for the duration of the contract. - Compressors will be attenuated models fitted with properly lined and sealed acoustic covers which will be kept closed whenever the machines are in use and all ancillary pneumatic tools shall be fitted with suitable silencers.		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
		▪ Machinery that is used intermittently will be shut down or throttled back to a minimum during periods when not in use. ▪ Any plant, such as generators or pumps, which is required to operate near any sensitive receptors before 07:00hrs or after 19:00hrs will be surrounded by an acoustic enclosure or portable screen. ▪ Diesel generators will be enclosed in sound proofed containers to minimise the potential for noise impacts. ▪ Residents will be notified in advance of all blasting schedules. ▪ During the course of the construction programme, supervision of the works will include ensuring compliance with the limits detailed in Table 11.1 of the EIAR using methods outlined in British Standard BS 5228-1:2009+A1:2014 <i>Code of practice for noise and vibration control on construction and open sites – Noise</i>.		
MM65	EIAR Section 11	The following mitigation measures will be employed to control the impact of vibration during blasting activities: ▪ Trial blasts will be undertaken to obtain scaled distance analysis; ▪ Appropriate burden to avoid over or under confinement of the charge; ▪ Accurate setting out and drilling; ▪ Appropriate charging; ▪ Appropriate stemming with appropriate material such as sized gravel or stone chipping; ▪ Delay detonation to ensure small maximum instantaneous charges; ▪ Decked charges and in-hole delays; ▪ Blast monitoring to enable adjustment of subsequent charges; ▪ Good blast design to maximise efficiency and reduce vibration; ▪ Avoid using exposed detonating cord on the surface; and ▪ During the course of the construction programme, supervision of the works will include ensuring compliance with the limits detailed in Table 11-2.		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
MM66	EIAR Section 4, 10 & 11	All construction operations shall comply with guidelines set out in British Standard documents <i>'BS 5338: Code of Practice for Noise Control on Construction and Demolition Sites'</i> and <i>'BS5228: Part 1: 1997: Noise & Vibration Control on Construction and Open Sites'</i> .		
Cultural Heritage				
MM67	EIAR Section 13	Archaeological monitoring of ground works (to include roads, substation, turbine hardstands, bases and cable trenching) will be undertaken at the construction phase of the development.		
MM68	EIAR Section 13	DG085-005 Site of Megalithic Structure – The excavation of the grid connection route at this location should be archaeologically monitored during construction. This is in order to ensure that no damage takes place to any sub-surface archaeological features relating to the recorded monument that may be present beneath the surface of the road. A report on the monitoring will be undertaken and submitted to the relevant authorities on completion of the work.		
MM69	EIAR Section 13	40909424 Road Bridge - Archaeological monitoring of ground works during construction where they extend past the road bridge. A report on the results of the monitoring will be compiled and submitted to the relevant authorities on completion of the work.		
MM70	EIAR Section 13	40909423 Milestone - Archaeological monitoring of ground works during construction where they extend past the monument. A report on the results of the monitoring will be compiled and submitted to the relevant authorities on completion of the work.		
Traffic				
MM71	EIAR Section 14	All of the deliveries comprising abnormally large loads will be made outside the normal peak traffic periods to avoid disruption to work and school related traffic.		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
MM72	EIAR Section 14	A programme of deliveries will be submitted to Donegal County Council in advance of deliveries of turbine components to site.		
Operational Phase				
MM73	EIAR Section 4	The removal and disposal of wastewater from the site will be carried out by a fully permitted waste collector holding valid Waste Collection Permits as issued under the Waste Management (Collection Permit) Regulations, 2007. Information on the appointed permitted contractor and evidence of a maintenance contract having been submitted to the Planning Authority prior to any construction works taking place.		

8 MONITORING PROPOSALS

All monitoring proposals relating to the pre-commencement, construction and operational phases of the Permitted Development were set out in various sections of the EIAR prepared as part of the planning permission application to An Bord Pleanála.

This section of the Construction and Environment Management Plan groups together all of the monitoring proposals presented in the EIAR. The monitoring proposals are presented in the following pages.

By presenting the monitoring proposals in the below format, it is intended to provide an easy to audit list that can be reviewed and reported on during the future phases of the project. The tabular format in which the below information is presented, can be further expanded upon during the course of future project phases to provide a reporting template for site compliance audits.

Table 8.1 Schedule of Monitoring Measures

Ref. No.	Reference	Survey/Monitoring Measure	Frequency	Reporting Measures	Responsibility
Pre-Commencement Phase					
MX1	ElAR Section 9	An inspection and maintenance plan for the on-site drainage system will be prepared in advance of commencement of any works.	On going	Monthly	ECOW
MX2	ElAR Section 9	Water sampling will be completed before, during and after the felling activity. The 'before' sampling should be conducted within 4 weeks of the felling activity, preferably in medium to high water flow conditions.	As Required	Monthly	Project Hydrologist
MX3	ElAR Section 13	Pre-construction archaeological testing of all turbine bases, hardstands, substation site, site compound, borrow pits and new roads will take place. A report on the archaeological testing will be submitted to the planning authority and the Department of Arts Heritage and the Gaeltacht.	Once	As required	Project Archaeologist
MX4	ElAR Section 7 Condition 16 CCS Section 10 Bird Monitoring Programme	Where construction works run into the subsequent breeding season following commencement, pre-construction bird surveys will be undertaken to confirm the absence of breeding Hen Harrier. If breeding activity is identified, the nest site will be located and no works shall be undertaken within a 500m buffer. No works within the buffer zone shall be permitted until it can be demonstrated that that Hen Harrier are no longer reliant on the nest site. Should pre-construction monitoring be required, the findings of these surveys will be incorporated into a report for submission to the planning authority before the end of the year in which surveys were completed.	As required	As required	Project Ornithologist
MX5	Condition 5 CCS Appendix 2	Vegetation sampling: A number of fixed relevé sites (i.e. permanent quadrats) will be set up in areas where active management is proposed of previously forested areas. Baseline data will be recorded prior to the commencement of habitat management activities set out in this outline plan. The character of each relevé will be recorded (e.g. species proportions present using Domin scale,	As required	As required	Project Ecologist

Ref. No.	Reference	Survey/Monitoring Measure	Frequency	Reporting Measures	Responsibility
		vegetation structure) and photographs will be taken of each relevé from a fixed point.			
MX6	Condition 5 CCS Appendix 2	Hydrological monitoring: Water levels within areas where drains are blocked will be recorded quarterly for two years. A number of phreatic stand pipes will be installed (prior to restoration) to allow monitoring of water levels within the restoration area and outside the restoration area in. In this way, any positive impacts on the local hydrology can be verified and quantified.	Prior to commencement	As required	Project Ecologist
MX7	Condition 15 CCS	Plant Species: Surveys for Irish Ladies tresses can only be conducted between early August and early September (NRA 2009). Surveys for Globeflower can be conducted between June and August. Surveys will only be required where works traverse potential suitable habitat as identified in Figure 3.4 of the EIAR. Works can proceed outside the identified areas.	Prior to commencement	As required	Project Ecologist
MX8	EIAR Section 6 Condition 15 CCS	Otter A pre-construction otter survey will be undertaken to identify evidence of otter within the works areas associated with the development	Prior to commencement	As required	Project Ecologist
Construction Phase					
MX9	EIAR Section 9	Daily monitoring of excavations by a suitably qualified person will occur during the construction phase. If high levels of seepage inflow occur, excavation work should immediately be stopped and a geotechnical assessment undertaken.	Daily	As required	ECoW
MX10	CEMP Section 3	Haul route will be condition monitored and maintained if necessary.	As required	As required	ECoW
MX11	EIAR Section 4	A system of peat monitoring will be implemented under the supervision of the project geotechnical engineer. This will include movement monitoring posts the findings of which will be reviewed by the geotechnical engineer.	Monthly or more frequently as required by construction programme	Monthly	Project Geotechnical Engineer

Ref. No.	Reference	Survey/Monitoring Measure	Frequency	Reporting Measures	Responsibility
MX12	EIAR Section 4	Check dams will be inspected and maintained regularly to insure adequate performance. Maintenance checks will also ensure the centre elevation of the dam remains lower than the sides of the dam.	As Required	As Necessary	ECOW
MX13	EIAR Section 4	Piped slope drains will be inspected weekly and following rainfall events. Inlet and outlets will be checked for sediment accumulation and blockages. Stake anchors or fill over the pipe will be checked for settlement, cracking and stability. Any seepage holes where pipe emerges from drain at the top of the pipe will be repaired promptly.	Weekly	As Necessary	ECOW
MX14	EIAR Section 4	Inspection and maintenance of all stilling ponds will be ongoing through the construction period. A water level indicator such as a staff gauge will be installed in each stilling pond with marks to identify when sediment is at 10% of the settlement pond capacity. Sediment will be cleaned out of the still pond when it exceeds 10% of pond capacity.	As Required	As Necessary	ECOW
MX15	EIAR Section 4	All culverts will be inspected regularly to ensure they are not blocked by debris, vegetation or any other material that may impede conveyance.	Weekly / Monthly	As Necessary	ECOW
MX16	EIAR Section 4 CEMP Section 3	The effectiveness of drainage measures designed to minimise runoff entering works areas and capture and treat silt-laden water from the works areas, will be monitored continuously by the ECoW or supervising hydrologist on-site. The ECoW or supervising hydrologist will respond to changing weather, ground or drainage conditions on the ground as the project proceeds, to ensure the effectiveness of the drainage design is maintained in so far as is possible. This may require the installation of additional check dams, interceptor drains or swales as deemed necessary on-site.	As Required	As Necessary	ECoW / Project Hydrologist

Ref. No.	Reference	Survey/Monitoring Measure	Frequency	Reporting Measures	Responsibility
MX17	EIAR Section 8, 9 CEMP Section 3	The plant used should be regularly inspected for leaks and fitness for purpose.	Daily	As Necessary	Plant Operators / ECoW
MX18	EIAR Section 9	Drains and silt traps will be maintained throughout all felling works, ensuring that they are clear of sediment build-up and are not severely eroded. Correct drain alignment, spacing and depth will ensure that erosion and sediment build-up are minimised and controlled.	Weekly/ Monthly	As Necessary	ECoW
MX19	EIAR Section 9	Regular inspections of all installed drainage systems will be undertaken, especially after heavy rainfall, to check for blockages, and ensure there is no build-up of standing water in parts of the systems where it is not intended. Inspections will also be undertaken after tree felling.	Weekly Monthly	As Necessary	ECoW
MX20	EIAR Section 9	During the construction phase field testing and laboratory analysis of a range of parameters with relevant regulatory limits and EQSs should be undertaken for each primary watercourse, and specifically following heavy rainfall events (i.e. weekly, monthly and event based).	Weekly, monthly & event based	As Necessary	ECoW / Project Hydrologist
MX21	EIAR Section 9	Sampling will be completed before, during and after the felling activity. The “during” sampling will be undertaken once a week or after rainfall events. The ‘after’ sampling should comprise as many samplings as necessary to demonstrate that water quality has returned to pre-activity status (i.e. where an impact has been shown).	As Required	Monthly	ECoW / Project Hydrologist
MX22	EIAR Section 5 CEMP Section 3	Training and supervision of drivers to ensure smooth machinery operation/driving, and to minimise unnecessary noise generation.	As Required	As Necessary	ECoW

Ref. No.	Reference	Survey/Monitoring Measure	Frequency	Reporting Measures	Responsibility
MX23	CEMP Section 3	Daily inspection of construction sites to examine dust measures and their effectiveness.	Daily	As Necessary	ECOW
MX24	ELAR Section 13	Archaeological monitoring of ground works during construction.	As Required	As Required	Project Archaeologist
MX25	ELAR Section 6	A detailed habitat enhancement management plan (HEMP) will be prepared for all areas that are subject to restoration. Ongoing monitoring to assess the effectiveness of the measures proposed and employed during habitat replacement. The monitoring measures will include vegetation sampling and hydrological monitoring.	As Required	Years 1, 2, 3, 5, 10, 15 and 25 following commencement of the plan.	Project Ecologist

Operational Phase

MX26	ELAR Section 7	To take account of both short-term and long-term effects on bird populations, post-construction monitoring should be conducted during the bird breeding season in years 1, 2, 3, 4, 5, 10 and 15 of the life of a wind farm. Ideally, post-construction monitoring will include ongoing breeding bird/activity surveys and a programme of regular corpse searching (at least as regularly as once per month) at the wind turbine sites in the same years to find the corpses of birds and bats that may be struck by the operating turbines.	Years 1, 2, 3, 4, 5, 10 and 15 for the period April - July	Annually at the end of years where surveys are completed	Project Ecologist
MX27	Condition 16 CCS Section 10 Bird Monitoring Programme	Hen harrier will be monitored in years 1,2,3,5,10 and 15 of wind farm operation by means of Vantage Point (VP) surveys	Years 1, 2, 3, 4, 5, 10 and 15 for the period April - July	Annually at the end of years where surveys are completed	Project Ecologist
MX28	Condition 16	Breeding raptor surveys in the breeding season (mid-March/April-July) and hen harrier roost surveys in the winter season.	Years 1, 2, 3, 4, 5, 10 and 15 for	Annually at the end of	Project Ecologist

Ref. No.	Reference	Survey/Monitoring Measure	Frequency	Reporting Measures	Responsibility
	CCS Section 10 Bird Monitoring Programme		the period April - July	years where surveys are completed	
MX29	EIAR Section 7	Hen Harrier Roost Surveys	Years 1, 2, 3, 4, 5, 10 and 15 for the period October – March	Annually at the end of years where surveys are completed	Project Ecologist
MX30	EIAR Section 7	Autumn Migration/Wintering Birds Survey	Years 1, 2, 3, 4, 5, 10 and 15 for the period September – March	Annually at the end of years where surveys are completed	Project Ecologist
MX31	EIAR Section 7	Corpse Searches (Bird Casualties) for birds that may potentially collide with operating turbines during the operational phase of the wind farm project will be implemented. Prior to the commencement of monthly surveys, a searcher efficiency test to allow monthly results to be calibrated according to the ability of the dog to detect carcasses and a carcass removal trial to assess the scavenger removal rate at the site will be undertaken. An annual report summarising the findings of the bird monitoring surveys at and in the vicinity of the permitted wind farm will be submitted to the Planning Authority following monitoring in years 1,2,3,5,10 and 15 of operation at the permitted wind farm	Monthly in years 1, 2, 3, 4, 5, 10 and 15 for the period	Annually at the end of years where surveys are completed	Project Ecologist
MX32	EIAR Section 9	Any excess build-up of silt levels at dams, the settlement pond, or any other drainage features that may decrease the effectiveness of the drainage feature, will be removed.	As Required	As Required	ECoW

Ref. No.	Reference	Survey/Monitoring Measure	Frequency	Reporting Measures	Responsibility
		This drainage infrastructure will remain in place until natural vegetation filters have regenerated.			
MX33	ELAR Section 11	Post commissioning operational noise monitoring is recommended to ensure compliance with the relevant planning noise condition.	As Required	As Required	Project Noise Consultant
MX34	Condition 5 CCS Appendix 2	The fixed relevees sites will then be re-examined during years 1, 2, 3, 5, 10, 15 and 25 following commencement of the plan in place in order to establish the extent of habitat improvement resulting from management practices. The finalised HEMP will contain the locations of the releves.	As required	As required	Project Ecologist
MX35	Condition 5 CCS Appendix 2	The efficacy of the habitat rehabilitation and enhancement measures employed will be reviewed in years 1, 2, 3, 5, 10, 15 and 25 following commencement of the plan on the basis of the results of vegetation sampling and water level readings from the managed areas. Analysis of the data collected will be the basis for a review of the measures and techniques employed. Should any adjustments to the plan will deemed necessary or advisable, these will be the subject of consultation with the NPWS prior to any alterations to the plan.	As required	As required	Project Ecologist
MX36	Condition 9 CCS Section 5	- Following commissioning of the permitted wind farm, a shadow flicker analysis will be produced using the as-built co-ordinates and the installed turbine technology on site. - If exceedances of the limits set by Condition no. 9 are predicted to occur, each of the potentially affected properties will be assessed to review orientation, landscaping and identify if there are any mitigating circumstances at the properties. Field investigations will also be carried out at the affected properties to allow the theoretical modelling of shadow flicker to be compared to actual occurrences. Field investigations will involve site visits which will be targeted at times when actual forecasted conditions required for shadow flicker are predicted.	As Required on completion of construction	As Required	ECoW

Ref. No.	Reference	Survey/Monitoring Measure	Frequency	Reporting Measures	Responsibility
		The timing and extent of field investigation and monitoring will be based on the findings of the Shadow Flicker Model and will be scheduled to coincide with the relevant periods of predicated shadow flicker occurrence. The field investigations will be based on a minimum of three site visits at each receptor and will be fully informed by weather conditions.			

9 PROGRAMME OF WORKS

The construction phase will take approximately 12-18 months to complete from starting on site to the commissioning of the electrical system and export of electricity from site.

The EIAR stipulated that in the interest of breeding birds, construction would not commence during the breeding bird season, which runs from April to July. The EIAR stipulated that construction may commence between August to the end of March, so that construction activities are ongoing by the time the next breeding bird season comes around and can continue throughout the next breeding season.

The phasing and scheduling main construction task items are outlined in Figure 8.1 below, where 1st February 2019 has been selected as an arbitrary start date for construction activities.

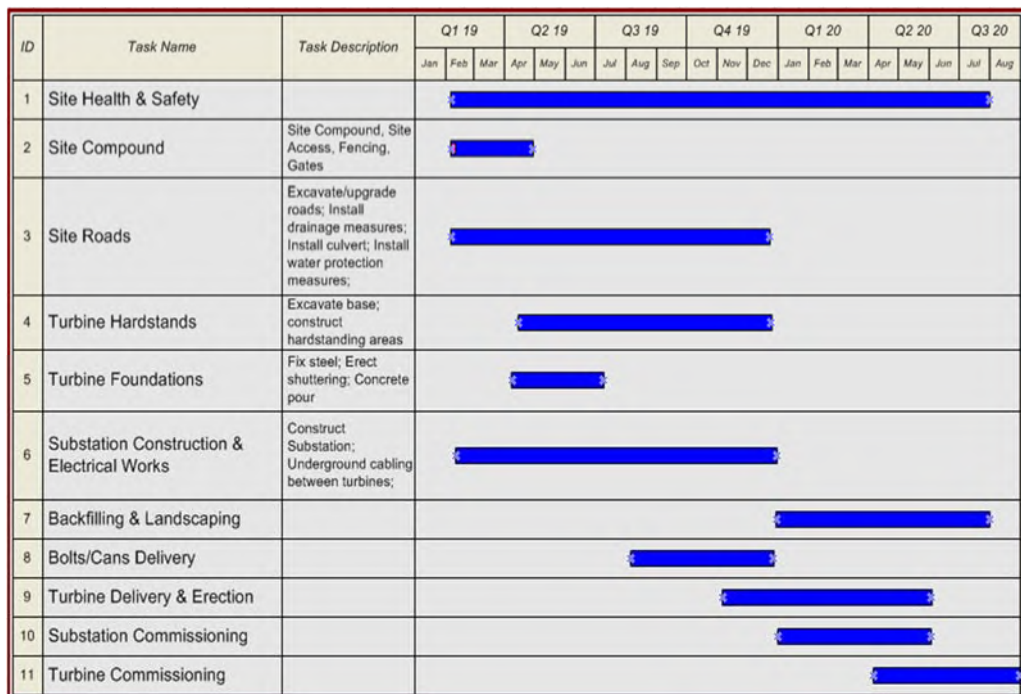


Figure 8.1 Indicative Construction Schedule

10 COMPLIANCE AND REVIEW

10.1 Site Inspections and Environmental Audits

Routine inspections of construction activities will be carried out on a daily and weekly basis by the ECoW and the Construction Manager to ensure all controls to prevent environmental impact, relevant to the construction activities taking place at the time, are in place.

Environmental inspections will ensure that the works are undertaken in compliance with this CEMP and all other planning application documents. Only suitably trained staff will undertake environmental site inspections.

10.2 Auditing

Environmental audits will be carried out during the construction phase of the project. In contrast to monitoring and inspection activities, audits are designed to shed light on the underlying causes of non-compliance, and not merely detect the non-compliance itself. In addition, audits are the main means by which system and performance improvement opportunities may be identified. Environmental audits will be carried out by contractor staff or alternatively by external personnel acting on their behalf. It is important that an impartial and objective approach is adopted. Environmental audits will be conducted at planned intervals to determine whether the CEMP is being properly implemented and maintained. The results of environmental audits will be provided to project management personnel.

10.3 Environmental Compliance

The following definitions shall apply in relation to the classification of Environmental Occurrences during construction of the wind farm:

Environmental Near Miss: An occurrence which if not controlled or due to its nature could lead to an Environmental Incident.

Environmental Incident: Any occurrence which has potential, due to its scale and nature, to migrate from source and have an environmental impact beyond the site boundary.

Environmental Exceedance Event: An environmental exceedance event occurs when monitoring results indicate that limits for a particular environmental parameter (as indicated in the Environmental Monitoring Programme) has been exceeded.

An exceedance will immediately trigger an investigation into the reason for the exceedance occurring and the application of suitable mitigation where necessary.

Exceedance events can be closed out on achieving a monitoring result below the assigned limit for a particular environmental parameter.

Environmental Non-Compliance: Non-fulfilment of a requirement and includes any deviations from established procedures, programs and other arrangements related to the EMP.

10.4 Corrective Action Procedure

A corrective action is implemented to rectify an environmental problem on-site. Corrective actions will be implemented by the Construction Manager, as advised by the Site ECoW. Corrective actions may be required as a result of the following;

- Environmental Audits;
- Environmental Inspections and Reviews;
- Environmental Monitoring;
- Environmental Incidents; and,
- Environmental Complaints.

A Corrective Action Notice will be used to communicate the details of the action required to the main contractor. A Corrective Action Notice is a form that describes the cause and effect of an environmental problem on site and the recommended corrective action that is required. The Corrective Action Notice, when completed, will include details of close out and follow up actions.

If an environmental problem occurs on site that requires immediate attention direct communications between the Construction Manager and the ECoW will be conducted. This in turn will be passed down to the site staff involved. A Corrective Action Notice will be completed at a later date.

10.5 Construction Phase Plan Review

This CEMP will be updated and reviewed prior to commencement of construction, and also every six months thereafter during the construction phase of the project.

Appendix 1

Site Layout Drawings

Project Design Drawing Notes
Drawings are for planning application purposes only.
2. Drawings are not to be used for construction.
3. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the written permission of McCarthy Keville O'Sullivan Ltd.
4. Drawings are the property of McCarthy Keville O'Sullivan Ltd. and should be taken off this drawing. All dimensions are in millimetres unless otherwise stated.
5. Drawings are for planning application purposes only and are not to be used for construction. Drawings are the property of McCarthy Keville O'Sullivan Ltd. and are not to be used for construction. Drawings are for planning application purposes only and are not to be used for construction. Drawings are the property of McCarthy Keville O'Sullivan Ltd. and are not to be used for construction.
6. This use of or reliance upon this drawing shall be deemed to be writing such written agreement to be sought from and sealed by the copyright holder to the use or reliance upon this drawing.
7. Drawings show typical turbine foot dimensions as per turbine drawing.
8. Final levels may vary depending on local ground conditions.
9. Internal electrical cable trench may be installed on either side of site roads.

Planning Application Site Boundary

Existing Road to be Upgraded

Existing Floating Road to be Upgraded

Proposed Road

Proposed Floating Road

Internal Electrical Cable Trench

Proposed Underground Grid Connection

Cabling Route

Directionally Drilled Cabling Route Section

Under NTS

Works Area

Soft Levelled Area

Crane Pad Handstanding Area

Turbine Foundation

Turbine Sweep Area

Borrow Pit

Proposed Amenity Track

Passing Bay

North Arrow

OS Licence No. A00201517 © Ordnance Survey Ireland/Government of Ireland

McCarthy Keville O'Sullivan Ltd.

Planning & Environmental Consultants

Block 1, Financial Services Centre,
Monaghan Road,
Galway, Ireland.
email: info@mcCarthyKevilleO'Sullivan.ie
Tel: +353 91 773611
Fax: +353 91 771279

McCarthy Keville O'Sullivan Ltd.

Planning & Environmental Consultants

Block 1, Financial Services Centre,
Monaghan Road,
Galway, Ireland.
email: info@mcCarthyKevilleO'Sullivan.ie
Tel: +353 91 773611
Fax: +353 91 771279

Site Layout (1:5,000)

Key Plan

McCarthy Keville O'Sullivan Ltd.

Planning & Environmental Consultants

Block 1, Financial Services Centre,
Monaghan Road,
Galway, Ireland.
email: info@mcCarthyKevilleO'Sullivan.ie
Tel: +353 91 773611
Fax: +353 91 771279

McCarthy Keville O'Sullivan Ltd.

Planning & Environmental Consultants

Block 1, Financial Services Centre,
Monaghan Road,
Galway, Ireland.
email: info@mcCarthyKevilleO'Sullivan.ie
Tel: +353 91 773611
Fax: +353 91 771279

McCarthy Keville O'Sullivan Ltd.

Planning & Environmental Consultants

Block 1, Financial Services Centre,
Monaghan Road,
Galway, Ireland.
email: info@mcCarthyKevilleO'Sullivan.ie
Tel: +353 91 773611
Fax: +353 91 771279

Project Design Drawing Notes
1. Drawings are for planning application purposes only.
2. Drawings are not to be used for construction.
3. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the express written permission of McCarthy Keville O'Sullivan Ltd.
4. No part of this drawing may be used for any other purpose without the express written permission of McCarthy Keville O'Sullivan Ltd.
5. All dimensions are in metres unless otherwise stated.
6. The use of or reliance upon this drawing shall be deemed to be the use of or reliance upon the drawing as it is and as it is written, such written agreement to be sought from and sealed by the copyright holder to the use or reliance upon this drawing.
7. Final levels may vary depending on local ground conditions.
8. Internal electrical cable trench may be installed on either side of site roads.
9. Final levels may vary depending on local ground conditions.
10. Final levels may vary depending on local ground conditions.

Drawing Legend

Planning Application Site Boundary	Existing Road to be Upgraded	Existing Footing Road to be Upgraded	Proposed Road	Proposed Footing Road	Internal Electrical Cable Trench	Proposed Underground Grid Connection Cabling Route	Discharge / Other Cabling Route Section Under NIS	River/Stream	River/Stream 50m Buffer	Lakes	Lakes 50m Buffer	Works Area	Soft Levelled Area	Crane Pad Handstanding Area	Turbine Foundation	Turbine Sweep Area	Borrow Pit	Cut	Fill	Passing Bay	Barn

Ordnance Survey Ireland Licence No. A70021817 © Ordnance Survey Ireland/Government of Ireland

N

Site Layout Plan
Sheet 1 of 3

PROJECT TITLE
Meerbog Wind Farm, Co. Donegal

DESIGNED BY
Joseph O'Brien


DRAWN BY
Michael Watson

PROJECT NO.
160502

DATE
14.12.2017

SCALE
1:5,000 @ A1

McCarthy Keville O'Sullivan Ltd.
Planning & Environmental Consultants
Block 1, Financial Services Centre,
Monaghan Road,
Galway, Ireland.
email: info@coarthyos.ie
tel: +353 91 735611
fax: +353 91 771279

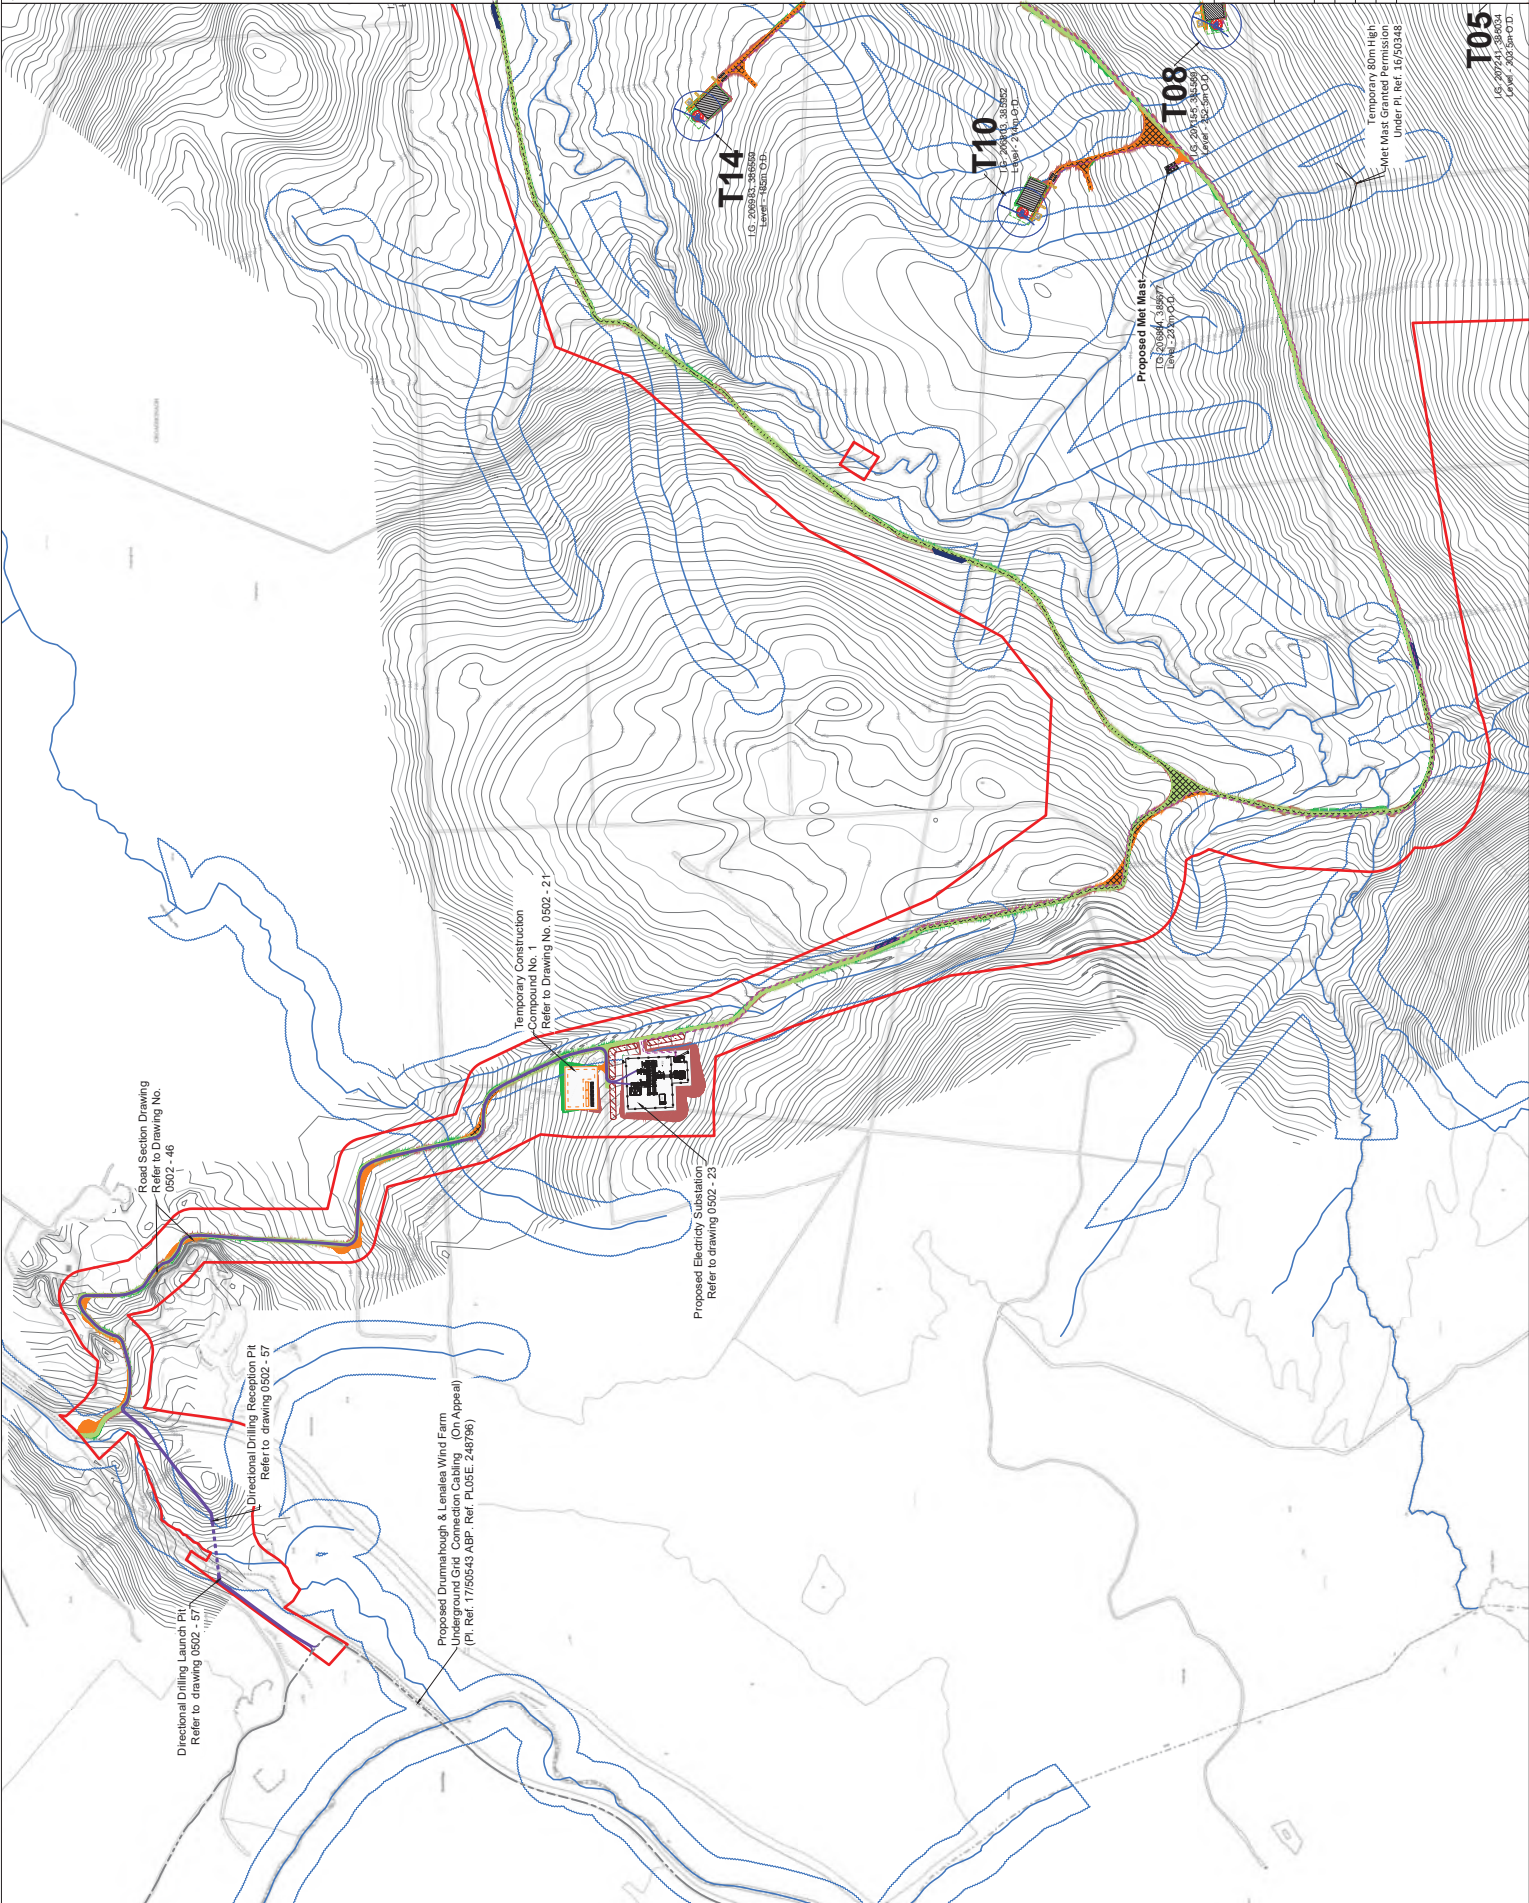

T05
Level 24m O.D.
Layer 25m O.D.



Project Design Drawings Notes

1. Drawings issued are for planning application purposes only.

2. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior written consent of McCarthy O'Sullivan Ltd.

3. The use of or reliance upon this drawing shall be deemed to be a warranty of the accuracy of the information contained herein and the drafter and are responsible for making and checking any and all dimensions and levels that relate to the works.

4. The use of or reliance upon this drawing shall be deemed to be a warranty of the accuracy of the information contained herein and the drafter and are responsible for making and checking any and all dimensions and levels that relate to the works.

5. The use of or reliance upon this drawing shall be deemed to be a warranty of the accuracy of the information contained herein and the drafter and are responsible for making and checking any and all dimensions and levels that relate to the works.

6. The use of or reliance upon this drawing shall be deemed to be a warranty of the accuracy of the information contained herein and the drafter and are responsible for making and checking any and all dimensions and levels that relate to the works.

7. The use of or reliance upon this drawing shall be deemed to be a warranty of the accuracy of the information contained herein and the drafter and are responsible for making and checking any and all dimensions and levels that relate to the works.

8. Final levels may vary depending on local ground conditions.

9. Internal electrical cables which may be installed on either side of the roads.

Drawing Legend

- Planning Application Site Boundary
- Existing Road to be Upgraded
- Existing Footing Road to be Upgraded
- Proposed Road
- Proposed Footing Road
- Internal Electrical Cable Trench
- River/Stream
- River/Stream 50m Buffer
- Lakes
- Lakes 50m Buffer
- Works Area
- Soft Levelled Area
- Crane Pad Handloading Area
- Turbine Foundation
- Turbine Sweep Area
- Borrow Pit
- Fill
- Cut
- Proposed Amenity Track



Ordnance Survey Ireland Licence No. AR0021817 © Ordnance Survey Ireland/Government of Ireland

**Site Layout Plan
Sheet 2 of 3**

DRAWN BY Joseph O'Brien		CHECKED BY Michael Watson	
PROJECT TITLE Meenbog Wind Farm, Co. Donegal		DRAWING TITLE 0502 - 05	
SCALE 1:5,000 @ A1		DATE 13.12.2017	



McCarthy O'Sullivan
Planning & Environmental Consultants
Block 1,
Glenageary Business Centre,
Glenageary, Ireland.
email: info@mcCarthyOS.ie
Tel: +353 91 729611
Fax: +353 91 771279

McCarthy O'Sullivan
Planning & Environmental Consultants
Block 1,
Glenageary Business Centre,
Glenageary, Ireland.
email: info@mcCarthyOS.ie
Tel: +353 91 729611
Fax: +353 91 771279

T14
IG 206387, 346630
Level - 187m O.D.

T13
IG 206379, 346630
Level - 227m O.D.

T10
IG 206803, 385932
Level - 214m O.D.

T11
IG 206820, 385930
Level - 242.5m O.D.

T12
IG 207065, 380843
Level - 227m O.D.

T08
IG 207455, 386564
Level - 282.5m O.D.

T06
IG 207303, 386280
Level - 499m O.D.

T07
IG 206281, 385404
Level - 283.5m O.D.

Temporary 80m High
Met Mast Granted Permission
Under Pt. 10, 10/5/2018

Borrow Pit No. 1
Refer to Drawing No.0502 - 32

Borrow Pit No. 2
Refer to Drawing No.0502 - 33

- Project Design Drawings Notes**
1. Drawings issued are for planning application purposes only.
 2. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior written consent of the copyright owner McCarthy Centre, O'Sullivan Ltd.
 3. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior written consent of the copyright owner McCarthy Centre, O'Sullivan Ltd.
 4. The use of or reliance upon any drawing shall be deemed to be a copy of the drawing and shall be subject to the same conditions of use as the drawing from which it was derived.
 5. The use of or reliance upon any drawing shall be deemed to be a copy of the drawing and shall be subject to the same conditions of use as the drawing from which it was derived.
 6. The use of or reliance upon any drawing shall be deemed to be a copy of the drawing and shall be subject to the same conditions of use as the drawing from which it was derived.
 7. The use of or reliance upon any drawing shall be deemed to be a copy of the drawing and shall be subject to the same conditions of use as the drawing from which it was derived.
 8. Final levels may vary depending on local ground conditions.
 9. Internal electrical cable trench may be installed on either side of the roads.

Drawing Legend

- Planning Application Site Boundary
- Existing Road to be Upgraded
- Existing Flooding Road to be Upgraded
- Proposed Road
- Proposed Fencing Road
- Internal Electrical Cable Trench
- River/Stream
- River/Stream 50m Buffer
- Works Area
- Soft Levelled Area
- Crane Pad Handwashing Area
- Turbine Foundation
- Turbine Sweep Area
- Borrow Pit
- Cut
- Fill
- Proposed Armament Track




**Site Layout Plan
Sheet 4 of 7**

DRAWN BY		CHECKED BY	
Joseph O'Brien		Michael Watson	
PROJECT TITLE		DRAWING NO.	
Meenbog Wind Farm, Co. Donegal		0502 - 11	
SCALE		DATE	
1:2,500 @ A1		13.12.2017	



McCarthy O'Sullivan
Planning & Environmental Consultants
Block 1, Financial Services Centre,
Moynagh Road,
Galway, Ireland.
email: info@mcCarthyosullivan.ie
Tel: +353 91 736811
Fax: +353 91 717179

McCarthy O'Sullivan
Planning & Environmental Consultants
Block 1, Financial Services Centre,
Moynagh Road,
Galway, Ireland.
email: info@mcCarthyosullivan.ie
Tel: +353 91 736811
Fax: +353 91 717179

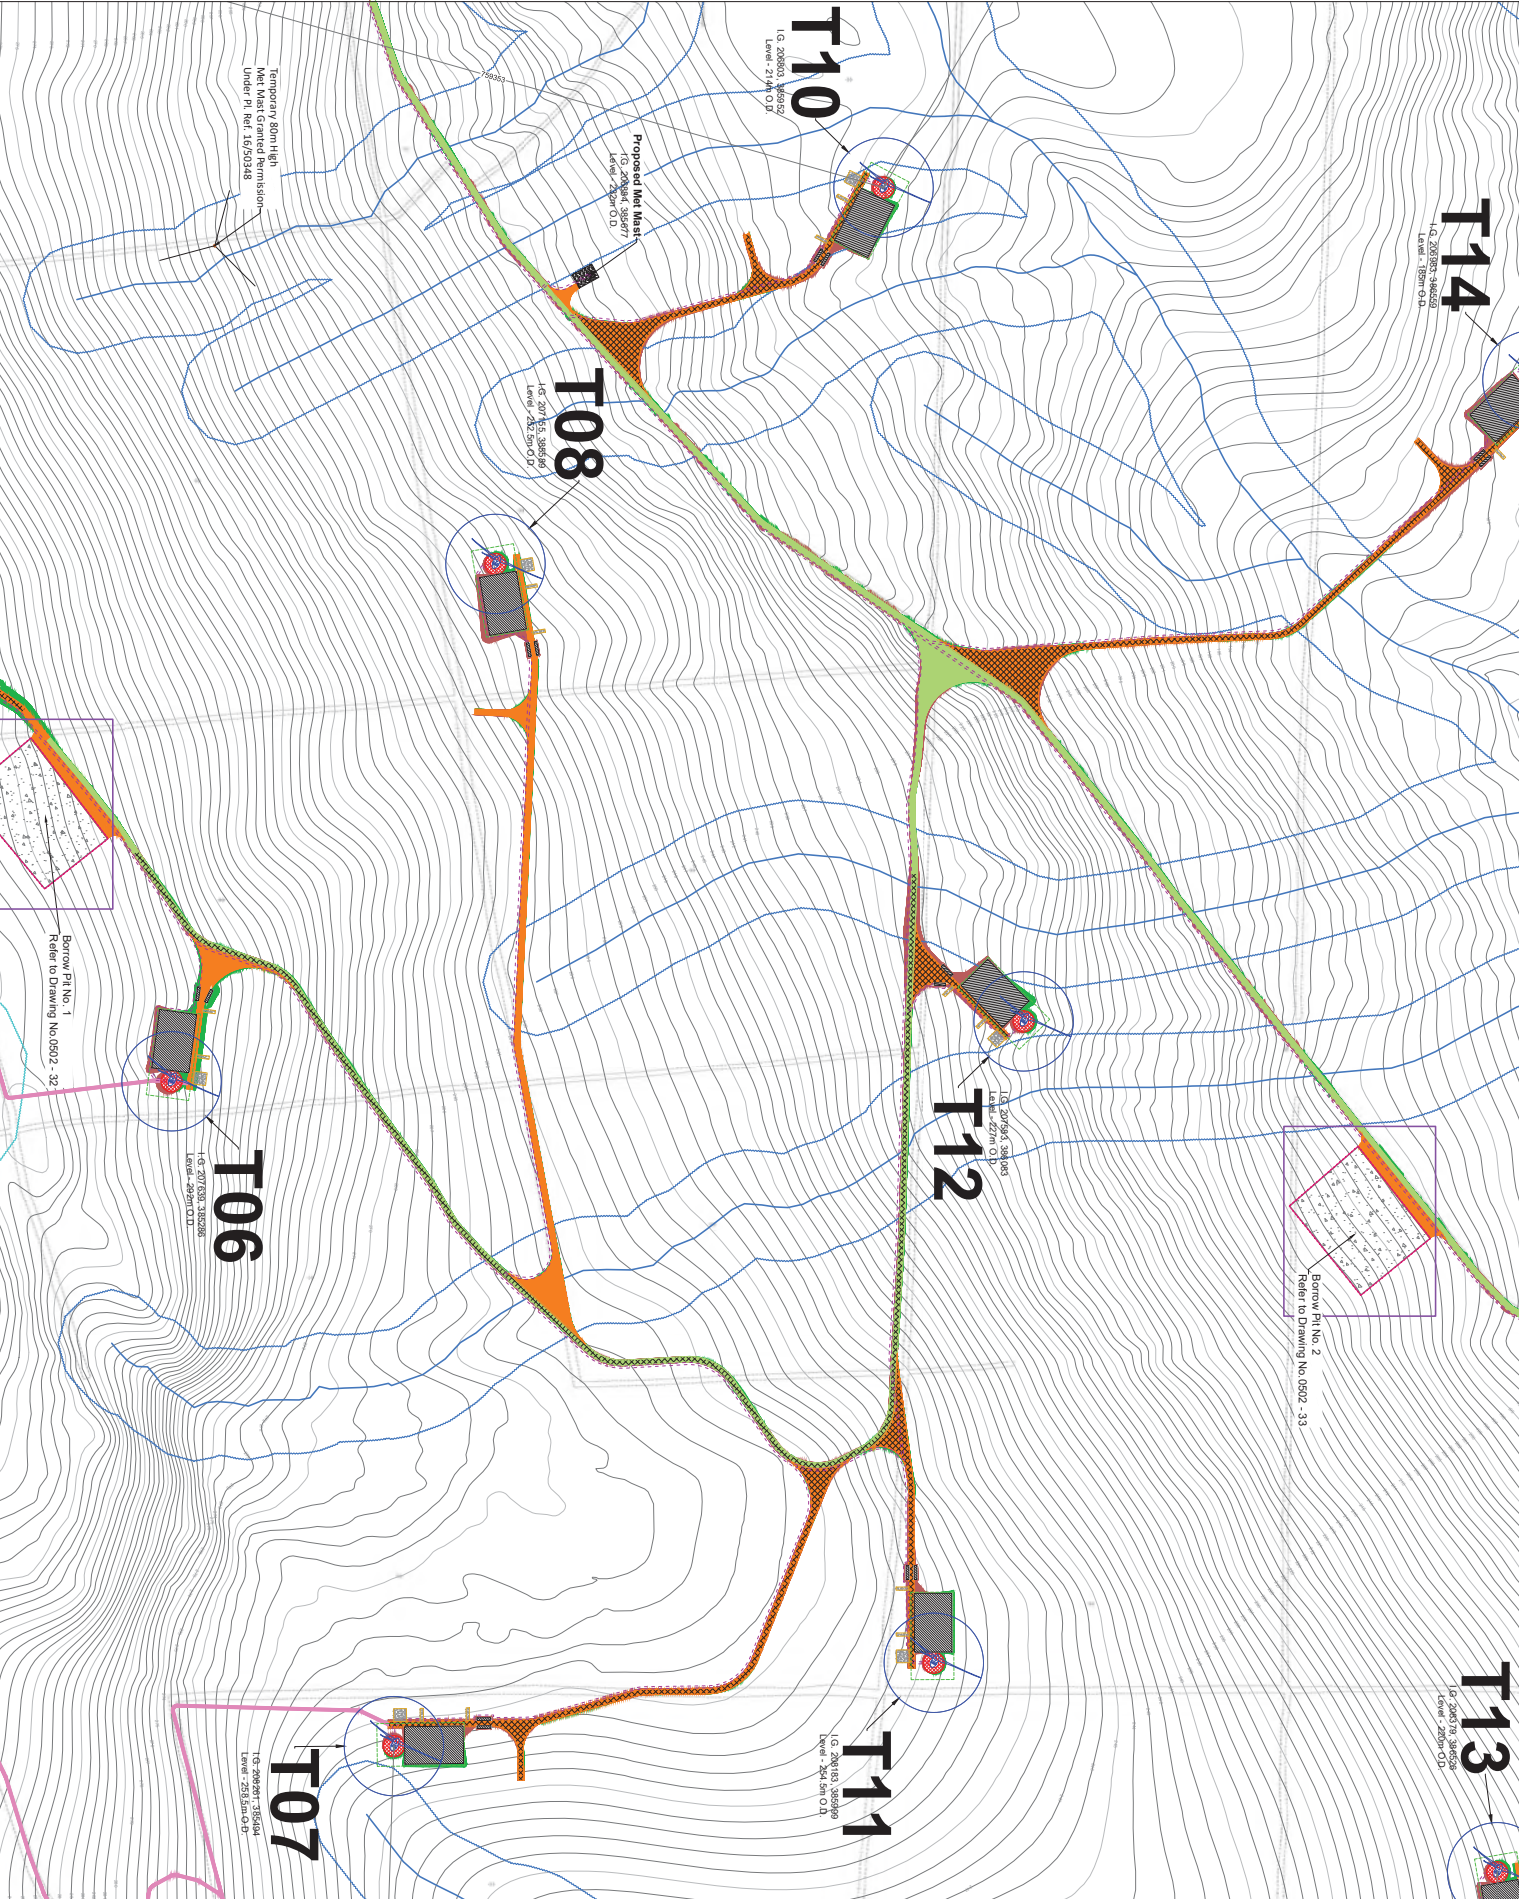

Project Design Drawing Notes

Drawing Legend

DRAWING TITLE:

Site Layout Plan

Sheet 5 of 7

PROJECT TITLE: Meenbog Wind Farm, Co. Donegal

DRAWING BY: Joseph O Brien	CHECKED BY: Michael Watson
PROJECT No.: 160502	DRAWING No.: 0502 - 12
SCALE: 1:2,500 @ A1	DATE: 12.12.2017


OS SHEET No.: 0387, 0398, 0399, 0403, 0401, 0423, 0424, 0425, 0426, 0427, 0450, 0451, 0452, 0453, 0454, 0478, 0479, 0480, 0481, 0482, 0506, 0507, 0508, 0509, 0535, 0536



McCarthy Keville O'Sullivan Ltd.
Planning & Environmental Consultants

Block 1,
 Galway Financial Services Centre,
 Mononeageisha Road,
 Galway, Ireland.

email: info@mccarthynos.ie
website: www.mccarthynos.ie
Tel: +353 91 735611
Fax: +353 91 771279

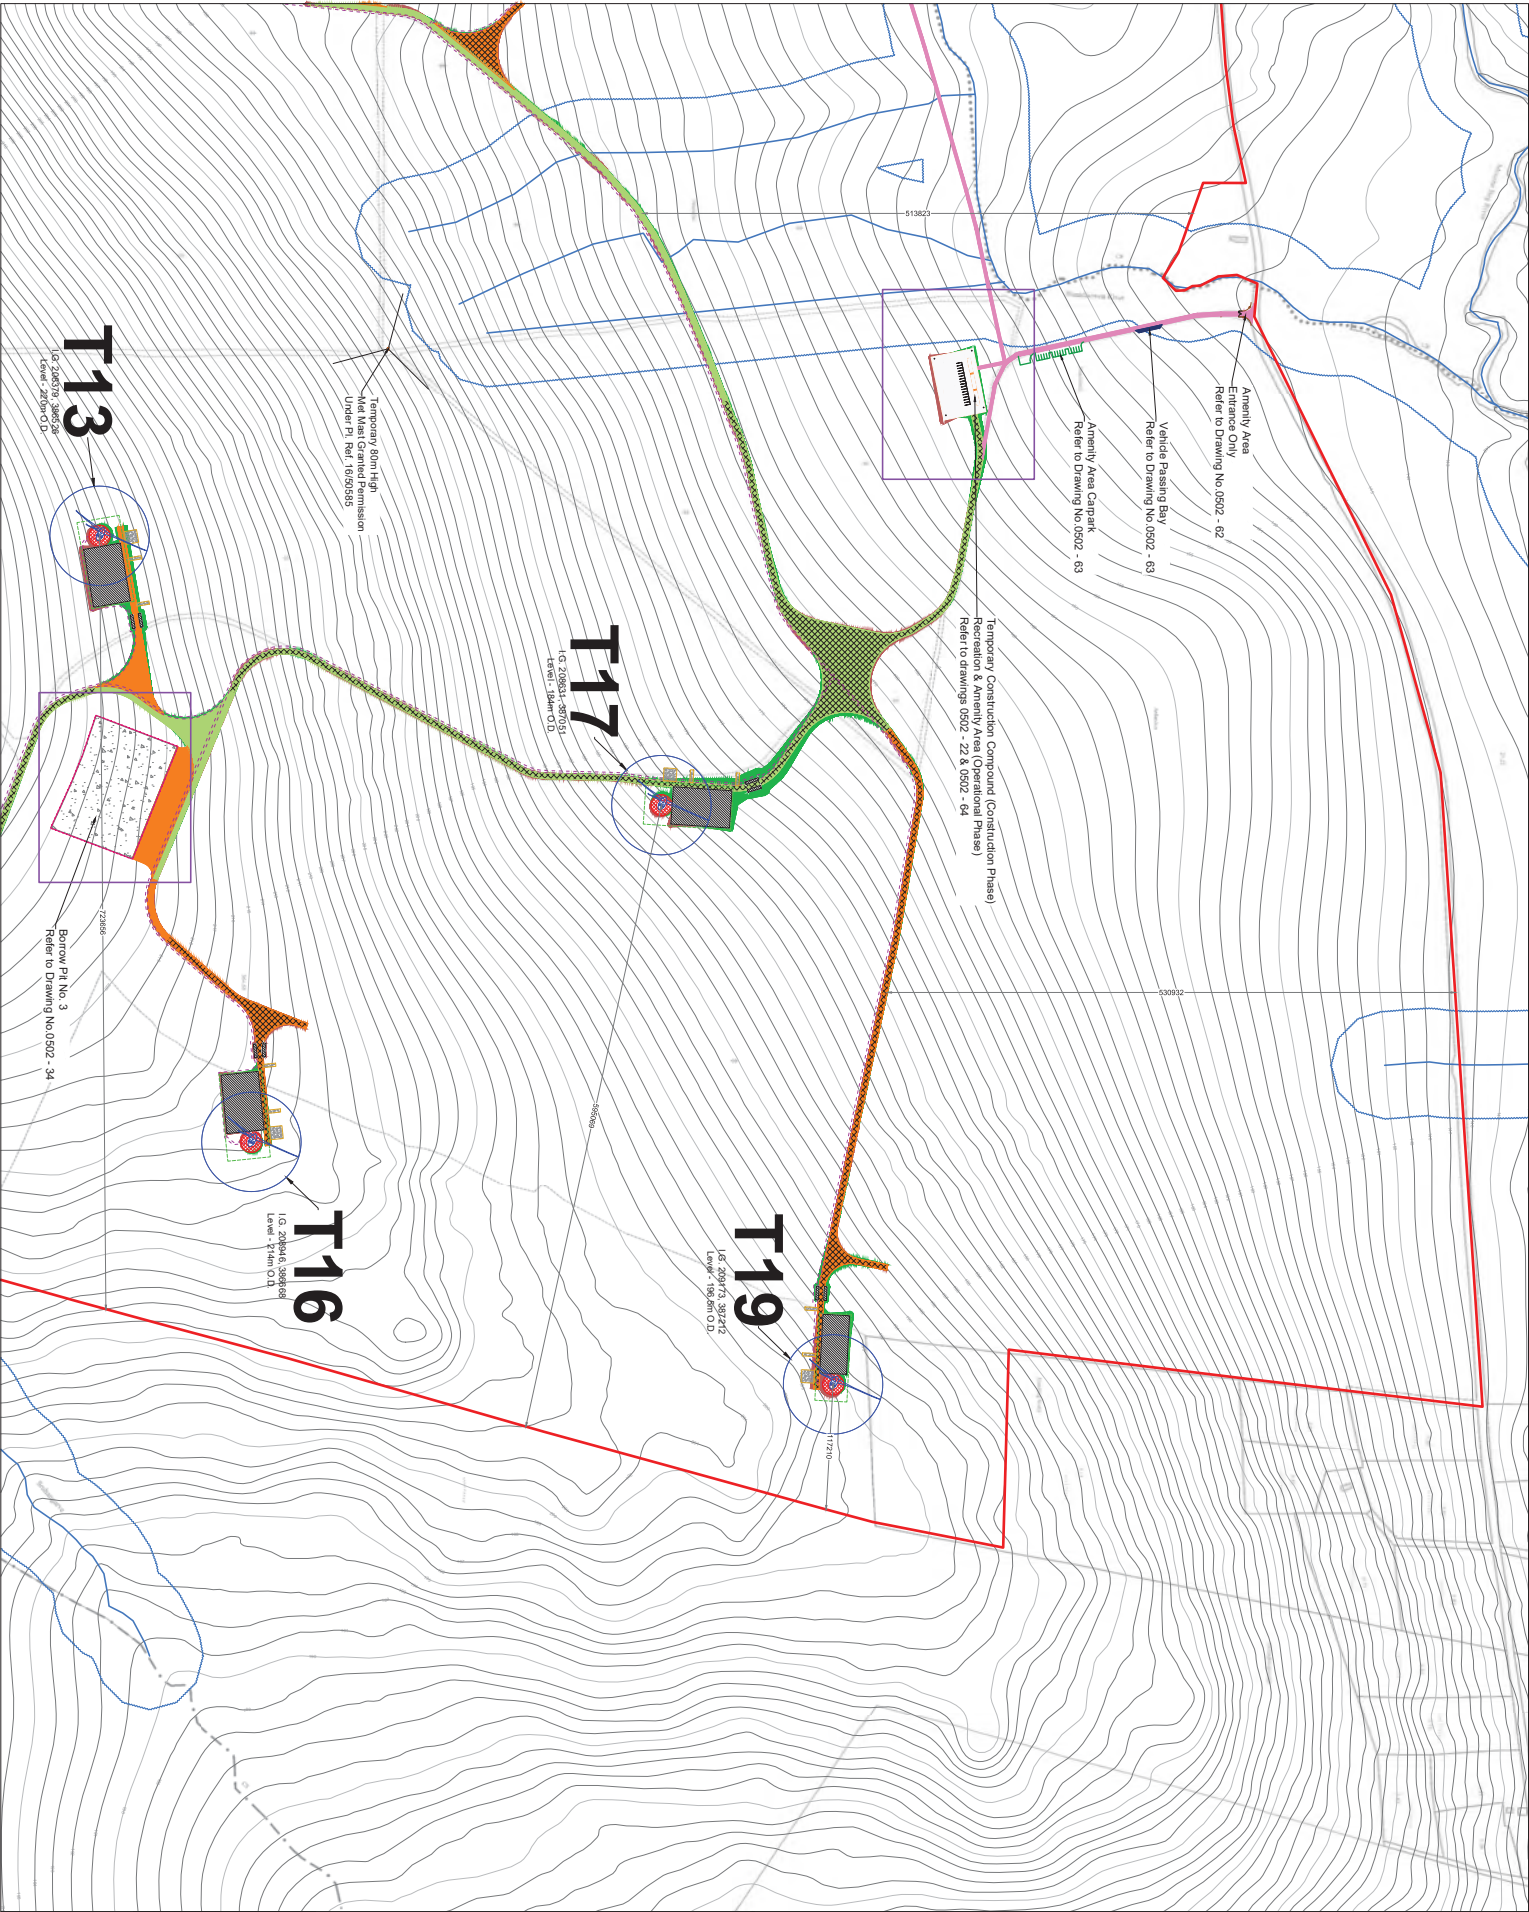

Project Design Drawings Notes

1. Drawings issued are for planning application purposes only.
2. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior written consent of McCarthy Keville O'Sullivan Ltd.
3. The use of reference upon this drawing shall be deemed to be the use of reference upon the original drawing. The use of reference upon this drawing shall be deemed to be the use of reference upon the original drawing. The use of reference upon this drawing shall be deemed to be the use of reference upon the original drawing.
4. The use of reference upon this drawing shall be deemed to be the use of reference upon the original drawing. The use of reference upon this drawing shall be deemed to be the use of reference upon the original drawing. The use of reference upon this drawing shall be deemed to be the use of reference upon the original drawing.
5. The use of reference upon this drawing shall be deemed to be the use of reference upon the original drawing. The use of reference upon this drawing shall be deemed to be the use of reference upon the original drawing. The use of reference upon this drawing shall be deemed to be the use of reference upon the original drawing.
6. The use of reference upon this drawing shall be deemed to be the use of reference upon the original drawing. The use of reference upon this drawing shall be deemed to be the use of reference upon the original drawing. The use of reference upon this drawing shall be deemed to be the use of reference upon the original drawing.
7. The use of reference upon this drawing shall be deemed to be the use of reference upon the original drawing. The use of reference upon this drawing shall be deemed to be the use of reference upon the original drawing. The use of reference upon this drawing shall be deemed to be the use of reference upon the original drawing.
8. Final levels may vary depending on local ground conditions.
9. Internal electrical cables which may be installed on either side of the roads.

Drawing Legend

- Planning Application Site Boundary
- Existing Road to be Upgraded
- Existing Feeder Road to be Upgraded
- Proposed Road
- Proposed Feeder Road
- Internal Electrical Cable Trench
- River/Stream
- River/Stream Gully Buffer
- Works Area
- Soft Levelled Area
- Crawler Pad Handwashing Area
- Turbine Foundation
- Turbine Swept Area
- Borrow Pit
- Cut
- Fill
- Proposed Amenity Track
- Passing Bay



Ordnance Survey Ireland Licence No. AR0021817 © Ordnance Survey Ireland/Government of Ireland

Site Layout Plan Sheet 6 of 7


PROJECT TITLE	MEENBOG WIND FARM, CO. DONEGAL
DRAWN BY	JOSEPH O'BRIEN
CHECKED BY	MICHAEL WATSON
PROJECT NO.	160502
DRAWING NO.	0502 - 13
SCALE	1:2,500 @ A1
DATE	13.12.2017



McCarthy Keville O'Sullivan Ltd.
Planning & Environmental Consultants
Block 1, Financial Services Centre,
Gateway, Ireland.
email: info@cmk-os.com
Tel: +353 91 739611
Fax: +353 91 771279

McCarthy Keville O'Sullivan
Planning & Environmental Consultants
Block 1, Financial Services Centre,
Gateway, Ireland.
email: info@cmk-os.com
Tel: +353 91 739611
Fax: +353 91 771279

Project Design Drawing Notes
1. Drawings are for planning application purposes only.
2. Drawings are not to be used for construction.
3. Copyright, all rights reserved. No part herewith may be copied or reproduced partially or wholly in any form whatsoever without the written consent of McCarthy O'Sullivan & Co. Ltd.
4. No part of this drawing is to be used for any other purpose without the written consent of McCarthy O'Sullivan & Co. Ltd.
5. All dimensions are in millimetres unless otherwise stated.
6. The use of or reliance upon this drawing shall be deemed to be a warranty by McCarthy O'Sullivan & Co. Ltd. in relation to the design and construction of the works shown hereon.
7. The use of or reliance upon this drawing shall be deemed to be a warranty by McCarthy O'Sullivan & Co. Ltd. in relation to the design and construction of the works shown hereon.
8. Final levels may vary depending on local ground conditions.
9. Internal electrical cable trench may be installed on either side of site roads.

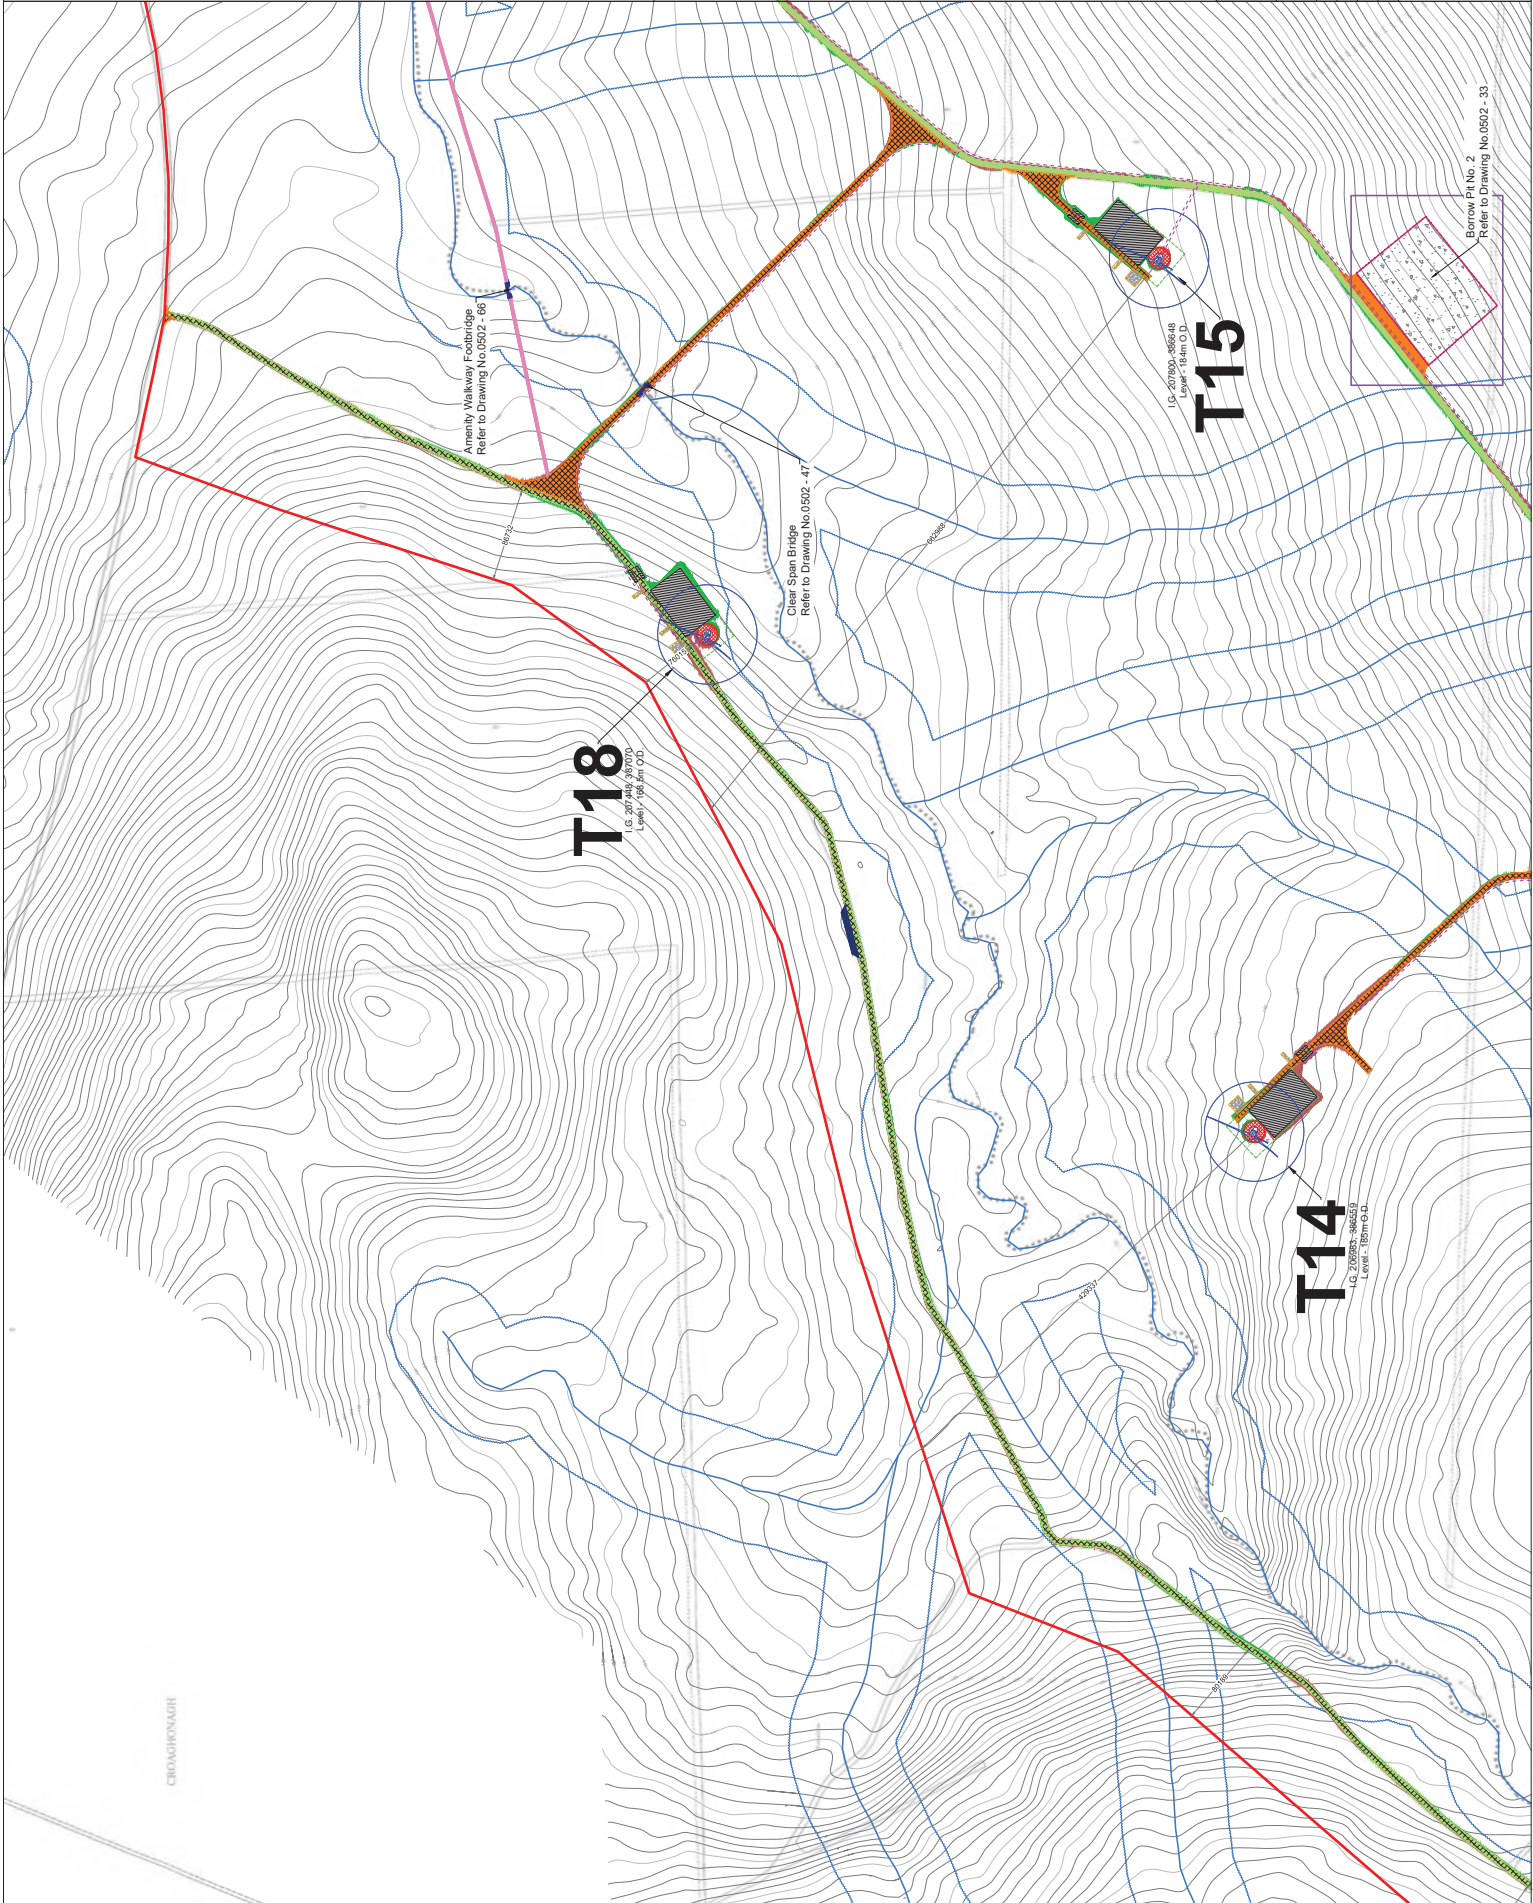

CROAGHONAGH

Drawing Legend

- Planning Application Site Boundary
- Existing Road to be Upgraded
- Proposed Road
- Proposed Floating Road
- Proposed Floating Road
- Internal Electrical Cable Trench
- River Stream
- River Stream 50m Buffer
- Works Area
- Soft Levelled Area
- Crane Pad Hardstanding Area
- Turbine Foundation
- Turbine Sweep Area
- Borrow Pit
- Cut
- Fill
- Passing Bay





Site Layout Plan
Sheet 7 of 7

McCarthy O'Sullivan & Co. Ltd.
Planning & Environmental Consultants
Block 1, Financial Services Centre,
Monaghan Road,
Galway, Ireland.
email: info@mcCarthyOSullivan.ie
Tel: +353 91 735611
Fax: +353 91 771279

McCarthy O'Sullivan & Co. Ltd.
Planning & Environmental Consultants
Block 1, Financial Services Centre,
Monaghan Road,
Galway, Ireland.
email: info@mcCarthyOSullivan.ie
Tel: +353 91 735611
Fax: +353 91 771279

McCarthy O'Sullivan & Co. Ltd.
Planning & Environmental Consultants
Block 1, Financial Services Centre,
Monaghan Road,
Galway, Ireland.
email: info@mcCarthyOSullivan.ie
Tel: +353 91 735611
Fax: +353 91 771279

Borrow Pit No. 2
Refer to Drawing No.0502 - 33


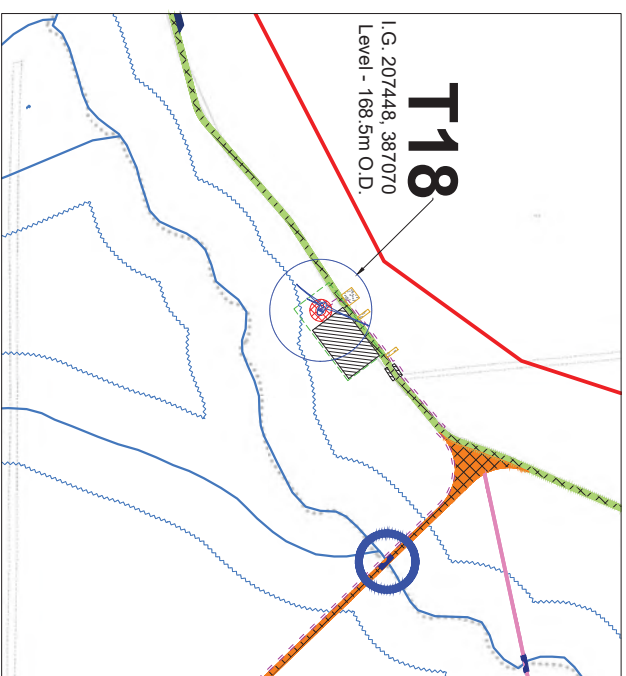
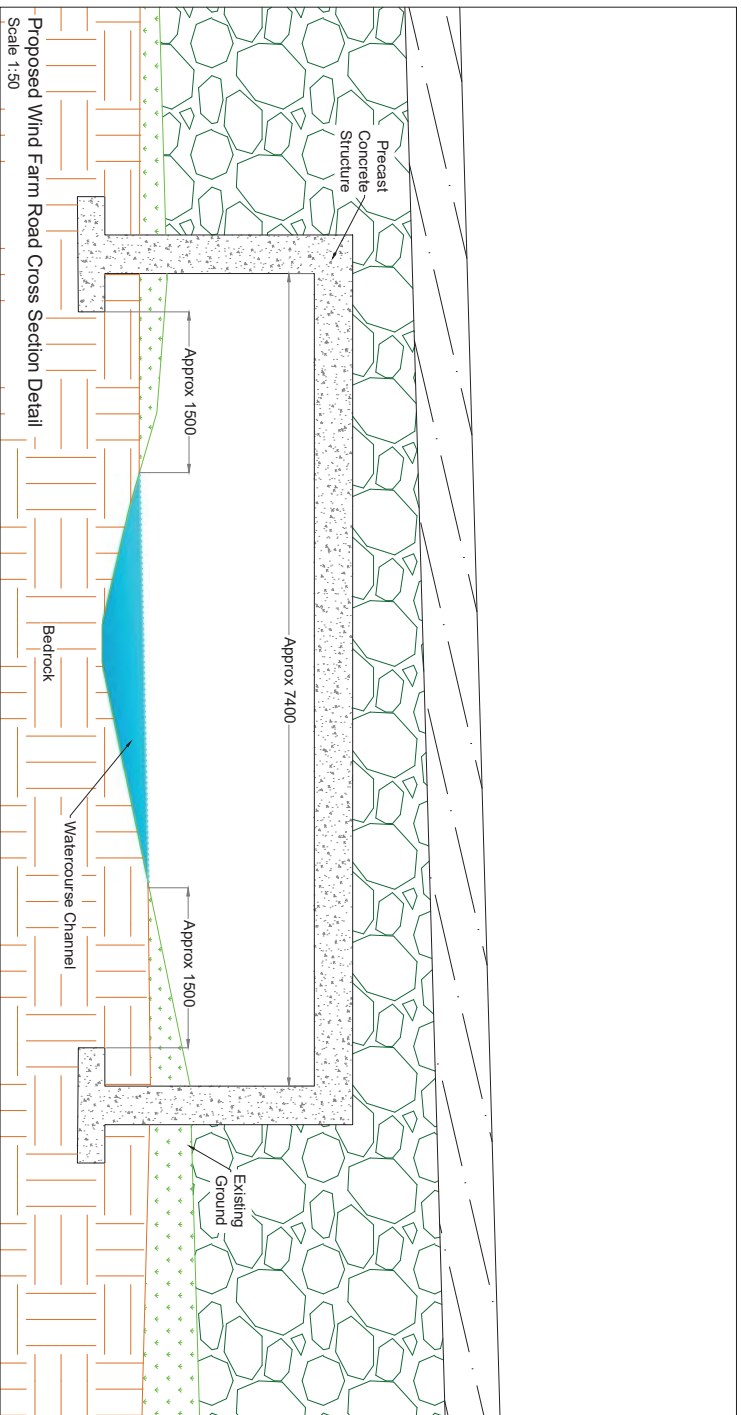


1:5,000 Location on Context Map





Ordnance Survey Ireland Licence No. AR0021817 © Ordnance Survey Ireland/Government of Ireland


[illegible]

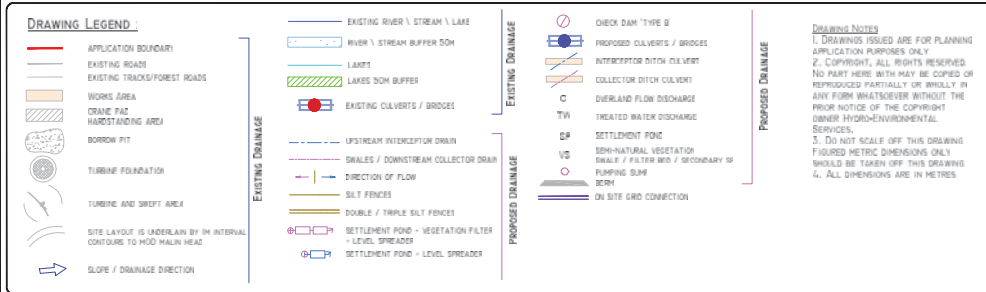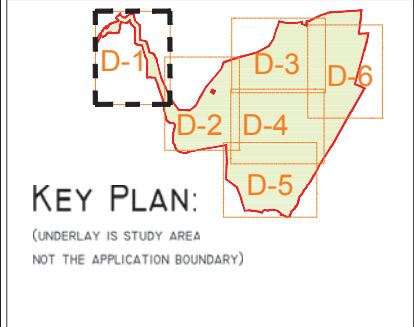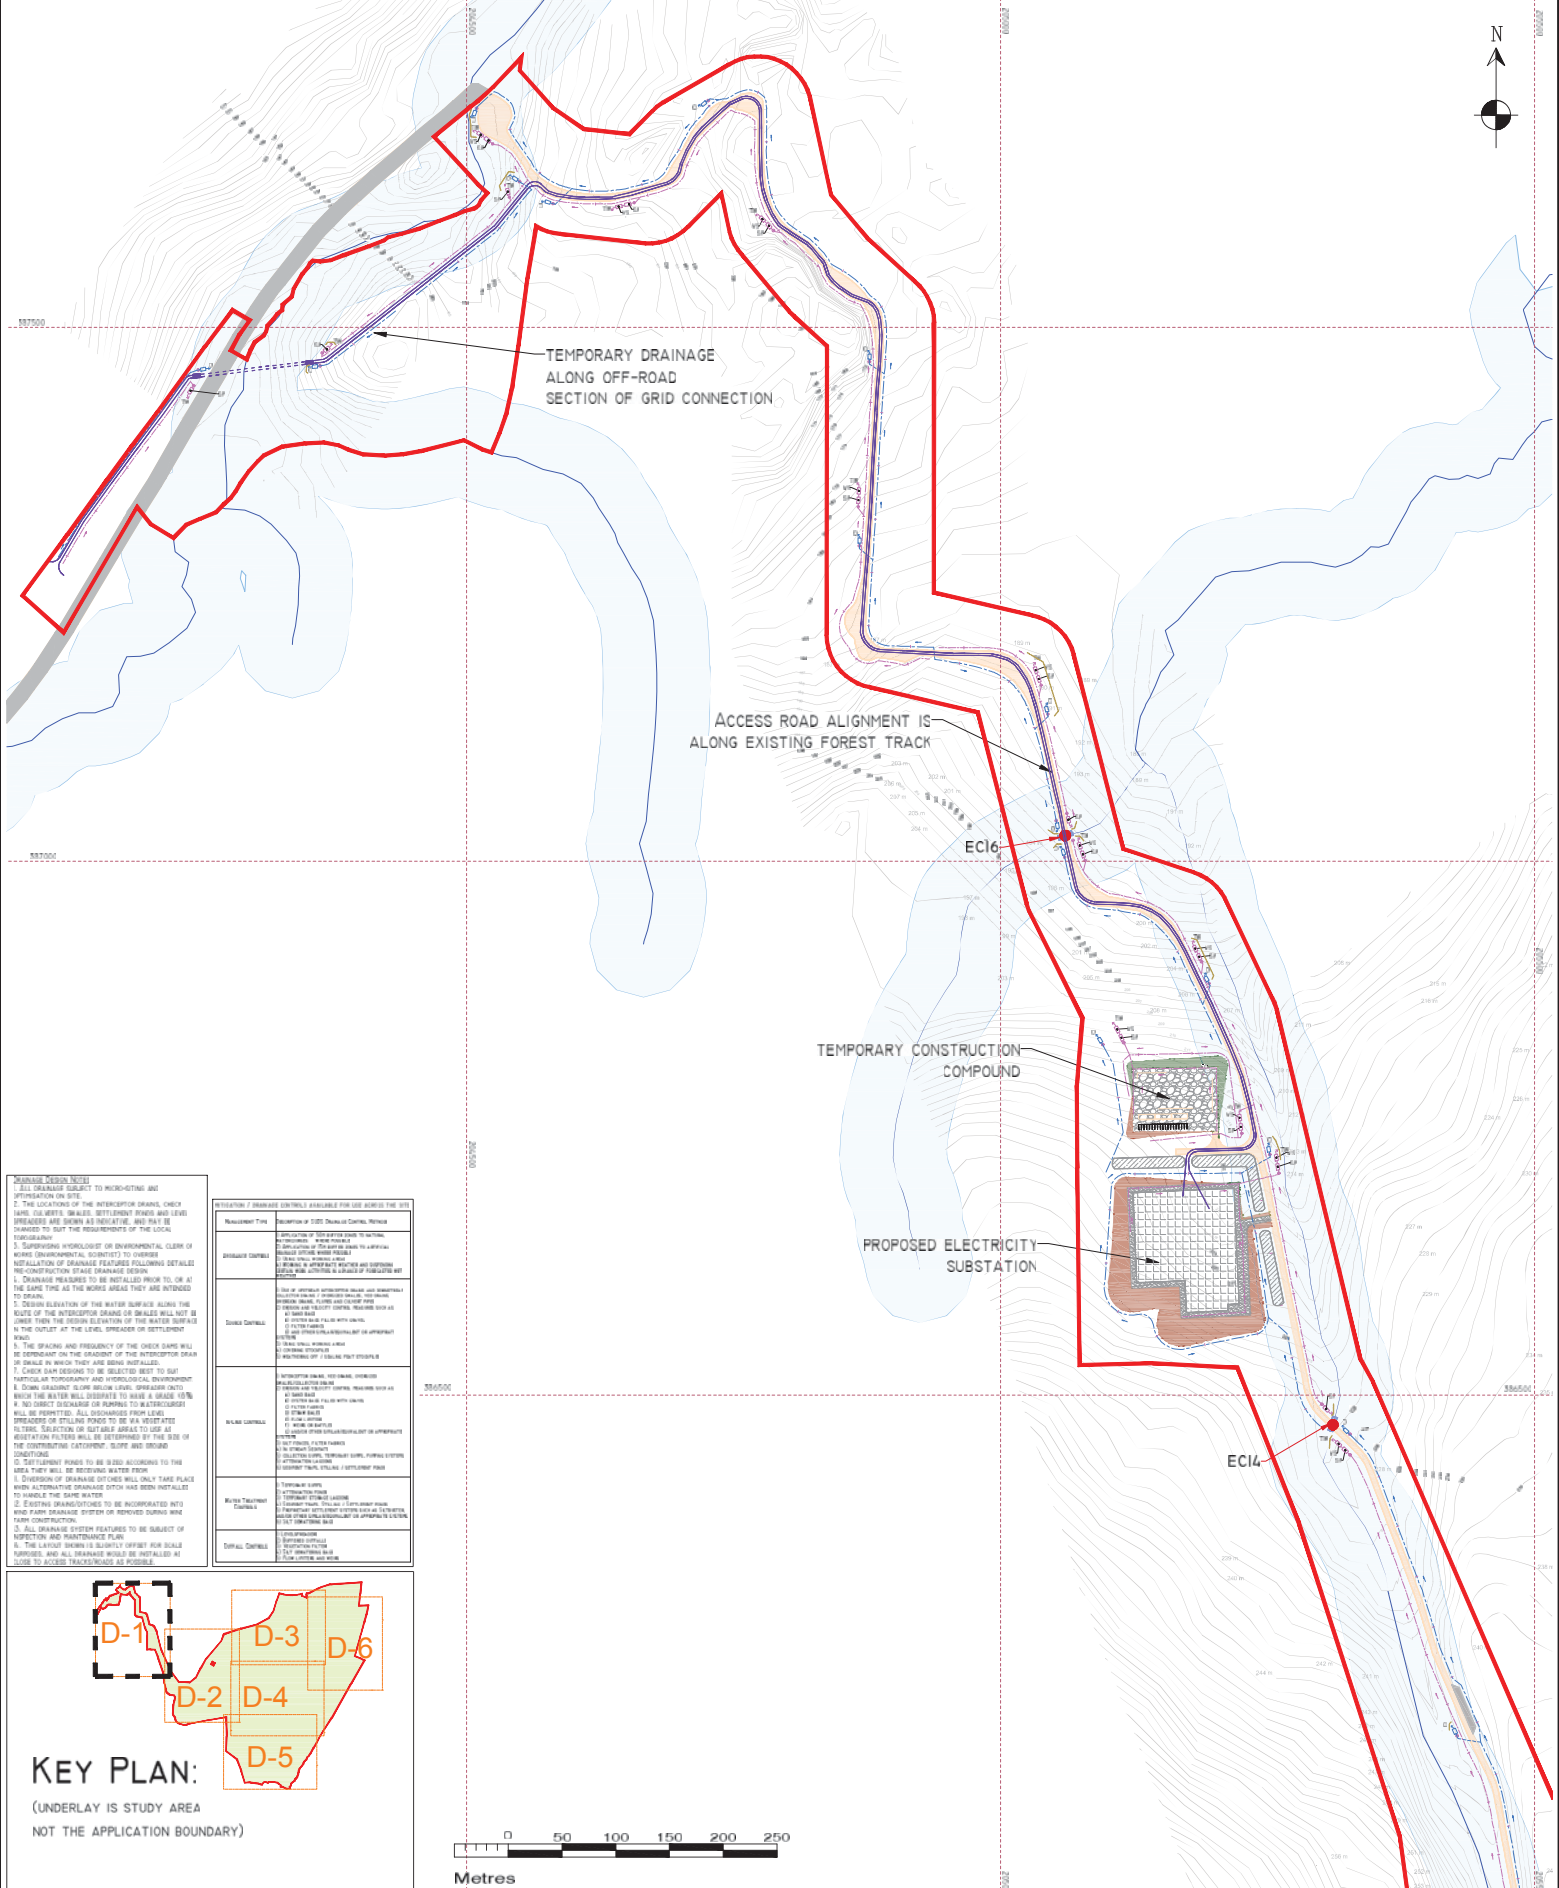

Ordnance Survey Ireland Licence No: EN 0044717 © Ordnance Survey Ireland/Government of Ireland				Client: MCCARTHY KEVILLE AND O'SULLIVAN	
				Job: MEENBOG WIND FARM, CO. DONEGAL	
13.12.17	Planning	MG	MG	Title: DRAINAGE LAYOUT SHEET 1 OF 6	
Date	Description	Chkd	Signed		
Revisions					
 HYDRO ENVIRONMENTAL SERVICES				Figure No: D101 (0502-15)	
Z Lower Irian St Dunganway Co. Waterford Ireland				Drawing No: P1249-2-1217-A1-D101(0502-15)-00A Sheet Size: A1 Scale: 1:2,500 (A1) Date: 13/12/2017 Drawn By: MG/GM Checked By: MG	

[illegible]

Scale: 1:2,500 (A1)	Drawn By: MG/GD
Date: 13/12/2017	Checked By: MG

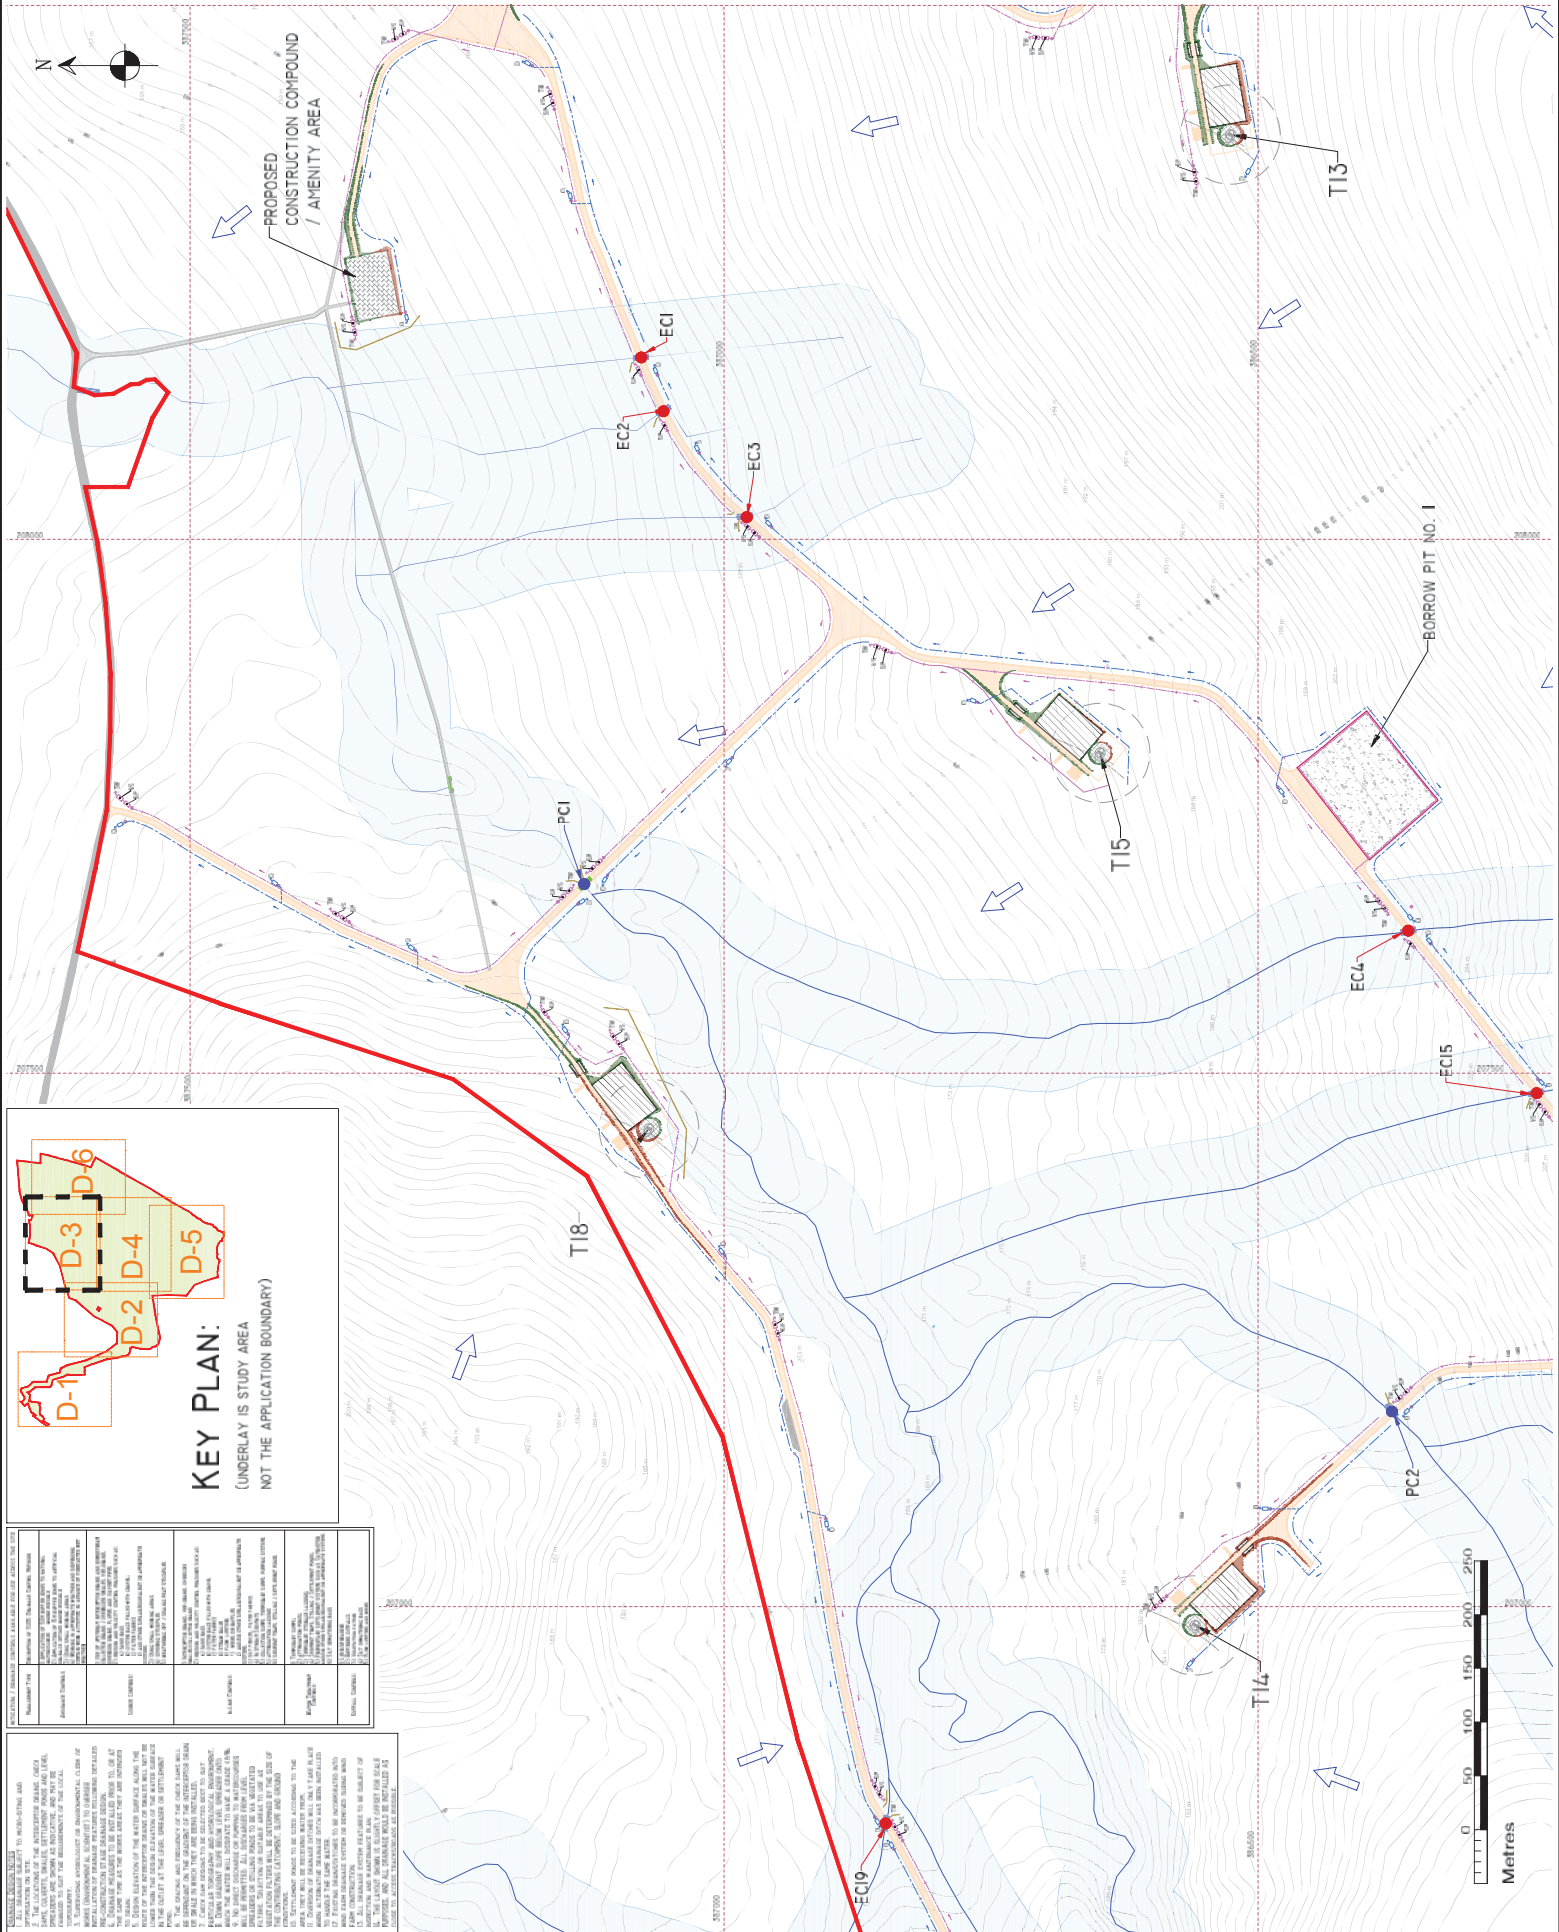[illegible][illegible]

DRAWING NOTES

1. DRAWINGS ISSUED ARE FOR PLANNING APPLICATION PURPOSES ONLY.
2. COPYRIGHT, ALL RIGHTS RESERVED. NO PART HERE WITH MAY BE COPIED OR REPRODUCED PARTIALLY OR WHOLLY IN ANY FORM WHATSOEVER WITHOUT THE PRIOR NOTICE OF THE COPYRIGHT OWNER HANSEN-ENVIRONMENTAL SERVICES.
3. DO NOT SCALE OFF THIS DRAWING. FINISHED METRIC DIMENSIONS ONLY SHOULD BE TAKEN OFF THIS DRAWING. ALL DIMENSIONS ARE IN METRES.

Date	Description	MG Checked	MG Signed
13.12.17	Planning		

Revisions

**HYDRO
ENVIRONMENTAL
SERVICES**

221 Lower Main St.
Dungeness
Co. W. Waford

tel. +353 (0) 59 441722
tel. +353 (0) 59 442444
email: info@hydroenviro.com.ie
www: www.hydroenviro.com.ie

Client: MCCARTHY KEVILLE AND O'SULLIVAN

Job:

Title:


SHEET 3 OF 6


Figure No: D103 (0502-17)

Drawing No: P1249-2-1217-A1-D103(0502-17)-00A

Sheet Size: A1	Project No.: P1247-Z
Scale: 1:2,500 (A1)	Drawn By: MG/GD

Date: 13/12/2017	Checked By: MG
------------------	----------------



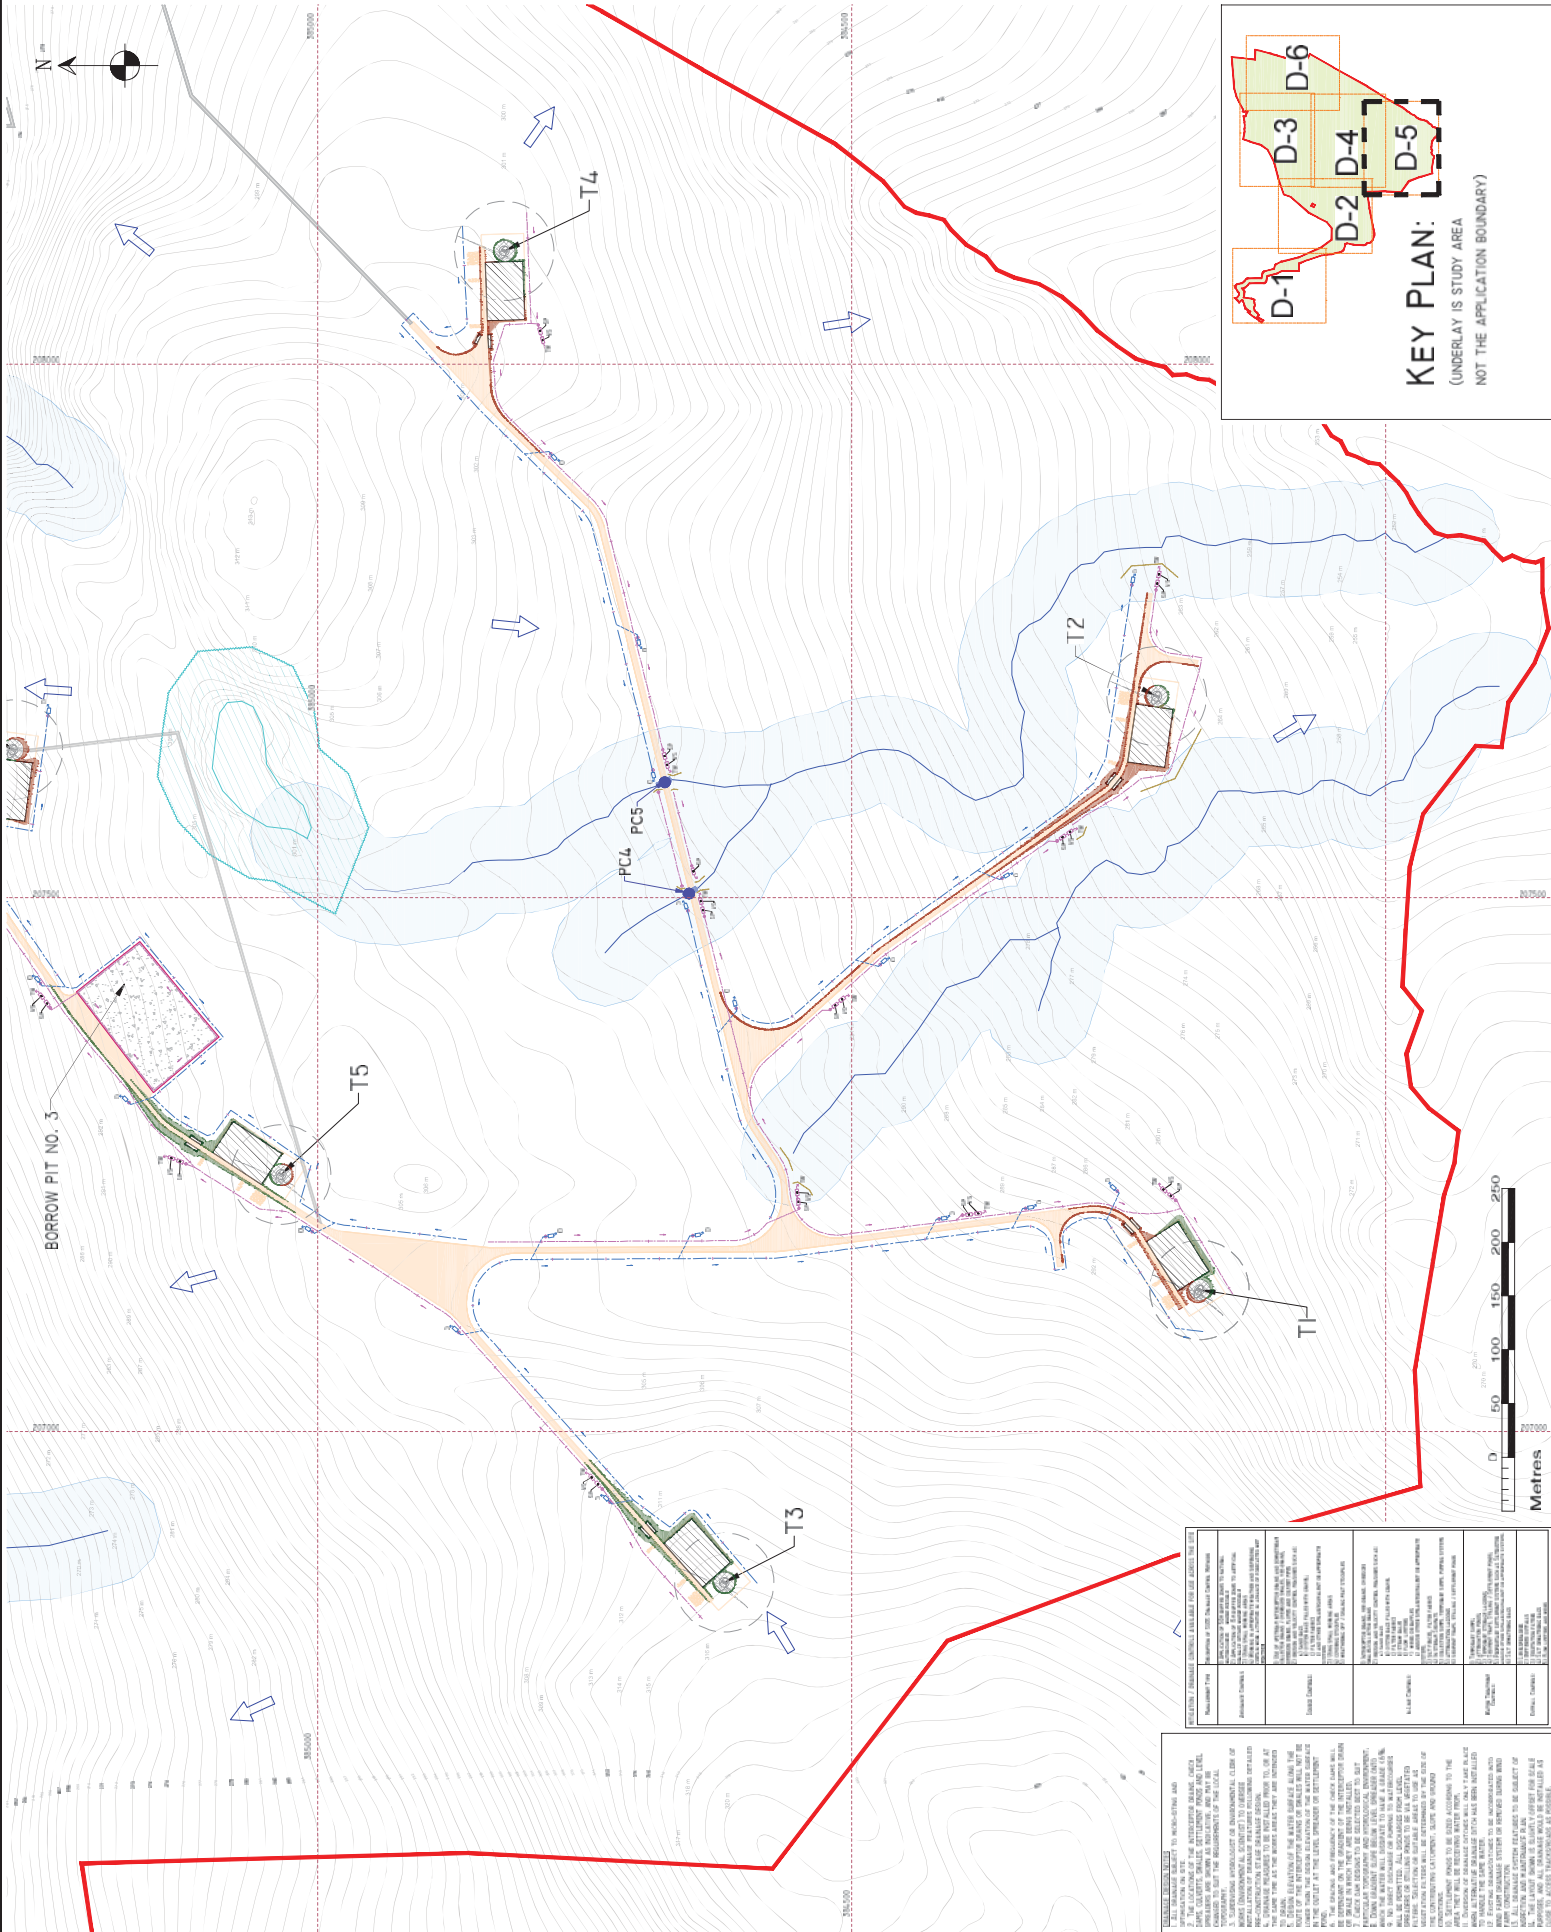
[illegible]

TRADE SHOW VISITS
 TRADE SHOW VISITS ARE FOR PLANNING APPLICATION PURPOSES ONLY.
 ALL RIGHTS RESERVED. NO PART HERE WITH MAY BE COPIED OR REPRODUCED PARTIALLY OR WHOLLY IN ANY FORM OR BY ANY MEANS, ELECTRONIC OR MECHANICAL, INCLUDING PHOTOCOPYING, RECORDING, OR BY ANY INFORMATION STORAGE AND RETRIEVAL SYSTEM, WITHOUT THE WRITTEN PERMISSION OF THE INTERNATIONAL ASSOCIATION OF BUSINESS DEVELOPERS.
 IT DOES NOT SCALE OFF THE DRAWING. FOLDED METRIC DIMENSIONS ONLY SHOULD BE TAKEN OFF THE DRAWING.

[illegible]


	HYDRO ENVIRONMENTAL SERVICES	
	27 Lower Main St. Dawson Co. Nelson BC V1C 1S1	
Tel: 250-333-0344 Fax: 250-333-0344 Email: info@hydroenv.com Web: www.hydroenv.com	McCARTHY KEVILLE AND O'SULLIVAN JOBS: MEENOGS WIND FARM, Co. DONEGAL Title: DRAINAGE LAYOUT SHEET 5 of 6	
Figure No: D105 (05/02-19)	Drawing No: P1249-2-1217-A-1-D105(05/02-19)00A Sheet Size: A1 Project No.: P1249-2 Drawn by: MCG/DG Date: 12/20/2017 Checked by: MCG	

[illegible]

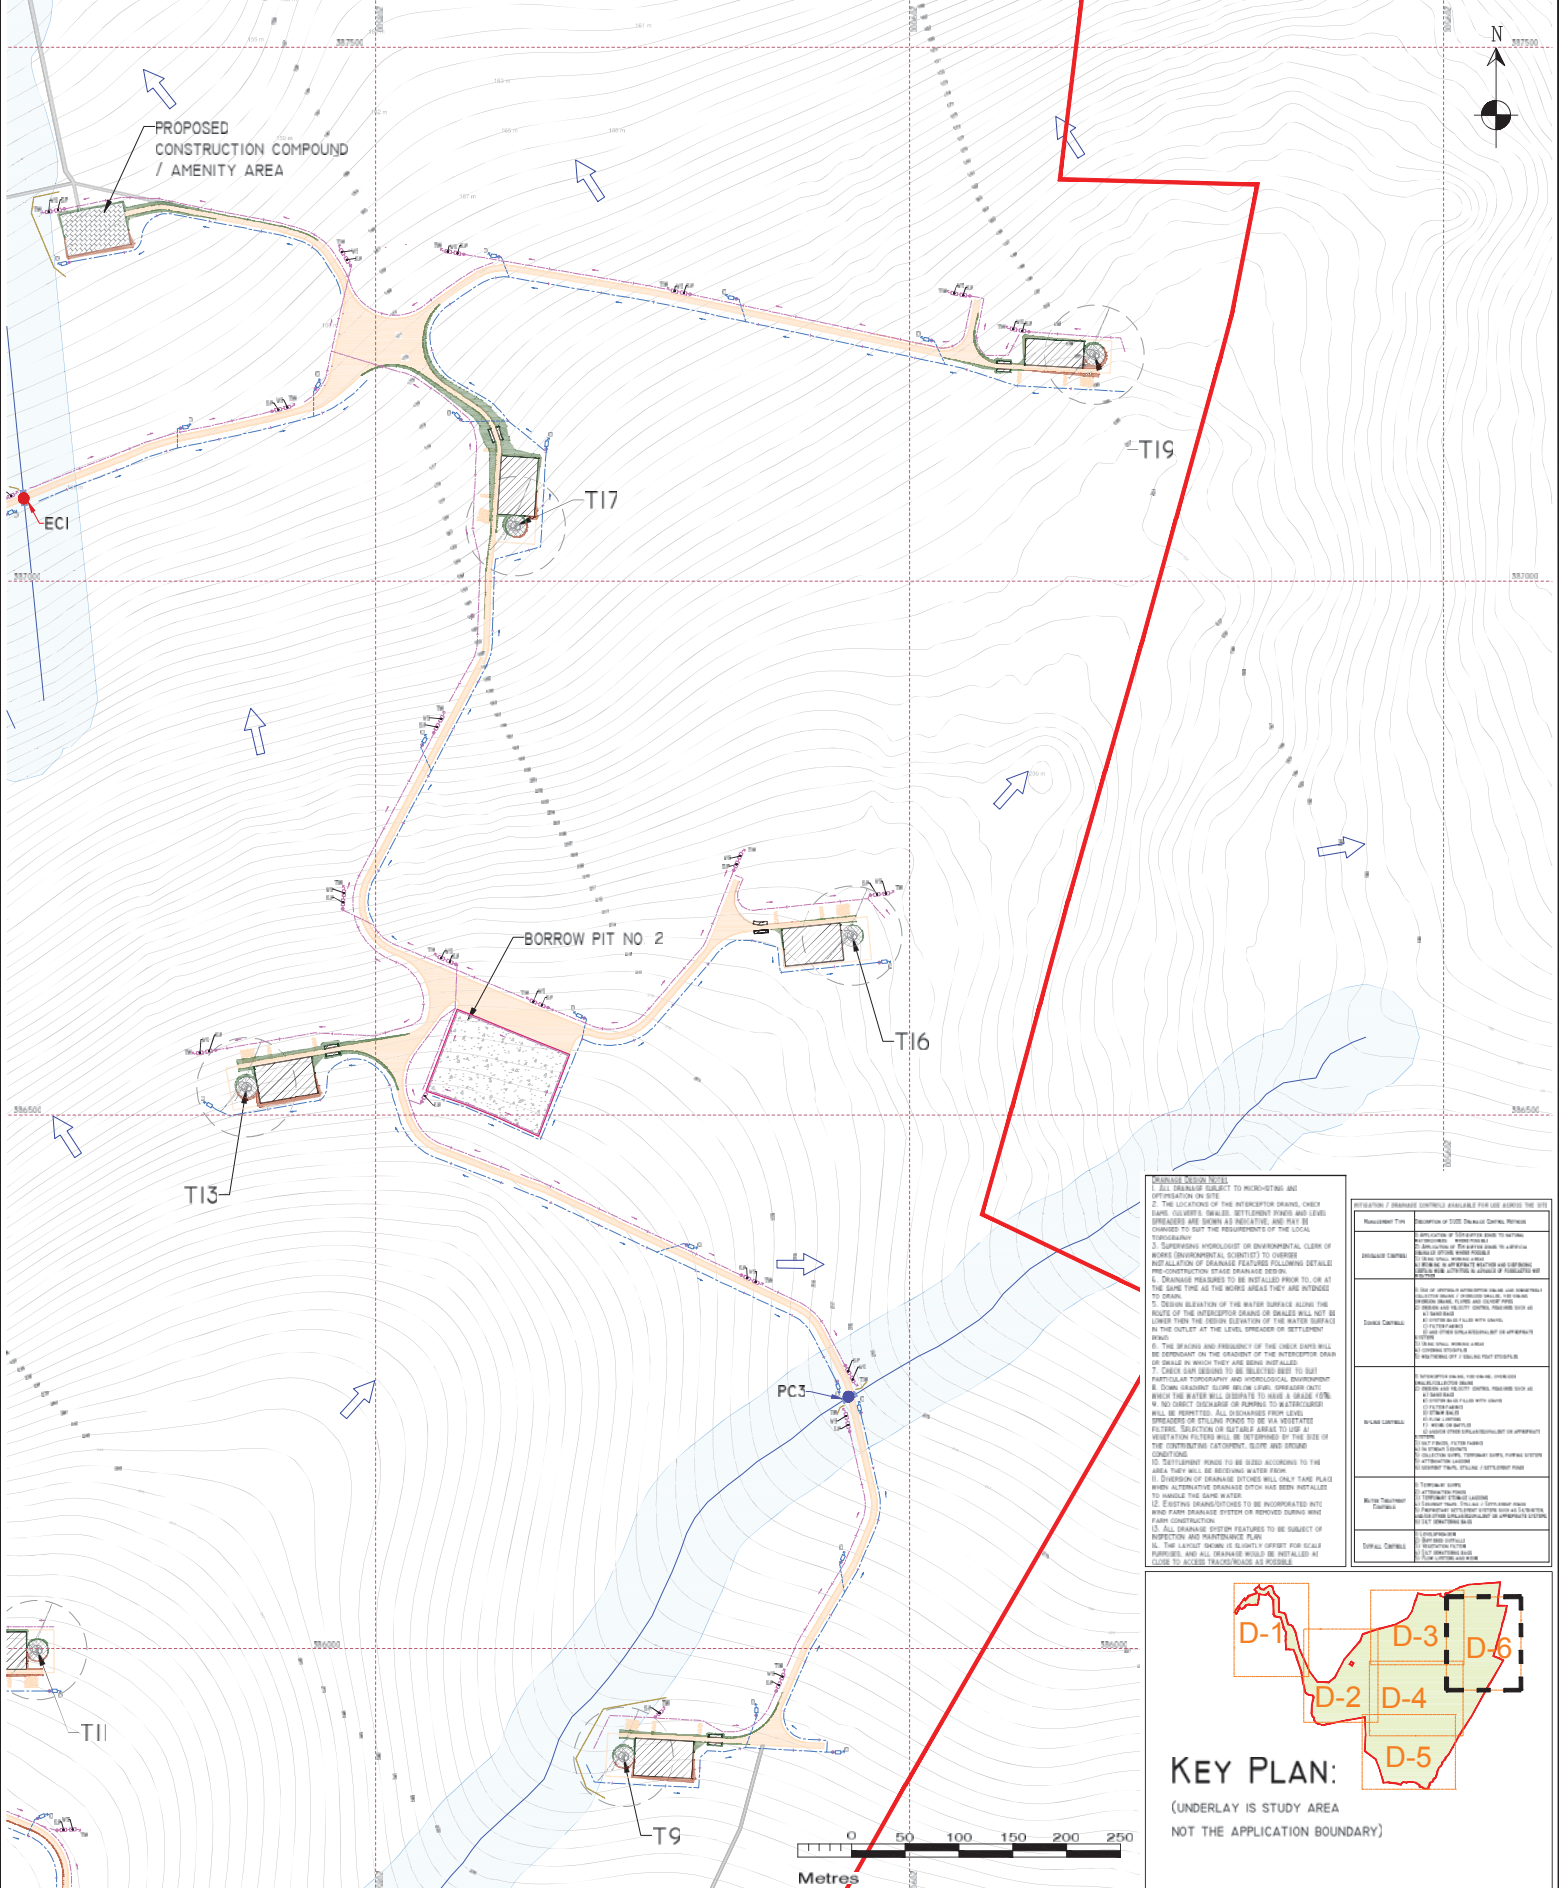

- DRAINAGE DESIGN NOTES**
1. ALL DRAINAGE SUBJECT TO MICRO-STAGING AND UPGRADATION ON SITE.
 2. THE LOCATIONS OF THE INTERCEPTOR DRAINS, CHECK DAMS, SLOTTED DRAINAGE PIPES AND LEADS, SPREADERS ARE SHOWN AS INDICATIVE, AND MAY BE CHANGED TO SUIT THE REQUIREMENTS OF THE LOCAL TERRAIN.
 3. SURVEYOR, HYDROLOGIST OR ENVIRONMENTAL SCIENTIST TO OVERSEE INSTALLATION OF DRAINAGE FEATURES FOLLOWING DETAILED PRE-CONSTRUCTION SPACE DRAINAGE DESIGN.
 4. DRAINAGE PIPES TO BE INSTALLED FROM TO, OR AT THE SAME TIME AS THE WORK AREAS THEY ARE INTENDED TO DRAIN.
 5. DRAIN ELEVATION OF THE WATER SURFACE ALONG THE ROUTE OF THE INTERCEPTOR DRAIN OR DRAINS WILL NOT BE LOWER THAN THE DESIGN ELEVATION OF THE WATER SURFACE IN THE OUTLET AT THE LEVEL SPREADER OF SETTLEMENT POND.
 6. THE SPACING AND FREQUENCY OF THE CHECK DAMS WILL BE DEPENDANT ON THE GRADIENT OF THE INTERCEPTOR DRAIN OF DRAIN IN WHICH THEY ARE BEING INSTALLED.
 7. CHECK DAMS SHOULD BE BEING INSTALLED TO SUIT PARTICULAR TOPOGRAPHY AND HYDROLOGICAL ENVIRONMENT.
 8. DOWN GRADIENT SLOPE FROM LEADS, SPREADERS ONLY AFTER THE WATER WILL SEPARATE TO HAVE A GRADE FENCE.
 9. NO DIRECT DISCHARGE OF RUNOFF TO WATERCOURSE WILL BE PERMITTED. ALL DISCHARGE FROM LEADS, SPREADERS OR OTHER POINTS TO BE VIA VEGETATED FILTER, SLOTTED OR PLATEAU LEADS TO USE AS VEGETATION FILTERS WILL BE DETERMINED BY THE SIZE OF THE CONTRIBUTING CATCHMENT, SLOPE AND GROUND CONDITIONS.
 10. SETTLEMENT POND TO BE SIZED ACCORDING TO THE AREA THEY WILL BE RECEIVING WATER FROM.
 11. DIVERSION OF DRAINAGE DITCHES WILL ONLY TAKE PLACE WHEN ACTIVE DRAINAGE DITCH HAS BEEN INSTALLED TO HANDLE THE SAME WATER.
 12. EXISTING DRAINAGE DITCHES TO BE INCORPORATED INTO NEW DRAINAGE SYSTEM OR REMOVED DURING ROAD PAVEMENT CONSTRUCTION.
 13. ALL DRAINAGE SYSTEM FEATURES TO BE SUBJECT OF INSPECTION AND MAINTENANCE PLAN.
 14. THE LAYOUT DRAWING IS QUANTITY GRAFT FOR SCALE PURPOSES, AND ALL DRAINAGE WOULD BE INSTALLED AT CLOSE TO ACCESS, TRACK/ROADS, AS POSSIBLE.

REGULATION / DRAINAGE CONTROL AVAILABLE FOR USE ABOVE THE SITE	
Regulation Type	Description of Ditch Drainage Control Features
Drainage Control	1. LOCATION OF INTERCEPTOR DRAIN TO NATURAL OR EXISTING DRAINAGE SYSTEM. 2. LOCATION OF INTERCEPTOR DRAIN TO EXISTING DRAINAGE SYSTEM. 3. LOCATION OF INTERCEPTOR DRAIN TO EXISTING DRAINAGE SYSTEM. 4. LOCATION OF INTERCEPTOR DRAIN TO EXISTING DRAINAGE SYSTEM.
Drainage Control	1. Use of vegetation to intercept runoff and control erosion. 2. Use of vegetation to intercept runoff and control erosion. 3. Use of vegetation to intercept runoff and control erosion. 4. Use of vegetation to intercept runoff and control erosion.
Drainage Control	1. Use of vegetation to intercept runoff and control erosion. 2. Use of vegetation to intercept runoff and control erosion. 3. Use of vegetation to intercept runoff and control erosion. 4. Use of vegetation to intercept runoff and control erosion.
Drainage Control	1. Use of vegetation to intercept runoff and control erosion. 2. Use of vegetation to intercept runoff and control erosion. 3. Use of vegetation to intercept runoff and control erosion. 4. Use of vegetation to intercept runoff and control erosion.
Drainage Control	1. Use of vegetation to intercept runoff and control erosion. 2. Use of vegetation to intercept runoff and control erosion. 3. Use of vegetation to intercept runoff and control erosion. 4. Use of vegetation to intercept runoff and control erosion.
Drainage Control	1. Use of vegetation to intercept runoff and control erosion. 2. Use of vegetation to intercept runoff and control erosion. 3. Use of vegetation to intercept runoff and control erosion. 4. Use of vegetation to intercept runoff and control erosion.
Drainage Control	1. Use of vegetation to intercept runoff and control erosion. 2. Use of vegetation to intercept runoff and control erosion. 3. Use of vegetation to intercept runoff and control erosion. 4. Use of vegetation to intercept runoff and control erosion.
Drainage Control	1. Use of vegetation to intercept runoff and control erosion. 2. Use of vegetation to intercept runoff and control erosion. 3. Use of vegetation to intercept runoff and control erosion. 4. Use of vegetation to intercept runoff and control erosion.
Drainage Control	1. Use of vegetation to intercept runoff and control erosion. 2. Use of vegetation to intercept runoff and control erosion. 3. Use of vegetation to intercept runoff and control erosion. 4. Use of vegetation to intercept runoff and control erosion.

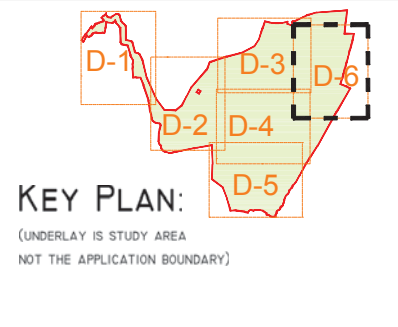

DRAWING LEGEND

- APPLICATION BOUNDARY
- EXISTING ROADS
- EXISTING TRACKS/FOREST ROADS
- WORKS AREA
- CRANE PAD
- HARDSTANDING AREA
- BORROW PIT
- TURBINE FOUNDATION
- TURBINE AND SHELTER AREA
- SITE LAYOUT IS UNDERLAIN BY 1M INTERVAL CONTOURS TO SHOW MAIN HEAD
- SLOPE / DRAINAGE DIRECTION

EXISTING DRAINAGE

- EXISTING RIVER / STREAM / LAKE
- RIVER / STREAM BUFFER SOH
- LAKE/ET
- LAKE/ET SOH BUFFER
- EXISTING CULVERTS / BRIDGES
- UPSTREAM INTERCEPTOR DRAIN
- DRAINS / DOWNSTREAM COLLECTOR DRAIN
- DIRECTION OF FLOW
- SILT FENCES
- DOUBLE / TRIPLE SILT FENCES
- SETTLEMENT POND - VEGETATION FILTER + LEVEL SPREADER
- SETTLEMENT POND - LEVEL SPREADER

PROPOSED DRAINAGE

- CHECK DAM TYPE B
- PROPOSED CULVERTS / BRIDGES
- INTERCEPTOR DITCH CULVERT
- COLLECTOR DITCH CULVERT
- OVERLAND FLOW DISCHARGE
- TREATED WATER DISCHARGE
- SETTLEMENT POND
- SEMI-NATURAL VEGETATION
- SWALE / FILTER BED / SECONDARY SILT SPREAD
- PUMPING SLUIC
- ON SITE GRID CONNECTION

DRAINAGE NOTES

1. DRAINAGE ISSUED ARE FOR PLANNING APPLICATION PURPOSES ONLY.

2. COPYRIGHT, ALL RIGHTS RESERVED. NO PART HERE WITH MAY BE COPIED OR REPRODUCED PARTIALLY OR WHOLLY IN ANY FORM OR MANNER WITHOUT THE PRIOR NOTICE OF THE COPYRIGHT OWNER HYDRO-ENVIRONMENTAL SERVICES.

3. DO NOT SCALE OFF THIS DRAWING. FIGURED METRIC DIMENSIONS ONLY SHOULD BE TAKEN OFF THIS DRAWING.

4. ALL DIMENSIONS ARE IN METRES.

Ordnance Survey Ireland Licence No. EN 004717
© Ordnance Survey Ireland/Geomatics Ireland

13.12.17	Planning	MG	MG
Date	Description	Chkd	Signed
Revisions			

HYDRO ENVIRONMENTAL SERVICES

22 Lower Main St
Dungarvan
Co. Waterford
Ireland

tel: +353 (0) 56 44122
tel: +353 (0) 56 44244
email: info@hydroenvironmental.ie
web: www.hydroenvironmental.ie

Client: MCCARTHY KEVILLE AND O'SULLIVAN

Job: MEENBOG WIND FARM, CO. DONEGAL

Title: DRAINAGE LAYOUT SHEET 6 OF 6

Figure No: D106 (0502-20)

Drawing No: P1249-2-1217-A1-D106(0502-20)-00A

Sheet Size: A1

Scale: 1:2,500 (A1)

Date: 13/12/2017

Checked By: MG

Project Design Drawing Notes

Drawings issued are for planning application purposes only. They are not to be used for construction purposes.

Copyright. All rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior written permission of McCarthy Keville O'Sullivan Ltd.

Dimensions. All dimensions are in millimetres unless otherwise stated.

Levels. All levels are in metres above sea level unless otherwise stated.

Responsibility. The client is responsible for obtaining all necessary permissions and consents for the proposed works and is responsible for taking and checking any and all dimensions and levels that relate to the works.

Use of drawing. The use of this drawing shall be deemed to be the use of the drawing as it is issued and shall be deemed to be the use of the drawing as it is issued and shall be deemed to be the use of the drawing as it is issued.

Disclaimer. The client is responsible for obtaining all necessary permissions and consents for the proposed works and is responsible for taking and checking any and all dimensions and levels that relate to the works.

Internal electrical cable trench may be installed on either side of site roads.

Drawing Legend

- Planning Application Site Boundary
- Underground Cabling Routes
- Proposed Drumabough & Leneela Wind Farm
- Cabling (On-Appraisal) (Pt. Ref. 17/56943 ABP Ref. Pt. REF. 24/7/16)
- Route of Meenbog Wind Farm
- Independent Grid Connection Cabling

Ordnance Survey Ireland Licence No. A0021917 © Ordnance Survey Ireland/Government of Ireland

N

Grid Connection (1:2,500) Key Plan

Meenbog Wind Farm, Co. Donegal

Drawn by: **Joseph O'Brien**


Checked by: **Michael Watson**


Project No: **0502 - A**

Scale: **1:20,000 @ A1**

Date: **20.12.2018**

McCarthy Keville O'Sullivan Ltd.
Planning & Environmental Consultants
Block 1, Financial Services Centre,
Monaghan Road,
Galway, Ireland.
email: info@mcCarthyKevilleO'Sullivan.ie
Tel: +353 91 735611
Fax: +353 91 771279

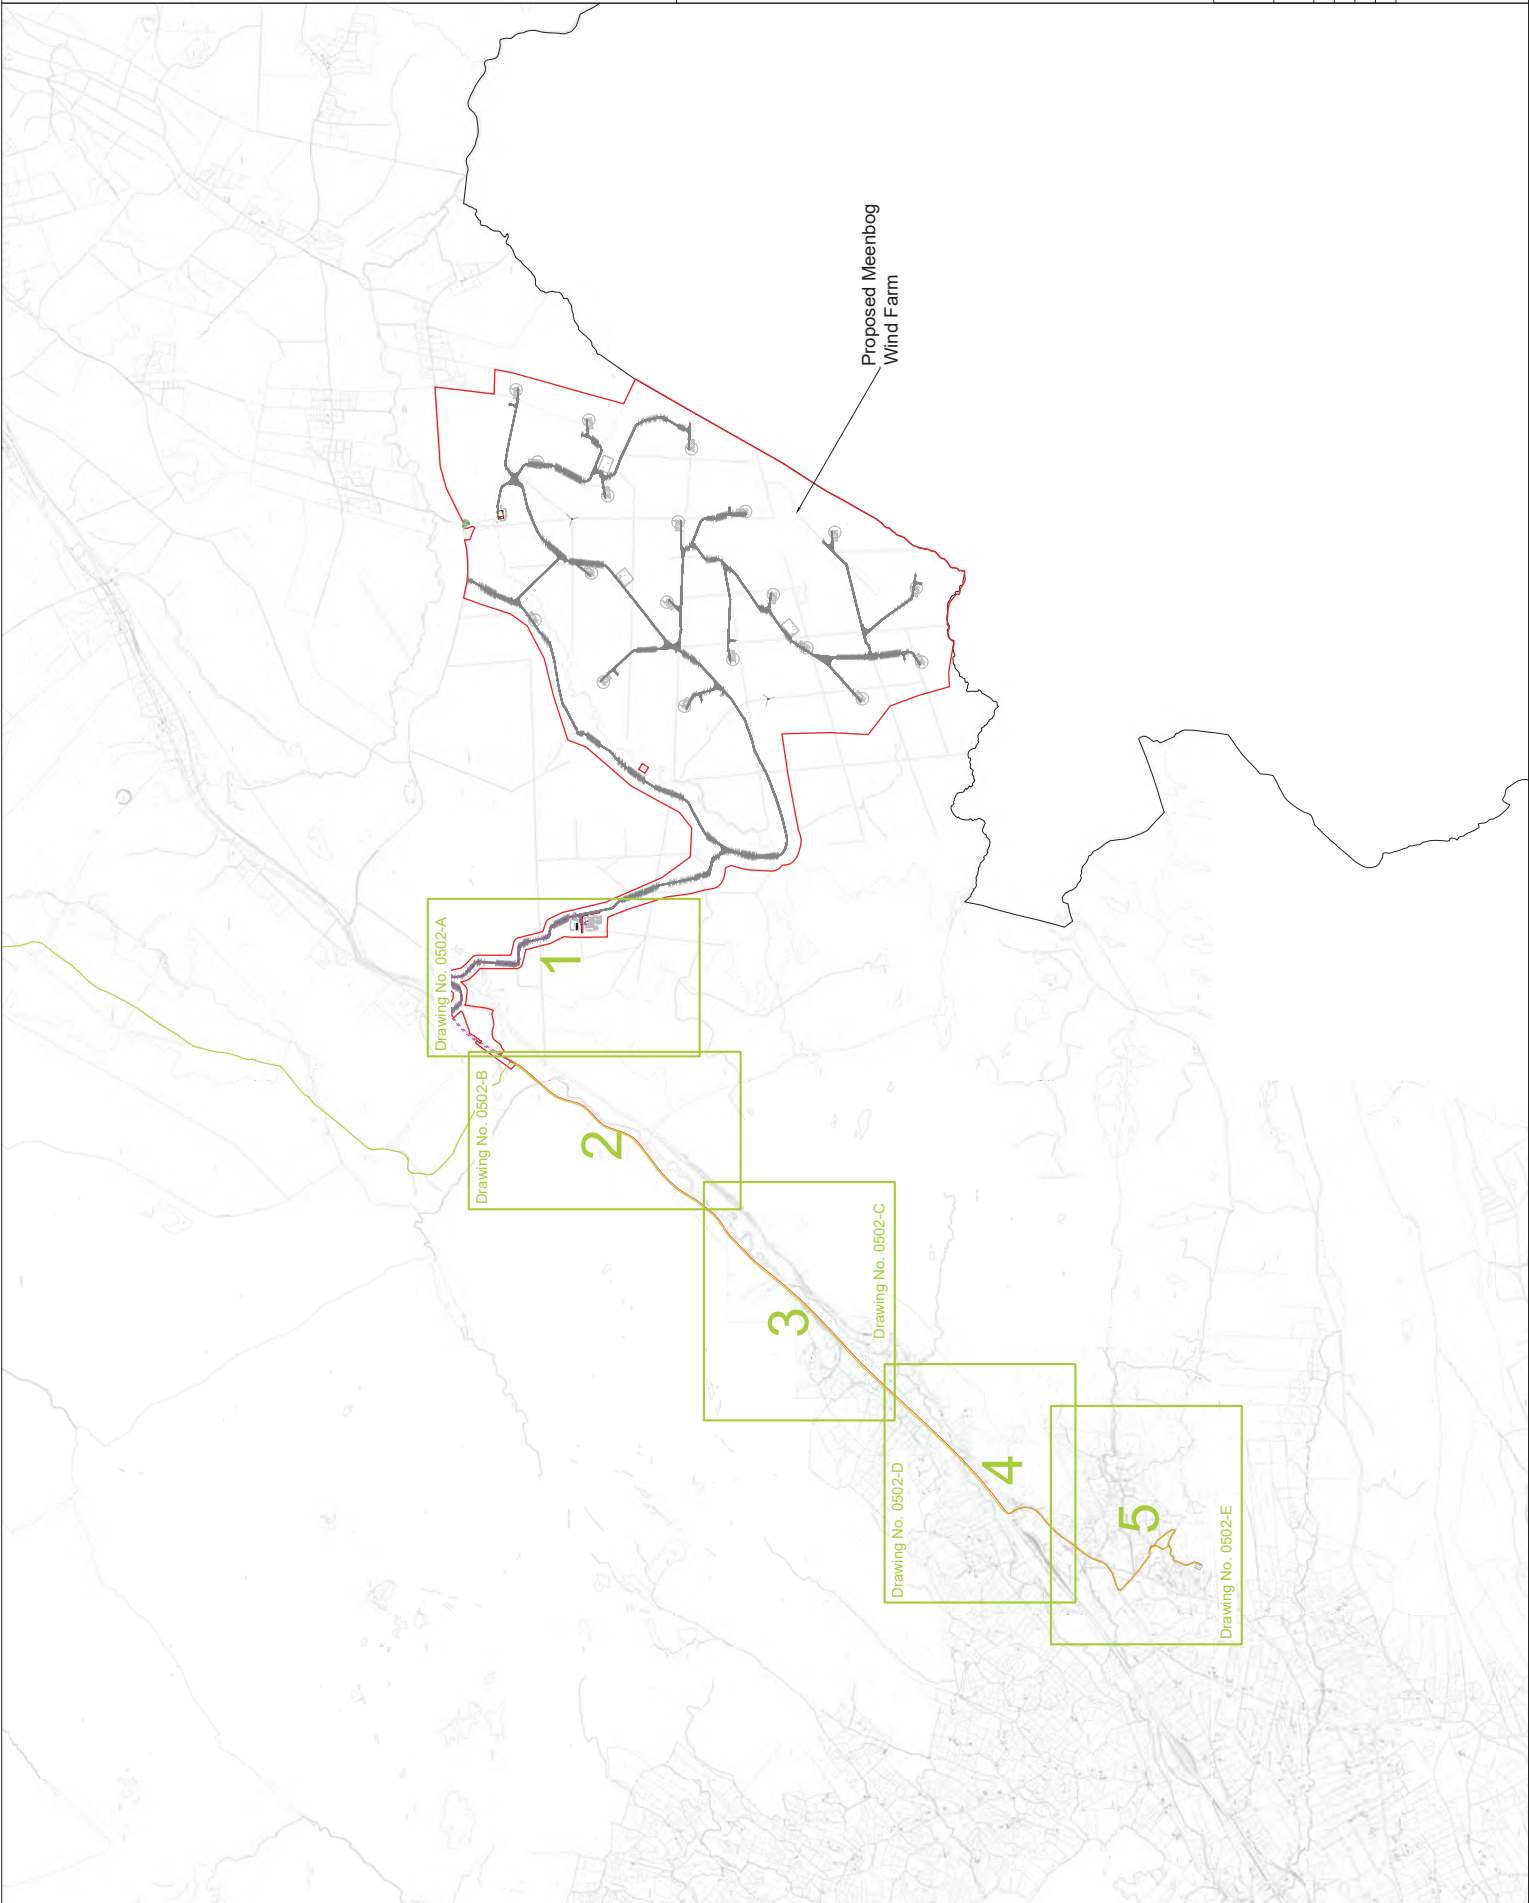

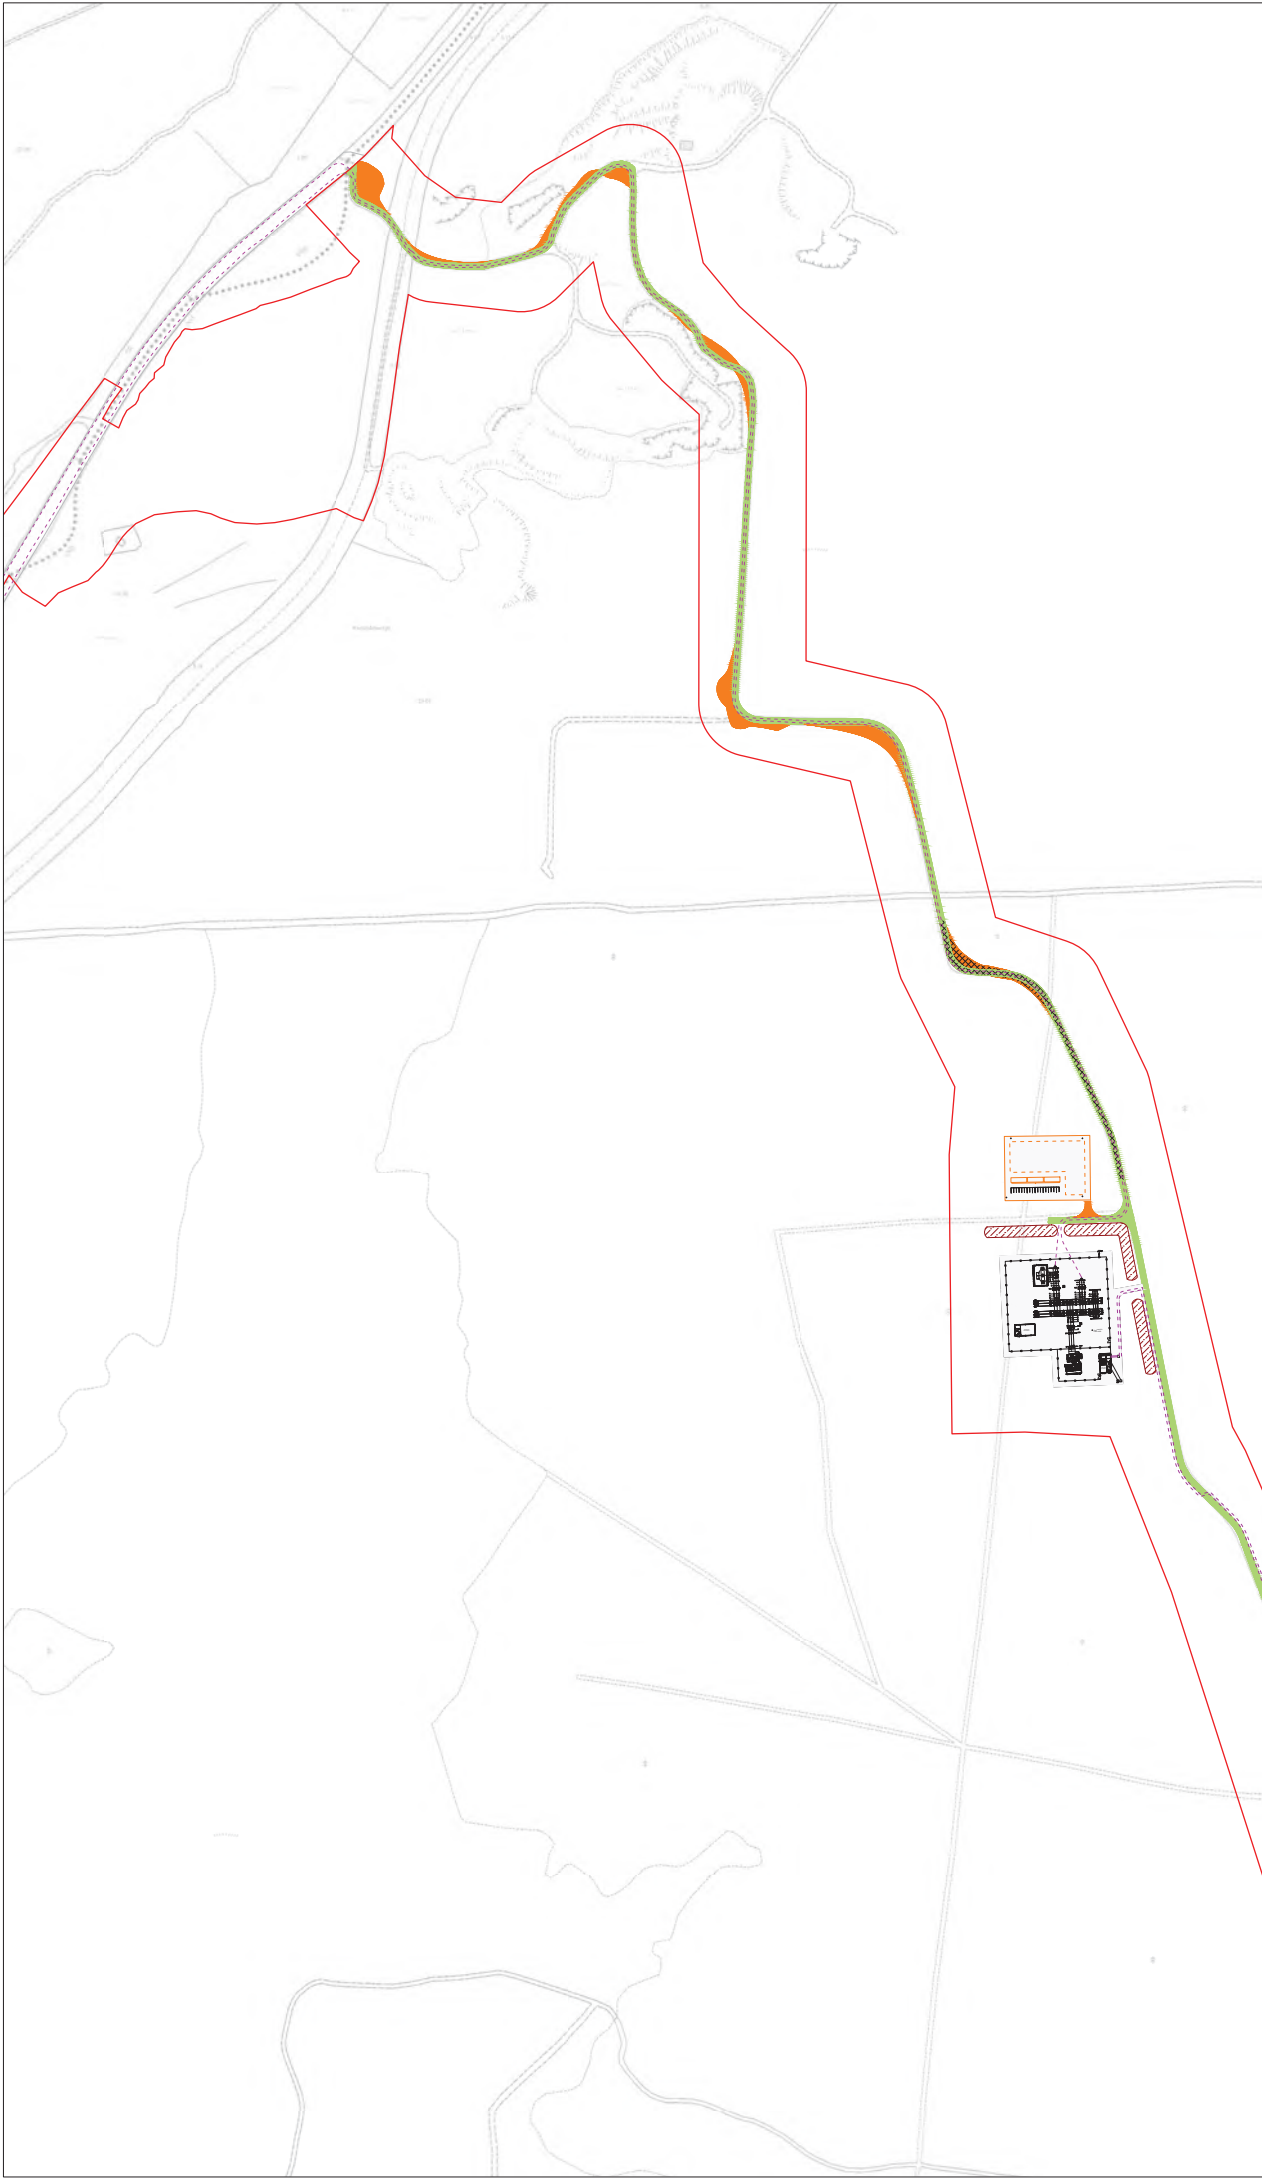

Project Design Drawing Notes

1. Drawings issued are for planning application purposes only.
2. Drawings not to be used for construction/contract conditions.
3. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior notice of the copyright owner McCarthy Keville O'Sullivan Ltd.
4. Do not scale off this drawing. Figured metric dimensions only should be taken off this drawing. All dimensions in millimeters unless otherwise stated.
5. All contractors, whether main or sub-contractors, must visit the site and are responsible for taking and checking any and all dimensions and levels that relate to the works.
6. The use of or reliance upon this drawing shall be deemed to be acceptance of these conditions of use unless otherwise agreed in writing, such written agreement to be sought from and issued by the copyright holder to the use or reliance upon this drawing.
7. Layout plans show typical Turbine rotor diameter as per turbine drawing.
8. Final levels may vary depending on local ground conditions.
9. Internal electrical cable trench may be installed on either side of site roads.


- Drawing Legend**
- Planning Application Site Boundary
 - Existing Road to be Upgraded
 - Existing Floating Road to be Upgraded
 - Proposed Road
 - Proposed Floating Road
 - Internal Electrical Cable Trench
 - Berm
 - Underground Cabling Routes

Drawing Title:
Grid Connection Layout
Plan Sheet 1 of 5

Project Title:
Meenbog Wind Farm, Co. Donegal

DRAWN BY: Joseph O'Brien	CHECKED BY: Michael Watson
PROJECT No: 160502	DRAWING No: 0502 - B
SCALE: 1:2,500 @ A1	DATE: 20.12.2018

OS SHEET No: 0001 0002 0003 0004 0005 0006 0007 0008 0009 0010 0011 0012 0013 0014 0015 0016 0017 0018 0019 0020 0021 0022 0023 0024 0025 0026 0027 0028 0029 0030 0031 0032 0033 0034 0035 0036 0037 0038 0039 0040 0041 0042 0043 0044 0045 0046 0047 0048 0049 0050 0051 0052 0053 0054 0055 0056 0057 0058 0059 0060 0061 0062 0063 0064 0065 0066 0067 0068 0069 0070 0071 0072 0073 0074 0075 0076 0077 0078 0079 0080 0081 0082 0083 0084 0085 0086 0087 0088 0089 0090 0091 0092 0093 0094 0095 0096 0097 0098 0099 0100 0101 0102 0103 0104 0105 0106 0107 0108 0109 0110 0111 0112 0113 0114 0115 0116 0117 0118 0119 0120 0121 0122 0123 0124 0125 0126 0127 0128 0129 0130 0131 0132 0133 0134 0135 0136 0137 0138 0139 0140 0141 0142 0143 0144 0145 0146 0147 0148 0149 0150 0151 0152 0153 0154 0155 0156 0157 0158 0159 0160 0161 0162 0163 0164 0165 0166 0167 0168 0169 0170 0171 0172 0173 0174 0175 0176 0177 0178 0179 0180 0181 0182 0183 0184 0185 0186 0187 0188 0189 0190 0191 0192 0193 0194 0195 0196 0197 0198 0199 0200 0201 0202 0203 0204 0205 0206 0207 0208 0209 0210 0211 0212 0213 0214 0215 0216 0217 0218 0219 0220 0221 0222 0223 0224 0225 0226 0227 0228 0229 0230 0231 0232 0233 0234 0235 0236 0237 0238 0239 0240 0241 0242 0243 0244 0245 0246 0247 0248 0249 0250 0251 0252 0253 0254 0255 0256 0257 0258 0259 0260 0261 0262 0263 0264 0265 0266 0267 0268 0269 0270 0271 0272 0273 0274 0275 0276 0277 0278 0279 0280 0281 0282 0283 0284 0285 0286 0287 0288 0289 0290 0291 0292 0293 0294 0295 0296 0297 0298 0299 0300 0301 0302 0303 0304 0305 0306 0307 0308 0309 0310 0311 0312 0313 0314 0315 0316 0317 0318 0319 0320 0321 0322 0323 0324 0325 0326 0327 0328 0329 0330 0331 0332 0333 0334 0335 0336 0337 0338 0339 0340 0341 0342 0343 0344 0345 0346 0347 0348 0349 0350 0351 0352 0353 0354 0355 0356 0357 0358 0359 0360 0361 0362 0363 0364 0365 0366 0367 0368 0369 0370 0371 0372 0373 0374 0375 0376 0377 0378 0379 0380 0381 0382 0383 0384 0385 0386 0387 0388 0389 0390 0391 0392 0393 0394 0395 0396 0397 0398 0399 0400 0401 0402 0403 0404 0405 0406 0407 0408 0409 0410 0411 0412 0413 0414 0415 0416 0417 0418 0419 0420 0421 0422 0423 0424 0425 0426 0427 0428 0429 0430 0431 0432 0433 0434 0435 0436 0437 0438 0439 0440 0441 0442 0443 0444 0445 0446 0447 0448 0449 0450 0451 0452 0453 0454 0455 0456 0457 0458 0459 0460 0461 0462 0463 0464 0465 0466 0467 0468 0469 0470 0471 0472 0473 0474 0475 0476 0477 0478 0479 0480 0481 0482 0483 0484 0485 0486 0487 0488 0489 0490 0491 0492 0493 0494 0495 0496 0497 0498 0499 0500 0501 0502 0503 0504 0505 0506 0507 0508 0509 0510 0511 0512 0513 0514 0515 0516 0517 0518 0519 0520 0521 0522 0523 0524 0525 0526 0527 0528 0529 0530 0531 0532 0533 0534 0535 0536 0537 0538 0539 0540 0541 0542 0543 0544 0545 0546 0547 0548 0549 0550 0551 0552 0553 0554 0555 0556 0557 0558 0559 0560 0561 0562 0563 0564 0565 0566 0567 0568 0569 0570 0571 0572 0573 0574 0575 0576 0577 0578 0579 0580 0581 0582 0583 0584 0585 0586 0587 0588 0589 0590 0591 0592 0593 0594 0595 0596 0597 0598 0599 0600 0601 0602 0603 0604 0605 0606 0607 0608 0609 0610 0611 0612 0613 0614 0615 0616 0617 0618 0619 0620 0621 0622 0623 0624 0625 0626 0627 0628 0629 0630 0631 0632 0633 0634 0635 0636 0637 0638 0639 0640 0641 0642 0643 0644 0645 0646 0647 0648 0649 0650 0651 0652 0653 0654 0655 0656 0657 0658 0659 0660 0661 0662 0663 0664 0665 0666 0667 0668 0669 0670 0671 0672 0673 0674 0675 0676 0677 0678 0679 0680 0681 0682 0683 0684 0685 0686 0687 0688 0689 0690 0691 0692 0693 0694 0695 0696 0697 0698 0699 0700 0701 0702 0703 0704 0705 0706 0707 0708 0709 0710 0711 0712 0713 0714 0715 0716 0717 0718 0719 0720 0721 0722 0723 0724 0725 0726 0727 0728 0729 0730 0731 0732 0733 0734 0735 0736 0737 0738 0739 0740 0741 0742 0743 0744 0745 0746 0747 0748 0749 0750 0751 0752 0753 0754 0755 0756 0757 0758 0759 0760 0761 0762 0763 0764 0765 0766 0767 0768 0769 0770 0771 0772 0773 0774 0775 0776 0777 0778 0779 0780 0781 0782 0783 0784 0785 0786 0787 0788 0789 0790 0791 0792 0793 0794 0795 0796 0797 0798 0799 0800 0801 0802 0803 0804 0805 0806 0807 0808 0809 0810 0811 0812 0813 0814 0815 0816 0817 0818 0819 0820 0821 0822 0823 0824 0825 0826 0827 0828 0829 0830 0831 0832 0833 0834 0835 0836 0837 0838 0839 0840 0841 0842 0843 0844 0845 0846 0847 0848 0849 0850 0851 0852 0853 0854 0855 0856 0857 0858 0859 0860 0861 0862 0863 0864 0865 0866 0867 0868 0869 0870 0871 0872 0873 0874 0875 0876 0877 0878 0879 0880 0881 0882 0883 0884 0885 0886 0887 0888 0889 0890 0891 0892 0893 0894 0895 0896 0897 0898 0899 0900 0901 0902 0903 0904 0905 0906 0907 0908 0909 0910 0911 0912 0913 0914 0915 0916 0917 0918 0919 0920 0921 0922 0923 0924 0925 0926 0927 0928 0929 0930 0931 0932 0933 0934 0935 0936 0937 0938 0939 0940 0941 0942 0943 0944 0945 0946 0947 0948 0949 0950 0951 0952 0953 0954 0955 0956 0957 0958 0959 0960 0961 0962 0963 0964 0965 0966 0967 0968 0969 0970 0971 0972 0973 0974 0975 0976 0977 0978 0979 0980 0981 0982 0983 0984 0985 0986 0987 0988 0989 0990 0991 0992 0993 0994 0995 0996 0997 0998 0999 1000 1001 1002 1003 1004 1005 1006 1007 1008 1009 1010 1011 1012 1013 1014 1015 1016 1017 1018 1019 1020 1021 1022 1023 1024 1025 1026 1027 1028 1029 1030 1031 1032 1033 1034 1035 1036 1037 1038 1039 1040 1041 1042 1043 1044 1045 1046 1047 1048 1049 1050 1051 1052 1053 1054 1055 1056 1057 1058 1059 1060 1061 1062 1063 1064 1065 1066 1067 1068 1069 1070 1071 1072 1073 1074 1075 1076 1077 1078 1079 1080 1081 1082 1083 1084 1085 1086 1087 1088 1089 1090 1091 1092 1093 1094 1095 1096 1097 1098 1099 1100 1101 1102 1103 1104 1105 1106 1107 1108 1109 1110 1111 1112 1113 1114 1115 1116 1117 1118 1119 1120 1121 1122 1123 1124 1125 1126 1127 1128 1129 1130 1131 1132 1133 1134 1135 1136 1137 1138 1139 1140 1141 1142 1143 1144 1145 1146 1147 1148 1149 1150 1151 1152 1153 1154 1155 1156 1157 1158 1159 1160 1161 1162 1163 1164 1165 1166 1167 1168 1169 1170 1171 1172 1173 1174 1175 1176 1177 1178 1179 1180 1181 1182 1183 1184 1185 1186 1187 1188 1189 1190 1191 1192 1193 1194 1195 1196 1197 1198 1199 1200 1201 1202 1203 1204 1205 1206 1207 1208 1209 1210 1211 1212 1213 1214 1215 1216 1217 1218 1219 1220 1221 1222 1223 1224 1225 1226 1227 1228 1229 1230 1231 1232 1233 1234 1235 1236 1237 1238 1239 1240 1241 1242 1243 1244 1245 1246 1247 1248 1249 1250 1251 1252 1253 1254 1255 1256 1257 1258 1259 1260 1261 1262 1263 1264 1265 1266 1267 1268 1269 1270 1271 1272 1273 1274 1275 1276 1277 1278 1279 1280 1281 1282 1283 1284 1285 1286 1287 1288 1289 1290 1291 1292 1293 1294 1295 1296 1297 1298 1299 1300 1301 1302 1303 1304 1305 1306 1307 1308 1309 1310 1311 1312 1313 1314 1315 1316 1317 1318 1319 1320 1321 1322 1323 1324 1325 1326 1327 1328 1329 1330 1331 1332 1333 1334 1335 1336 1337 1338 1339 1340 1341 1342 1343 1344 1345 1346 1347 1348 1349 1350 1351 1352 1353 1354 1355 1356 1357 1358 1359 1360 1361 1362 1363 1364 1365 1366 1367 1368 1369 1370 1371 1372 1373 1374 1375 1376 1377 1378 1379 1380 1381 1382 1383 1384 1385 1386 1387 1388 1389 1390 1391 1392 1393 1394 1395 1396 1397 1398 1399 1400 1401 1402 1403 1404 1405 1406 1407 1408 1409 1410 1411 1412 1413 1414 1415 1416 1417 1418 1419 1420 1421 1422 1423 1424 1425 1426 1427 1428 1429 1430 1431 1432 1433 1434 1435 1436 1437 1438 1439 1440 1441 1442 1443 1444 1445 1446 1447 1448 1449 1450 1451 1452 1453 1454 1455 1456 1457 1458 1459 1460 1461 1462 1463 1464 1465 1466 1467 1468 1469 1470 1471 1472 1473 1474 1475 1476 1477 1478 1479 1480 1481 1482 1483 1484 1485 1486 1487 1488 1489 1490 1491 1492 1493 1494 1495 1496 1497 1498 1499 1500 1501 1502 1503 1504 1505 1506 1507 1508 1509 1510 1511 1512 1513 1514 1515 1516 1517 1518 1519 1520 1521 1522 1523 1524 1525 1526 1527 1528 1529 1530 1531 1532 1533 1534 1535 1536 1537 1538 1539 1540 1541 1542 1543 1544 1545 1546 1547 1548 1549 1550 1551 1552 1553 1554 1555 1556 1557 1558 1559 1560 1561 1562 1563 1564 1565 1566 1567 1568 1569 1570 1571 1572 1573 1574 1575 1576 1577 1578 1579 1580 1581 1582 1583 1584 1585 1586 1587 1588 1589 1590 1591 1592 1593 1594 1595 1596 1597 1598 1599 1600 1601 1602 1603 1604 1605 1606 1607 1608 1609 1610 1611 1612 1613 1614 1615 1616 1617 1618 1619 1620 1621 1622 1623 1624 1625 1626 1627 1628 1629 1630 1631 1632 1633 1634 1635 1636 1637 1638 1639 1640 1641 1642 1643 1644 1645 1646 1647 1648 1649 1650 1651 1652 1653 1654 1655 1656 1657 1658 1659 1660 1661 1662 1663 1664 1665 1666 1667 1668 1669 1670 1671 1672 1673 1674 1675 1676 1677 1678 1679 1680 1681 1682 1683 1684 1685 1686 1687 1688 1689 1690 1691 1692 1693 1694 1695 1696 1697 1698 1699 1700 1701 1702 1703 1704 1705 1706 1707 1708 1709 1710 1711 1712 1713 1714 1715 1716 1717 1718 1719 1720 1721 1722 1723 1724 1725 1726 1727 1728 1729 1730 1731 1732 1733 1734 1735 1736 1737 1738 1739 1740 1741 1742 1743 1744 1745 1746 1747 1748 1749 1750 1751 1752 1753 1754 1755 1756 1757 1758 1759 1760 1761 1762 1763 1764 1765 1766 1767 1768 1769 1770 1771 1772 1773 1774 1775 1776 1777 1778 1779 1780 1781 1782 1783 1784 1785 1786 1787 1788 1789 1790 1791 1792 1793 1794 1795 1796 1797 1798 1799 1800 1801 1802 1803 1804 1805 1806 1807 1808 1809 1810 1811 1812 1813 1814 1815 1816 1817 1818 1819 1820 1821 1822 1823 1824 1825 1826 1827 1828 1829 1830 1831 1832 1833 1834 1835 1836 1837 1838 1839 1840 1841 1842 1843 1844 1845 1846 1847 1848 1849 1850 1851 1852 1853 1854 1855 1856 1857 1858 1859 1860 1861 1862 1863 1864 1865 1866 1867 1868 1869 1870 1871 1872 1873 1874 1875 1876 1877 1878 1879 1880 1881 1882 1883 1884 1885 1886 1887 1888 1889 1890 1891 1892 1893 1894 1895 1896 1897 1898 1899 1900 1901 1902 1903 1904 1905 1906 1907 1908 1909 1910 1911 1912 1913 1914 1915 1916 1917 1918 1919 1920 1921 1922 1923 1924 1925 1926 1927 1928 1929 1930 1931 1932 1933 1934 1935 1936 1937 1938 1939 1940 1941 1942 1943 1944 1945 1946 1947 1948 1949 1950 1951 1952 1953 1954 1955 1956 1957 1958 1959 1960 1961 1962 1963 1964 1965 1966 1967 1968 1969 1970 1971 1972 1973 1974 1975 1976 1977 1978 1979 1980 1981 1982 1983 1984 1985 1986 1987 1988 1989 1990 1991 1992 1993 1994 1995 1996 1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019 2020 2021 2022 2023 2024 2025 2026 2027 2028 2029 2030 2031 2032 2033 2034 2035 2036 2037 2038 2039 2040 2041 2042 2043 2044 2045 2046 2047 2048 2049 2050 2051 2052 2053 2054 2055 2056 2057 2058 2059 2060 2061 2062 2063 2064 2065 2066 2067 2068 2069 2070 2071 2072 2073 2074 2075 2076 2077 2078 2079 2080 2081 2082 2083 2084 2085 2086 2087 2088 2089 2090 2091 2092 2093 2094 2095 2096 2097 2098 2099 2100 2101 2102 2103 2104 2105 2106 2107 2108 2109 2110 2111 2112 2113 2114 2115 2116 2117 2118 2119 2120 2121 2122 2123 2124 2125 2126 2127 2128 2129 2130 2131 2132 2133 2134 2135 2136 2137 2138 2139 2140 2141 2142 2143 2144 2145 2146 2147 2148 2149 2150 2151 2152 2153 2154 2155 2156 2157 2158 2159 2160 2161 2162 2163 2164 2165 2166 2167 2168 2169 2170 2171 2172 2173 2174 2175 2176 2177 2178 2179 2180 2181 2182 2183 2184 2185 2186 2187 2188 2189 2190 2191 2192 2193 2194 2195 2196 2197 2198 2199 2200 2201 2202 2203 2204 2205 2206 2207 2208 2209 2210 2211 2212 2213 2214 2215 2216 2217 2218 2219 2220 2221 2222 2223 2224 2225 2226 2227 2228 2229 2230 2231 2232 2233 2234 2235 2236 2237 2238 2239 2240 2241 2242 2243 2244 2245 2246 2247 2248 2249 2250 2251 2252 2253 2254 2255 2256 2257 2258 2259 2260 2261 2262 2263 2264 2265 2266 2267 2268 2269 2270 2271 2272 2273 2274 2275 2276 2277 2278 2279 2280 2281 2282 2283 2284 2285 2286 2287 2288 2289 2290 2291 2292 2293 2294 2295 2296 2297 2298 2299 2300 2301 2302 2303 2304 2305 2306 2307 2308 2309 2310 2311 2312 2313 2314 2315 2316 2317 2318 2319 2320 2321 23

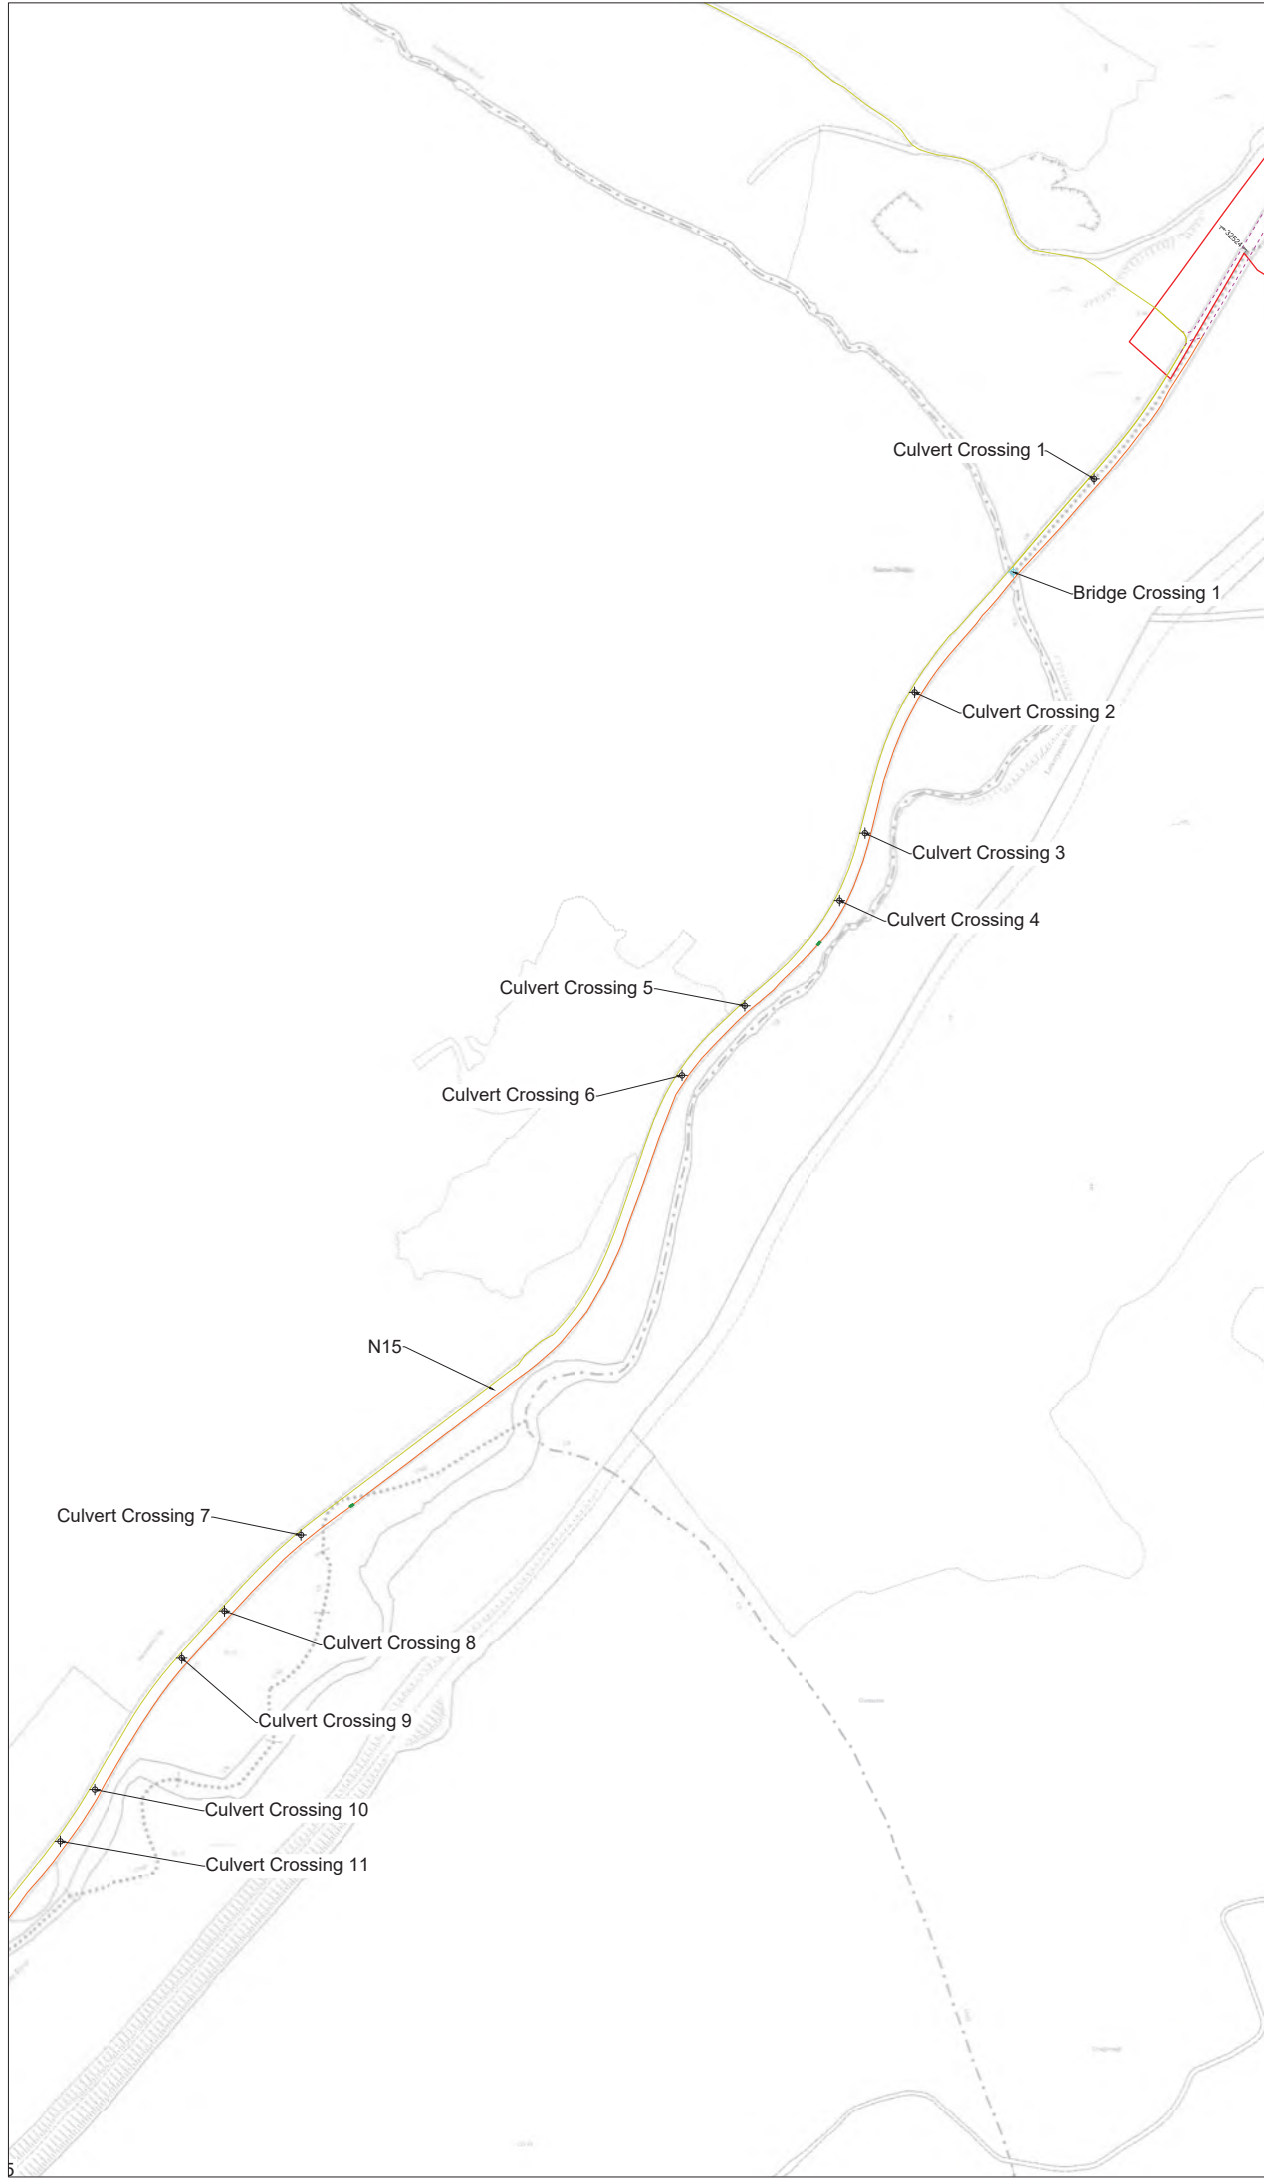

- Project Design Drawing Notes**
1. Drawings issued are for planning application purposes only.
 2. Drawings not to be used for construction/contract conditions.
 3. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior notice of the copyright owner McCarthy Keville O'Sullivan Ltd.
 4. Do not scale off this drawing. Figured metric dimensions only should be taken off this drawing. All dimensions in millimeters unless otherwise stated.
 5. All contractors, whether main or sub-contractors, must visit the site and are responsible for taking and checking any and all dimensions and levels that relate to the works.
 6. The use of or reliance upon this drawing shall be deemed to be acceptance of these conditions of use unless otherwise agreed in writing, such written agreement to be sought from and issued by the copyright holder to the use or reliance upon this drawing.
 7. Layout plans show typical Turbine rotor diameter as per turbine drawing.
 8. Final levels may vary depending on local ground conditions.
 9. Internal electrical cable trench may be installed on either side of site roads.

- Drawing Legend**
- Planning Application Site Boundary
 - Underground Cabling Routes
 - Proposed Drumnahough & Lenalea Wind Farm Underground Grid Connection Cabling (On Appeal) (Pl. Ref. 17/50543 ABP. Ref. PLOSE: 248796)
 - Route of Meenbog Wind Farm Independent Grid Connection Cabling
 - Culvert Crossing
 - Bridge Crossing
 - Joint Bay



Drawing Title:
**Grid Connection Layout
Plan Sheet 2 of 5**

Project Title:
Meenbog Wind Farm, Co. Donegal

DRAWING BY: Joseph O'Brien	CHECKED BY: Michael Watson
PROJECT NO.: 160502	DRAWING NO.: 0502 - C
SCALE: 1:2,500 @ A1	DATE: 20.12.2018

C/S SHEET NO. 0001 0002 0003 0004 0005 0006 0007 0008 0009 0010 0011 0012 0013 0014 0015 0016 0017 0018 0019 0020 0021 0022 0023 0024 0025 0026 0027 0028 0029 0030 0031 0032 0033 0034 0035 0036 0037 0038 0039 0040 0041 0042 0043 0044 0045 0046 0047 0048 0049 0050 0051 0052 0053 0054 0055 0056 0057 0058 0059 0060 0061 0062 0063 0064 0065 0066 0067 0068 0069 0070 0071 0072 0073 0074 0075 0076 0077 0078 0079 0080 0081 0082 0083 0084 0085 0086 0087 0088 0089 0090 0091 0092 0093 0094 0095 0096 0097 0098 0099 0100 0101 0102 0103 0104 0105 0106 0107 0108 0109 0110 0111 0112 0113 0114 0115 0116 0117 0118 0119 0120 0121 0122 0123 0124 0125 0126 0127 0128 0129 0130 0131 0132 0133 0134 0135 0136 0137 0138 0139 0140 0141 0142 0143 0144 0145 0146 0147 0148 0149 0150 0151 0152 0153 0154 0155 0156 0157 0158 0159 0160 0161 0162 0163 0164 0165 0166 0167 0168 0169 0170 0171 0172 0173 0174 0175 0176 0177 0178 0179 0180 0181 0182 0183 0184 0185 0186 0187 0188 0189 0190 0191 0192 0193 0194 0195 0196 0197 0198 0199 0200 0201 0202 0203 0204 0205 0206 0207 0208 0209 0210 0211 0212 0213 0214 0215 0216 0217 0218 0219 0220 0221 0222 0223 0224 0225 0226 0227 0228 0229 0230 0231 0232 0233 0234 0235 0236 0237 0238 0239 0240 0241 0242 0243 0244 0245 0246 0247 0248 0249 0250 0251 0252 0253 0254 0255 0256 0257 0258 0259 0260 0261 0262 0263 0264 0265 0266 0267 0268 0269 0270 0271 0272 0273 0274 0275 0276 0277 0278 0279 0280 0281 0282 0283 0284 0285 0286 0287 0288 0289 0290 0291 0292 0293 0294 0295 0296 0297 0298 0299 0300 0301 0302 0303 0304 0305 0306 0307 0308 0309 0310 0311 0312 0313 0314 0315 0316 0317 0318 0319 0320 0321 0322 0323 0324 0325 0326 0327 0328 0329 0330 0331 0332 0333 0334 0335 0336 0337 0338 0339 0340 0341 0342 0343 0344 0345 0346 0347 0348 0349 0350 0351 0352 0353 0354 0355 0356 0357 0358 0359 0360 0361 0362 0363 0364 0365 0366 0367 0368 0369 0370 0371 0372 0373 0374 0375 0376 0377 0378 0379 0380 0381 0382 0383 0384 0385 0386 0387 0388 0389 0390 0391 0392 0393 0394 0395 0396 0397 0398 0399 0400 0401 0402 0403 0404 0405 0406 0407 0408 0409 0410 0411 0412 0413 0414 0415 0416 0417 0418 0419 0420 0421 0422 0423 0424 0425 0426 0427 0428 0429 0430 0431 0432 0433 0434 0435 0436 0437 0438 0439 0440 0441 0442 0443 0444 0445 0446 0447 0448 0449 0450 0451 0452 0453 0454 0455 0456 0457 0458 0459 0460 0461 0462 0463 0464 0465 0466 0467 0468 0469 0470 0471 0472 0473 0474 0475 0476 0477 0478 0479 0480 0481 0482 0483 0484 0485 0486 0487 0488 0489 0490 0491 0492 0493 0494 0495 0496 0497 0498 0499 0500 0501 0502 0503 0504 0505 0506 0507 0508 0509 0510 0511 0512 0513 0514 0515 0516 0517 0518 0519 0520 0521 0522 0523 0524 0525 0526 0527 0528 0529 0530 0531 0532 0533 0534 0535 0536 0537 0538 0539 0540 0541 0542 0543 0544 0545 0546 0547 0548 0549 0550 0551 0552 0553 0554 0555 0556 0557 0558 0559 0560 0561 0562 0563 0564 0565 0566 0567 0568 0569 0570 0571 0572 0573 0574 0575 0576 0577 0578 0579 0580 0581 0582 0583 0584 0585 0586 0587 0588 0589 0590 0591 0592 0593 0594 0595 0596 0597 0598 0599 0600 0601 0602 0603 0604 0605 0606 0607 0608 0609 0610 0611 0612 0613 0614 0615 0616 0617 0618 0619 0620 0621 0622 0623 0624 0625 0626 0627 0628 0629 0630 0631 0632 0633 0634 0635 0636 0637 0638 0639 0640 0641 0642 0643 0644 0645 0646 0647 0648 0649 0650 0651 0652 0653 0654 0655 0656 0657 0658 0659 0660 0661 0662 0663 0664 0665 0666 0667 0668 0669 0670 0671 0672 0673 0674 0675 0676 0677 0678 0679 0680 0681 0682 0683 0684 0685 0686 0687 0688 0689 0690 0691 0692 0693 0694 0695 0696 0697 0698 0699 0700 0701 0702 0703 0704 0705 0706 0707 0708 0709 0710 0711 0712 0713 0714 0715 0716 0717 0718 0719 0720 0721 0722 0723 0724 0725 0726 0727 0728 0729 0730 0731 0732 0733 0734 0735 0736 0737 0738 0739 0740 0741 0742 0743 0744 0745 0746 0747 0748 0749 0750 0751 0752 0753 0754 0755 0756 0757 0758 0759 0760 0761 0762 0763 0764 0765 0766 0767 0768 0769 0770 0771 0772 0773 0774 0775 0776 0777 0778 0779 0780 0781 0782 0783 0784 0785 0786 0787 0788 0789 0790 0791 0792 0793 0794 0795 0796 0797 0798 0799 0800 0801 0802 0803 0804 0805 0806 0807 0808 0809 0810 0811 0812 0813 0814 0815 0816 0817 0818 0819 0820 0821 0822 0823 0824 0825 0826 0827 0828 0829 0830 0831 0832 0833 0834 0835 0836 0837 0838 0839 0840 0841 0842 0843 0844 0845 0846 0847 0848 0849 0850 0851 0852 0853 0854 0855 0856 0857 0858 0859 0860 0861 0862 0863 0864 0865 0866 0867 0868 0869 0870 0871 0872 0873 0874 0875 0876 0877 0878 0879 0880 0881 0882 0883 0884 0885 0886 0887 0888 0889 0890 0891 0892 0893 0894 0895 0896 0897 0898 0899 0900 0901 0902 0903 0904 0905 0906 0907 0908 0909 0910 0911 0912 0913 0914 0915 0916 0917 0918 0919 0920 0921 0922 0923 0924 0925 0926 0927 0928 0929 0930 0931 0932 0933 0934 0935 0936 0937 0938 0939 0940 0941 0942 0943 0944 0945 0946 0947 0948 0949 0950 0951 0952 0953 0954 0955 0956 0957 0958 0959 0960 0961 0962 0963 0964 0965 0966 0967 0968 0969 0970 0971 0972 0973 0974 0975 0976 0977 0978 0979 0980 0981 0982 0983 0984 0985 0986 0987 0988 0989 0990 0991 0992 0993 0994 0995 0996 0997 0998 0999 1000 1001 1002 1003 1004 1005 1006 1007 1008 1009 1010 1011 1012 1013 1014 1015 1016 1017 1018 1019 1020 1021 1022 1023 1024 1025 1026 1027 1028 1029 1030 1031 1032 1033 1034 1035 1036 1037 1038 1039 1040 1041 1042 1043 1044 1045 1046 1047 1048 1049 1050 1051 1052 1053 1054 1055 1056 1057 1058 1059 1060 1061 1062 1063 1064 1065 1066 1067 1068 1069 1070 1071 1072 1073 1074 1075 1076 1077 1078 1079 1080 1081 1082 1083 1084 1085 1086 1087 1088 1089 1090 1091 1092 1093 1094 1095 1096 1097 1098 1099 1100 1101 1102 1103 1104 1105 1106 1107 1108 1109 1110 1111 1112 1113 1114 1115 1116 1117 1118 1119 1120 1121 1122 1123 1124 1125 1126 1127 1128 1129 1130 1131 1132 1133 1134 1135 1136 1137 1138 1139 1140 1141 1142 1143 1144 1145 1146 1147 1148 1149 1150 1151 1152 1153 1154 1155 1156 1157 1158 1159 1160 1161 1162 1163 1164 1165 1166 1167 1168 1169 1170 1171 1172 1173 1174 1175 1176 1177 1178 1179 1180 1181 1182 1183 1184 1185 1186 1187 1188 1189 1190 1191 1192 1193 1194 1195 1196 1197 1198 1199 1200 1201 1202 1203 1204 1205 1206 1207 1208 1209 1210 1211 1212 1213 1214 1215 1216 1217 1218 1219 1220 1221 1222 1223 1224 1225 1226 1227 1228 1229 1230 1231 1232 1233 1234 1235 1236 1237 1238 1239 1240 1241 1242 1243 1244 1245 1246 1247 1248 1249 1250 1251 1252 1253 1254 1255 1256 1257 1258 1259 1260 1261 1262 1263 1264 1265 1266 1267 1268 1269 1270 1271 1272 1273 1274 1275 1276 1277 1278 1279 1280 1281 1282 1283 1284 1285 1286 1287 1288 1289 1290 1291 1292 1293 1294 1295 1296 1297 1298 1299 1300 1301 1302 1303 1304 1305 1306 1307 1308 1309 1310 1311 1312 1313 1314 1315 1316 1317 1318 1319 1320 1321 1322 1323 1324 1325 1326 1327 1328 1329 1330 1331 1332 1333 1334 1335 1336 1337 1338 1339 1340 1341 1342 1343 1344 1345 1346 1347 1348 1349 1350 1351 1352 1353 1354 1355 1356 1357 1358 1359 1360 1361 1362 1363 1364 1365 1366 1367 1368 1369 1370 1371 1372 1373 1374 1375 1376 1377 1378 1379 1380 1381 1382 1383 1384 1385 1386 1387 1388 1389 1390 1391 1392 1393 1394 1395 1396 1397 1398 1399 1400 1401 1402 1403 1404 1405 1406 1407 1408 1409 1410 1411 1412 1413 1414 1415 1416 1417 1418 1419 1420 1421 1422 1423 1424 1425 1426 1427 1428 1429 1430 1431 1432 1433 1434 1435 1436 1437 1438 1439 1440 1441 1442 1443 1444 1445 1446 1447 1448 1449 1450 1451 1452 1453 1454 1455 1456 1457 1458 1459 1460 1461 1462 1463 1464 1465 1466 1467 1468 1469 1470 1471 1472 1473 1474 1475 1476 1477 1478 1479 1480 1481 1482 1483 1484 1485 1486 1487 1488 1489 1490 1491 1492 1493 1494 1495 1496 1497 1498 1499 1500 1501 1502 1503 1504 1505 1506 1507 1508 1509 1510 1511 1512 1513 1514 1515 1516 1517 1518 1519 1520 1521 1522 1523 1524 1525 1526 1527 1528 1529 1530 1531 1532 1533 1534 1535 1536 1537 1538 1539 1540 1541 1542 1543 1544 1545 1546 1547 1548 1549 1550 1551 1552 1553 1554 1555 1556 1557 1558 1559 1560 1561 1562 1563 1564 1565 1566 1567 1568 1569 1570 1571 1572 1573 1574 1575 1576 1577 1578 1579 1580 1581 1582 1583 1584 1585 1586 1587 1588 1589 1590 1591 1592 1593 1594 1595 1596 1597 1598 1599 1600 1601 1602 1603 1604 1605 1606 1607 1608 1609 1610 1611 1612 1613 1614 1615 1616 1617 1618 1619 1620 1621 1622 1623 1624 1625 1626 1627 1628 1629 1630 1631 1632 1633 1634 1635 1636 1637 1638 1639 1640 1641 1642 1643 1644 1645 1646 1647 1648 1649 1650 1651 1652 1653 1654 1655 1656 1657 1658 1659 1660 1661 1662 1663 1664 1665 1666 1667 1668 1669 1670 1671 1672 1673 1674 1675 1676 1677 1678 1679 1680 1681 1682 1683 1684 1685 1686 1687 1688 1689 1690 1691 1692 1693 1694 1695 1696 1697 1698 1699 1700 1701 1702 1703 1704 1705 1706 1707 1708 1709 1710 1711 1712 1713 1714 1715 1716 1717 1718 1719 1720 1721 1722 1723 1724 1725 1726 1727 1728 1729 1730 1731 1732 1733 1734 1735 1736 1737 1738 1739 1740 1741 1742 1743 1744 1745 1746 1747 1748 1749 1750 1751 1752 1753 1754 1755 1756 1757 1758 1759 1760 1761 1762 1763 1764 1765 1766 1767 1768 1769 1770 1771 1772 1773 1774 1775 1776 1777 1778 1779 1780 1781 1782 1783 1784 1785 1786 1787 1788 1789 1790 1791 1792 1793 1794 1795 1796 1797 1798 1799 1800 1801 1802 1803 1804 1805 1806 1807 1808 1809 1810 1811 1812 1813 1814 1815 1816 1817 1818 1819 1820 1821 1822 1823 1824 1825 1826 1827 1828 1829 1830 1831 1832 1833 1834 1835 1836 1837 1838 1839 1840 1841 1842 1843 1844 1845 1846 1847 1848 1849 1850 1851 1852 1853 1854 1855 1856 1857 1858 1859 1860 1861 1862 1863 1864 1865 1866 1867 1868 1869 1870 1871 1872 1873 1874 1875 1876 1877 1878 1879 1880 1881 1882 1883 1884 1885 1886 1887 1888 1889 1890 1891 1892 1893 1894 1895 1896 1897 1898 1899 1900 1901 1902 1903 1904 1905 1906 1907 1908 1909 1910 1911 1912 1913 1914 1915 1916 1917 1918 1919 1920 1921 1922 1923 1924 1925 1926 1927 1928 1929 1930 1931 1932 1933 1934 1935 1936 1937 1938 1939 1940 1941 1942 1943 1944 1945 1946 1947 1948 1949 1950 1951 1952 1953 1954 1955 1956 1957 1958 1959 1960 1961 1962 1963 1964 1965 1966 1967 1968 1969 1970 1971 1972 1973 1974 1975 1976 1977 1978 1979 1980 1981 1982 1983 1984 1985 1986 1987 1988 1989 1990 1991 1992 1993 1994 1995 1996 1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019 2020 2021 2022 2023 2024 2025 2026 2027 2028 2029 2030 2031 2032 2033 2034 2035 2036 2037 2038 2039 2040 2041 2042 2043 2044 2045 2046 2047 2048 2049 2050 2051 2052 2053 2054 2055 2056 2057 2058 2059 2060 2061 2062 2063 2064 2065 2066 2067 2068 2069 2070 2071 2072 2073 2074 2075 2076 2077 2078 2079 2080 2081 2082 2083 2084 2085 2086 2087 2088 2089 2090 2091 2092 2093 2094 2095 2096 2097 2098 2099 2100 2101 2102 2103 2104 2105 2106 2107 2108 2109 2110 2111 2112 2113 2114 2115 2116 2117 2118 2119 2120 2121 2122 2123 2124 2125 2126 2127 2128 2129 2130 2131 2132 2133 2134 2135 2136 2137 2138 2139 2140 2141 2142 2143 2144 2145 2146 2147 2148 2149 2150 2151 2152 2153 2154 2155 2156 2157 2158 2159 2160 2161 2162 2163 2164 2165 2166 2167 2168 2169 2170 2171 2172 2173 2174 2175 2176 2177 2178 2179 2180 2181 2182 2183 2184 2185 2186 2187 2188 2189 2190 2191 2192 2193 2194 2195 2196 2197 2198 2199 2200 2201 2202 2203 2204 2205 2206 2207 2208 2209 2210 2211 2212 2213 2214 2215 2216 2217 2218 2219 2220 2221 2222 2223 2224 2225 2226 2227 2228 2229 2230 2231 2232 2233 2234 2235 2236 2237 2238 2239 2240 2241 2242 2243 2244 2245 2246 2247 2248 2249 2250 2251 2252 2253 2254 2255 2256 2257 2258 2259 2260 2261 2262 2263 2264 2265 2266 2267 2268 2269 2270 2271 2272 2273 2274 2275 2276 2277 2278 2279 2280 2281 2282 2283 2284 2285 2286 2287 2288 2289 2290 2291 2292 2293 2294 2295 2296 2297 2298 2299 2300 2301 2302 2303 2304 2305



Project Design Drawing Notes

1. Drawings issued are for planning application purposes only.

2. Copyright: all rights reserved. No part thereof may be copied or reproduced partially or wholly in any form whatsoever without the prior written consent of McCarthy Keville O'Sullivan Ltd.

3. The use of or reliance upon this drawing shall be deemed to be a warranty by the author, and the author shall be responsible for taking and checking any and all dimensions and levels that relate to the works.

4. The use of or reliance upon this drawing shall be deemed to be a warranty by the author, and the author shall be responsible for taking and checking any and all dimensions and levels that relate to the works.

5. The use of or reliance upon this drawing shall be deemed to be a warranty by the author, and the author shall be responsible for taking and checking any and all dimensions and levels that relate to the works.

6. The use of or reliance upon this drawing shall be deemed to be a warranty by the author, and the author shall be responsible for taking and checking any and all dimensions and levels that relate to the works.

7. The use of or reliance upon this drawing shall be deemed to be a warranty by the author, and the author shall be responsible for taking and checking any and all dimensions and levels that relate to the works.

8. Final levels may vary depending on local ground conditions.

Drawing Legend

- Proposed Dunmough & Lavelle Wind Farm Underground Grid Connection (PII Ref: 17/2545/ABP Ref: P.DOE 248796)
- Route of Meenbog Wind Farm
- Independent Grid Connection Chasing
- Culvert Crossing
- Joint Bay




Ordnance Survey Ireland Licence No. AR0021817 © Ordnance Survey Ireland/Government of Ireland

**Grid Connection Layout
Plan Sheet 3 of 5**

DRAWING TITLE	
Meenbog Wind Farm, Co. Donegal	
PROJECT TITLE	
Joseph O'Brien	
PROJECT NO.	
160502	
DRAWING NO.	
0502 - D	
SCALE	
1:2,500 @A1	
DATE	
20.12.2018	



McCarthy Keville O'Sullivan Ltd.
Planning & Environmental Consultants
Block 1, Financial Services Centre,
Moynagh Park Road,
Galway, Ireland.
email: info@cmk-os.com
Tel: +353 91 729611
Fax: +353 91 771279

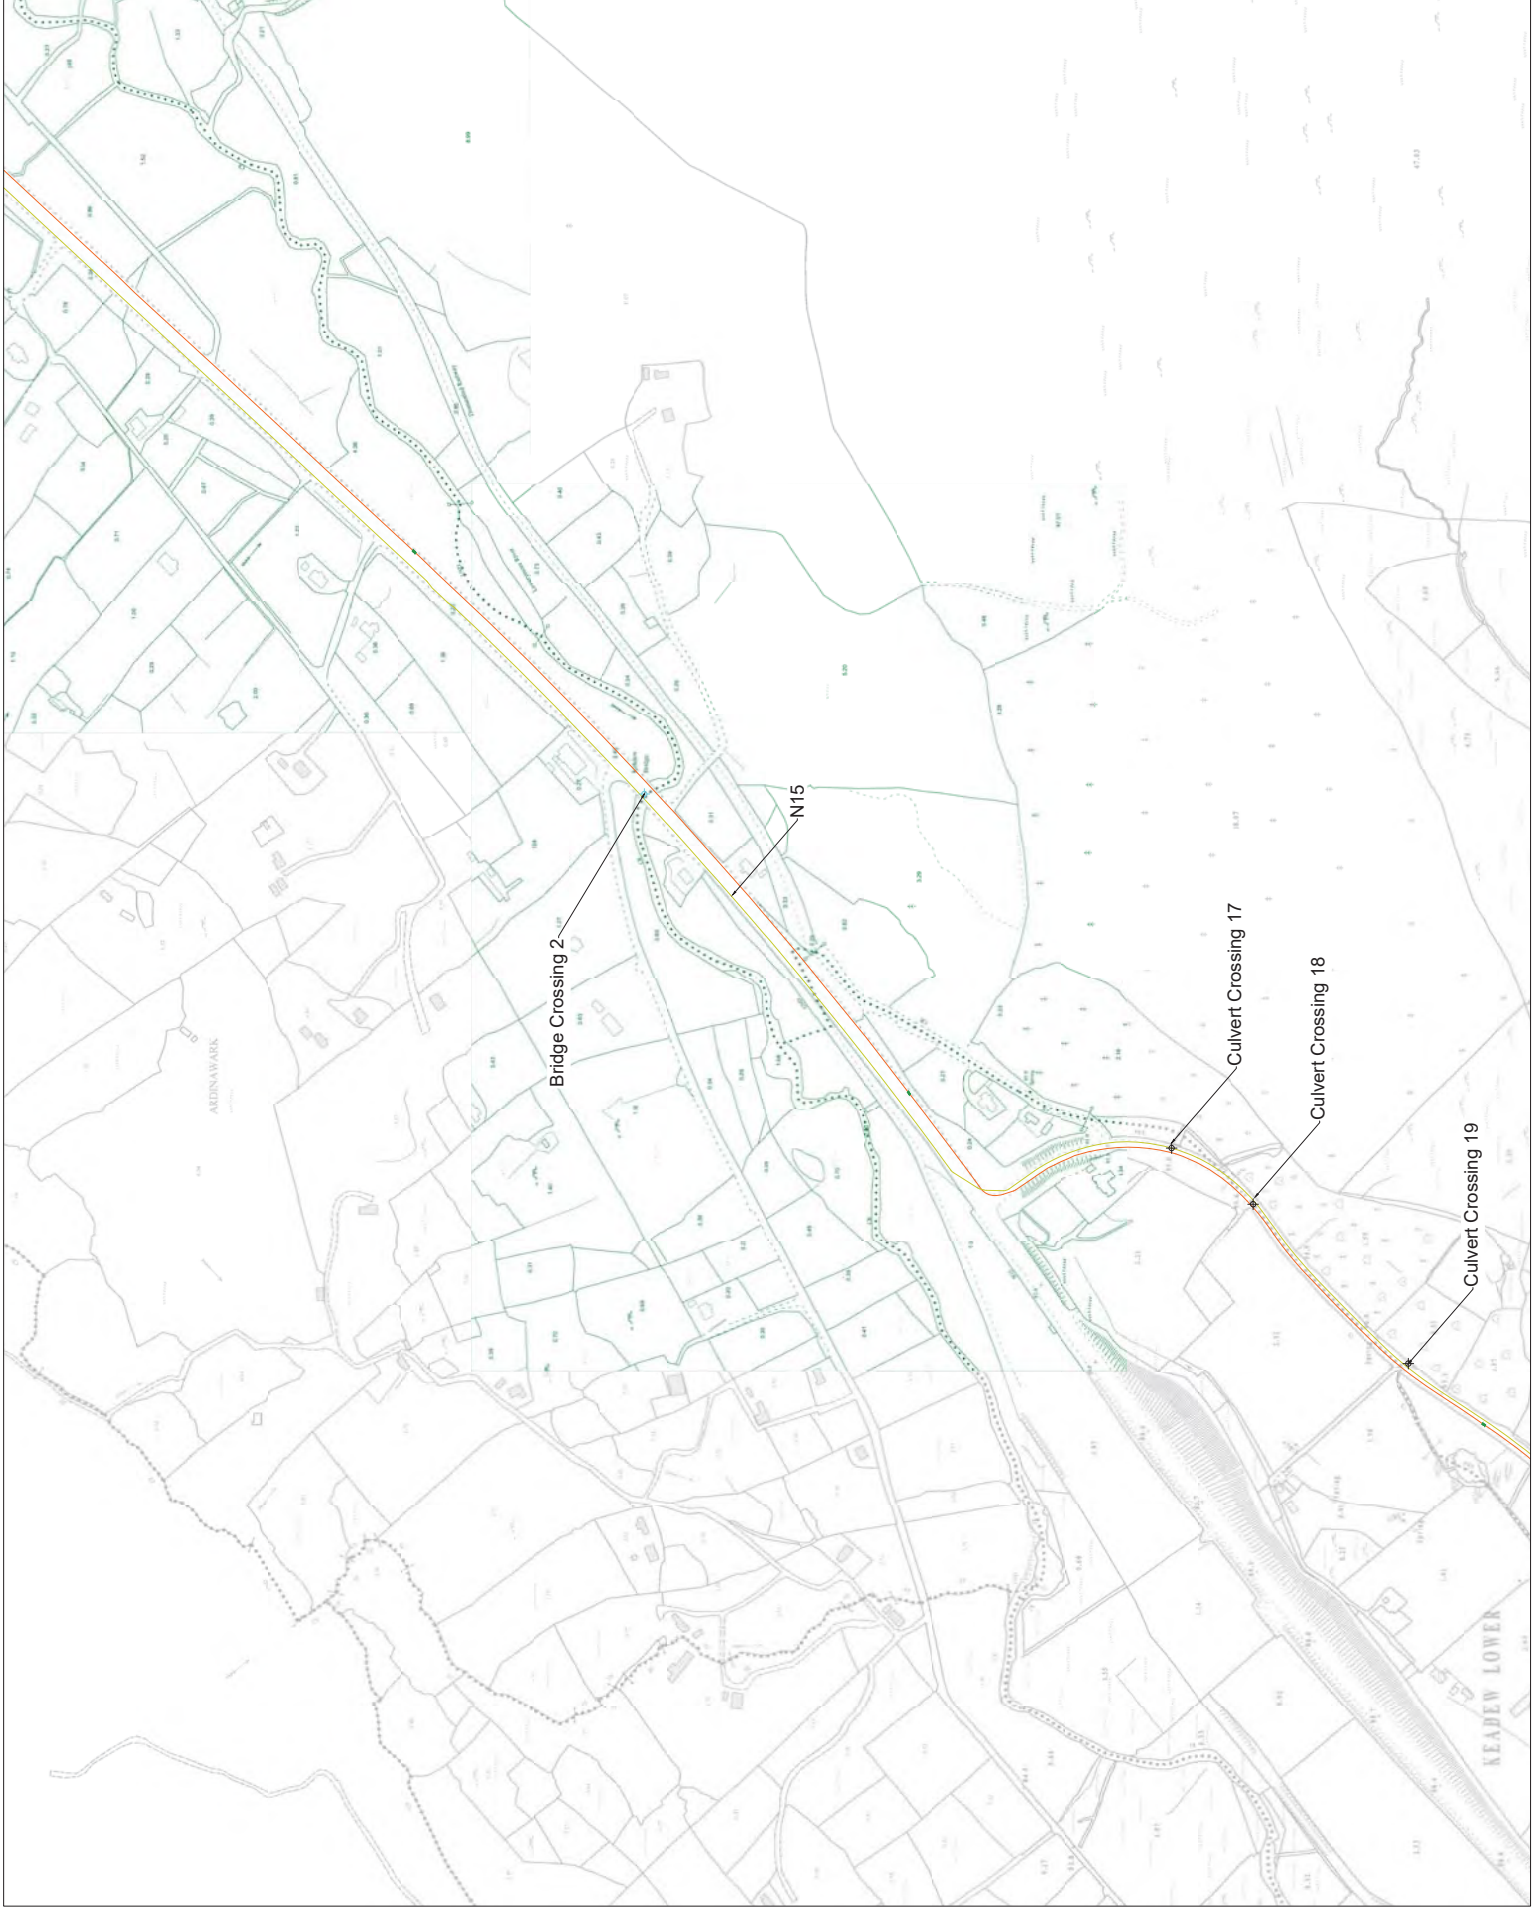

Project Design Drawing Notes

Drawings issued are for planning application purposes only. They are not to be used for construction purposes.

2. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior written permission of McCarthy Keville O'Sullivan Ltd. Any use of this drawing for any other purpose without the prior written permission of McCarthy Keville O'Sullivan Ltd. shall be at the user's risk and the user shall be liable for any and all consequences thereof.

3. The use of or reliance upon this drawing shall be deemed to be the user's responsibility and the user shall be deemed to be the copyright holder to the use or reliance upon this drawing.

4. Final levels may vary depending on local ground conditions.

Drawing Legend

- Proposed Drummabough & Leneela Wind Farm Underground Grid Connection Cable (Ref. Ref. 17/56343 ABP Ref. RLOE 248796)
- Route of Meerbog Wind Farm Independent Grid Connection Cabling
- Culvert Crossing
- Bridge Crossing
- Joint Bay



DRAWING TITLE
Grid Connection Layout
Plan Sheet 4 of 5

PROJECT TITLE
Meerbog Wind Farm, Co. Donegal

DRAWN BY
Joseph O'Brien

CHECKED BY
Michael Watson


PROJECT NO.
160502

UNIVERSITY
0502 - E

SCALE
1:2,500 @ A1

DATE
20.12.2018

CUSTOMER
McCarthy Keville O'Sullivan Ltd.
Planning & Environmental Consultants
Block 1, Financial Services Centre,
Monaghan Road,
Galway, Ireland.
email: info@coarthykes.ie
tel: +353 91 735611
fax: +353 91 771279

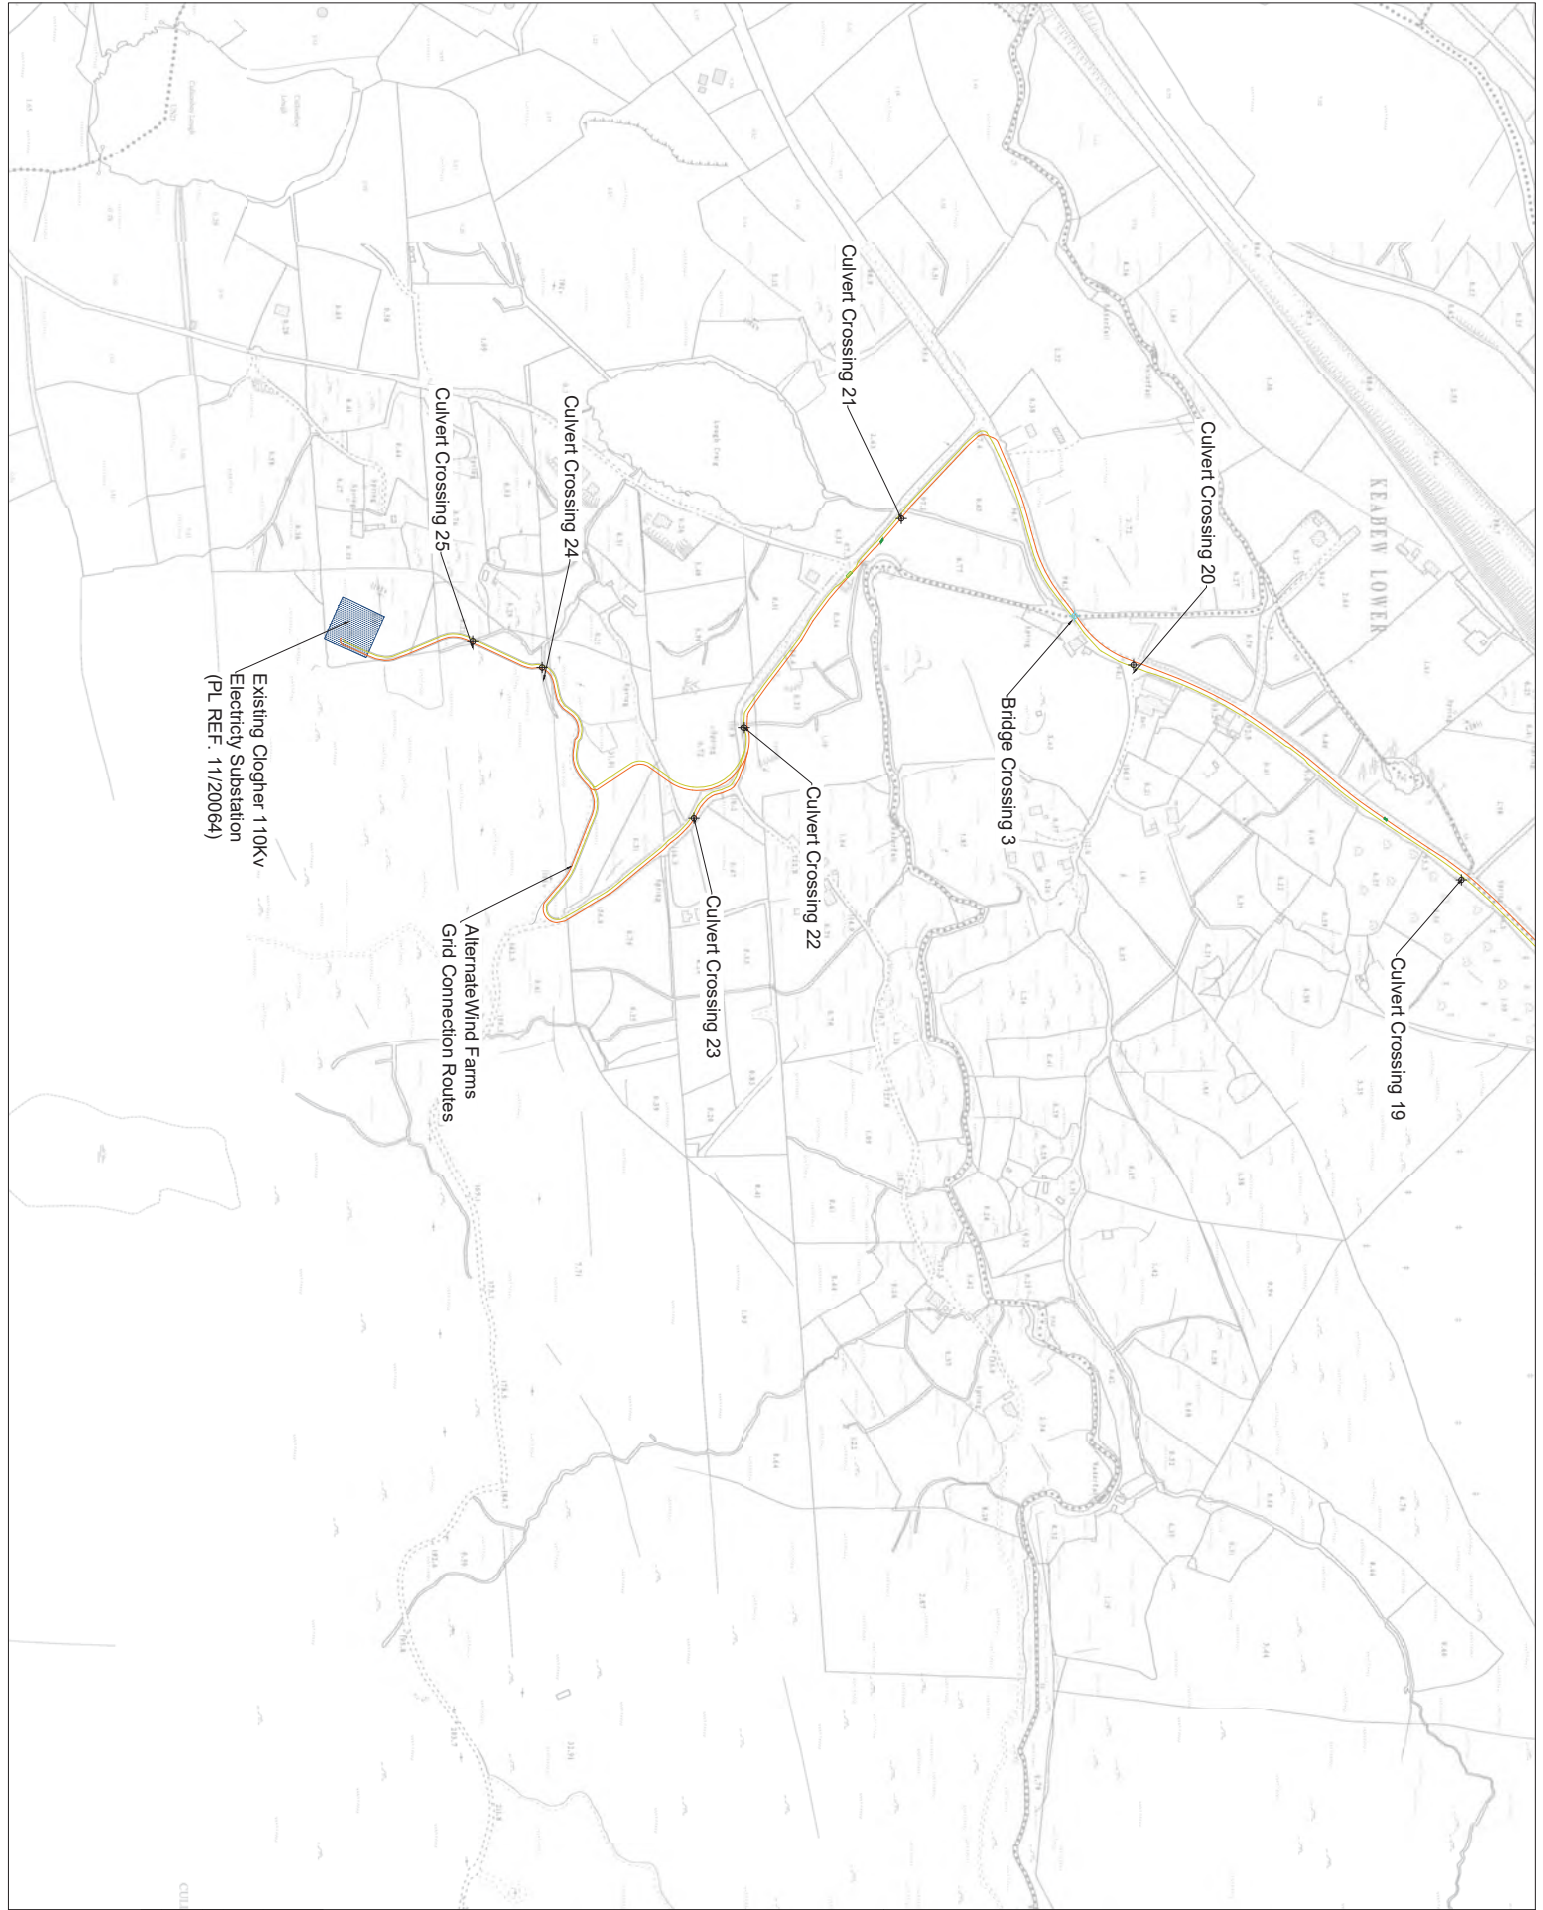

Printed Design Drawing Notes

1. Drawings issued are for planning application purposes only.

2. Drawings are not to be used for construction purposes.

3. Copyright, all rights reserved. No part thereof may be copied or reproduced partially or wholly in any form whatsoever without the prior consent of the copyright owner McCarthy Keville O'Sullivan Ltd.

4. The use of the copyright owner McCarthy Keville O'Sullivan Ltd. should be taken of this drawing. All dimensions in millimetres unless otherwise stated.

5. The use of the copyright owner McCarthy Keville O'Sullivan Ltd. should be taken of this drawing. All dimensions in millimetres unless otherwise stated.

6. The use of the copyright owner McCarthy Keville O'Sullivan Ltd. should be taken of this drawing. All dimensions in millimetres unless otherwise stated.

7. The use of the copyright owner McCarthy Keville O'Sullivan Ltd. should be taken of this drawing. All dimensions in millimetres unless otherwise stated.

8. Final levels may vary depending on local ground conditions.

Proposed Dunmough & Lavelle Wind Farm Underground Grid Connection (PL Ref: 11/20054) ABP Ref: R.05E.248(796)

Route of Meenbog Wind Farm Independent Grid Connection Chasing

Culvert Crossing

Bridge Crossing

Joint Bay

Drawing Legend

- Proposed Dunmough & Lavelle Wind Farm Underground Grid Connection (PL Ref: 11/20054) ABP Ref: R.05E.248(796)
- Route of Meenbog Wind Farm Independent Grid Connection Chasing
- Culvert Crossing
- Bridge Crossing
- Joint Bay



Grid Connection Layout Plan Sheet 5 of 5

DRAWING TITLE	
Meenbog Wind Farm, Co. Donegal	
PROJECT TITLE	
Meenbog Wind Farm, Co. Donegal	
DRAWN BY	
Joseph O'Brien	
CHECKED BY	
Michael Watson	
PROJECT NO.	
160502	
DATE	
20.12.2018	
SCALE	
1:2,500 @A1	



McCarthy Keville O'Sullivan
Planning & Environmental Consultants
Block 1, Financial Services Centre,
Moynagh Road,
Galway, Ireland.
email: info@mcCarthyKevilleO'Sullivan.ie
Tel: +353 91 729611
Fax: +353 91 771279

Appendix 2

Schedule of Works Operation Record

Works item no.	Description	Estimated Duration of the works	Risk Schedule 1:very high risk Schedule 2:high risk Schedule 3:intermediate risk	Pre-commencement Triggers all four triggers should be met				Works Abandonment Triggers If any four triggers are met			
				Trigger 1	Trigger 2	Trigger 3	Trigger 4	Trigger 1	Trigger 2	Trigger 3	Trigger 4
1	Enabling works including felling, site compound establishment welfare facilities, site office and fencing	2 months	Schedule 2	Drainage treatment infrastructure installed prior to works commencing And in good working order	River/ watercourse turbidity	Turbidity measuring sonde installed prior to works commencing and operating correctly	Weather forecast: (a) during the planned works period (b) observed on site	Damage to silt fence/other drainage measure or drainage point close to capacity	River/ watercourse turbidity	Alarm notification from sonde during the works activity. Immediate investigation	Weather forecast: (a) during the planned works period (b) observed on site
				Drainage measures to be installed as per EIS & drainage management plan	Turbidity at baseline levels	Determined by the proximity of the planned sonde location to the works and if readings will be of benefit i.e. if sonde is upstream of the works.	Schedule 2 rainfall figures (see below) utilising reliable forecasting source	Works cease and emergency response procedure activated including the use and installation of additional pumping equipment, sediments, siltbags and silt fencing	Turbidity 20% above baseline conditions or > 15ntu – subject to baseline data analysis	Works cease and investigation conducted.	Schedule 2 rainfall figures (see below)
2	Borrow pit establishment. Preliminary enabling works and rock excavation operations	6 months	Schedule 1	Drainage measures to be installed as per EIS & drainage management plan	Turbidity at baseline levels	Sonde must be operational with alarm and data analysed before works commence	Schedule 1 rainfall figures (see below) utilising reliable forecasting source	Works cease and emergency response procedure activated including the use and installation of additional pumping equipment, sediments, siltbags and silt fencing	Turbidity 20% above baseline conditions or > 15ntu – subject to baseline data analysis	Works cease and investigation conducted.	Schedule 1 rainfall figures (see below)

Works item no.	Description	Estimated Duration of the works	Risk Schedule 1:very high risk Schedule 2:high risk Schedule 3:intermediate risk	Pre-commencement Triggers all four triggers should be met				Works Abandonment Triggers If any four triggers are met			
				Trigger 1	Trigger 2	Trigger 3	Trigger 4	Trigger 1	Trigger 2	Trigger 3	Trigger 4
				Drainage treatment infrastructure installed prior to works commencing And in good working order	River/ watercourse turbidity	Turbidity measuring sonde installed prior to works commencing and operating correctly	Weather forecast: (a) during the planned works period (b) observed on site	Damage to silt fence/ other drainage measure or drainage point close to capacity	River/ watercourse turbidity	Alarm notification from sonde during the works activity. Immediate investigation	Weather forecast: (a) during the planned works period (b) observed on site
3	Site Roads (Stage 1). Excavate new roads, upgrade/widen existing	3-4 months	Schedule 1	Drainage measures to be installed as per EIS & drainage management plan	Turbidity at baseline levels	Sondes in-situ and operational	Schedule 1 rainfall figures (see below) utilising reliable forecasting source	Works cease and emergency response procedure activated including the use and installation of additional pumping equipment, sedimats, siltbags and silt fencing	Turbidity 20% above baseline conditions or >15ntu – subject to baseline data analysis	Works cease and investigation conducted.	Schedule 1 rainfall figures (see below)
4	Turbine foundation excavation and installation	6 months	Schedule 1	Drainage measures to be installed as per EIS & drainage management plan	Turbidity at baseline levels	Sondes in-situ and operational	Schedule 1 rainfall figures (see below) utilising reliable forecasting source	Works cease and emergency response procedure activated including the use and installation of additional pumping equipment, sedimats, siltbags and silt fencing	Turbidity 20% above baseline conditions or >15ntu – subject to baseline data analysis	Works cease and investigation conducted.	Schedule 1 rainfall figures (see below)

Works item no.	Description	Estimated Duration of the works	Risk Schedule 1:very high risk Schedule 2:high risk Schedule 3:intermediate risk	Pre-commencement Triggers all four triggers should be met				Works Abandonment Triggers If any four triggers are met			
				Trigger 1	Trigger 2	Trigger 3	Trigger 4	Trigger 1	Trigger 2	Trigger 3	Trigger 4
				Drainage treatment infrastructure installed prior to works commencing And in good working order	River/ watercourse turbidity	Turbidity measuring sonde installed prior to works commencing and operating correctly	Weather forecast: (a) during the planned works period (b) observed on site	Damage to silt fence/other drainage measure or drainage point close to capacity	River/ watercourse turbidity	Alarm notification from sonde during the works activity. Immediate investigation	Weather forecast: (a) during the planned works period (b) observed on site
5	Substation construction and connection to the grid	6 months	Schedule 2	Drainage measures to be installed as per EIS & drainage management plan	Turbidity at baseline levels	Sondes in-situ and operational	Schedule 2 rainfall figures (see below) utilising reliable forecasting source	Works cease and emergency response procedure activated including the use and installation of additional pumping equipment, sediments, siltbags and silt fencing	Turbidity 20% above baseline conditions or > 15ntu – subject to baseline data analysis	Works cease and investigation conducted.	Schedule 2 rainfall figures (see below)
6	Duct installation between turbines and substation and cabling	4 months	Schedule 1	Drainage measures to be installed as per EIS & drainage management plan	Turbidity at baseline levels	Sondes in-situ and operational	Schedule 1 rainfall figures (see below) utilising reliable forecasting source	Works cease and emergency response procedure activated including the use and installation of additional pumping equipment, sediments, siltbags and silt fencing	Turbidity 20% above baseline conditions or > 15ntu – subject to baseline data analysis	Works cease and investigation conducted.	Schedule 1 rainfall figures (see below)

Works item no.	Description	Estimated Duration of the works	Risk Schedule 1:very high risk Schedule 2:high risk Schedule 3:intermediate risk	Pre-commencement Triggers all four triggers should be met				Works Abandonment Triggers If any four triggers are met			
				Trigger 1	Trigger 2	Trigger 3	Trigger 4	Trigger 1	Trigger 2	Trigger 3	Trigger 4
				Drainage treatment infrastructure installed prior to works commencing And in good working order	River/ watercourse turbidity	Turbidity measuring sonde installed prior to works commencing and operating correctly	Weather forecast: (a) during the planned works period (b) observed on site	Damage to silt fence/ other drainage measure or drainage point close to capacity	River/ watercourse turbidity	Alarm notification from sonde during the works activity. Immediate investigation	Weather forecast: (a) during the planned works period (b) observed on site
7	Site Roads (Stage 2). Further upgrade/maintenance and final surfacing prior to turbine delivery	4 months	Schedule 1	Drainage measures to be installed as per EIS & drainage management plan	Turbidity at baseline levels	Sondes in-situ and operational	Schedule 1 rainfall figures (see below) utilising reliable forecasting source	Works cease and emergency response procedure activated including the use and installation of additional pumping equipment, sedimats, siltbags and silt fencing	Turbidity 20% above baseline conditions or >15ntu – subject to baseline data analysis	Works cease and investigation conducted.	Schedule 1 rainfall figures (see below)
8	Crane delivery and mobilisation	1 month	Schedule 3	Activity not dependent on drainage treatment infrastructure	Turbidity at baseline levels	Sondes in-situ and operational	Schedule 3 rainfall figures (see below) utilising reliable forecasting source	Activity not dependent on drainage treatment infrastructure	Activity not anticipated to effect turbidity	Activity not dependent on sonde data	Activity not weather dependent
9	Turbine delivery	3 months	Schedule 3	Activity not dependent on drainage treatment infrastructure	Activity not anticipated to effect turbidity	Activity not dependent on sonde data	Activity not weather dependent	Activity not dependent on drainage treatment infrastructure	Activity not anticipated to effect turbidity	Activity not dependent on sonde data	Activity not weather dependent

Works item no.	Description	Estimated Duration of the works	Risk Schedule 1:very high risk Schedule 2:high risk Schedule 3:Intermediate risk	Pre-commencement Triggers all four triggers should be met				Works Abandonment Triggers If any four triggers are met			
				Trigger 1	Trigger 2	Trigger 3	Trigger 4	Trigger 1	Trigger 2	Trigger 3	Trigger 4
10	Turbine erection	2-3 months		Drainage treatment infrastructure installed prior to works commencing And in good working order	River/ watercourse turbidity	Turbidity measuring sonde installed prior to works commencing and operating correctly	Weather forecast: (a) during the planned works period (b) observed on site	Damage to silt fence/other drainage measure or drainage point close to capacity	River/ watercourse turbidity	Alarm notification from sonde during the works activity. Immediate investigation	Weather forecast: (a) during the planned works period (b) observed on site
11	Commissioning and testing of operational turbines	2 months	Schedule 3	Activity not dependent on drainage treatment infrastructure	Activity not anticipated to effect turbidity	Activity not dependent on sonde data	Activity not determined by rainfall	Activity not dependent on drainage treatment infrastructure	Activity not anticipated to effect turbidity	Activity not dependent on sonde data	Activity not weather dependent
			Schedule 3	Activity not dependent on drainage treatment infrastructure	Activity not anticipated to effect turbidity	Activity not dependent on sonde data	Activity not weather dependent	Activity not dependent on drainage treatment infrastructure	Activity not anticipated to effect turbidity	Activity not dependent on sonde data	Activity not weather dependent

Trigger 4: activities should not begin or should cease if the following rainfall amounts are forecasted:	
Schedule 1 – Very high-risk activities	>10 mm/hr (i.e. high intensity local rainfall events)
	>25 mm in a 24-hour period (heavy frontal rainfall lasting most of the day); or,
	> half monthly average rainfall in any 7 days.
	No overland flow or pathway for water movement Conditions on the ground match the forecast
Schedule 2 – High risk activities	>10 mm/hr (i.e. high intensity local rainfall events)
	>25 mm in a 24-hour period (heavy frontal rainfall lasting most of the day); or,
	> half monthly average rainfall in any 7 days.
	Conditions on the ground match the forecast
Schedule 3 – Intermediate risk	>10 mm/hr (i.e. high intensity local rainfall events)
	>25 mm in a 24-hour period (heavy frontal rainfall lasting most of the day); or,
	> half monthly average rainfall in any 7 days.
	Conditions on the ground match the forecast

Appendix 3

Wind Farm Site Culvert Assessment

Crossing ID	Location Description	Eastings	Northings	Culvert Type	Culvert Dimensions (m)			Channel Dimensions			Water Depth (m)	Catchment Area (km2)	Existing Culvert Capacity (m3/s)	100 Year Flow (m3/s)	Hydraulic Status of Existing Crossing	Minimum Pipe Culvert Diameter Required (mm)
					Diameter	Width	Height	Bottom Width	Top Width	Depth						
EC1	Road between T15 and T17	208149	387078	Pipe	600	-	-	0.7	1	1.5	0.2	0.083	0.54	0.171	Adequate	-
EC2	Road between T15 and T17	208130	387042	Pipe	400	-	-	1.5	2	1.5	0.15	0.083	0.165	0.171	Upgrade Required	900
EC3	Road between T15 and T17	208038	387003	Pipe	600	-	-	2	3	2	0.2	0.083	0.54	0.171	Adequate	-
EC4	Southwest of Borrow Pit 1	207640	386362	Pipe	600	-	-	1.5	1.5	0.7	0.3	0.448	0.54	0.767	Upgrade Required	900
EC5	Southwest of proposed met mast	205684	385277	Box	-	2.5	1.5	2.5	2.5	1.2	0.2	2.58	26.005	3.644	Adequate	-
EC6	Southwest of proposed met mast	205791	385190	Pipe	900	-	-	1	1	1.3	0.1	0.9	1.66	1.427	Adequate	-
EC7	Southwest of T10	207012	385739	Pipe	500	-	-	0.5	1	1.5	0.2	0.16	0.32	0.307	Adequate	-
EC8	South of T10	206842	385408	Pipe	400	-	-	-	1.5	1	0.15	0.15	0.165	0.290	Upgrade Required	900
EC9	Southwest of T12	207461	385985	Pipe	900	-	-	0.5	1	1	0.2	0.2	1.66	0.374	Adequate	-
EC10	Southeast of T12	207708	385973	Pipe	900	-	-	1.5	1.5	1	0.1	0.189	1.66	0.356	Adequate	-
EC11	East of T8	207843	385627	Pipe	600	-	-	0.5	0.5	1	0.25	0.136	0.54	0.266	Adequate	-
EC12	Northwest of T14	206593	384481	Pipe	600	-	-	0.5	1.5	1	0.15	0.192	0.54	0.361	Adequate	-
EC13	South of substation	205692	385486	Pipe	600	-	-	1.5	2	2.5	0.1	0.1	0.54	0.202	Adequate	-
EC14	Just north of proposed substation	205314	386479	Pipe	750	-	-	1.5	1.5	1	0.2	0.3	1	0.537	Adequate	-
EC15	Southwest of Borrow Pit 1	207480	386240	n/a	-	-	-	1	1.2	0.7	0.25	0.24	-	0.440	Not determined	900
EC16	Furthest west along the site entrance road	205040	387030	-	-	-	-	-	-	-	-	-	-	-	Not determined	-
EC17	South of T10	206842	385408	Pipe	400	-	-	0.5	1.5	1	0.15	0.15	9.2	0.000	Upgrade Required	900
EC18	West of T10	206135	386006	Pipe	300	-	-	1	1.5	1	0.1	0.164	0.066	0.314	Upgrade Required	900
EC19	North of T14	206804	386851	Pipe	900	-	-	1.5	2	1.5	0.2	0.57	1.66	0.951	Adequate	-

Appendix 4

Traffic Management Plan

Note: Traffic Management Plan is included as Appendix 4-7 of this rEiAR.
