



APPENDIX 3-2

**Construction
Environmental
Management Plan**

Construction and Environmental Management Plan

Meenbog Wind Farm Development at
Meenbog & Adjacent Townlands, Co.
Donegal



Planning & Environmental Consultants

DOCUMENT DETAILS

Client: **Planree Ltd.**

Project title: **Meenbog Wind Farm**

Project Number: **160502**

Document Title: **Construction and Environmental Management Plan**

Doc. File Name: **CEMP F- 2019.02.01- 160502-b**

Prepared By: **McCarthy Keville O'Sullivan Ltd.**
Planning & Environmental Consultants
Block 1, G.F.S.C.
Moneenageisha Road, Galway



Document Issue:

Rev	Status	Issue Date	Document File Name	Author(s)	Approved By:
01	Draft	21/11/2017	CEMP D1-2017.11.21-160502	OC	MW
02	Final	13/12/2017	CEMP F-2017.12.13-160502	OC	MW
03	Draft	18/12/2018	CEMP D1-2018.12.18-160502-b	OC	MW
04	Final	01/02/2019	CEMP D1-2018.12.18-160502-b	OC	MW

Table of Contents

1	Introduction.....	1
1.1	Scope of Construction and Environmental Management Plan.....	1
2	Site and Project Details	3
2.1	Site Location and Description	3
2.2	Description of the Development	3
2.3	Targets and Objectives.....	4
2.4	Construction Methodologies Overview	5
2.4.1	Introduction	5
2.4.2	Overview of Proposed Construction Methodology.....	5
2.4.2.1	Temporary Construction Compound	5
2.4.2.2	Borrow Pit	6
2.4.2.3	Drainage System.....	7
2.4.2.4	Upgrade of Existing Roads	8
2.4.2.5	New Site Access Roads	8
2.4.2.6	Watercourse/Culvert Crossing on the Wind Farm Site	9
2.4.2.7	Crane Hardstands.....	11
2.4.2.8	Turbine and Anemometry Mast Foundations.....	11
2.4.2.9	Electricity Substation and Control Buildings	13
2.4.2.10	Cable Trenching	13
2.4.2.11	Grid Connection.....	14
2.4.2.11.1	Parallel Road Excavations inroad & in Grass margin.....	14
2.4.2.11.2	Existing Underground Services	16
2.4.2.11.3	Joint Bays	16
2.4.2.11.4	Watercourse/Culvert Crossing – Grid Connection Cable Route.....	17
2.4.2.11.5	General Construction Measures.....	20
2.4.2.12	Recreation and Amenity Areas	20
2.4.2.13	Decommissioning.....	20
3	Environmental Management	22
3.1	Introduction.....	22
3.2	Protecting Water Quality.....	22
3.2.1	Environmental Management in the Construction Phase	22
3.2.2	Site Drainage Design.....	22
3.2.3	Legislation and Best Practice Guidance	22
3.2.4	Site Drainage and Management	23
3.2.4.1	Preparative Site Drainage Management.....	23
3.2.4.2	Pre-emptive Site Drainage Management.....	24
3.2.4.3	Reactive Site Drainage.....	24
3.2.4.4	Operational Phase Drainage.....	24
3.3	Refuelling, Fuel and Hazardous Materials Storage.....	25
3.4	Cement Based Products Control Measures	25
3.5	Peat Stability Management	26
3.5.1	General Recommendations for Good Construction Practice.....	26
3.6	Traffic Management.....	27

3.6.1	Turbine and Materials Transport Route	27
3.7	Ecological Management.....	28
3.8	Dust Control.....	29
3.9	Noise Control	29
3.10	Invasive Species Management.....	30
3.10.1	General Best Practice Control Methods	30
3.10.2	Site Management.....	30
3.10.3	Establishing Good Site Hygiene	30
3.11	Waste Management	31
3.11.1	Legislation	31
3.11.2	Waste Management Hierarchy.....	31
3.11.3	Construction Phase Waste Management Plan	32
3.11.3.1	Description of the Works.....	32
3.11.3.2	Waste Arisings and Proposals for Minimisation, Reuse and Recycling of Construction Waste.....	33
3.11.3.3	Waste Arising from Construction Activities.....	33
3.11.3.4	Waste Arising from Decommissioning	34
3.11.4	Reuse	34
3.11.5	Recycling	34
3.11.6	Implementation	34
3.11.6.1	Roles and Responsibilities for Waste Management.....	34
3.11.6.2	Training.....	34
3.11.6.3	Record Keeping	35
3.11.7	Waste Management Plan Conclusion	35
4	Drainage Management Plan	36
4.1	Wind Farm Drainage	36
4.1.1	Introduction	36
4.1.2	Existing Drainage Features	36
4.1.3	Drainage Design Principles	37
4.1.4	Site Management & Pollution Prevention	37
4.1.5	Pre-Construction Drainage Management	38
4.1.6	Construction Phase Drainage Management Plan	39
4.1.6.1	Drainage Design	39
4.1.6.1.1	Interceptor Drains.....	39
4.1.6.1.2	Swales.....	40
4.1.6.1.3	Check Dams	41
4.1.6.1.4	Level Spreaders.....	41
4.1.6.1.5	Piped Slope Drains.....	42
4.1.6.1.6	Vegetation Filters.....	43
4.1.6.1.7	Settlement Ponds	43
4.1.6.1.8	Dewatering Silt Bags	44
4.1.6.1.9	Siltbuster.....	44
4.1.6.1.10	Culverts	45
4.1.6.1.11	Silt Fences.....	46
4.1.6.2	Construction Compound Drainage.....	47
4.1.6.3	Borrow Pit Drainage	47
4.1.6.4	Tree Felling Drainage Controls.....	48
4.1.6.5	Cable Trench Drainage	49
4.1.7	Drainage Maintenance	49
4.1.8	Operational Phase Drainage Management	50

5	Environmental Management Implementation	52
5.1	Roles and Responsibilities	52
5.1.1	Wind Farm Construction Manager/Site Supervisor	52
5.1.2	Site Environmental Clerk of Works	53
5.1.3	Project Ecologist	54
5.1.4	Project Hydrologist	54
5.1.5	Project Geotechnical Engineer / Geologist	54
5.2	Monitoring of Surface Water Quality	55
5.2.1	Pre-Construction Drainage Inspection and Monitoring	56
5.2.2	Construction Phase Drainage Inspection and Monitoring:	56
5.2.2.1	In-situ field monitoring:	57
5.2.2.2	Monthly Laboratory Analysis Sampling	57
5.2.2.3	Continuous Turbidity Monitoring	57
5.2.2.4	Monitoring Parameters	57
5.2.3	Surface Water Monitoring Reporting	58
5.2.4	Post-Construction Monitoring	58
5.3	Environmental Awareness and Training	58
5.3.1	Environmental Induction	58
5.3.2	Toolbox Talks	59
6	Emergency Response Plan	60
6.1	Emergency Response	60
6.1.1	Roles and Responsibilities	60
6.1.2	Initial Steps	61
6.1.3	Site Evacuation/Fire Drill	62
6.1.4	Excessive Peat Movement	62
6.1.5	Onset of Peat Slide	62
6.1.6	Spill Control Measures	63
6.2	Contacting the Emergency Services	64
6.2.1	Emergency Communications Procedure	64
6.2.2	Contact Details	64
6.2.3	Procedure for Personnel Tracking	65
6.3	Induction Checklist	65
7	Mitigation Proposals	66
8	Monitoring Proposals	83
9	Programme of Works	92
10	Compliance and Review	93
10.1	Site Inspections and Environmental Audits	93
10.2	Auditing	93
10.3	Environmental Compliance	93
10.4	Corrective Action Procedure	94
10.5	Construction Phase Plan Review	94

1 INTRODUCTION

This Construction and Environmental Management Plan (CEMP) has been developed by McCarthy Keville O' Sullivan Ltd. on behalf of Planree Ltd. The CEMP provides the environmental management framework to be adhered to during the pre-commencement, construction and operational phases of the development and it incorporates the mitigating principles to ensure that the work is carried out in a way that minimises the potential for any environmental impacts to occur. This CEMP has been prepared in conjunction with the Environmental Impact Assessment Report (EIAR), Natura Impact Statement (NIS) and the Condition Compliance Statement (CCS) of the permitted Meenbog Wind Farm.

This CEMP identifies the key planning and environmental considerations that must be adhered to and delivered during site construction and operation. This report is intended as a single, amalgamated document that can be used during the future phases of the project, as a single consolidated point of reference relating to all construction, environmental and drainage requirements for the planning authority, developer and contractors alike.

The CEMP has been prepared in accordance with the planning permission conditions set by An Bord Pleanála under ABP-300460-17 which relates to the development of Meenbog Wind Farm including junction accommodation works along the turbine delivery route and connection to the national grid

1.1 Scope of Construction and Environmental Management Plan

This report is presented as a guidance document for the construction phase of the Meenbog Wind Farm. It outlines clearly the mitigation measures and monitoring proposals that are required to be adhered to in order to construct the wind farm in an appropriate manner. The report is divided into ten sections, as outlined below.

Section 1 provides a brief introduction as to the scope of the report

Section 2 outlines the site and project details, detailing the targets and objectives of this plan along with providing an overview of anticipated construction methodologies that will be adopted throughout the project.

Section 3 sets out details of the environmental controls on site which looks at noise and dust controls. Site drainage measures, peat management and a waste management plan are also included in this section.

Section 4 sets out the development drainage management plan which provides details of the various drainage infrastructure that will be installed to manage and control the quality of surface water runoff from the site.

Section 5 sets out a fully detailed implementation plan for the environmental management of the project outlining the roles and responsibilities of the project team

Section 6 outlines the Emergency Response Plan to be adopted in the event of an emergency in terms of site health and safety and environmental protection

Section 7 consists of a summary table of all mitigation proposals to be adhered to during the implementation of the project, categorised into three separate headings, 1) pre-commencement measures; 2) construction-phase measures and 3) operational-phase measures.

Section 8 consists of a summary table of all monitoring requirements and proposals to be adhered to during the implementation of the project, categorised into three separate headings, 1) pre-commencement measures; 2) construction-phase measures and 3) operational-phase measures.

Section 9 sets out an anticipated programme for the timing of the works.

Section 10 outlines the proposals for reviewing compliance with the provisions of this report.

2 SITE AND PROJECT DETAILS

2.1 Site Location and Description

The site of the Permitted Development is located in the townlands of Meenbog and Croaghonagh and adjacent townlands associated with the underground electrical cabling, listed in Table 2.1, in County Donegal. The Permitted Development will comprise of the provision of a total of 19 No. wind turbines, with a maximum ground to top blade tip height of up to 156.5m and all associated infrastructure.

The wind farm site measures approximately 990 hectares or 2,446 acres. The Grid Reference co-ordinates for the approximate centre of the site are (E207,963 N385,970). The Permitted Development is located approximately eight kilometres south west of the towns of Ballybofey and Stranorlor and approximately 15 kilometres northwest of the town of Castlederg, Co. Tyrone.

The electrical connection from the Permitted Development to the national grid will be completed by underground cabling which will run within the public road corridor to the existing Clogher 110 kV Electricity Substation.

Table 2.1 Townlands containing infrastructure

Development Infrastructure	Townland
Current Wind Farm Site & Amenity Area Development	Meenbog
	Croaghonagh
	Cashelnavean
Grid Connection Route	
	Tawnawully Mountains
	Keadew Upper
	Friarbush
	Ardinawark
	Keadew Lower
	Cullionbuoy

2.2 Description of the Development

During the construction phase of the project, civil works will include constructing the reinforced concrete foundations; access road construction and upgrade of existing access roads; construction of temporary compounds; construction of substation; upgrading existing watercourse crossings, construction of underground cabling; and a permanent meteorological mast.

The design life of the project is expected to be 30 years.

The key components of the wind farm include the following:

- 19 no. Wind Turbines with a maximum blade tip height of 156.5 metres;
- 19 no. Hardstand Areas to facilitate cranes for turbine erection and to act as construction material storage compounds;
- 1 no. Permanent Meteorological Mast;

- 1 no. 110kV Electricity substation and control building with 2 no. control buildings with welfare facilities, associated electrical plant and equipment, security fencing and waste water holding tank;
- 110kV underground grid connection cabling;
- Upgrade of access junctions;
- Upgrade of existing tracks, roads and provision of new site access roads and hardstand areas;
- 3 no. borrow pits;
- 2 no. temporary construction compounds;
- Recreation and amenity works, including marked trails (upgrade of existing tracks and provision of new tracks), picnic, amenity and play areas, car parking and vehicular access;
- Site drainage
- Forestry felling
- Permanent signage;
- All associated site development and ancillary works

The permitted site layout showing individual elements of the development is shown in Figure 2.1 & 2.2 and in the Site Layout Drawings included in Appendix 1.

2.3 Targets and Objectives


In so far as they have been completed to date, or are to be further completed in future, the construction phase works are designed to approved standards, which include specified materials, standards, specifications and codes of practice. The design of the project has considered environmental issues and this is enhanced by the works proposals.

The key site targets are as follows;

- Adopt a sustainable approach to construction and, ensure sustainable sources for materials supply where possible;
- Keeping all watercourses free from obstruction and debris;
- Avoidance of any pollution incident or near miss as a result of working around or close to existing watercourses and having emergency measures in place;
- Correct fuel storage and refuelling procedures to be followed;
- Air and noise pollution prevention to be implemented;
- Construction Methods and designs will be altered where it is found there is an adverse effect on the environment;
- Good waste management and house-keeping to be implemented;
- Using recycled materials if possible, *e.g.* excavated stone, soil and subsoil material;
- Avoidance of vandalism;
- Monitoring of the works and any adverse effects that it may have on the environment and,
- Provide adequate environmental training and awareness for all project personnel.

The key site objectives are as follows;

- Keep impact of construction to a minimum on the local environment, watercourses and wildlife;
- Comply with all relevant water quality legislation;

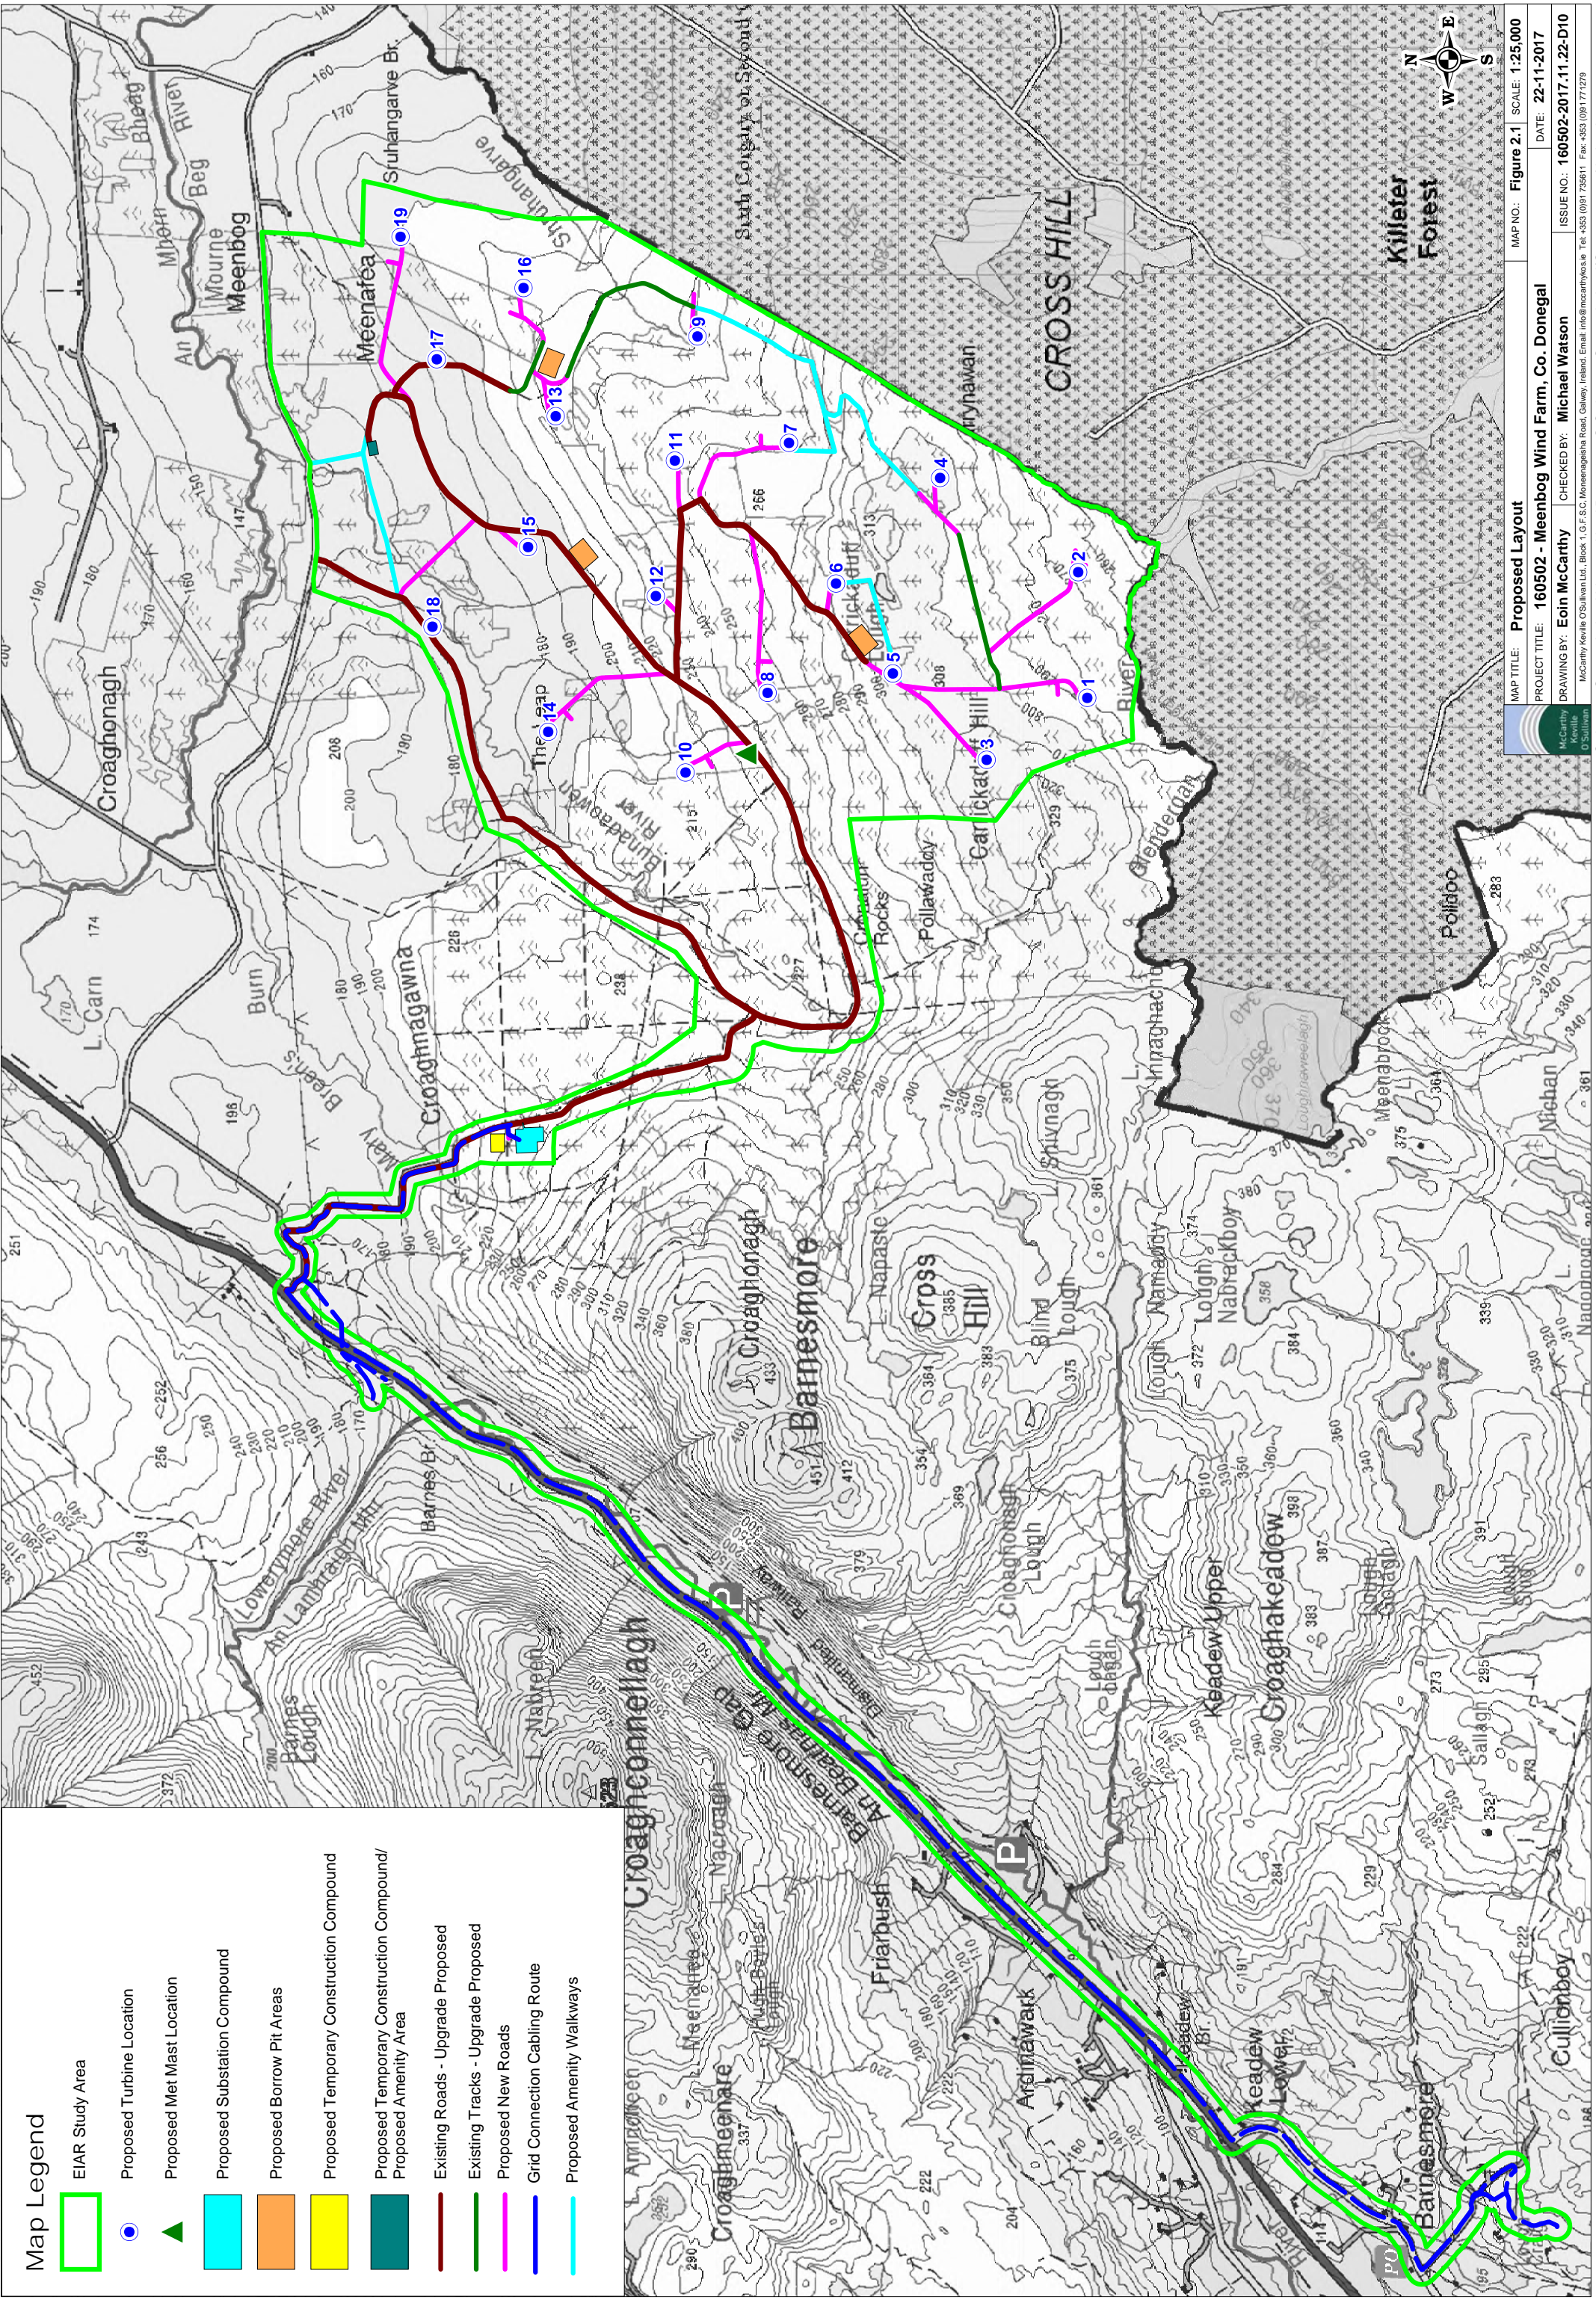

Map Legend






- EIA Study Area
- Proposed Turbine Location
- Proposed Met Mast Location
- Proposed Substation Compound
- Proposed Borrow Pit Areas
- Proposed Temporary Construction Compound
- Proposed Temporary Construction Compound/
Proposed Amenity Area
- Existing Roads - Upgrade Proposed
- Existing Tracks - Upgrade Proposed
- Proposed New Roads
- Grid Connection Cabling Route
- Proposed Amenity Walkways


McCarthy O'Sullivan Ltd.
 Block 1, G.F.S. Moreenaghaha Road, Galway, Ireland. Email: info@mcCarthyosullivan.ie Tel: +353 (0)91 738611 Fax: +353 (0)91 771279

PROJECT TITLE: Proposed Layout
CHECKED BY: Michael Watson
DRAWING BY: Eoin McCarthy
ISSUE NO.: 160502-2017.11.22-D10

MAP NO.: Figure 2.1 **SCALE:** 1:25,000
DATE: 22-11-2017

Map Legend

-  EIS Study Area
-  Proposed Meenbog Wind Farm Electricity Substation
-  Existing Clogher 110kV Substation Location
-  Bridge Crossing Locations
-  Meenbog Wind Farm to Clogher Substation Cabling Route

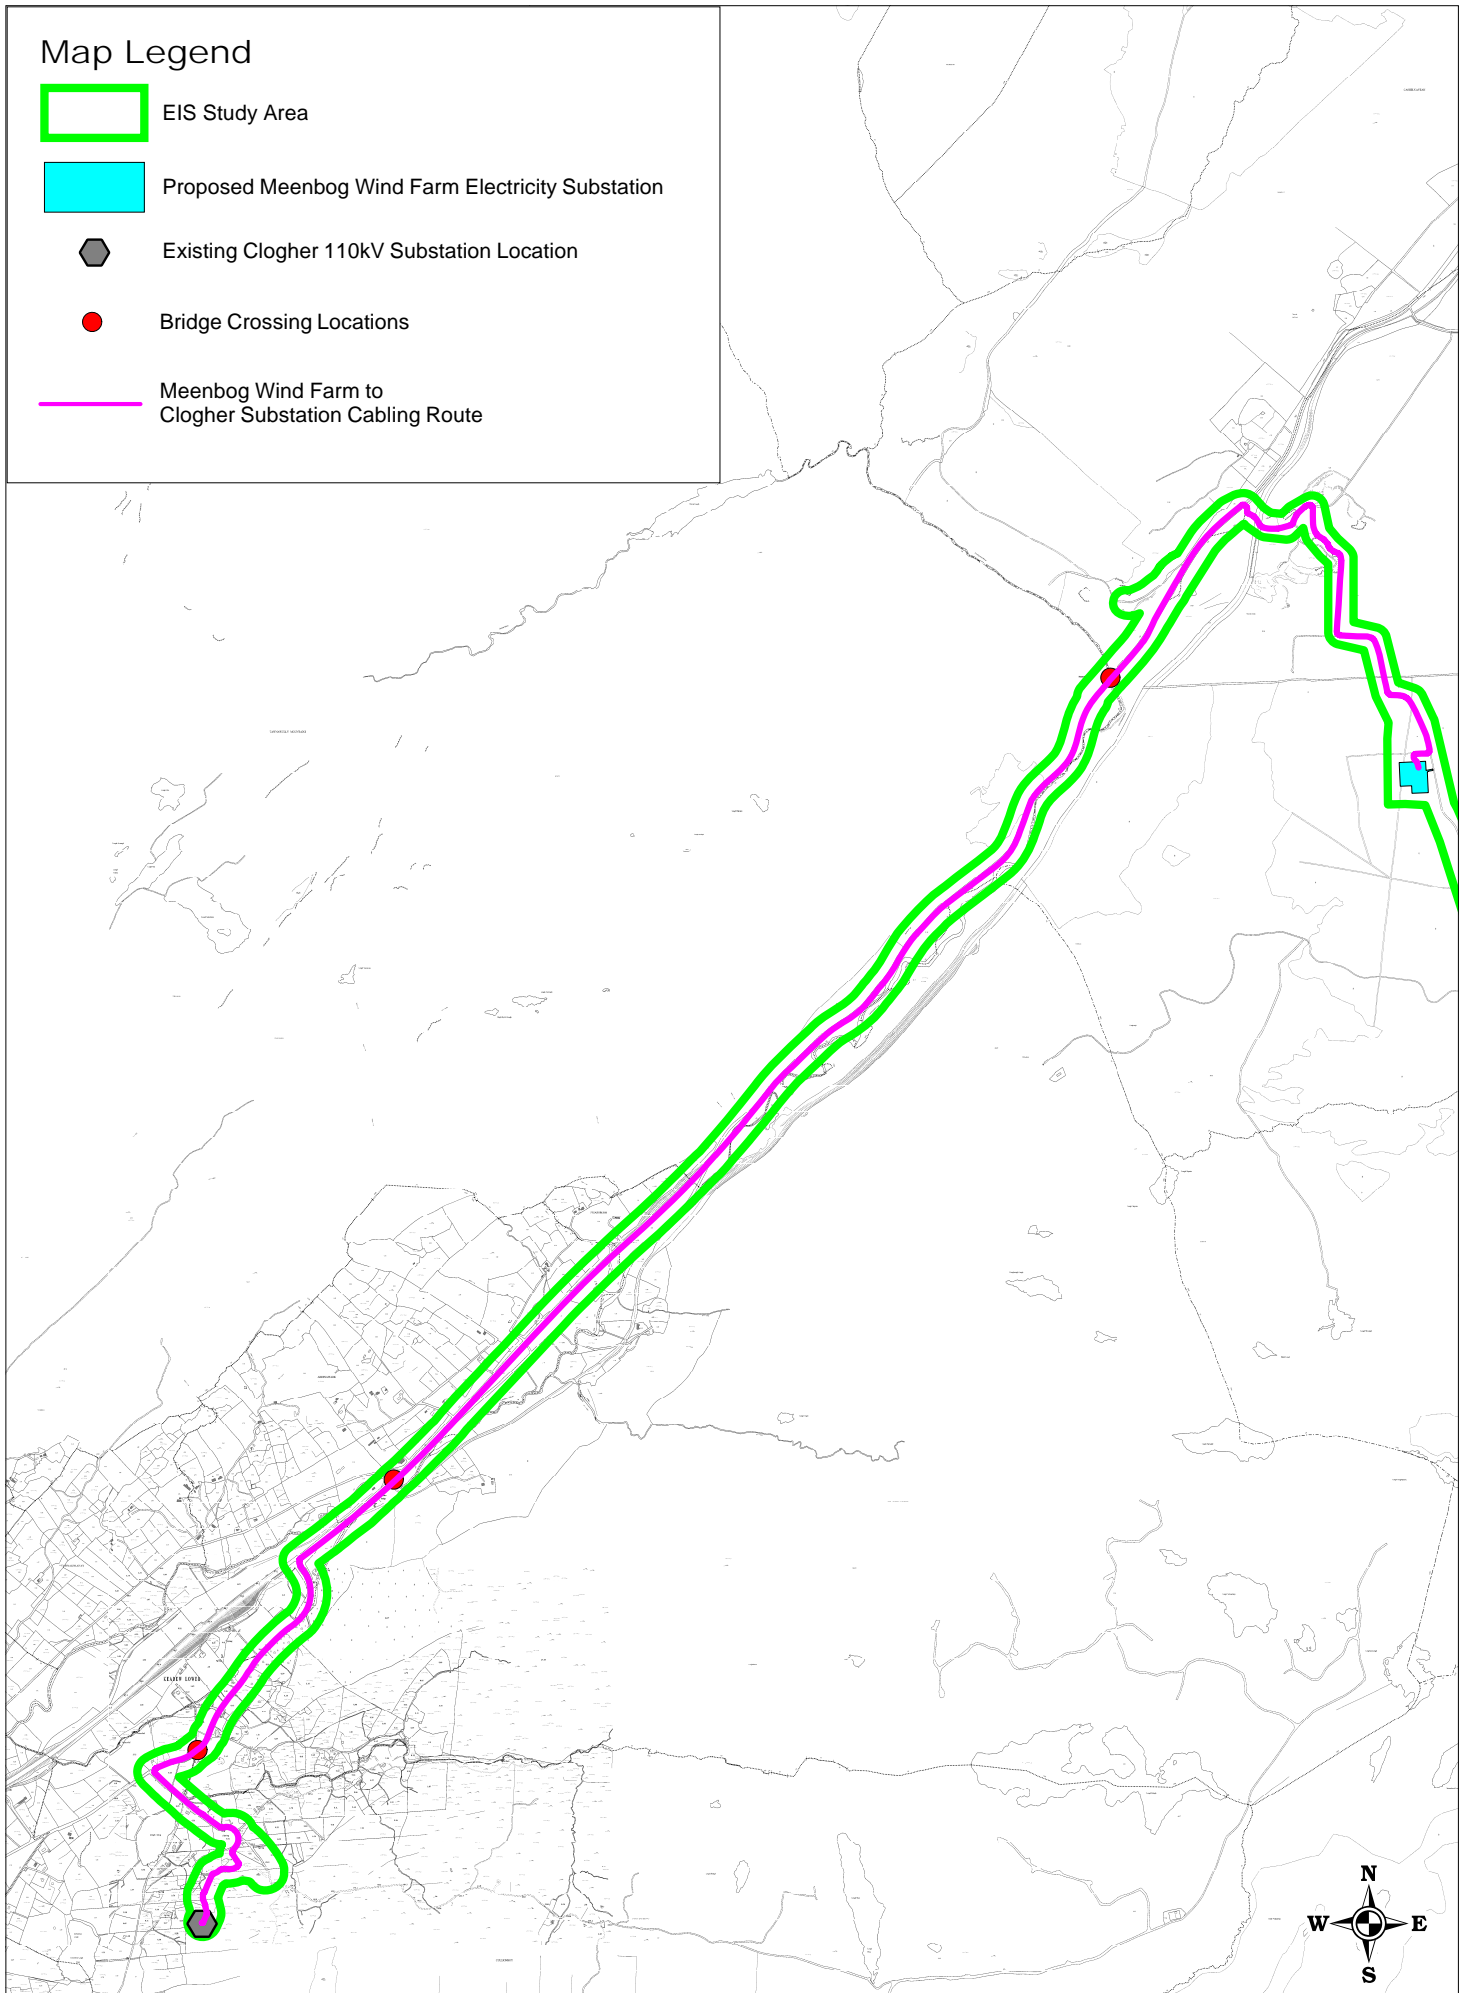

	MAP TITLE: Grid Connecton Cabling Arrangement		MAP NO.: Figure 2.2	SCALE: 1:30000
	PROJECT TITLE: 160502 - Meenbog Wind Farm, Co. Galway		OS SHEET NO.: n/a	DATE: 20-12-2018
	DRAWING BY: Eoin Gilson	CHECKED BY: Michael Watson	ISSUE NO.: 160502-2018.12.20-F	
	<small>McCarthy Keville O'Sullivan Ltd., Block 1, G.F.S.C. Moneenageisha Road, Galway, Ireland. Email: info@mccarthykos.ie Tel: +353 (0)91 735611 Fax: +353 (0)91 771279</small>			

- Ensure construction works and activities are completed in accordance with mitigation and best practice approach presented in the Environmental Report and associated planning documentation;
- Ensure construction works and activities are completed in accordance with any planning conditions for the development;
- Ensure construction works and activities have minimal impact/disturbance to local landowners and the local community;
- Ensure construction works and activities have minimal impact on the Natural Environment;

2.4 Construction Methodologies Overview

2.4.1 Introduction

Mid Cork Electrical Ltd. have been appointed as the contractor for the civil works for the construction phase of the Permitted Development. The appointed contractor for the works will be required to comply with this CEMP and any revisions made to this document in the preparation of method statements for the various elements of the construction phase of the Permitted Development. An overview of the proposed Construction Methodologies is provided below.

2.4.2 Overview of Proposed Construction Methodology

The proposed anticipated construction methodology is summarised under the following main headings:

- Temporary Construction Compounds;
- Borrow Pits;
- Site Drainage;
- Upgrade of Existing Roads;
- New Site Access Roads;
- Crane Hardstands;
- Turbine and Anemometry Mast Foundations;
- Electricity Substation and Control Buildings;
- Peat Repositories (cells within borrow pits);
- Cable Trenching;
- Grid Connection Cabling; and,
- Recreation and Amenity Areas
- Decommissioning

2.4.2.1 Temporary Construction Compound

There are two temporary construction compounds permitted for the site. One will be located in the northwest of the site, just north of the substation location. The second temporary construction compound is located north of the site, northwest of Turbine no. 17 which will become an amenity area on completion on the construction of the wind farm. The location of the construction compound is shown on the site layout drawings in Figure 2.1. The compound will typically be constructed as follows:

- The area to be used as the compound will be marked out at the corners using ranging rods or timber posts. Drainage runs and associated settlement ponds (refer to Section 3.1.1 below) will be installed around the perimeter;
- The compound will be established using a similar technique as the construction of the excavated site tracks as discussed below;

- Where required, a layer of geogrid will be installed and compacted layers of well graded granular material will be spread and lightly compacted to provide a hard area for site offices and storage containers;
- Areas within the compound will be constructed as site roads and used as vehicle hardstandings during deliveries and for parking;
- A bunded containment area will be provided within the compound for the storage of lubricants, oils and site generators etc.;
- If necessary the compound will be fenced and secured with locked gates, although fencing would only be utilised where significant risk of danger to third parties or vandalism is envisaged; and,
- Upon completion of the project the compound will be decommissioned by backfilling the area with the material arising during excavation, landscaping with topsoil as required. (North-eastern compound will be repurposed as an amenity area as described in Section 4.6 of the EIAR)
- During the construction phase, a self-contained port-a-loo with an integrated waste holding tank will be used on site for toilet facilities. This will be maintained by the service contractor as required and will be removed from the site on completion of the construction phase.
- The water supply to the site will be from a temporary water storage tank which will be filled using a mobile water tank which will source water locally as required.

2.4.2.2 Borrow Pit

The development will comprise three borrow pits one of which is located in the southern section of the site, north of turbine no. 5. The other borrow pits are located in north of the site, south of turbine no. 15 and east of turbine no. 13 as shown in Figure 2.1. The borrow pits will typically be excavated as follows:

- The areas to be used for both borrow pit will be marked out at the corners using ranging rods or timber posts. Drainage runs and associated settlement ponds will be installed around the perimeter;
- The initial borrow pit excavation will involve removal of peat and overburden from the top of bedrock. These materials will be used to form a berm on the downhill side of the borrow pit to provide screening of the borrow pit operations;
- Interceptor drainage ditches will be excavated on all sides of the borrow pit to catch surface water runoff, and direct it to downstream re-distribution locations;
- The bedrock material will be extracted from the borrow pit and stockpiled or used as required;
- The use of material won from the borrow pit will be sequential with new road construction or turbine base formations;
- Temporary stockpiling of aggregates will be required to accommodate the cut and fill operations within the borrow pit, and the progression of access roads and turbine excavations;
- As the borrow pit excavations progress and become deeper, surface water and groundwater ingress will be removed via pumping to settlement ponds, and re-distribution locally across natural vegetated areas. Where required, additional specialist treatment will be employed to ensure no deterioration in downstream water quality occurs;
- When extraction ceases within the borrow pit, the uphill face of the rock will be stepped and deposits of soil will be placed which will assist in the re-vegetation of the rock face.

- The extraction area of the borrow pit will have to be permanently secured and a stock-proof fence will be erected around the borrow pit to prevent access to these areas as well as the installation of appropriate health and safety signage.

Once the required volume of rock has been extracted from the borrow pit areas, it is intended to reinstate these areas with peat and overburden excavated from the works areas of the Permitted Development.

The total estimated volume of peat and spoil to be excavated and managed during the construction phase of the Permitted Development is 330,820m³. The borrow pit areas, within the site of the Permitted Development will undergo restoration with this peat and spoil material after all rock has been excavated from the borrow pit. The volume of excavated peat and overburden will be managed as outlined below:

- Excavators will remove the peat from the permanent development footprint areas i.e. excavated roads, hardstanding areas and turbine foundation areas.
- Temporary, sealed stockpiling areas, located adjacent to the hardstanding areas and turbine foundation areas, will be chosen following onsite discussions between the construction site manager, an ecologist, a geotechnical engineer and hydrologist.
- The excavators will move the excavated peat to the designated temporary stockpiling areas within the construction and soft levelled areas.
- The temporary stockpiling areas will be surrounded by silt fences to ensure sediment-laden run-off does not occur.
- The excavated peat will remain in these areas over a period of time until the volume of the peat has reduced as the water drains out of the mounded peat.
- The excavators will then load the peat directly into dump trucks, to transport the peat to the nearest borrow pit area.
- The material will be backfilled into the borrow areas and will be spread evenly across the area.
- The peat and subsoil will also as part of landscaping and reinstatement along access roads and turbine excavations.

This method of managing the volume of surplus peat and other overburden material will ensure that no excavated material will be left on-site, or stockpiled adjacent to access roads and turbine locations, following the completion of the construction works.

2.4.2.3 Drainage System

The early establishment of temporary drainage facilities will manage the risk of impacts on watercourses on and adjacent to the site during construction. In addition, construction operations will adopt best working practices. The development of the site will need to be phased accordingly. The construction of the drainage will start from the downstream sections and progress upstream, connecting conveyance systems with other drainage features as each development phase progresses. They will therefore need to be designed with sufficient flexibility to respond to an early phase incoming flow during the construction phase.

The implementation of a Scheduling of Works Operating Record (SOWOR) prior to commencement will provide a series of pre-commencement triggers which set out specific conditions which will be met before the commencement of works particularly sensitive areas. These pre-commencement triggers will apply to the installation of any drainage infrastructure. An example of an SOWOR is included in Appendix 2.

Detailed measures to address surface water management based upon the design criteria and philosophy will be implemented. The drainage system will be excavated and constructed in conjunction with the road and hard standing construction. Drains will be excavated, and settlement ponds constructed to eliminate any suspended solids within surface water running off the site. Surface drainage design and management is summarised with in Section 3.2 and 4 below.

2.4.2.4 Upgrade of Existing Roads

It is proposed to utilise the existing road network as much as possible (approximately 14.5 km will be used). These roads will require upgrading which will entail widening of the roadway to a total running width of approximately six metres, with wider sections at corners and on the approaches to turbine locations, and the laying of a new surface dressing on the existing section of roadway where necessary. The road widening will be undertaken as follows:

- If it is considered that the current road formation level is adequate to support required bearing, then no upgrade or widening works will be completed;
- Otherwise, where required, the subsoil in the existing road verge will be excavated down to a suitable formation layer and the spoil used for the restoration of borrow pits or in reinstatement areas;
- Well-graded imported granular fill will be spread and compacted in layers with an overall thickness of up to 300mm to provide a homogeneous running surface. The thickness of layers and amount of compaction required will be decided by the Construction Manager based on the characteristics of the material and the compaction plant to be used. These layers of granular fill will be brought to the same level as the top of the existing road surface;
- A layer of geogrid will be installed directly onto the top of the granular fill layer and the existing road surface where required; and,
- A layer of finer well graded stone for the running surface will be laid on the geogrid and compacted.
- Prior to any works commencing on the upgrade of existing roads, the requirement for additional roadside drainage will be considered by the Project Hydrologist in line with the proposals outlined in Section 4
- Where road widening is required in an area where the peat depth is greater than c1.5m, it will be necessary to complete the road upgrade using a floating road methodology as summarised in the section that follows.

2.4.2.5 New Site Access Roads

There is approximately 7.7 km of new access roads to be installed at the site. In a number of areas across the site, floating roads will be required where peat depths exceed c1.5m. Floating roads will be constructed using either a lightweight construction methodology which includes the use of layers of brash and lumber either side of a geogrid membrane where required and capped with suitable stone material or the use of geogrid capped with a stone material. The new access roads will be constructed as follows:


- Establish alignment of the new site roads from the construction drawings and mark out the centrelines with ranging rods or timber posts;
- The road layout has been designed to avoid crossings of natural watercourses where possible;
- Where existing culverts are to be upgraded or extended, the works will be carried out to follow a method statement to be agreed with Inland Fisheries Ireland.

- The access tracks will be of single-track design with an overall width of 6m. There will be some local widening on the bends, junctions and around turbine bases for the safe passage of large vehicles;
- Any excavated road section's will, where it is considered beneficial have turf stripped over the area of the excavation and stored growing side up for reuse. This area will be oversized to facilitate the excavated subsoil material. The subsoil material will subsequently be capped with topsoil to form an earth bund around the excavated material;
- Where the Geotechnical Engineer confirms it is more suitable, a non-excavated ground bearing road will be employed. In this case a reinforced sub-base will be placed directly on the existing ground using geotextile separation layer and layers of geogrid reinforcing as designed by the Geotechnical Engineer to achieve the bearing capacity required for the road running surface.
- All peat excavated will be used as part of the borrow pit restoration or in reinstatement areas. Topsoil will be temporarily stockpiled locally for reuse for landscaping the backfill placed above the foundations. A bund constructed of the excavated subsoil covered with a layer of Geogrid and capped with the peat topsoil for landscaping purposes will form the down-gradient boundary to the reinstatement areas;
- The subsoil will be excavated down to a suitable formation layer of either firm clay or bedrock;
- Where floating roads are to be constructed, the subsoil will not be excavated but a layer of geo-grid or layers of brash and lumber will be laid directly on to the peat surface.
- Well-graded granular fill will be spread and compacted in layers with an overall thickness of up to 750mm and a suitable capping layer to provide a homogeneous running surface. The thickness of layers and amount of compaction required will be decided by the Construction Manager based on the characteristics of the material and the compaction plant to be used;
- All new roadways will be constructed with a camber to aid drainage of surface water;
- Batters will generally be sloped to between 1:1 and 1:2 (depending on depth and type of material) and will be left as cut to re-vegetate naturally with local species. Design slopes will be informed by the Geotechnical Engineer;
- At bends or steep inclines from the roads, reflective snow poles will be erected to warn traffic on dark mornings and evenings that there is a turn in the road or a sharp incline beyond the site road.
- The granular fill use to complete the final running surface of the roads on site will be tested to BS812-111:1990 "Ten percent fines value".

2.4.2.6 Watercourse/Culvert Crossing on the Wind Farm Site

A survey of all existing stream culverts and stream crossings along existing roads (for upgrade) and access roads was undertaken as part of the drainage mapping. There are a total of 19 no. existing watercourse crossings and 5 no. new watercourse crossings. The locations of existing and new crossings are shown on Figure 2.3. The minimum required culvert dimensions of new culverts are shown in Appendix 3 which has informed the selection of both piped culvert and clear span bridge methodologies for the watercourse crossings.

It is proposed to construct c. 5m wide clear-span bridge over the Bunadaowen River within the Permitted Development site to provide access to Turbine No. 18 in the eastern half of the site. The crossing will comprise a pre-cast concrete clear span bridge as shown in Drawing 0502 - 47 in Appendix 1.

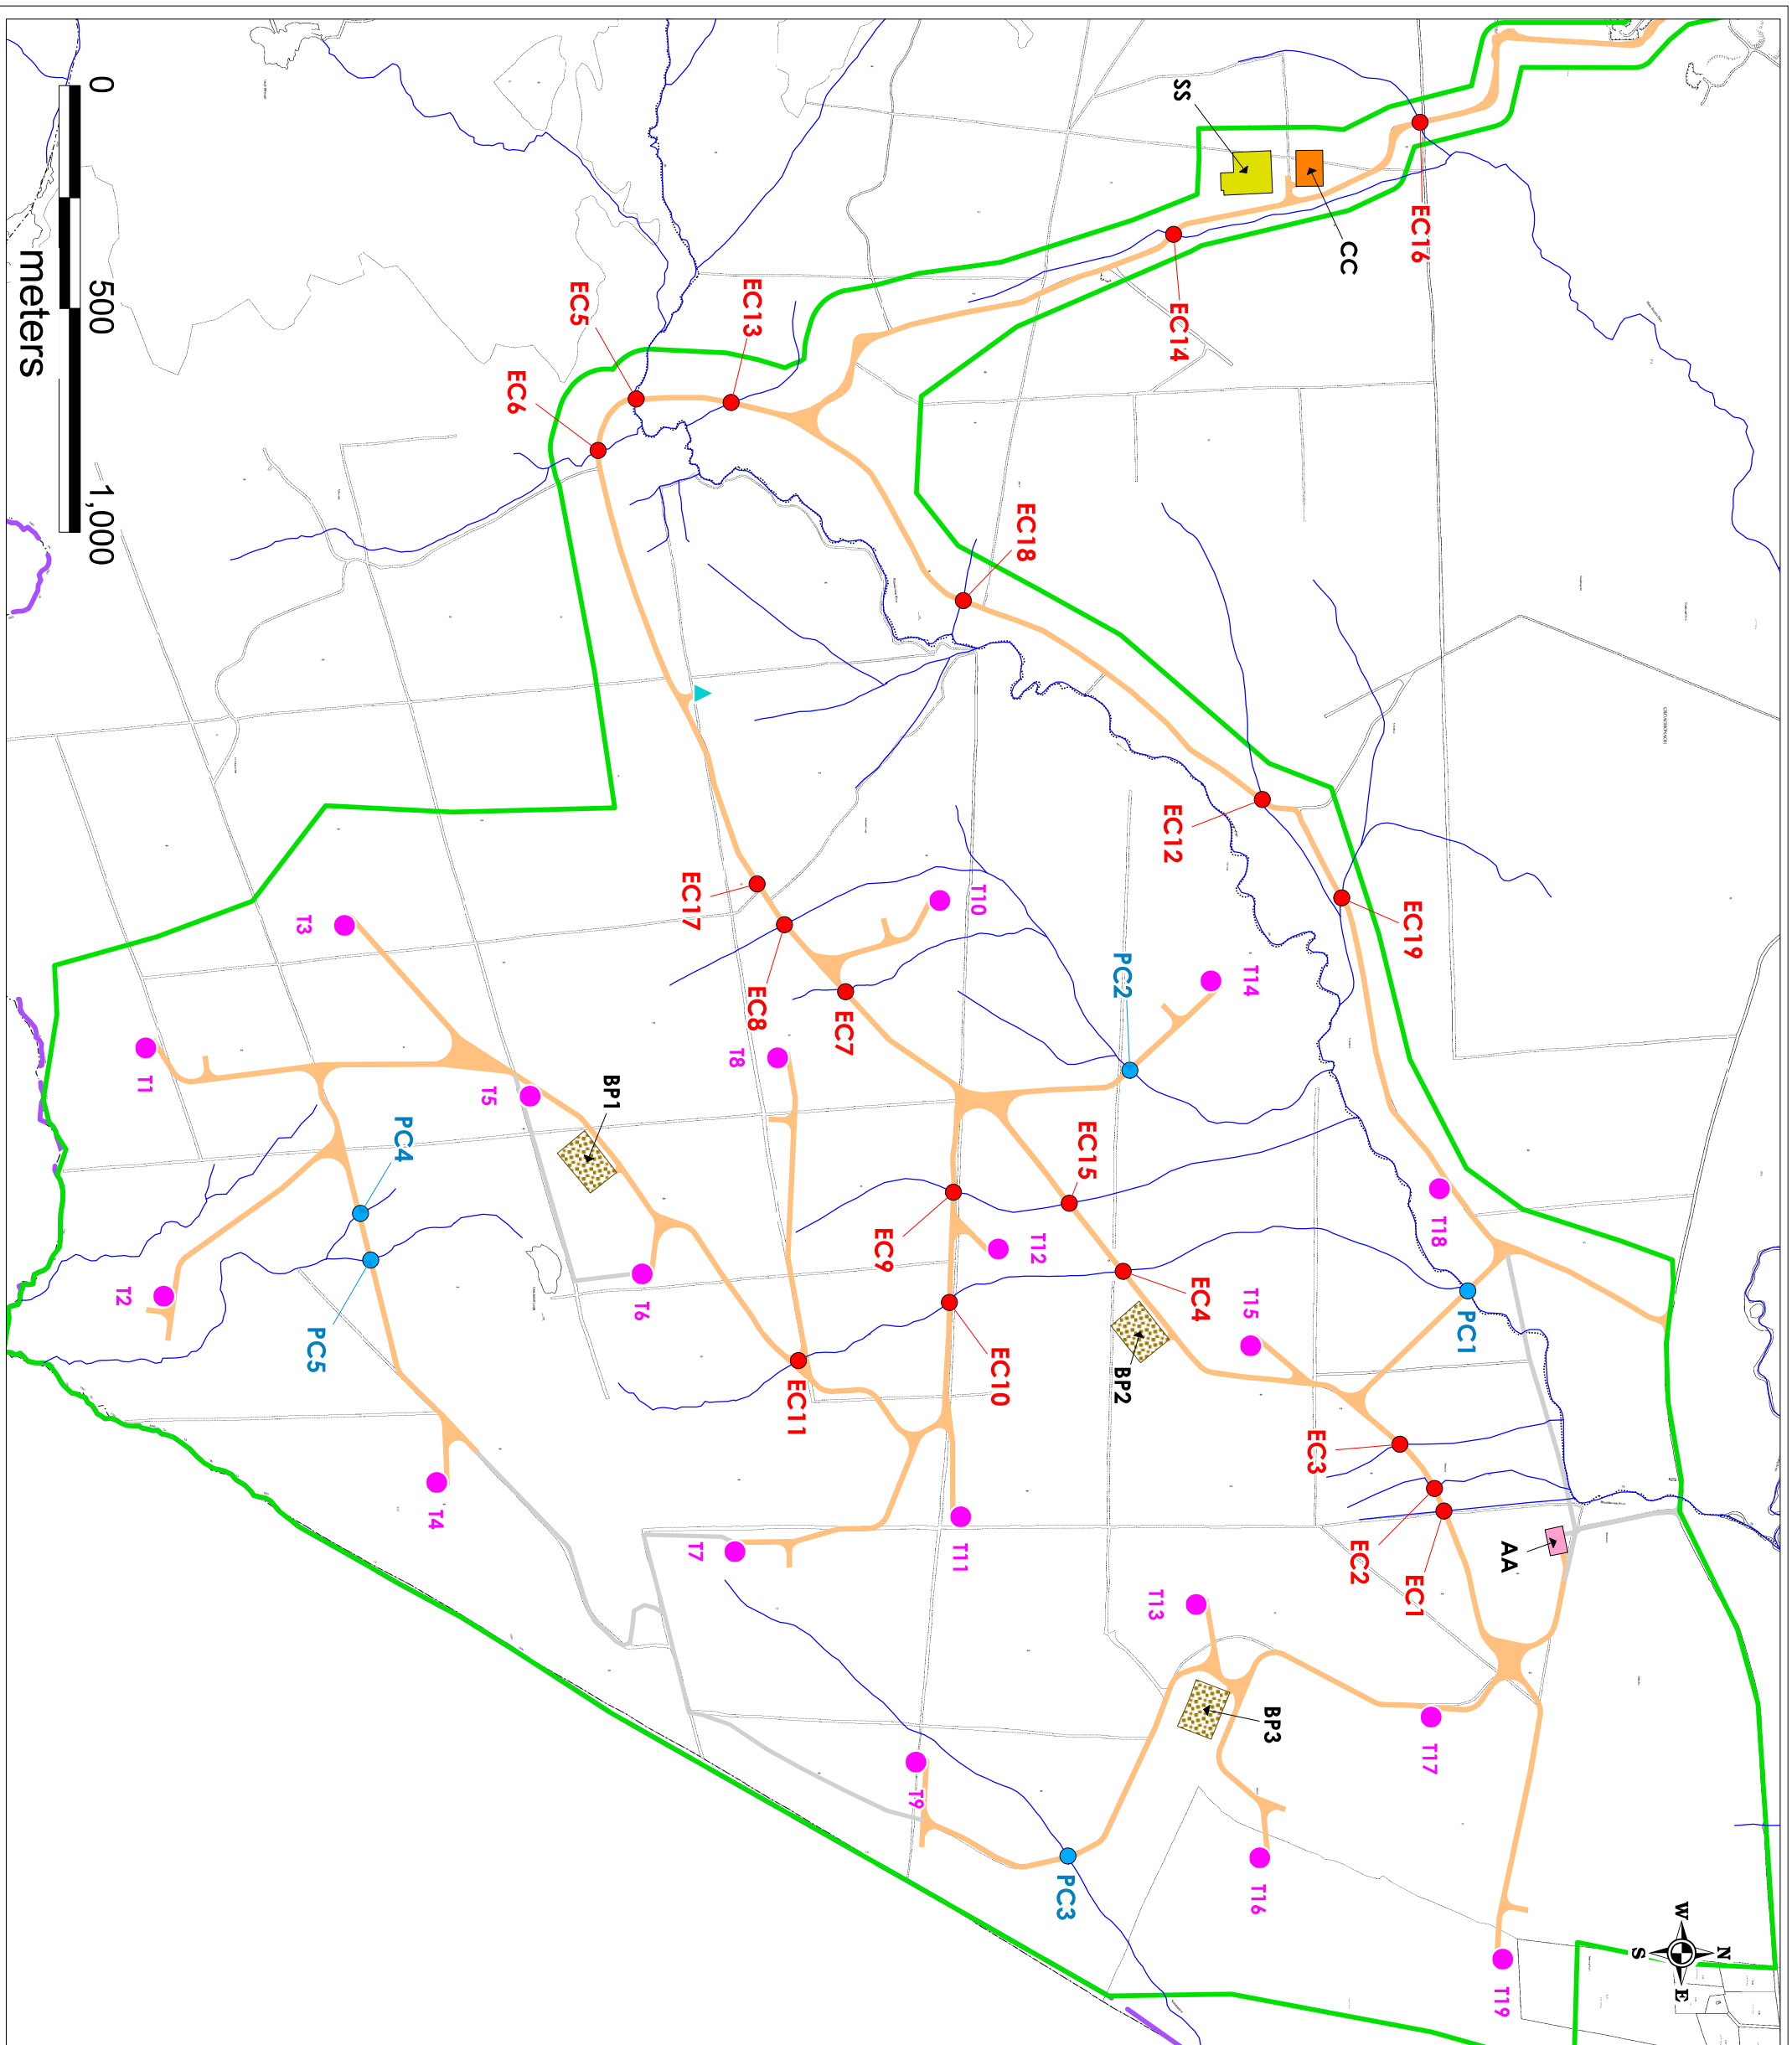

- Legend**
- EIA Site Boundary
 - Proposed Turbine Layout
 - ▲ Proposed Met Mast
 - Existing Culvert Locations
 - Proposed Culvert Locations
 - Grid Connection Route
 - Rivers/Streams
 - Northern Ireland Border
 - Access Road
 - Amenity Track
 - Proposed Borrow Pit (BP)
 - Proposed Construction Compound (CC)
 - Proposed Substation (SS)
 - Proposed Construction Compound / Amenity Area (AA)



HYDRO ENVIRONMENTAL SERVICES

22 Lower Main St | tel: +353 (0)58 44122
 Dungarvan | fax: +353 (0)58 44244
 Co Waterford | email: info@hydroenvironmental.ie
 Ireland | web: www.hydroenvironmental.ie

Client: McCarthy Keville O'Sullivan

Job: Meenbog WF, Co. Donegal

Title: Existing and Proposed Culvert Locations Map

Figure No: 2.3.

Drawing No: P1249-2-1117-A3-909-00A

Sheet Size: A3 | Project No: P1249-2

Scale: 1:20,000 | Drawn By: GD

Date: 20/11/2017 | Checked By: MG

The typical construction methodology for the installation of a pre-cast concrete clear-span bridge is presented below:

- The access road on the approach to the watercourse will be completed to a formation level which is suitable for the passing of plant and equipment required for the installation of the watercourse crossing.
- All drainage measures along the site road will be installed in advance of the works.
- The abutment will consist of concrete panels which will be installed on a concrete lean mix foundation to provide a suitable base. The base will be excavated to rock or competent ground with a mechanical excavator with the foundation formed in-situ using a semi-dry concrete lean mix. The base will be excavated along the stream bank with no instream works required.
- Access to the opposite side of the river for excavation and foundation installation will require the installation of pre-cast concrete slab across the river to provide temporary access for the excavator.
- All pre-cast concrete panels and slabs/beams will be installed using a crane which will be set up on the southern side of the stream and will be lifted into place from the stream back with no contact with the watercourse.
- A concrete deck will be poured over the beams/slabs which span across the river. This will be shuttered, sealed and water tested before concrete pouring can commence. The deck will be leak tested before concrete pouring can commence.
- Once the culvert is in position stone backfill will be placed and compacted against the culvert up to the required level above the foundations.

When the concrete beams are cured the filling and compaction of the road will be completed. The road finish level will be decided by the Project Engineer.

All other new crossings will be completed using piped culvert, the crossings will be installed as follows:

- The access road on the approach watercourse will be completed to a formation level which is suitable for the passing of plant and equipment required for the installation of the watercourse crossing.
- The installation of the culvert will take place in low flow conditions.
- Where a flow exists, the water running through the watercourse channel will be pumped around the water crossing location and back into the watercourse channel downstream of the works area.
- Where over pumping is required, measures will be taken to ensure that the pumped water discharge does not disturb the stream bed with the force of water from the discharge. A steel plate to reduce the force of the flow will be used where appropriate.
- The project engineer will determine the required gradient of the culvert. The pipe must be laid at a gradient that will ensure water is contained within the pipe at all times. Where necessary a rock armour dam will be installed within the stream to reduce flow and ensure an acceptable depth of water remains within the pipe. Where a gradient of 1 – 1.5% is identified, the use of a baffle has been recommended.
- The bed of the watercourse channel will be excavated, if necessary, to achieve the correct line and to allow the pipe to be embedded 300mm into the base of the existing drain.

- The embedded section will be allowed to fill naturally with existing material within the base of the drain or with suitable drainage material such as gravel or round shingle where deemed applicable.
- The culvert will be lowered into place using an excavator with a lifting mechanism.
- Large stone boulders (approx. 400mm), sourced from the on-site borrow pits, will be placed over the culvert to create a headwall for the culvert and a suitable sub-base for road construction.
- Smaller 50mm stone, sourced on site will be placed upon the sub-base to construct the road over the water crossing.

Any watercourse crossings required will be installed outside of the salmonid spawning season, October to June in any year, in accordance with Inland Fisheries Ireland best practice (IFI, 2016). This will ensure no potential impacts on salmonid spawning habitat.

All of the above works will be supervised by the Environmental Clerk of Works and the project hydrologist.

2.4.2.7 Crane Hardstands

All crane pads will be designed taking account of the loadings provided by the turbine manufacturer and will consist of a compacted stone structure. The crane hardstands will be constructed in a similar manner to the excavated site roads and will measure approximately to the turbine manufacturer's requirements. Where an excavated crane hardstand cannot be used due to the depth of peat, the hardstand will be supported by using reinforced concrete piles as per the methodology outlined for piled foundations summarised below. The position of the crane pads varies between turbine locations depending on topography, position of the site access road, and the turbine position.

2.4.2.8 Turbine and Anemometry Mast Foundations

The wind turbines and anemometry mast foundations will be a reinforced concrete base designed to Eurocode 2/BS8110. Foundation loads will be provided by wind turbine and mast supplier, and factors of safety will be applied to these in accordance with European design regulations. The turbine will be anchored to the foundation using a bolt assembly which shall be cast into the concrete. The anemometry mast is a free-standing structure which is also anchored to the reinforced concrete foundation. It is anticipated that the foundations for both the turbines and the anemometry mast will be either ground bearing or piled foundations and that the formation level of the turbine foundations will be on the lower mineral subsoil or bedrock. Bases will measure approximately 20 metres in diameter. They will likely be formed one metre below the base of the peat layer on stiff subsoil material or bedrock, or at a suitable level directed by the Geotechnical Engineer/Designer. The foundations will be constructed as follows:

- The extent of the excavation will be marked out and will include an allowance for trimming the sides of the excavation to provide a safe working area and slope batter;
- Where practical, the peat will be stripped over the area of the excavation and stored growing side up for reuse, the subsoil will be excavated and stored to one side for reuse during the landscaping around the finished turbine;
- No material will be removed from site and storage areas will be stripped of vegetation prior to stockpiling in line with best working practices;
- All groundwater and surface water arising from turbine base excavation will be pumped to the dirty water system prior to discharge from the works area;

- Soil excavation shall be observed by a qualified archaeologist in accordance with a scheme of archaeological monitoring to identify any significant remains as they come to light and,
- The foundations excavation will be raised to formation level by compacted layers of well graded granular material will be spread and compacted to provide a hard area for the turbine foundation.

Standard excavated reinforced concrete bases will be completed as follows:

- A layer of concrete blinding will be laid approximately 75mm thick directly on top of the newly exposed formation, tamped and finished with a screed board to leave a flat level surface. The concrete should be protected from rainfall during curing and all surface water runoff from the curing concrete should be prevented from entering surface water drainage directly;
- High tensile steel reinforcement will be fixed in accordance with the designer's drawings & schedules. The foundation anchorage system will be installed, levelled and secured to the blinding using steel box section stools;
- Ductwork will be installed as required, and formwork erected around the steel cage and propped from the backside as required;
- The foundation anchorage system will be checked both for level and line prior to the concrete being installed in the base. These checks will be passed to turbine manufacturer for their approval;
- Concrete will be placed using a concrete pump and compacted when in the forms using vibrating pokers to the levels and profile indicated on the drawings. Upon completion of the concreting works the foundation base will be covered and allowed to cure;
- Steel shutters will be used to pour the circular chimney section;
- Earth wires will be placed around the base; and,
- The foundation will be backfilled with a cohesive material, where possible using the material arising during the excavation and landscaped using the vegetable soil set aside during the excavation.
- Soil, rock and other materials excavated during construction shall not be left stockpiled on site following completion of works. Excavated areas shall be appropriately restored within three months of the date of commissioning of the wind farm

Reinforced concrete piled foundations will be completed as follows:

- The extent of the excavation will be marked out and will include an allowance for trimming the sides of the excavation to provide a safe working area and slope batter;
- No material will be removed from site and placement areas will be stripped of vegetation prior to stockpiling in line with best working practices;
- A piling platform for the piling rig will be constructed. This can be done in two ways depending on the bearing capacity of the underlying soil.
 - The first method is to lay geo-textile on the existing surface and a stone layer will then be placed on top of the geo-textile by an excavator and compacted in order to give the platform sufficient bearing capacity for the piling rig.
 - The second method is to excavate the soils to a suitable intermediate mineral subsoil and backfill to the formation level.
- The piling rig, fitted with an auger, will then bore through the soft material with a sleeve fitted around the auger to prevent the sidewalls of the peat from

collapsing. The borehole is then extended to a suitable depth into the subsoil/bedrock.

- When the auger and the sleeve are removed high tensile steel cages will be lowered into the boreholes. These steel cages will extrude above the level of the top of the concrete pile.
- As the auger is removed concrete is pumped into the borehole.
- Reinforcing steel on the top of the pile will tie to the foundation base steel.

The procedure for standard excavated reinforced concrete bases as outlined above can be applied from here.

2.4.2.9 Electricity Substation and Control Buildings

The electricity substation and control buildings will be constructed within the site, adjacent to the existing access road, as shown in Figure 2.1. The dimensions of the substation area will be set to meet the requirements and specifications of ESB/Eirgrid and the necessary equipment to safely and efficiently operate the wind farm;

The substation will be constructed by the following methodology:

- The area of the substation will be marked out using ranging rods or wooden posts and the soil stripped and removed to a temporary placement area for later use in landscaping. No material will be removed from site and the temporary placement areas will be stripped of vegetation prior to stockpiling in line with best working practises;
- Wind farm control buildings will also be built within the substation compound;
- All groundwater and surface water arising from turbine base excavation will be pumped to the dirty water system and treated in settlement ponds, and/or specialist treatment systems, prior to discharge from site; and,
- The foundations will be excavated down to the level indicated by the project engineer. The foundations will be shuttered and poured with reinforced concrete. An anti-bleeding admixture will be included in the concrete mix;
- The substation will be constructed with masonry blockwork. The block work walls will be built up from the footings to DPC level and the floor slab constructed, having first located any ducts or trenches required by the follow on mechanical and electrical contractors;
- The block work will then be raised to wall plate level and the gables & internal partition walls formed. Scaffold will be erected around the outside of the building for this operation;
- Concrete roof slabs will be lifted into position using an adequately sized mobile crane;
- The timber roof trusses will then be lifted into position using a telescopic load all or mobile crane depending on site conditions. The roof trusses will then be felted, battened, tiled and sealed against the weather.
- A rainwater harvesting system will be installed to provide the small volume of water required for the operation of the substation and control building.
- The electrical equipment will be installed and commissioned.
- Perimeter fencing will be erected around the substation and control building compound area.
- All wastewater from the staff welfare facilities in the control buildings by means of a sealed storage tank which will be fitted with an automated alarm system that will provide sufficient notice that the tank requires emptying.

2.4.2.10 Cable Trenching

The transformer in each turbine is connected to the substation through a network of buried electrical cables. The ground is trenched typically using a mechanical

excavator. The top layer of soil is removed and saved so that it is replaced on completion. The cables will be laid within 3 no. 160mm diameter HDPE ducting laid in a trefoil formation with 2 no. 125mm HDPE comms ducts laid above within the same trench.

The cabling ducts are bedded with suitable material unless the ground conditions are such that no bedding is required. The cables will be laid at a depth that meets all national and international requirements and will generally be approximately 1.3m below ground level; a suitable marking tape is installed between the cables and the surface. On completion, the ground will be reinstated as previously described above. The route of the cable ducts will follow the access track to each turbine location and are visible on the site layout drawings included as Appendix 1.

2.4.2.11 Grid Connection

A connection to the national electricity grid will be made by underground electricity cabling originating from the Meenbog Wind Farm substation and will run south connecting to the existing electricity Clogher 110kV electricity substation. The installation methodology for the underground electrical cable is summarised in the following sections. Should Eirgrid require the provision of any additional ducting at the time of completing the wind farm grid connection works, this can be accommodated within the same works programme using the methodologies as set out below for cabling works and watercourses crossings.

2.4.2.11.1 Parallel Road Excavations inroad & in Grass margin

The grid connection route generally follows the existing road corridor except for a section of approximately 300m southeast of the N15 and 230m northwest of the N15 that will cross cut over bog, grassland and scrub habitats to facilitate directional drilling, under the N15 and a tributary of the Lowerymore River as set out in Figure 2.2 and Appendix 1. The grid connection cabling is summarised as follows:

- The area where excavations are planned will be surveyed and all existing services will be identified.
- All relevant bodies i.e. ESB, Donegal County Council etc. will be contacted and all drawings for all existing services sought.
- A traffic management plan for the grid connection cabling works will be prepared in advance of any works commencing.
- A road opening licence will be obtained where required and all plant operators and general operatives will be inducted and informed as to the location of any services.
- Excavation permit will be completed and all plant operators and general operatives will be inducted and informed as to the location of any services.
- A 13 tonne rubber tracked 360-degree excavator will be used to excavate the trench to the dimensions specified in the ESB Networks manuals. The 110kV trench material build-up is designed to the "Functional Specification for the Installation of Ducts and Ancillary Structures for 110kV Underground Power Cables and Associated Communications Cables for Contestable Projects" No. 18150.
- All excavated material not used for backfilling will be removed to the on-site borrow pit areas or to an approved tip or if suitable stock piled and reused where appropriate.
- The trench depth is specified at c. 1250mm therefore trench support will be installed with the trench sides benched or battered back where appropriate.
- Any ingress of ground water will be removed from the trench using submersible pumps.

- A silt filtration system will be used to prevent contamination of any watercourse.
- Once the trench has been excavated a base layer of 15 N CBM4 concrete will be installed and compacted. All concrete will be offloaded directly from the concrete truck directly into the trench.
- Ducting will then be placed in the trench as per specification, approved cable ties will be used where required to secure the trefoil ducts together (at 3 metre centres).
- Once the trefoil ducts have been installed couplers will be fitted and capped to prevent any dirt etc. entering the duct. In poor ground conditions, the end of the trefoil ducts will be shimmed up off of the bed of the trench to prevent any possible ingress of water dirt. The shims will be removed again once the next length has been connected.
- Extreme care will be taken to ensure that all duct collars (both ends) are clean and in good condition prior to ducts being joined.
- The as built location of the ducting will be surveyed using a total station/GPS.
- 15 N CBM4 concrete will be carefully installed so as not to displace the ducting to the underside of the communications duct and compacted as per approved detail. See Plate 2.1.
- Spacers will be used to ensure that the correct cover is achieved at both sides of the trefoil ducting.
- ESB marker board will be fitted above the trefoil ducting.
- The Communication duct will be fitted and kept to one side of the trench ensuring that the minimum cover is achieved and 15N CBM4 concrete will be placed to the specified cover and compacted, see Plate 2.1.
- ESB red marker board will be installed and the remainder of trench will be backfilled in two compacted layers with approved material (lean mix concrete/clause 804).
- Yellow marker tape will be installed as per approved detail specifications, 300 mm maximum below finished road/ground level.
- The finished surface will be reinstated as per original specification or to the requirements of the land owner/Local Authority as appropriate.
- Marker Posts will denote all changes of direction, road crossings, etc.



Plate 2.1 Typical Trench Views

2.4.2.11.2 Existing Underground Services

Any underground services encountered along the route will be surveyed for level and the ducting will pass over the service provided adequate cover is available. A minimum clearance of 300mm will be required between the bottom of the ducts and the service in question. If the clearance cannot be achieved the ducting will pass under the service and again 300 mm clearance between the top of the communications duct and bottom of the service will be achieved. In deeper excavations, an additional layer of marker tape will be installed between the communications layer and yellow top-level marker tape. If the required separation distances cannot be achieved then a number of alternative options are available such as using steel plates laid across the width of the trench and using 35N concrete surrounding the ESB ducts where adjacent services are within 600mm, with marker tape on the side of the trench. Back fill around any utility services will be with dead sand/pea shingle where appropriate. All excavations will be kept within the roadway boundaries, i.e. in road or grass margin.

2.4.2.11.3 Joint Bays

Joint bays are pre-cast concrete chambers where lengths of cable ducting will be connected. They will be located at various points along the ducting route approximately every 600-1000 meters. Where possible joint bays will be located in areas where there is a natural widening/wide grass margin on the road in order to accommodate easier construction, cable installation and create less traffic congestion. During construction, the joint bay locations will be completely fenced off and will be incorporated into the traffic management system. Once they have been constructed they will be backfilled temporarily until cables are being installed.

2.4.2.11.4 Watercourse/Culvert Crossing – Grid Connection Cable Route

The underground cable route crosses a number of minor culverts throughout its length and 3 no. bridge crossings. The construction methodology has been designed to eliminate the requirement for in-stream works. A general description of the various construction methods employed at culvert and bridge crossings are described in the following paragraphs below. A list of the bridge crossings and the proposed crossing method at each location is provided in Table 2.1 below. The crossing methodologies employed at the remaining 25 No. culvert crossings, along the grid connection cable route, will be selected from the suite of watercourse crossing options outlined below, as appropriate, depending on culvert type, depth, size and local ground conditions.

The bridge crossing locations are shown in Figure 2.2. The culvert crossing and bridge crossing locations are also shown on the underground cable route drawings included as Appendix 1.

Piped Culvert Crossings over Culvert – Option 1

Watercourses will not be directly impacted upon since no instream works or bridge/culvert alterations are proposed. Where sufficient cover exists above the culvert, the trench will be excavated above the culvert and the ducts will be installed in the trefoil arrangement passing over the sealed pipe where no contact will be made with the watercourse. This method of duct installation is further detailed in Figure 2.4

Piped Culvert Crossings under Culvert – Option 2

Watercourses will not be directly impacted upon since no instream works or bridge/culvert alterations are planned. Where the culvert consists of a socketed concrete or sealed plastic pipe, a trench will then be excavated beneath the culvert and cable ducts will be passed under the sealed pipe as outlined in Figure 2.5.

If this duct installation method cannot be achieved due to the invert level of the existing culvert or due to the composition of the culvert e.g. stone culverts, the ducts will be installed by alternative means as set out in the following sections.

Flatbed Formation over Culverts or at Road Level – Option 3

Where cable ducts are to be installed over an existing culvert where sufficient cover cannot be achieved by installing the ducts in a trefoil arrangement, the ducts will be laid in a much shallower trench the depth of which will be determined by the location of the top of the culvert. The ducts will be laid in this trench in a flatbed formation over the existing culvert and will be encased in 6mm thick steel galvanized plate with a 30N concrete surround as per ESB Networks specification. This method of duct installation is further detailed in Figure 2.6.

Where a bridge or culvert has insufficient deck cover to fully accommodate the required ducts, the ducts can be laid in a flatbed formation partially within the existing road surface. Where this option is to be employed, the ducts will also be encased in steel with a concrete surround as per Eirgrid and/or ESB Networks specifications. In order to achieve cover over these ducts and restore the carriageway of the road, it may be necessary to locally raise the pavement level to fully cover the ducts. The increase road level will be achieved by overlaying the existing pavement with a new wearing course as required. Any addition of a new pavement will be tied back into the existing road pavement at grade. After the crossing over the culvert has been achieved, the ducts will resume to the trefoil arrangement within a standard trench. This method of duct installation is further detailed in Figure 2.7.

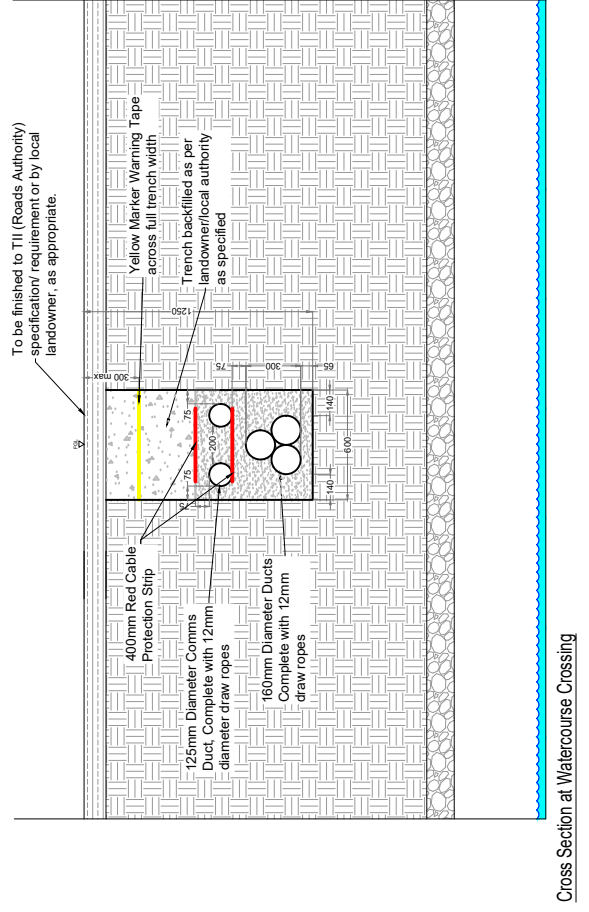
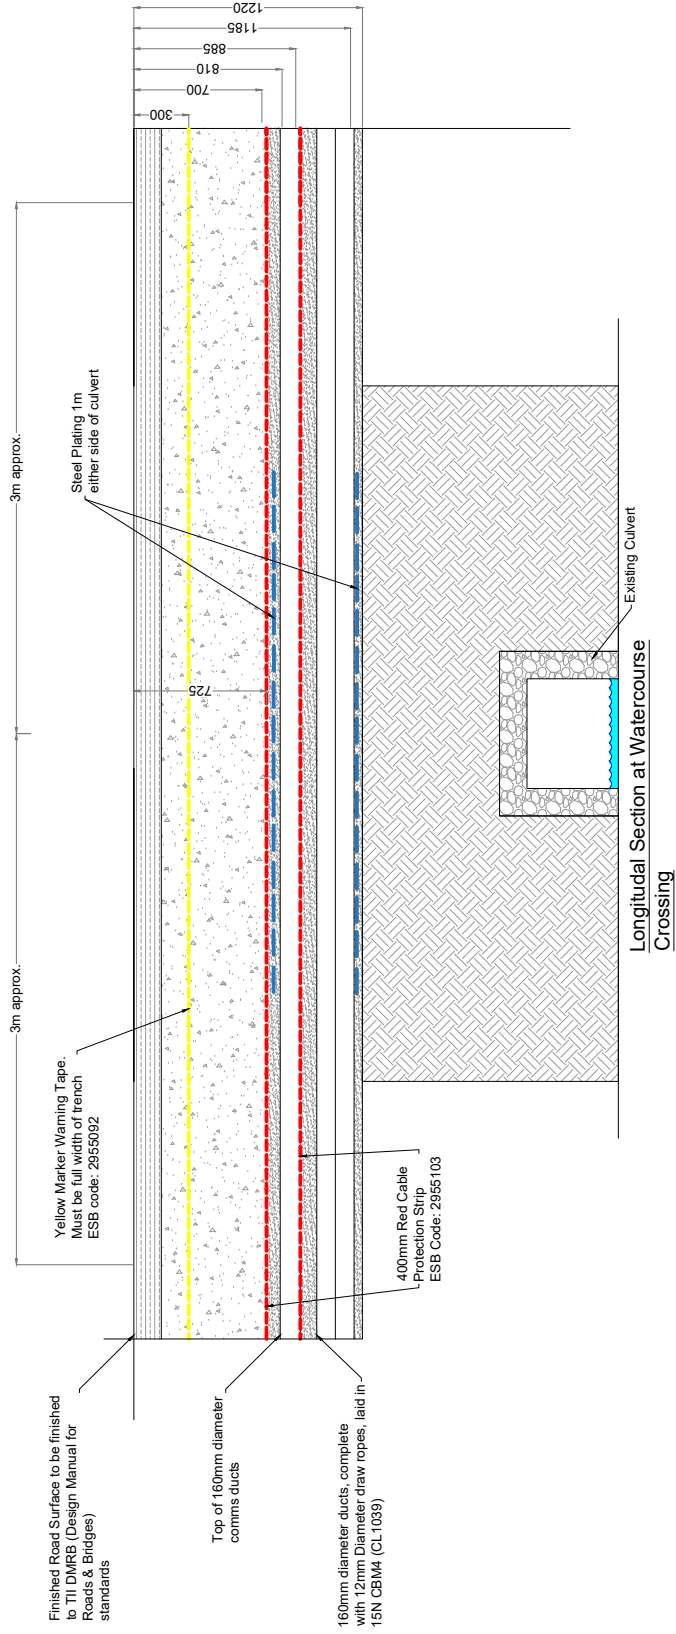


Figure 2.4
Cable Trench Over Culvert

DRAWING FILE		PROJECT FILE		CHECKED BY	
Meembog Wind Farm, Co. Donegal		Meembog Wind Farm, Co. Donegal		Michael Watson	
DRAWN BY		DESIGNED BY		DATE	
Joseph O'Brien		160902		0502 - 53	
SCALE		1:30 @ A3		20.12.2018	

		McCarthy Keville O'Sullivan Ltd. Planning & Environmental Consultants Block 1, The Industrial Centre, Moylagh Road, Galway, Ireland. website: www.mcsot.com email: info@mcsot.com Fax: +353 91 771279	
--	--	---	--



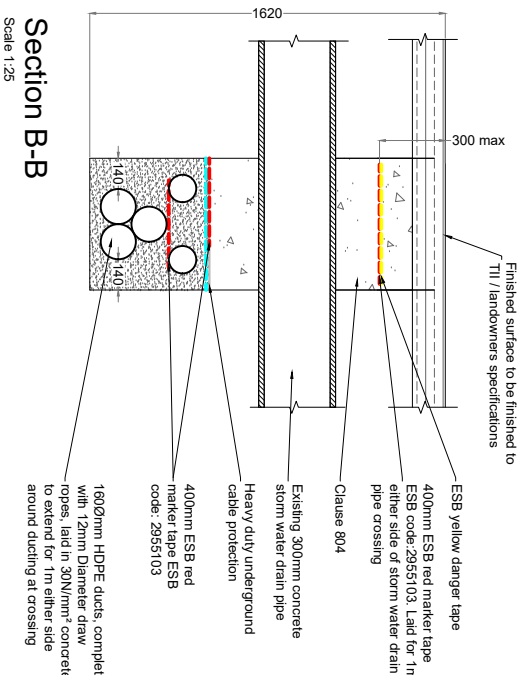



Figure 2.5
Cable Trench Under Piped Culvert

DRAWN BY:	PROJECT TITLE:
MEENBORG WIND FARM, CO. DONEGAL	
DATE:	CLIENT:
20.12.2018	Michael Watson
SCALE:	PROJECT NO.:
1:25 @ A3	160802
	DATE:
	20.12.2018


McCarthy Kenille O'Sullivan Ltd.
Planning & Environmental Consultants
Block 1,
Newry Road,
Galway, Ireland
email: info@mcCarthyKenille.ie
website: www.mcCarthyKenille.ie
Fax: +353 91 77219

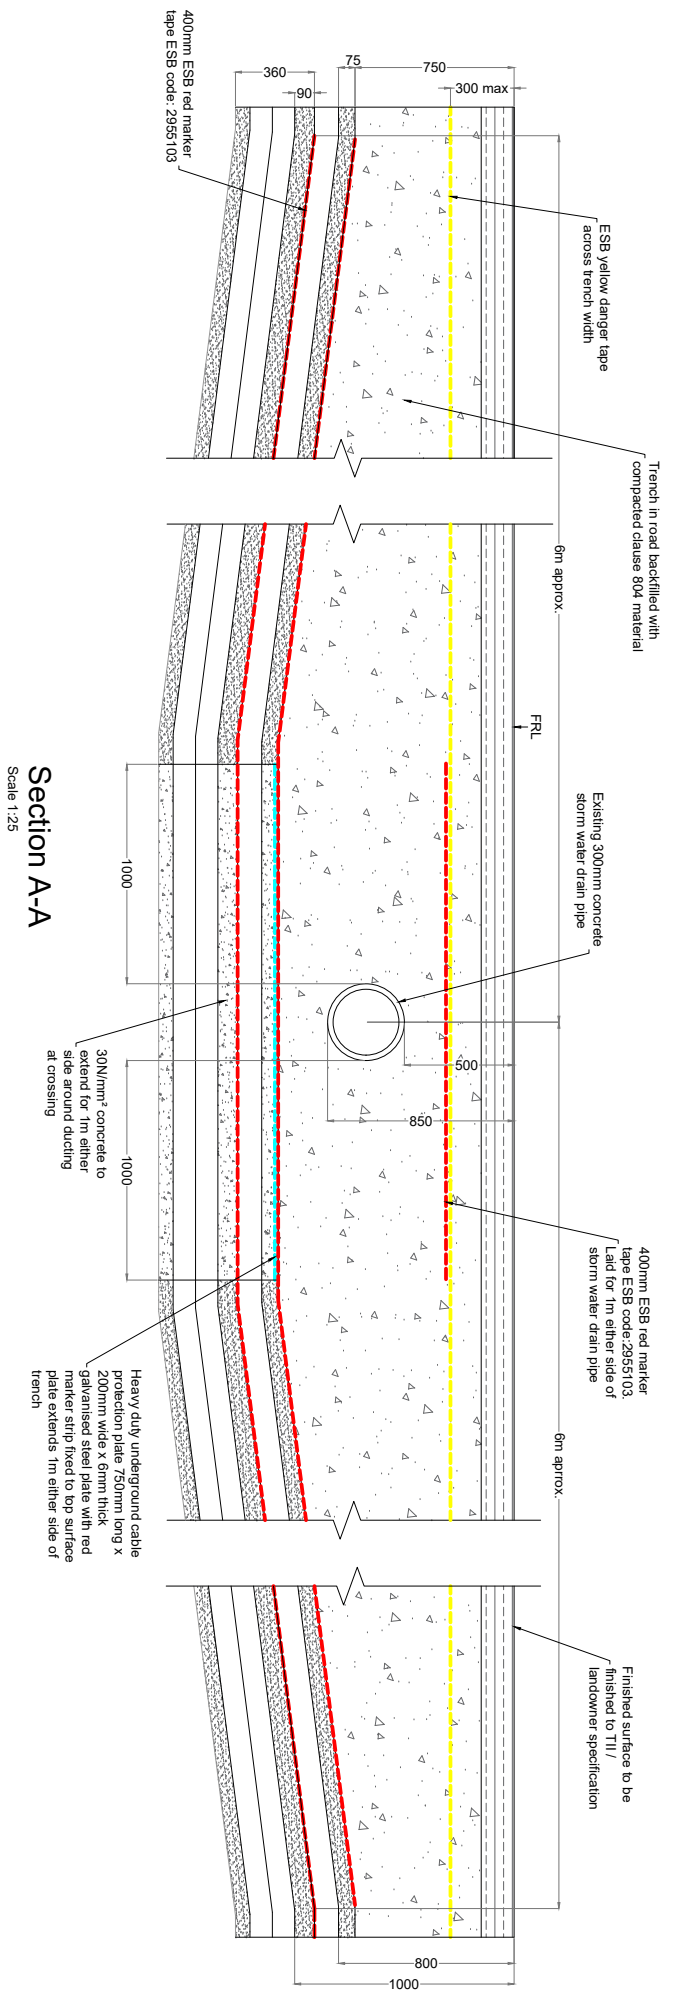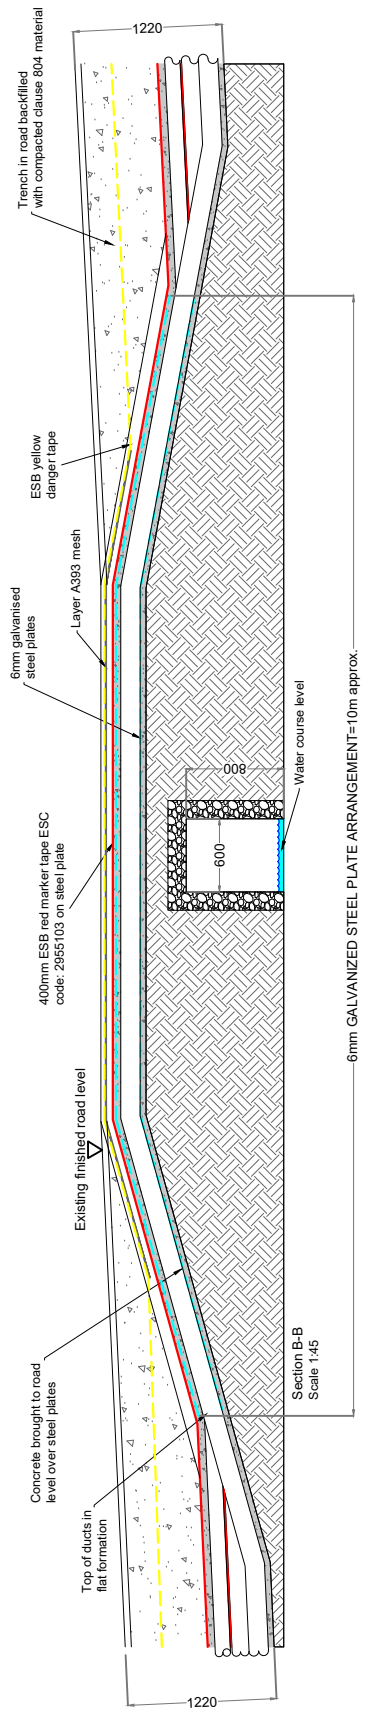

Section B-B
Scale 1:45

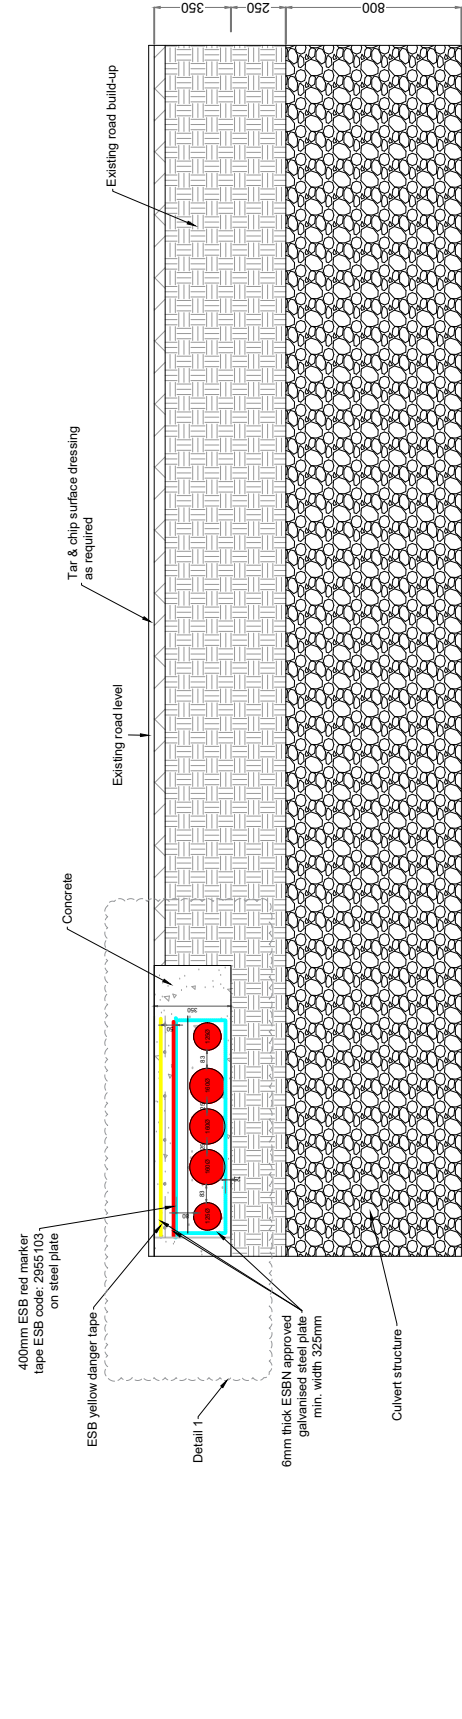

Section A-A
Scale 1:25

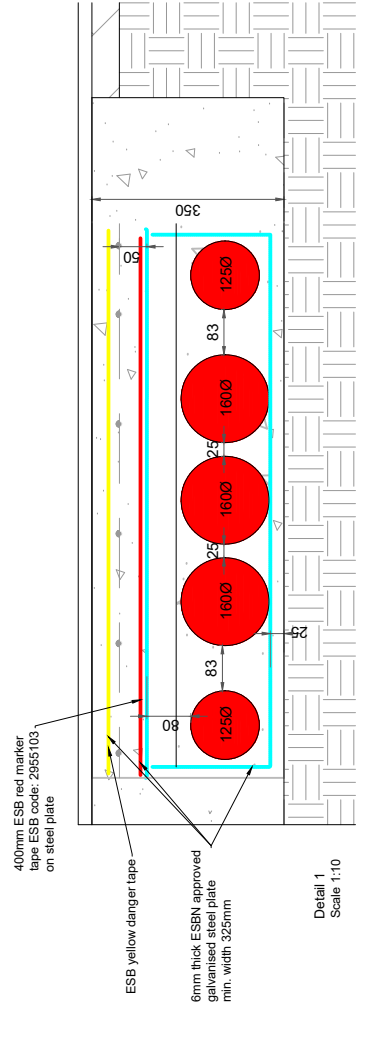

Detail 1
Scale 1:10

Figure 2.6

DRAMA TITLE
Cable Trench Flatbed Formation Over Culvert

PROJECT TITLE
Meenbog Wind Farm, Co. Donegal

DRAWN BY
Joseph O'Brien

CHECKED BY
Michael Watson

PROJECT NO.
160902

FORM NO.
0502 - 55

SCALE
As Shown @ A3

DATE
20.12.2018

McCarthy Keville O'Sullivan Ltd.
Planning & Environmental Consultants
Block 1, Industrial Estate, Carrisade Centre,
Marine Road,
Galway, Ireland.
email: info@mcCarthyks.ie
website: www.mcCarthyks.ie
Fax: +353 91 771279

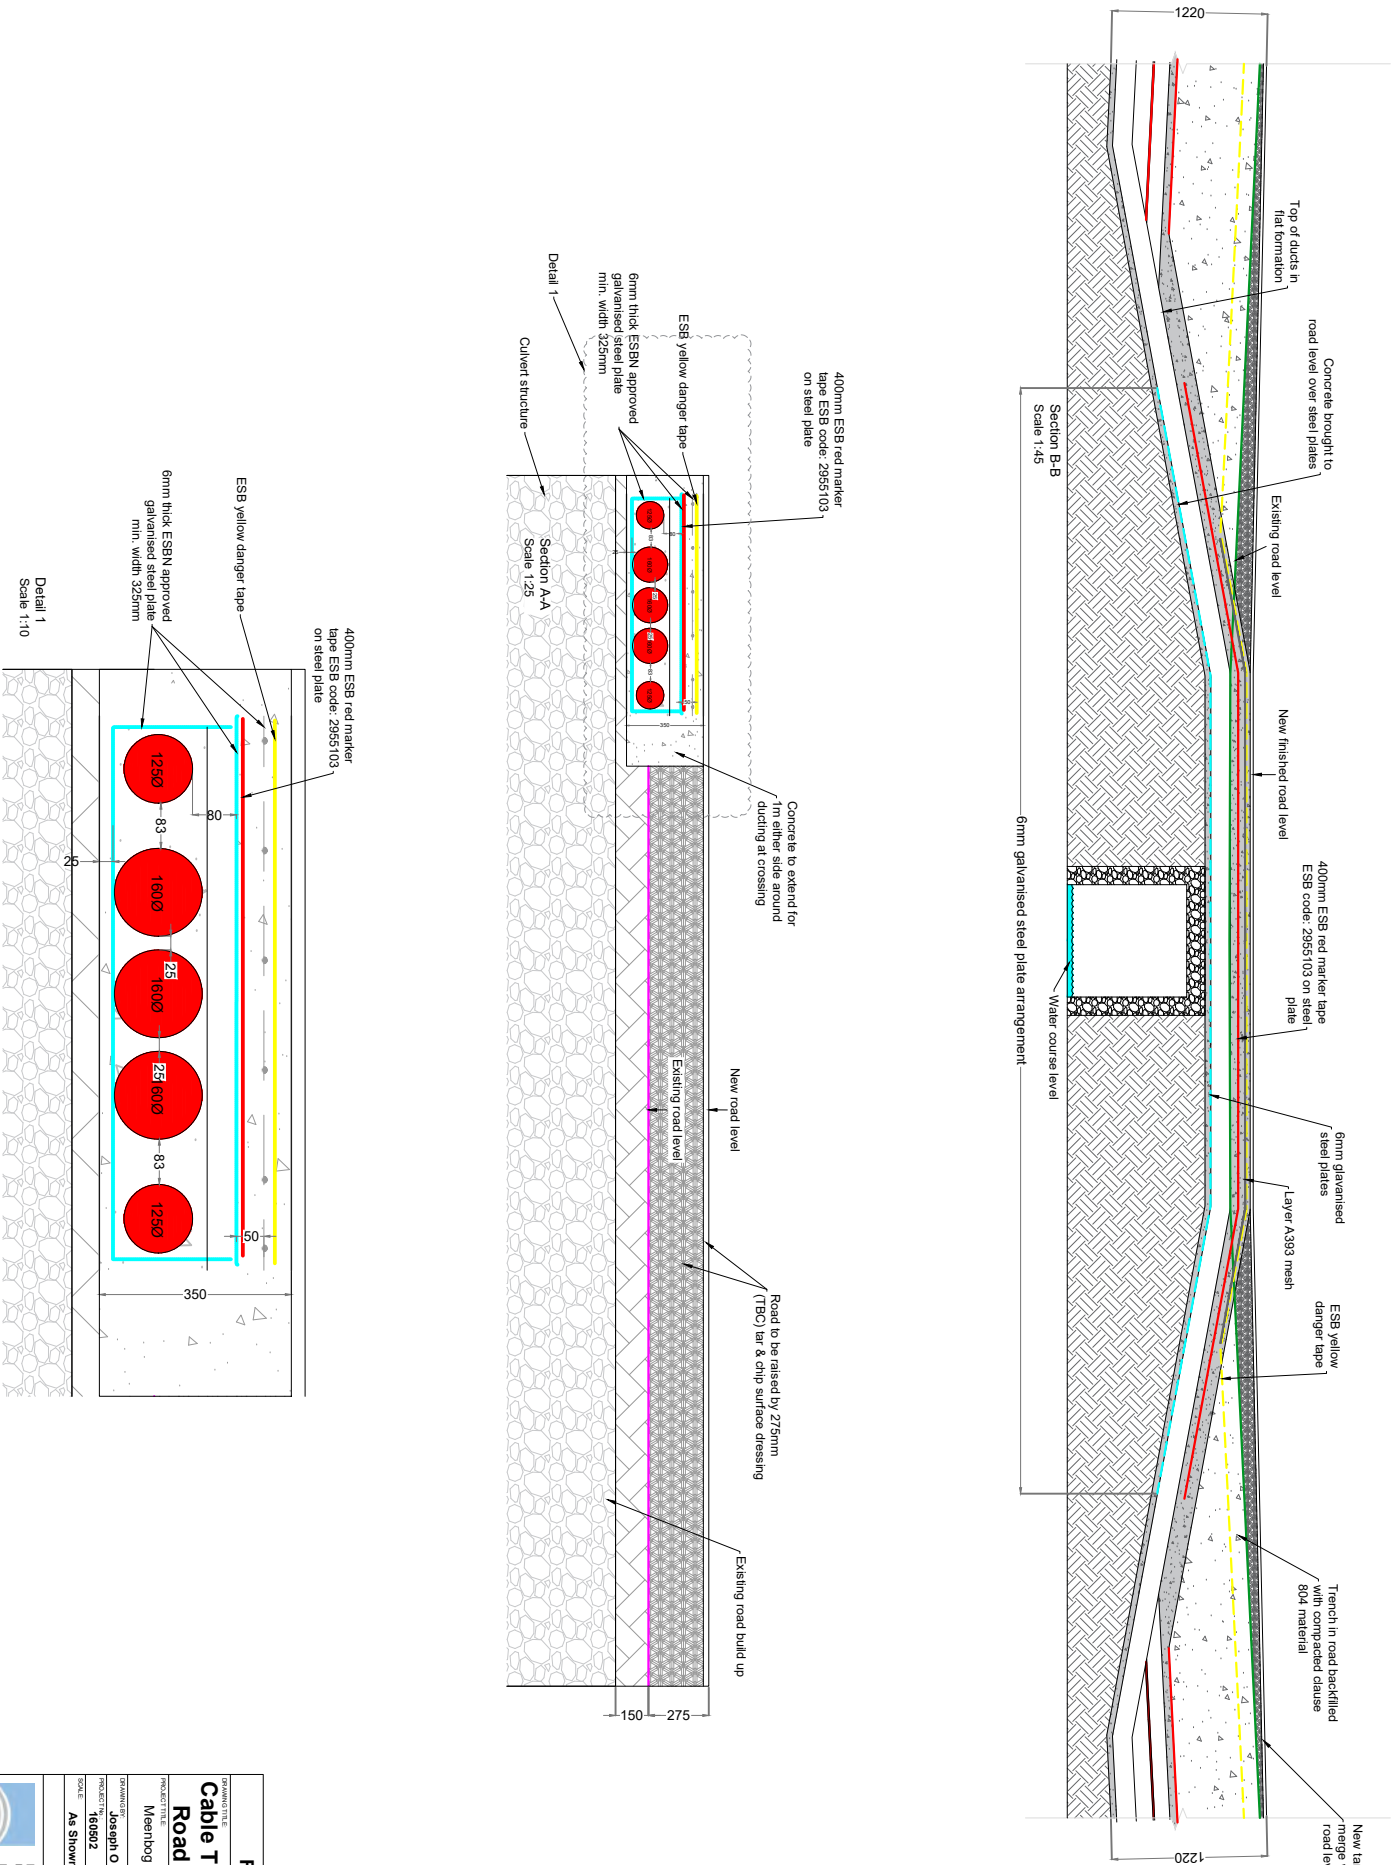


Figure 2.7

DRAWING TITLE	Cable Trench Flatbed at Road Surface Level		
PROJECT TITLE	Meenbrog Wind Farm, Co. Donegal		
DRAWING NO.	160902	DATE	20.12.2018
DESIGNED BY	Joseph O'Brien	CHECKED BY	Michael Watson
SCALE	As Shown @ A3		

McCarthy Kenille O'Sullivan Ltd.
 Planning & Environmental Consultants
 Block 1,
 Newry Park,
 Galway, Ireland
 email: info@mcCarthyKenille.com
 website: www.mcCarthyKenille.com
 Tel: +353 91 77219
 Fax: +353 91 77219

The flatbed formation methodology will also be used at bridge structures where there is an existing footpath. The cables will be installed in the same flatbed arrangement where the existing footpath will be excavated to allow for the installation of the cables. The footpath will be reinstated after cable ducts have been installed. Where there is no existing footpath, it is proposed to install a footpath to encase the cable ducts after they have been laid in the flatbed formation.

Directional Drilling – Option 4

In the event that none of the above methods are appropriate, directional drilling will be utilised.

The directional drilling method of duct installation will be carried out using Vermeer D36 x 50 Directional Drill (approximately 22 tonnes), or similar plant, will be utilised for the horizontal directional drilling at watercourse/culvert crossings listed above. The launch and reception pits will be approximately 0.55m wide, 2.5m long and 1.5m deep. The pits will be excavated with a suitably sized excavator. The drilling rig will be securely anchored to the ground by means of anchor pins which will be attached to the front of the machine. The drill head will then be secured to the first drill rod and the operator shall commence to drill into the launch pit to a suitable angle which will enable him to obtain the depths and pitch required to the line and level of the required profile. Drilling of the pilot bore shall continue with the addition of 3.0m long drill rods, mechanically loaded and connected into position.

During the drilling process, a mixture of a natural, inert and fully biodegradable drilling fluid such as *Clear Bore™* and water is pumped through the centre of the drill rods to the reamer head and is forced in to void and enables the annulus which has been created to support the surrounding subsoil and thus prevent collapse of the reamed length. Depending on the prevalent ground conditions, it may be necessary to repeat the drilling process by incrementally increasing the size of the reamers. When the reamer enters the launch pit, it is removed from the drill rods which are then passed back up the bore to the reception pit and the next size reamer is attached to the drill rods and the process is repeated until the required bore with the allowable tolerance is achieved.

The use of a natural, inert and biodegradable drilling fluid such as *Clear Bore™* is intended to negate any adverse impacts arising from the use of other, traditional polymer-based drilling fluids and will be used sparingly as part of the drilling operations. It will be appropriately stored prior to use and deployed in the required amounts to avoid surplus. Should any excess drilling fluid accumulate in the reception or drilling pits, it will be contained and removed from the site in the same manner as other subsoil materials associated with the drilling process to a licensed recovery facility.

Backfilling of launch & reception pits will be conducted in accordance with the normal specification for backfilling excavated trenches. The directional drilling methodology is further detailed in Figure 2.8.

Horizontal Drilling – Option 5

The process of horizontal drilling is carried out by an auger boring machine. The methods employed are similar to directional drilling (a launch and reception pit are required). The drilling pit for horizontal drilling is excavated to a depth greater than that required for directional drilling. This is necessary as the drilling process is horizontal only and cannot drill in a downward direction to get under a watercourse as in the case of directional drilling. Therefore, the drilling pit is excavated to a base level

at which the drilling will take place which will be a minimum of 3 metres below the bed of the watercourse. The auger boring machine is mobilised within the drilling pit where an air driven auger cutting head bores through the ground horizontally. The drilled bore is supported by a steel sleeve which is hammered through the opening by air compressors during drilling to avoid collapse. The spoil material passes back through the auger within the steel sleeve and out of the bored channel. The process is continued until the crossing reaches the opposing reception pit on the other side of the watercourse. Electrical ducts will be passed through the sleeves and the steel sleeves will then be removed. The entire excavation will be backfilled as necessary. The horizontal drilling methodology is illustrated in Figure 2.9.

Table 2.1 Grid Connection Route Bridge Crossings Methodology

Bridge Crossing no.	Name	Description	Watercourse Crossing Option	Extent of In-stream Works
1	Lowerymore Bridge	The existing bridge consists of a concrete deck which cannot be excavated for a cable trench therefore the cable will be installed under the watercourse by means of directional or horizontal drilling which will ensure that no contact will be made with the watercourse during the works.	Option 4	None. No in-stream works required.
2	Lower Keadew Bridge	The existing bridge consists of a concrete deck which cannot be excavated for a cable trench therefore the cable will be installed under the watercourse by means of directional or horizontal drilling which will ensure that no contact will be made with the watercourse during the works.	Option 4	None. No in-stream works required.
3	Barnesmore Bridge	Stone arch bridge which cannot be excavated for a cable trench therefore the cable will be installed under the watercourse by means of directional or horizontal drilling which will ensure that no contact will be made with the watercourse during the works.	Option 4	None. No in-stream works required.

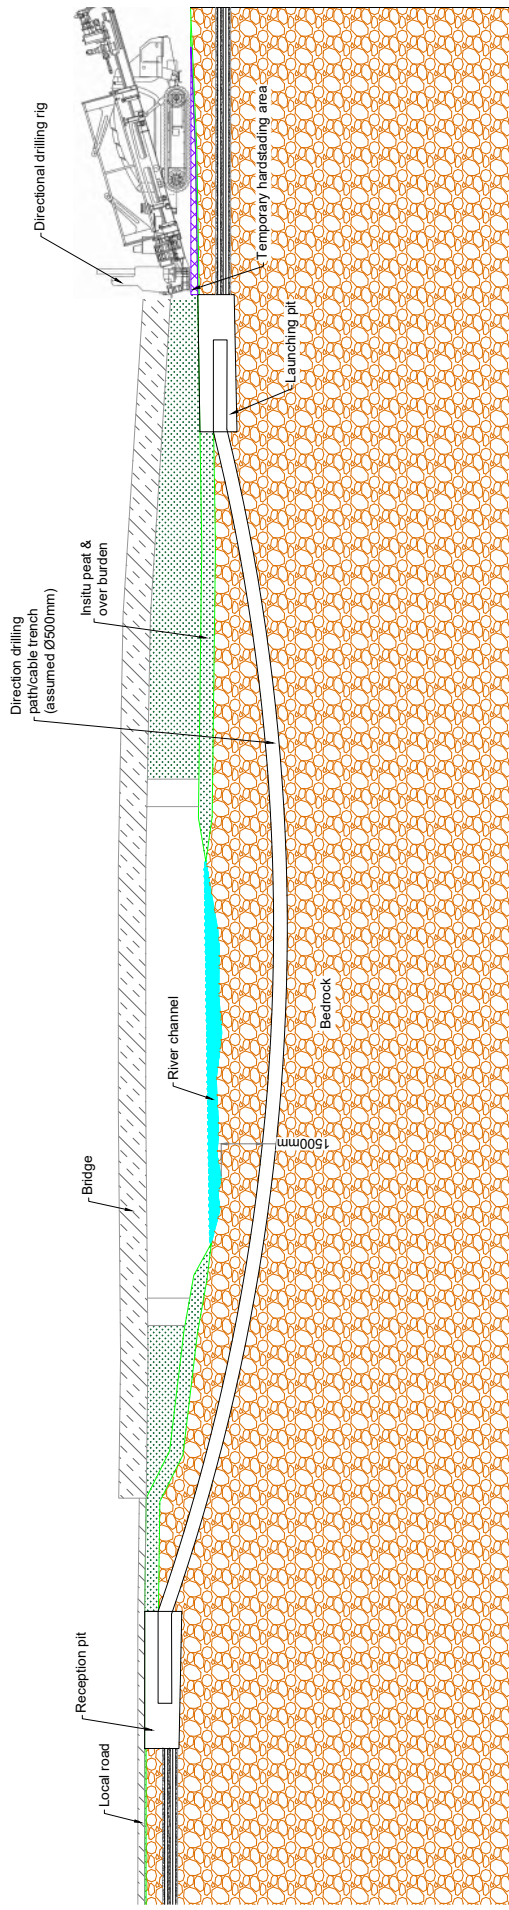


Figure 2.8

Directional Drilling

PROJECT FILE: Meenbog Wind Farm, Co. Donegal

DRAWN BY: Joseph O'Brien

CHECKED BY: Michael Watson

PROJECT NO: 160902

EXPIRES: 0902 - 57

SCALE: 1:200 @ A3

DATE: 20.12.2018

McCarthy Keville O'Sullivan Ltd.
 Planning & Environmental Consultants
 Block 1, Industrial Estate, Carrisheen Centre,
 Newry Road, Carrisheen,
 Maryborough Road,
 Galway, Ireland.
 website: www.mcskoyos.ie
 email: info@mcskoyos.ie
 Tel: +353 91 771279
 Fax: +353 91 771279

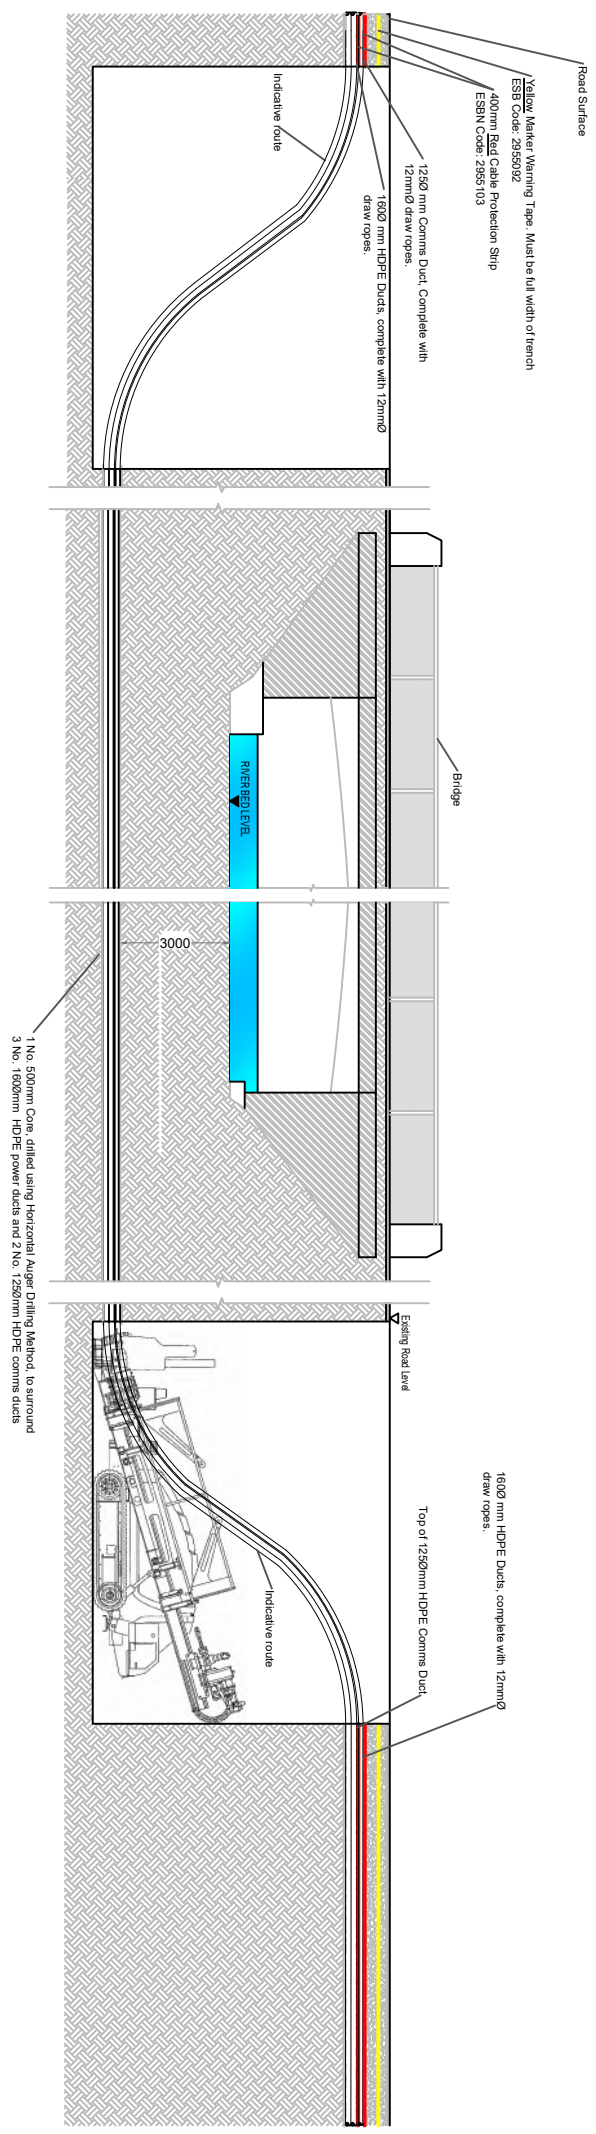


Figure 2.9

DRAWING TITLE	
Horizontal Auger Drilling	
PROJECT TITLE	
Meenbrog Wind Farm, Co. Donegal	
DRAWN BY	CHECKED BY
Joseph O'Brien	Michael Watson
PROJECT NO.	DATE
160802	0902 - 58
SCALE	
1: 150 @ A2	20.12.2018

McCarthy Keville O'Sullivan Ltd.
 Planning & Environmental Consultants
 Block 1,
 Gateway Financial Services Centre,
 Newry Road,
 Galway, Ireland
 email: info@mcCarthyKeville.com
 website: www.mccarthyKeville.com
 Fax: +353 91 77219

2.4.2.11.5 General Construction Measures

Prior to any works commencing a dilapidation survey will be conducted of the entire grid connection route, photographing and noting any existing damage or defects to structure or road surfaces. A copy of this survey will be submitted to Donegal County Council prior to works commencing.

Communication with the public, local residences and businesses along the route will be an important responsibility of the project supervisor. Keeping all affected parties up to date and informed both shortly prior and during the construction period at all times. Two to three weeks before any work commencing reasonable efforts will be made to inform all affected parties of the oncoming works.

Signage will be erected in the weeks prior to any works commencing along and on adjacent roads to the cable route notifying the public of the forthcoming construction. Contact details for the contractor and details of license will also be posted along the cable route during construction.

Every effort will be made to minimise the impact of the above works on local residences and traffic. Consideration will also be given to the agricultural community and works will be organised and sequenced so as not to inconvenience any such activities.

- All personnel will be inducted and made familiar with the method statements, risk assessments and traffic management plans involved.
- All site-specific safety rules will be adhered to.
- All plant operators will have appropriate CSCS training.
- All personnel will have SOLAS Safe Pass training
- Fire extinguishers and first aid supplies will be available in the work area.
- The road way will be maintained in clean condition at all times.
- Helmets, high visibility clothing and safety footwear will be worn at all times.
- A competent foreman will be on site at all times.
- Excavations are back filled at the end of each working day.
- The trench will not be over crowded.
- Unauthorised access will be monitored and prevented.
- Pipe work will be lifted into position manually.
- Hand dig will be used to expose any services detected during the survey.

2.4.2.12 Recreation and Amenity Areas

The recreation and amenity facilities consist of a series of marked walkways, complimented by waypoint signage, and visitor facilities in the form of a car park, play areas, barbeque area, picnic area and community garden. The walkways will be constructed with the same methodology for site access roads. The temporary construction compound located in the north of the site will provide an amenity area within the site once the Permitted Development has been commissioned. This area will be developed as a compound initially so it will be well established requiring only minor works to accommodate the facilities.

Waypoint signage will be installed throughout the recreation and amenity area to provide information and location reference point for facility users. The signage will be installed as part of the amenity walkway construction where the signage poles will be erected in concrete footings.

2.4.2.13 Decommissioning

The design life of the wind farm is 30 years after which time decommissioning will occur. At the end of the design life of the wind farm, or if the operations at the wind farm cease for a period of greater than one year, the turbines, met mast and all their

associated above ground components will be removed from site. The turbine foundations will be covered with soil to facilitate re-vegetation. The management of waste materials arising from the decommissioning of the development is outlined in the Waste Management Plan (Section 4 below).

Site roadways could be in use for other purposes other than the wind operation of the wind farm by the time the decommissioning of the project is to be considered, and therefore it may be more appropriate to leave the site roads in situ for future use. If it were to be confirmed that the roads were not required in the future for any other useful purpose, they could be removed

The substation will remain in place as it will be under the ownership of the ESB/EirGrid. Underground cables will be removed and the ducting left in place.

A full reinstatement plan will be submitted to Donegal County Council three months prior to decommissioning.

3 ENVIRONMENTAL MANAGEMENT

3.1 Introduction

This CEMP has been prepared and presented as a standalone document and includes all drainage measures required to construct the wind farm. The drainage proposals will be developed further prior to the commencement of construction however, any such improvements will be in line with the principles and mitigation presented in the EIAR. The following sections give an overview of the drainage design, dust and noise control measures and a waste management plan for the site.

3.2 Protecting Water Quality

3.2.1 Environmental Management in the Construction Phase

Timing of road works can strongly influence the potential for damaging the freshwater environment. Operations during wetter periods of the year pose a significantly greater risk of causing erosion and siltation, which can be particularly severe following major rainfall or snowmelt events. Traditionally, wind farm construction undertaken during the drier summer months would result in significantly less erosion and siltation. Construction activities in the hydrological buffer zones shall be avoided during or after prolonged rainfall or an intense rainfall event and work will cease entirely near watercourses when it is evident that water quality is being impacted. Given that this site has an established road network and existing watercourse crossing points, there will be minimal impacts on watercourses.

3.2.2 Site Drainage Design

The site drainage features for this site have previously been outlined in Section 4.7 of the EIAR and are again further developed in Section 4 of this CEMP. The protection of the watercourses within and surrounding the site, and downstream catchments that they feed is of utmost importance in considering the most appropriate drainage proposals for the site of the Permitted Development. No routes of any natural drainage features will be altered as part of the Permitted Development as new watercourse crossings are kept to a minimum to facilitate the Permitted Development. Turbine locations and associated roadways were originally selected to avoid natural watercourses and existing roads are to be used wherever possible. The Permitted Development has where possible, been kept a minimum of 50 metres from natural watercourses. There will be no direct discharges to any natural watercourses, with all drainage waters being dispersed as overland flows. Buffer zones around the existing natural drainage features have informed the layout of the Permitted Development.

Existing artificial drains in the vicinity of existing site roads will be maintained in their present location where possible. If it is expected that these artificial drains will receive drainage water from works areas, check dams will be added (as specified below) to control flows and sediment loads in these existing artificial drains. If road widening or improvement works are necessary along the existing roads, where possible, the works will take place on the opposite side of the road to the drain.

3.2.3 Legislation and Best Practice Guidance

The drainage design has been prepared based on experience of the project team of other wind farm sites in peat-dominated environments, and the number of best practice guidance documents.

There is no one guidance document that deals with drainage management and water quality controls for wind farm developments. However, a selection of good practice approaches have been adopted in preparation of this CEMP, and these are taken from the various best practice guidance documents listed below. These relate to infrastructure and operational works on forested sites, forest road design, water quality controls for linear projects, forestry road drainage and management of geotechnical risks. To achieve best practice in terms of water protection through construction management all drainage management is prepared in accordance with guidance contained in the following:

- Forestry Commission (2004): Forests and Water Guidelines, Fourth Edition. Publ. Forestry Commission, Edinburgh;
- Coillte (2009): Forest Operations & Water Protection Guidelines;
- Forest Service (Draft): Forestry and Freshwater Pearl Mussel Requirements – Site Assessment and Mitigation Measures;
- Forest Service (2000): Forestry and Water Quality Guidelines. Forest Service, DAF, Johnstown Castle Estate, Co. Wexford;
- Forest Service, (2000): Code of Best Forest Practice – Ireland. Forest Service, DAF, Johnstown Castle Estate, Co. Wexford;
- COFORD (2004): Forest Road Manual – Guidelines for the design, construction and management of forest roads;
- MacCulloch (2006): Guidelines for risk management of peat slips on the construction of low volume low cost roads over peat (Frank MacCulloch Forestry Civil Engineering Forestry Commission, Scotland);
- Authority (2005): Guidelines on Procedures for Assessment and Treatment of Geology, Hydrology and Hydrogeology for National Road Schemes;
- Wind Farm Development Guidelines for Planning Authorities (September 1996);
- Requirements for the Protection of Fisheries Habitat during Construction and Development Works at River Sites. Eastern Regional Fisheries Board;
- Guidelines on Protection of Fisheries During Construction Works Adjacent to Waters, Inland Fisheries Ireland (2016);
- Good Practice During Wind Farm Construction (Scottish Natural Heritage, 2010);
- PPG1 - General Guide to Prevention of Pollution (UK Guidance Note);
- PPG5 – Works or Maintenance in or Near Water Courses (UK Guidance Note);
- CIRIA (Construction Industry Research and Information Association) guidance on 'Control of Water Pollution from Linear Construction Projects' (CIRIA Report No. C648, 2006);
- Control of water pollution from construction sites - Guidance for consultants and contractors. CIRIA C532. London, 2001; and,
- Control of water pollution from linear construction projects -Technical guidance. CIRIA C648 London, 2006.

3.2.4 Site Drainage and Management

3.2.4.1 Preparative Site Drainage Management

The materials and equipment necessary to implement the drainage measures outlined above will be brought on-site in advance of any works commencing.

An adequate quantity of straw bales, clean stone, terram, stakes, etc. will be kept on site at all times to implement the drainage design measures as necessary. The drainage measures outlined in the above will be installed prior to, or at the same time as the works they are intended to drain.

3.2.4.2 Pre-emptive Site Drainage Management

The works programme for the groundworks element of the construction phase will take account of weather forecasts and predicted rainfall in particular. Large excavations, large movements of overburden or large-scale overburden or soil stripping will be suspended or scaled back if heavy rain is forecast. The extent to which works will be scaled back or suspended will relate directly to the amount of rainfall forecast.

3.2.4.3 Reactive Site Drainage

The final drainage design prepared for the site has provided for reactive management of drainage measures. The effectiveness of drainage measures designed to minimise runoff entering works areas and capture and treat silt-laden water from the works areas, will be monitored continuously by the Environmental Clerk of Works (ECoW) on-site. The ECoW or supervising hydrologist will respond to changing weather, ground or drainage conditions on the ground as the project proceeds, to ensure the effectiveness of the drainage design is maintained in so far as is possible. This may require the installation of additional check dams, interceptor drains, or swales as deemed necessary on-site. The drainage design may have to be modified on the ground as necessary, and the modifications will draw on the various features outlined above in whatever combinations are deemed to be most appropriate to situation on the ground at a particular time.

In the event that works are giving rise to siltation of watercourses, the ECoW or supervising hydrologist will stop all works in the immediate area around where the siltation is evident. The source of the siltation will be identified and additional drainage measures such as those outlined above will be installed in advance of works recommencing.

3.2.4.4 Operational Phase Drainage

The project hydrologist will inspect and review the drainage system after construction has been completed to provide guidance on the requirements of an operational phase drainage system. This operational phase drainage system will have been installed during the construction phase in conjunction with the road and hardstanding construction work as described below:

- Interceptor drains will be maintained up-gradient of all infrastructure to collect clean surface runoff, in order to minimise the amount of runoff reaching areas where suspended sediment could become entrained. It will then be directed to areas where it can be re-distributed over the ground by means of a level spreader.
- Swales/road side drains will be maintained to intercept and collect runoff from access roads and hardstanding areas of the site, likely to have entrained suspended sediment, and channel it to stilling ponds for sediment settling;
- Check dams will be maintained at regular intervals along interceptor drains and swales/roadside drains in order to reduce flow velocities and therefore minimise erosion within the system during storm rainfall events; and,
- Stilling ponds/settlement ponds, emplaced downstream of swales and roadside drains, will buffer volumes of runoff discharging from the drainage system during periods of high rainfall, by retaining water until the storm hydrograph has receded, thus reducing the hydraulic loading to watercourses. The stilling ponds will be sized according to the size of the area they will be receiving water from but will be sufficiently large to accommodate peak flows storm events. Inspection and maintenance of all settlement ponds will be ongoing through the construction period.

3.3 Refuelling, Fuel and Hazardous Materials Storage

The following mitigation measures are proposed to avoid release of hydrocarbons at the site:

- Minimal refuelling or maintenance of construction vehicles or plant will take place on site. Off-site refuelling should occur at a controlled fuelling station;
- On-site refuelling will take place using a mobile double skinned fuel bowser. The fuel bowser, a double-axel custom-built refuelling trailer will be re-filled off site and will be towed around the site by a 4x4 jeep to where machinery is located. It is not practical for all vehicles to travel back to a single refuelling point, given the size of the cranes, excavators, etc. that will be used during the construction of the wind farm. The 4x4 jeep will also carry fuel absorbent material and pads in the event of any accidental spillages. The fuel bowser will be parked on a level area in the construction compound when not in use. Only designated trained and competent operatives will be authorised to refuel plant on site. Mobile measures such as drip trays and fuel absorbent mats will be used during all refuelling operations.
- Fuels volumes stored on site should be minimised. Any fuel storage areas will be bunded appropriately for the fuel storage volume for the time period of the construction and fitted with a storm drainage system and an appropriate oil interceptor;
- The electrical substation building will be bunded appropriately to the volume of oils likely to be stored, and to prevent leakage of any associated chemicals and to groundwater or surface water. The bunded area will be fitted with a storm drainage system and an appropriate oil interceptor;
- The plant used should be regularly inspected for leaks and fitness for purpose; and,
- An emergency plan for the construction phase to deal with accidental spillages will be contained within Environmental Management Plan. Spill kits will be available to deal with and accidental spillage in and outside the refuelling area.

3.4 Cement Based Products Control Measures

The following mitigation measures are proposed to avoid release of cement leachate from the site:

- No batching of wet-cement products will occur on site;
- Ready-mixed supply of wet concrete products and where possible, emplacement of pre-cast elements, will take place. Where possible pre-cast elements for culverts and concrete works will be used;
- No washing out of any plant used in concrete transport or concreting operations will be allowed on-site;
- Where concrete is delivered on site, only chute cleaning will be permitted, using the smallest volume of water possible. No discharge of cement contaminated waters to the construction phase drainage system or directly to any artificial drain or watercourse will be allowed.
- Use weather forecasting to plan dry days for pouring concrete;
- Ensure pour site is free of standing water and plastic covers will be ready in case of sudden rainfall event;
- The small volume of water that will be generated from washing of the concrete lorry's chute will be directed into a concrete washout area, typically built using straw bales and lined with an impermeable membrane. Two examples are shown in Plates 3.1 and 3.2 below. The areas are generally covered when not in use to prevent rainwater collecting. In periods of dry weather, the areas can be

uncovered to allow much of the water to be lost to evaporation. At the end of the concrete pours, any of the remaining liquid contents is tankered off-site. Any solid contents that will have been cleaned down from the chute will have solidified and can be broken up and disposed of along with other construction waste.

The 50m wide river buffer zone and 20 m existing artificial drainage buffer will be emplaced for the duration of the construction phase. No construction activity will occur within the buffer zone with the exception of bridge and culvert construction. The buffer zone will:

- Prevent any cement based products accidentally entrained in the construction phase drainage system entering directly into watercourses, achieved in part by ending drain discharge outside the 50m buffer zone and allowing percolation across the vegetation of the buffer zone;
- Provide a buffer against accidental direct run-off to surface waters by any pollutants, or by pollutants entrained in surface water run-off.



Plate 3.1 Concrete washout area



Plate 3.2 Concrete washout area

3.5 Peat Stability Management

The management of the peat volumes summarised in Section 2.4.2.2 in terms of peat stability is summarised in this section. Peat instability or failure refers to a significant mass movement of a body of peat that would have an adverse impact on wind farm development and the surrounding environment. Peat failure excludes localised movement of peat that could occur below an access road, creep movement or erosion type events. In the absence of appropriate mitigation, the consequence of peat failure at the study area may result in:

- Death or injury to site personnel;
- Damage to machinery;
- Damage or loss of access tracks;
- Drainage disrupted;
- Site works damaged or unstable;
- Contamination of watercourses, water supplies by sediment particulates; and,
- Degradation of the environment.

3.5.1 General Recommendations for Good Construction Practice

The peat stability assessment indicates that there is insignificant risk of peat failure, although drainage mitigation measures would be required to prevent the build-up of water in the peat and reduce the risk of failure (AGEC, 2017).

The following issues incorporated into the construction phase of the project will assist in the management of the risks for this site (AGEC, 2017):

- Appointment of experienced and competent contractors;
- The site should be supervised by experienced and qualified personnel;
- Allocate sufficient time for the project (be aware that decreasing the construction time has the potential to increase the risk of initiating a peat movement);
- Prevent undercutting of slopes and unsupported excavations;
- Maintain a managed robust drainage system;
- Prevent placement of loads/overburden on marginal ground;
- Set up, maintain and report readings from peat stability monitoring systems;
- Ensure construction method statements are followed or where agreed modified/ developed; and,
- Revise and amend the Geotechnical Risk Register as construction progresses.

3.6 Traffic Management

Traffic Management Plans for the construction phase of the wind farm and grid connection are included in Appendix 4. The Traffic Management Plans have been prepared to consider both the wind farm and the grid connection works as standalone projects.


Where grid connection works relating to the Meenbog Wind Farm are ongoing, the contractor will schedule and phase these works accordingly to ensure that these works do not coincide with intensive periods of construction on the wind farm development and thus reduce the impact of concurrent construction specific to the wind farm.

3.6.1 Turbine and Materials Transport Route

Material such as concrete will be sourced from a local quarry and will access the site using the N15 as the primary haul route to access the site as outlined in Figure 3.1. All deliveries will access the site via the western or northern entrance using this haul route. All deliveries of construction materials to the site will take place within the defined working hours of 7am – 7pm. It may be necessary on occasion, to commence works before 7am where concrete pours will be required to start earlier due to the volume of concrete required and the location of the concrete pour relative to the concrete supplier's batching plant. Main pours will be planned days and weeks in advance and will ensure disruption to work and school related traffic is avoided. The locations of all turbine foundations where large concrete pours will take place are off the public road and will be accessed by the internal site roads and will therefore eliminate the potential for queuing of trucks on the adjoining public road network. The typical vehicle type for delivery of construction materials to site with the exception of the wind turbines will be with standard heavy goods vehicles (HGV).

A detailed traffic and transport management plan for turbine delivery will be prepared by the haulage company, when appointed and will be submitted to Donegal County Council for approval. The plan will include:

- A delivery schedule.
- A schedule of control measures for exceptional wide and heavy loads.
- Details of temporary works or any other minor alteration identified.
- A dry run of the route using vehicles with similar dimensions.

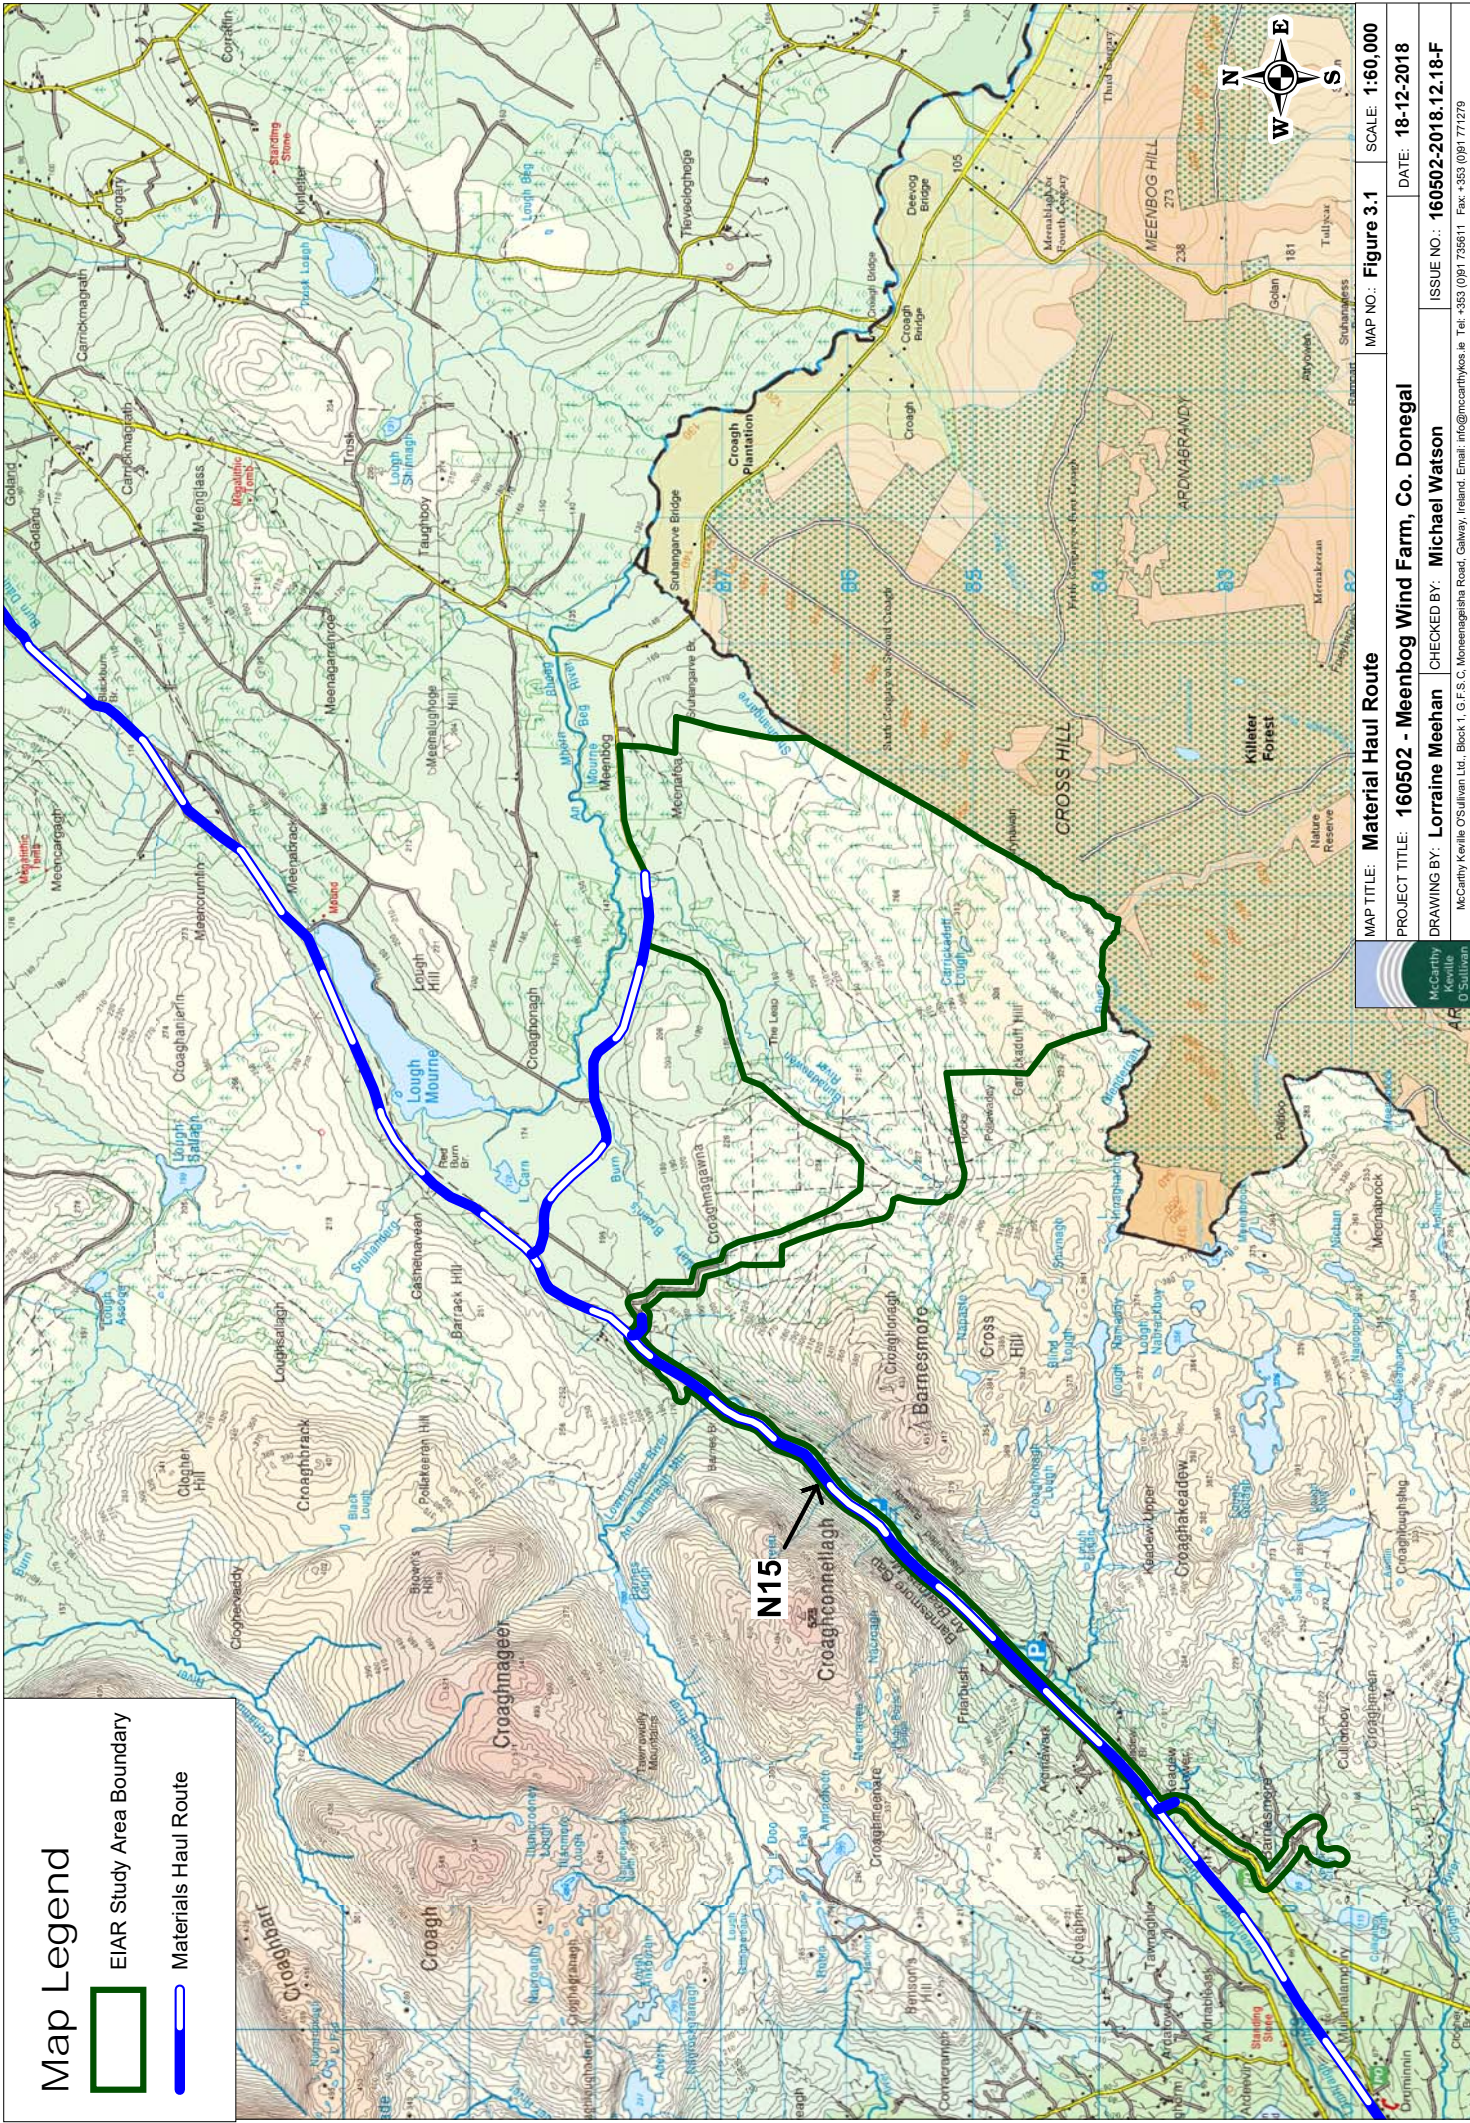

Map Legend

- EIA Study Area Boundary
- Materials Haul Route

MAP TITLE: **Material Haul Route**

MAP NO.: **Figure 3.1** SCALE: **1:60,000**

PROJECT TITLE: **160502 - Meenbog Wind Farm, Co. Donegal**

DATE: **18-12-2018**


DRAWING BY: **Lorraine Meehan** CHECKED BY: **Michael Watson**

ISSUE NO.: **160502-2018.12.18-F**

McCarty Kevin O'Sullivan Ltd., Block 1, G.F.S.C. Maresnagh Road, Galway, Ireland. Email: info@mcCarthyKos.ie Tel: +353 (0)91 736511 Fax: +353 (0)91 771279

Ordnance Survey Ireland Licence No. AR 0021817 © Ordnance Survey Ireland/Government of Ireland

Map Legend

 EIAR Study Area Boundary

 Turbine Delivery Route




Killybegs

DONEGAL BAY
Bá Dhún na nGall

MAP TITLE: Turbine Delivery Route

PROJECT TITLE: 160502 - Meenbog Wind Farm, Co. Donegal

DRAWING BY: Lorraine Meehan CHECKED BY: Michael Watson



McCarthy
Keady
O'Sullivan

Ordnance Survey Ireland Licence No. AR 0021817 © Ordnance Survey Ireland/Government of Ireland

MAP NO.: Figure 3.2 SCALE: 1:150,000

DATE: 18-12-2018

ISSUE NO.: 160502-2018.12.18-F

McCarthy Keady O'Sullivan Ltd., Block 1, G.F.S.C. Monaghan Road, Galway, Ireland. Email: info@mcCarthyKeady.com Tel: +353 (0)91 736611 Fax: +353 (0)91 771279

The turbine transport route from the N15 National Secondary Road to the development sites are shown on Figure 3.2 also. The deliveries of turbine components to the site will be made in convoys of three to four vehicles at a time, and mostly at night when roads are quietest. Convoys will be accompanied by escorts at the front and rear operating a "stop and go" system. Although the turbine delivery vehicles are large, they will not prevent other road users or emergency vehicles passing, should the need arise. The delivery escort vehicles will ensure the turbine transport is carried out in a safe and efficient manner with minimal delay or inconvenience for other road users. It is not anticipated that any section of the local road network will be closed during transport of turbines, although there will be some delays to local traffic at pinch points. During these periods it may be necessary to operate local diversions for through traffic. All deliveries comprising abnormally large loads will be made outside the normal peak traffic periods to avoid disruption to work and school-related traffic.

Prior to the Traffic Management Plan for turbine delivery being finalised, a full dry run of the transport operation along the proposed route will be completed using vehicles with attachments to simulate the dimensions of the wind turbine transportation vehicles. This dry run will inform the final traffic management plan. All turbine deliveries will be provided for in a transport management plan which will have to be prepared in advance of the turbine delivery stage, when the exact transport arrangements are known, delivery dates confirmed and escort proposals in place. Such a transport management plan is typically submitted to the Planning Authority for agreement in advance of any abnormal loads using the local roads, and will provide for all necessary safety measures, including a convoy and Garda escort as required, off-peak turning/reversing movements and any necessary safety controls.

The roads and bridges all haul route will be subject to a condition survey by a suitably qualified engineer both before and after construction. Protection measures for such infrastructure as specified by the appointed engineers report will be implemented in full prior to construction.

In the event of construction damage arising on any roads or bridges along the haul route it will be rectified immediately by the developer under consultation with the relevant roads engineer.

Prior to the delivery of oversized loads, the developer will engage with the local community to provided information on the scale, time and duration of such deliveries. This information will be informed by pre-delivery surveys which will be completed by the suppliers. This information will be relayed to the local community by information leaflet and a website if deemed necessary.









The proposed construction will run from February 2019 – July 2020 as summarised in Section 9 below. This is the timescale within which it is intended to use the public road network as outlined in Figures 3.1 & 3.2 to facilitate construction of the development.


3.7 Ecological Management

The construction works associated with the upgrade of the existing access track adjacent to the Croaghonagh Bog Special Area of Conservation (site code: 000129) shall not encroach upon the Special Area of Conservation. Figure 3.3 set out the location of Croaghonagh Bog relative to the development site.

Surveys for Irish Ladies tresses can only be conducted will be carried out prior to works in applicable areas between **early August and early September** (NRA 2009). Surveys

Map Legend

-  EIAR Study Area
-  Croaghonagh Bog SAC
-  Proposed Turbine Location
-  Existing Roads - Upgrade
-  Existing Tracks - Upgrade
-  New Roads
-  Amenity Walkways
-  Grid Connection Route

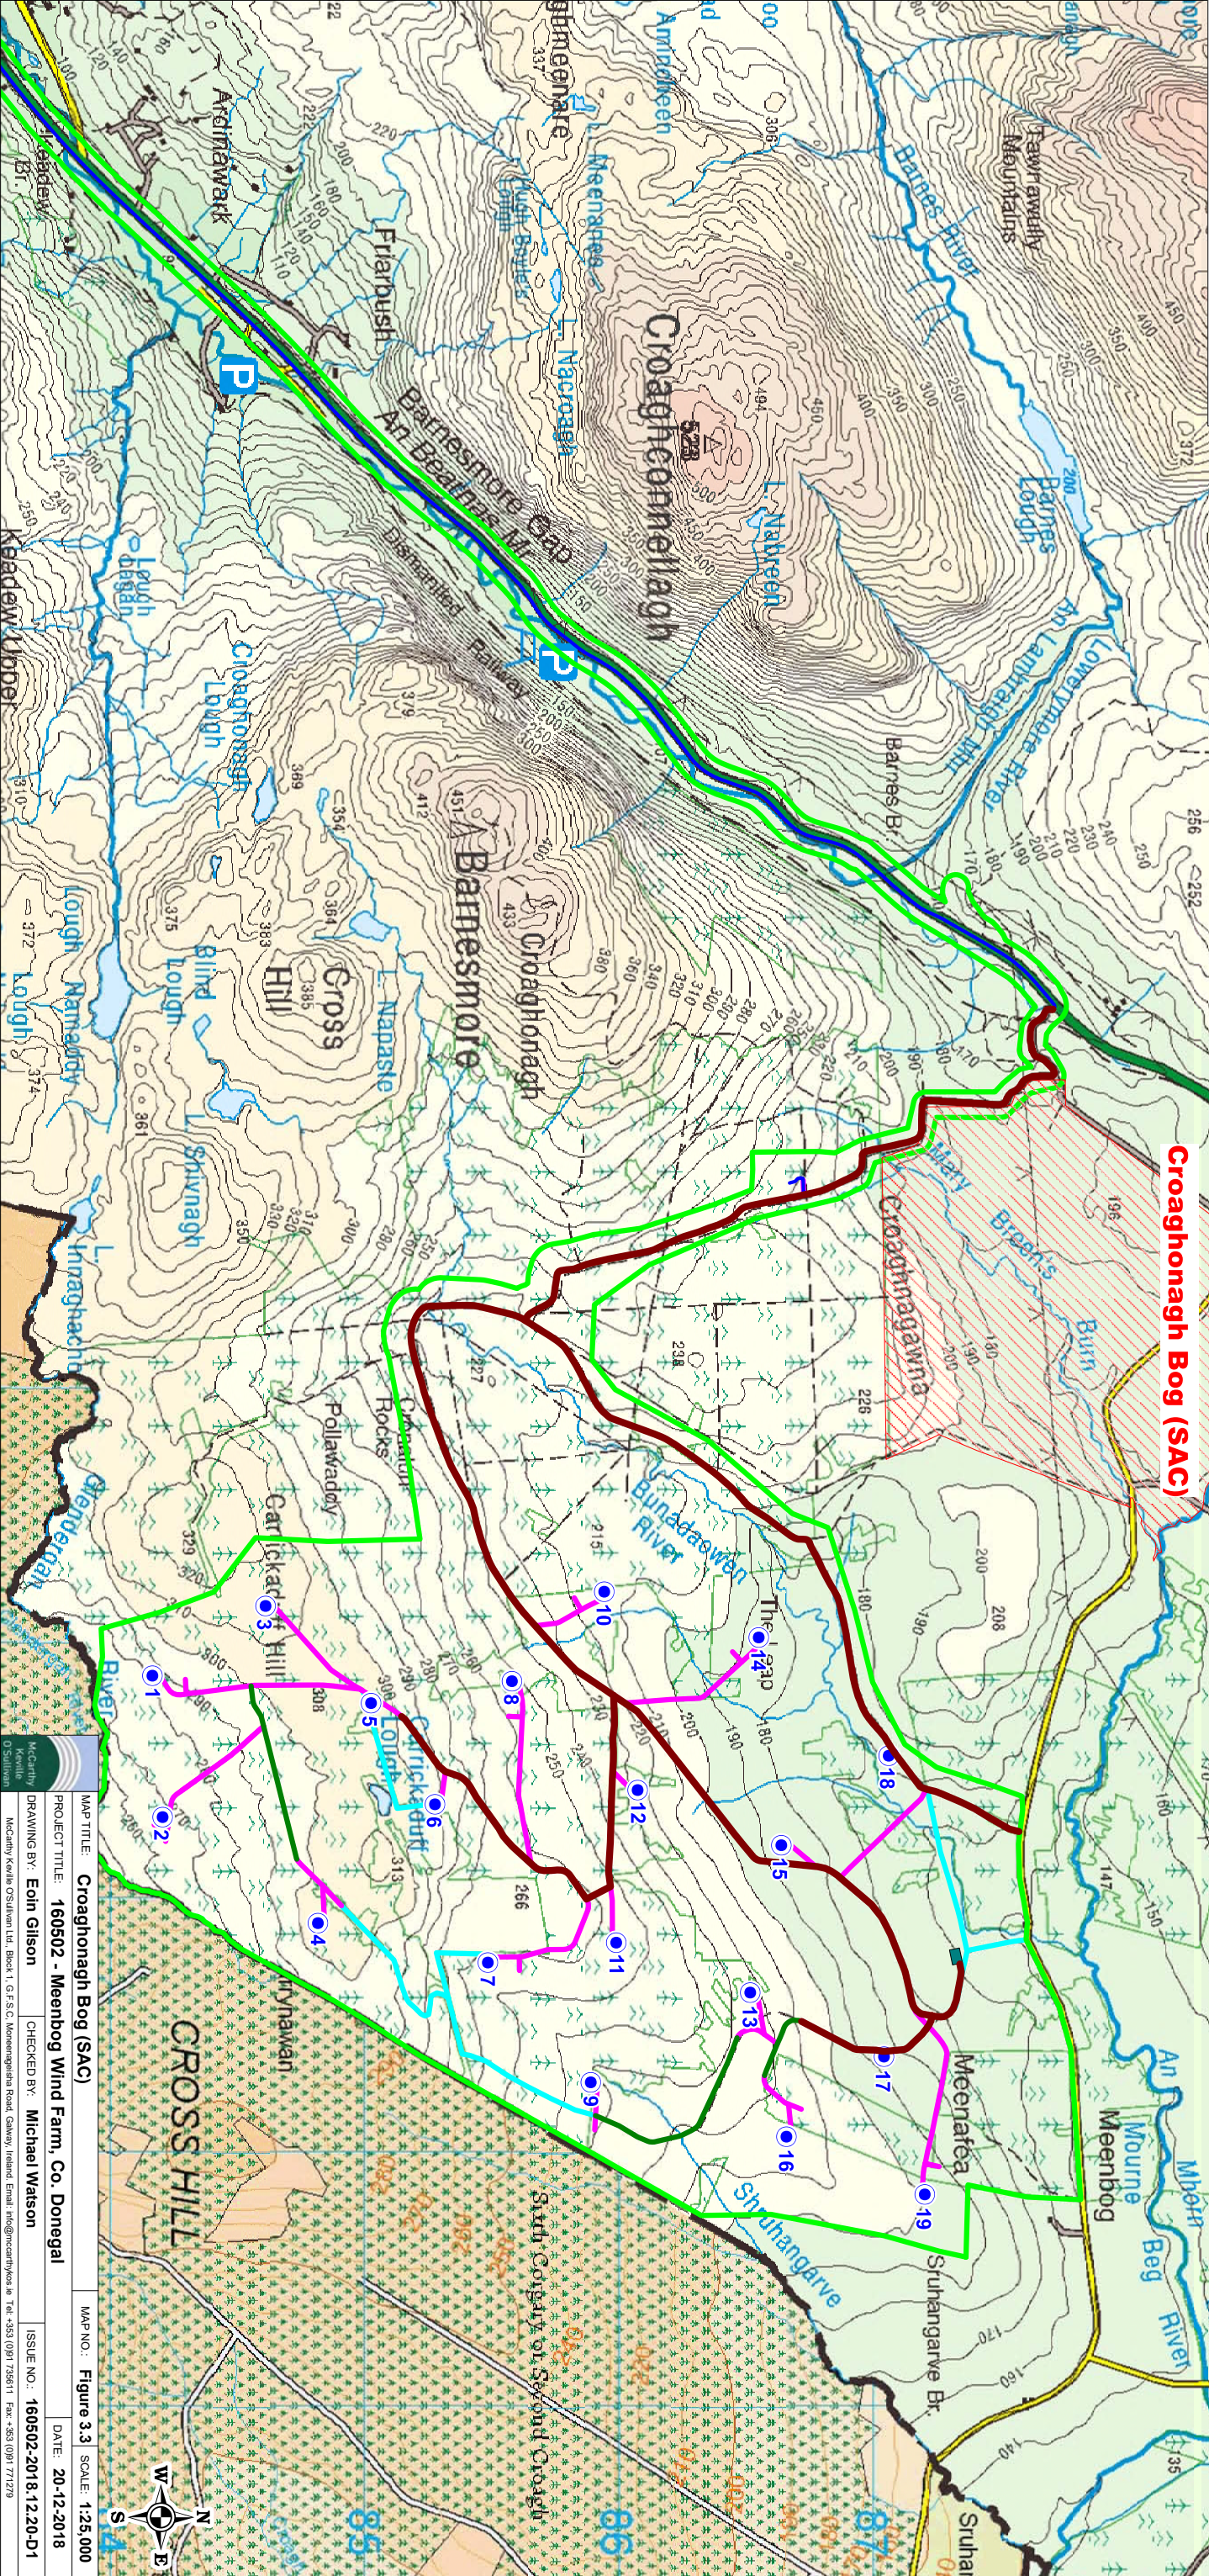

Land & Property Services Intellectual Property is protected by Crown Copyright and is reproduced with the permission of Land & Property Services under Delegated Authority from the Controller of HMSO, © Crown Copyright and database right Licence No. 2892 (2017)













Ordnance Survey Ireland Licence No. AR 0021815 © Ordnance Survey Ireland/Government of Ireland


MAP TITLE: **Croaghonagh Bog (SAC)** MAP NO.: **Figure 3.3** SCALE: **1:25,000**


PROJECT TITLE: **160502 - Meenbog Wind Farm, Co. Donegal** DRAWING BY: **Eoin Gilson** CHECKED BY: **Michael Watson** ISSUE NO.: **160502-2018.12.20-D1** DATE: **20-12-2018**

McIntyre Kevin O'Sullivan Ltd., Block 1, G.F.S.C. Meenaghalla Road, Glenties, Ireland Email: info@mcintyre.ie Tel: +353 (0)91 775811 Fax: +353 (0)91 771279

Legend

-  Globeflower & Irish lady's-tresses survey area
-  Proposed Turbine Location
-  Proposed Met Mast Location
-  Proposed New Roads
-  Grid Connection Cabling Route
-  Existing Tracks - Upgrade Proposed
-  Existing Roads - Upgrade Proposed
-  Proposed Substation Compound
-  EIA/R Study Area
-  Proposed Temporary Construction Compound
-  Proposed Borrow Pit Areas
-  Proposed Temporary Construction Compound/ Proposed Amenity Area

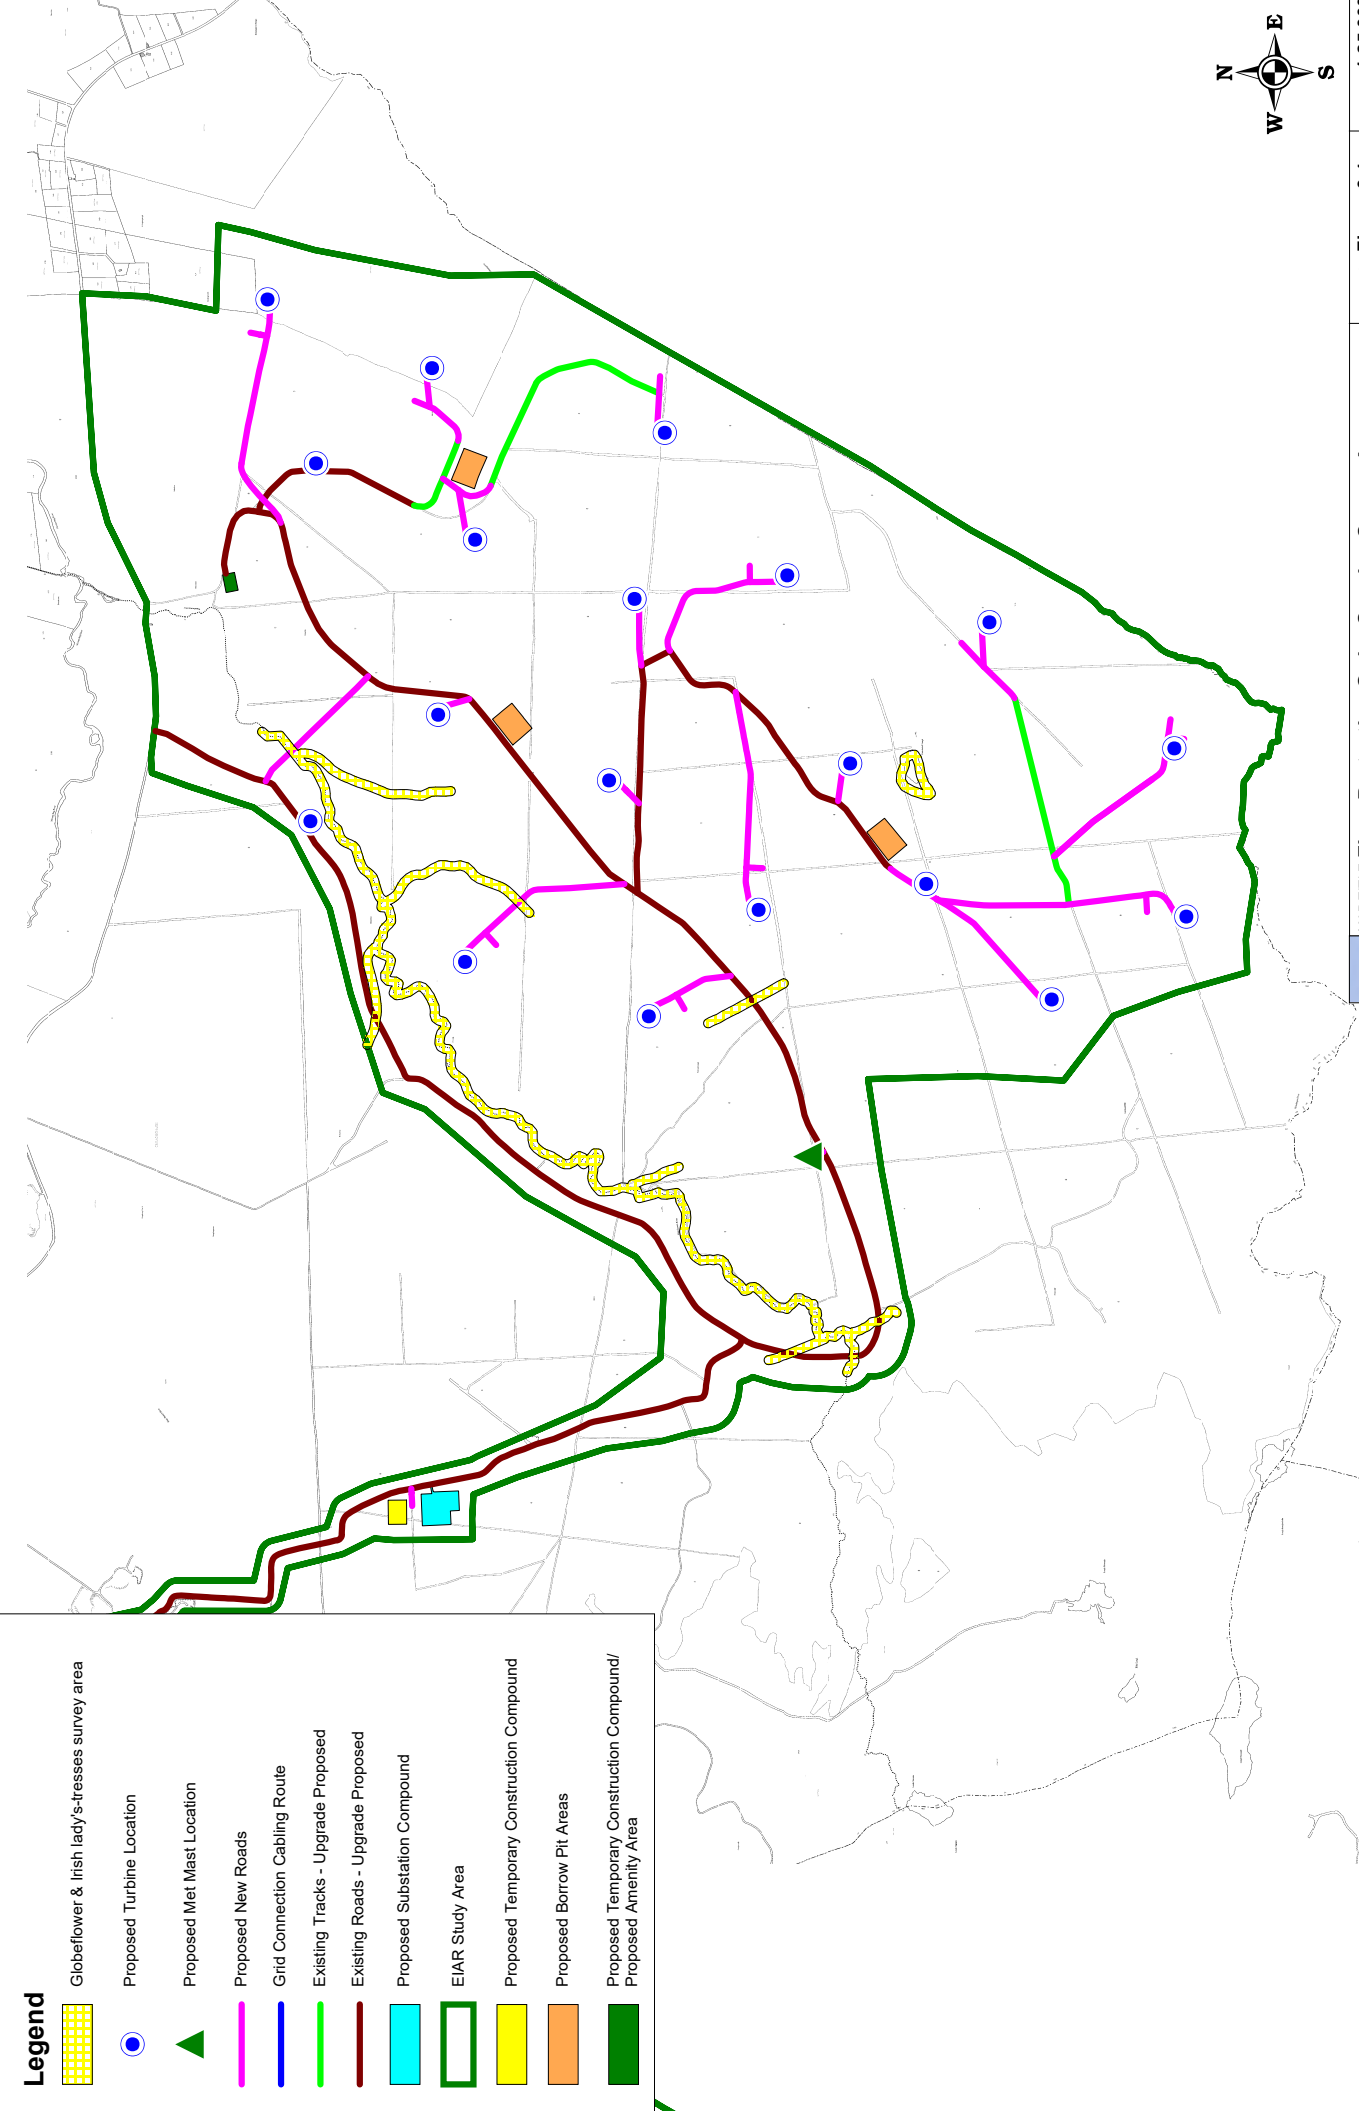

		MAP TITLE: Flora Protection Order Species Survey Area	MAP NO.: Figure 3.4	SCALE: 1:25,000
PROJECT TITLE: Meenbog Wind Farm		OS SHEET NO.: N/A	DATE: 17-11-2017	ISSUE NO.: 160502-2017.11.10-F
DRAWING BY: David McNicholas		CHECKED BY: Pat Roberts		
McCarthy Keville O'Sullivan Ltd., Block 1, G.F.S.C. Maresnangola Road, Galway, Ireland. Email: info@mcCarthyKeville.com Tel: +353 (0)91 736511 Fax: +353 (0)91 771279				
Ordnance Survey Ireland Licence No. AR 0021817 © Ordnance Survey Ireland/Government of Ireland				

for Globeflower will be conducted between **June and August**. Surveys will only be required where works traverse potential suitable habitat as identified in Figure 3.4. Works can proceed outside the identified areas.

3.8 Dust Control

Construction dust can be generated from many on-site activities such as excavation and backfilling. The extent of dust generation will depend on the type of activity undertaken, the location, the nature of the dust, *i.e.* soil, sand, peat, etc. and the weather. In addition, dust dispersion is influenced by external factors such as wind speed and direction and/or, periods of dry weather. Construction traffic movements also have the potential to generate dust as they travel along the haul route.

Proposed measures to control dust include:

- Any site roads with the potential to give rise to dust will be regularly watered, as appropriate, during dry and/or windy conditions;
- The designated public roads outside the site and along the main transport routes to the site will be regularly inspected by the ECoW for cleanliness, and cleaned as necessary;
- Material handling systems and material storage areas will be designed and laid out to minimise exposure to wind;
- Water misting or sprays will be used as required if particularly dusty activities are necessary during dry or windy periods;
- Water misting or bowsers will operate on-site as required to mitigate dust in dry weather conditions;
- The transport of soils or other material, which has significant potential to generate dust, will be undertaken in tarpaulin-covered vehicles where necessary;
- All construction related traffic will have speed restrictions on un-surfaced roads to 20 kph;
- Daily inspection of construction sites to examine dust measures and their effectiveness.
- When necessary, sections of the haul route will be swept using a truck mounted vacuum sweeper; and,
- All vehicles leaving the construction areas of the site will pass through a wheel cleansing area prior to entering the local road network.

3.9 Noise Control

The operation of plant and machinery, including construction vehicles, is a source of potential impact that will require mitigation at all locations within the site. Proposed measures to control noise include:

- Diesel generators will be enclosed in sound proofed containers to minimise the potential for noise impacts;
- Plant and machinery with low inherent potential for generation of noise and/or vibration will be selected. All construction plant and equipment to be used on-site will be modern equipment and will comply with the European Communities (Construction Plant and Equipment) (Permissible Noise Levels) Regulations;
- Regular maintenance of plant will be carried out in order to minimise noise emissions. Particular attention will be paid to the lubrication of bearings and the integrity of silencers;
- All vehicles and mechanical plant will be fitted with effective exhaust silencers and maintained in good working order for the duration of the works;

- Compressors will be of the “sound reduced” models fitted with properly lined and sealed acoustic covers which will be kept closed whenever the machines are in use and all ancillary pneumatic tools shall be fitted with suitable silencers;
- Machines, which are used intermittently, will be shut down during those periods when they are not in use;
- Training will be provided by the ECoW to drivers to ensure smooth machinery operation/driving, and to minimise unnecessary noise generation; and,
- Local areas of the haul route will be condition monitored and maintained if necessary.

3.10 Invasive Species Management

A baseline invasive species survey will be carried out at the site to identify the presence and location of any invasive species (listed under the Third Schedule of the European Communities (Birds and Natural Habitats) Regulations 2011 (S.I. 477 of 2011) by a suitably qualified ecologist. If the presence of such species is found at or adjacent to the site, particularly in areas where its excavation may be required, an invasive species management plan will be prepared for the site to prevent the introduction or spread of any invasive species within the footprint of the works. An invasive species management plan, if required, will set out best practice control methods as summarised in the following sections.

3.10.1 General Best Practice Control Methods

The following general best practice guidelines in the treatment and control of invasive species during construction works are outlined below having regard to guidance documents outlined in Section 2.5 particularly those issued by the National Roads Authority (2010).

3.10.2 Site Management

Careful preparation of the site and planning of the works is crucial to successful treatment of invasive species. The following list of guidelines, which is not exhaustive, shall be followed by all on-site personnel. Only those who have been inducted into biosecurity measures on-site may enter the contaminated zones within the works areas. Should any risk of contaminated material escaping be observed by the site supervisor, the management plan for the site must be amended by an appropriately qualified person to mitigate against the risk.

3.10.3 Establishing Good Site Hygiene

- A risk assessment and method statement must be provided by the Contractor prior to commencing works.
- Fences will be erected around areas of infestation, as confirmed by test pits, and warning signs shall be erected.
- A designated wash-down area will be created, where power-washed material from machinery can be contained, collected and disposed of with other contaminated material. This area will contain a washable membrane or hard surface.
- Stockpile areas will be chosen to minimise movement of contaminated soil.
- Stockpiles will be marked and isolated.
- Contaminated areas which will not be excavated will be protected by a root barrier membrane if they are likely to be disturbed by machinery. Root barrier membranes will be protected by a layer of sand above and below and topped with a layer of hardcore.

- The use of vehicles with caterpillar tracks within contaminated areas will be avoided to minimise the risk of spreading contaminated material.
- An ECoW/suitably qualified ecologist will be on site to monitor and oversee the implementation of invasive species management plans.

Plant and equipment which is operated within an area for the management of materials in contaminated areas should be decontaminated prior to relocating to a different works area. The decontamination procedures should take account of the following:

- Personnel may only clean down if they are familiar with the plant and rhizome material and can readily identify it.
- Decontamination will only occur within designated wash-down areas.
- Vehicles will be cleaned using stiff-haired brush and pressure washers, paying special attention to any areas that might retain rhizomes e.g. wheel treads and arches.
- All run-off will be isolated and treated as contaminated material. This will be disposed of in already contaminated areas.

3.11 Waste Management

This section of the CEMP provides a waste management plan (WMP) which outlines the best practice procedures during the excavation and construction phases of the project. The WMP will outline the methods of waste prevention and minimisation by recycling, recovery and reuse at each stage. Disposal of waste will be seen as a last resort.

3.11.1 Legislation

The Waste Management Act 1996 to 2011 and its subsequent amendments provide for measures to improve performance in relation to waste management, recycling and recovery. The Act also provides a regulatory framework for meeting higher environmental standards set out by other national and EU legislation.

The Act requires that any waste related activity has to have all necessary licenses and authorisations. It will be the duty of the Waste Manager on the site of the development to ensure that all contractors hired to remove waste from the site have valid Waste Collection Permits. It will then be necessary to ensure that the waste is delivered to a licensed or permitted waste facility. The hired waste contractors and subsequent receiving facilities must adhere to the conditions set out in their respective permits and authorisations.

The Department of the Environment provides a document entitled, 'Best Practice Guidelines on the Preparation of Waste Management Plans for Construction and Demolition Projects' (2006). It is important to emphasise that no demolition will take place at this site however, this document was referred to throughout the process of completing this WMP.

3.11.2 Waste Management Hierarchy

The waste management hierarchy sets out the most efficient way of managing waste in the following order:

Prevention and Minimisation:

The primary aim of the WMP will be to prevent and thereby reduce the amount of waste generated at each stage of the project.

Reuse of Waste:

Reusing as much of the waste generated on site as possible will reduce the quantities of waste that will have to be transported off site to recovery facilities or landfill.

Recycling of Waste:

There are a number of established markets available for the beneficial use of Construction and Demolition waste such as using waste concrete as fill for new roads.

At all times during the implementation of the WMP, disposal of waste to landfill will be considered only as a last resort.

3.11.3 Construction Phase Waste Management Plan

3.11.3.1 Description of the Works

The Permitted Development will involve the construction of turbines, associated new site roads and upgrade of some existing roads, a substation & control building and an anemometry mast.

The turbines will be manufactured off site and delivered to site where on-site assembly will occur.

The turbine and anemometry mast foundations will consist of stone excavated from the onsite borrow pit and a concrete base which will contain reinforcing steel. These concrete foundations will be shuttered with steel formwork specifically designed for the works and re-usable off site on similar projects.

The substation and control buildings will be constructed on a concrete foundation with the buildings constructed with concrete masonry blocks with a timber roof structure and roof tile or slate covering. The roof structure will be made up of prefabricated roof trusses manufactured off site to minimise timber cutting on site.

The site roads will be constructed with rock won from the onsite borrow pit.

The waste types arising from the construction phase of the Permitted Development are outlined in Table 3.2 below.

Table 3.2 Expected waste types arising during the Construction Phase

Materials type	Example	EW Code
Cables	Electrical wiring	17 04 11
Cardboard	Boxes, cartons	15 01 01
Composite packaging	Containers	15 01 05
Metals	Copper, aluminium, lead, iron and steel	17 04 07
Inert materials	Sand, stones, plaster, rock, blocks	17 01 07
Mixed municipal waste	Daily canteen waste from construction workers, miscellaneous	20 03 01
Plastic	PVC frames, electrical fittings	17 02 03
Plastic packaging	Packaging with new materials	15 01 02
Tiles and ceramics	Slates and tiles	17 01 03
Wooden packaging	Boxes, pallets	15 01 03

Hazardous wastes that may occur on site during the construction phase of the Permitted Development may include oil, diesel fuel, chemicals, paints, preservatives

etc. All hazardous wastes will be stored in bunded containers/areas before being collected by an authorised waste contractor and brought to an EPA licensed waste facility. As mentioned above, hazardous wastes will be kept separate from non-hazardous wastes to ensure that contamination does not occur.

3.11.3.2 Waste Arisings and Proposals for Minimisation, Reuse and Recycling of Construction Waste

Construction waste will arise on the project mainly from excavation and unavoidable construction waste including material surpluses and damaged materials and packaging waste.

Appropriate measures should be taken to ensure excess waste is not generated during construction, including;

- Ordering of materials should be on an 'as needed' basis to prevent over supply to site. Co-ordination is required with suppliers enabling them to take/buy back surplus stock.
- Purchase of materials pre-cut to length to avoid excess scrap waste generated on site.
- Request that suppliers use least amount of packaging possible on materials delivered to the site.
- Ensuring correct storage and handling of goods to avoid unnecessary damage that would result in their disposal
- Ensuring correct sequencing of operations.
- Use reclaimed materials in the construction works.

Hazardous waste will be kept separate from all other construction waste to prevent contamination and removed appropriately.

3.11.3.3 Waste Arising from Construction Activities

All waste generated on site will be contained in waste skips at a waste storage area on site. This waste storage area will be kept relatively tidy with the various waste skip clearly labelled to indicate the allowable material to be disposed of therein.

The expected waste volumes generated on site are unlikely to be large enough to warrant source segregation. Therefore, all wastes streams generated on site will be deposited into a single skip. This waste material will be transferred to a Materials Recovery Facility (MRF) by a fully licensed waste contractor where the waste will be sorted into individual waste streams for recycling, recovery or disposal.

The waste generated from the turbine erection will be limited to the associated protective covers which are generally reusable. Considering the specialist nature of this packaging material the majority will be taken back by suppliers for their own reuse. Any other packaging waste generated from the turbine supply will be deposited in the on-site skip and subsequently transferred to the MRF

It is not envisaged that there will be any waste material arising from the materials used to construct the road as only the quantity of stone necessary will be excavated from the borrow pit on an 'as needed' basis.

Site personnel will be instructed at induction that no under no circumstances can waste be brought to site for disposal in the on-site waste skip. It must also be made clear that the burning of waste material on site is forbidden.

3.11.3.4 Waste Arising from Decommissioning

The lengthy time frame between the completion of the construction phase and decommissioning will result in the only materials remaining on site at that time are likely to be turbines and associated cabling and crushed stone used in construction of roads, hardstand, foundations etc.

The waste types arising from the decommissioning of the development are outlined in Table 3.3 below.

Table 3.3 Expected waste types arising during Decommissioning

Materials type	Example	EWC Code
Cables	Electrical wiring	17 04 11
Metals	Copper, aluminium, lead, iron and rebar	17 04 07
Inert materials	Crushed stone,	17 01 07

3.11.4 Reuse

Many construction materials can be reused a number of times before they have to be disposed of:

- Concrete can be reused as aggregate for roads cable trench backfilling material.
- Plastic packaging etc. can be used to cover materials on site or reused for the delivery of other materials.
- Excavated peat will be can be reused for reinstatement of the areas around turbine foundations and adjacent to site roads.

3.11.5 Recycling

If a certain type of construction material cannot be reused on site, then recycling is the most suitable option. The opportunity for recycling on site will be restricted to the associated packaging from the wind turbines.

All waste that is produced during the construction phase including dry recyclables will be deposited in the on-site skip initially and sent for subsequent segregation at a remote facility. The low volume of such material that is anticipated to be generated at the Permitted Development is the justification for adopting this method of waste management.

3.11.6 Implementation

3.11.6.1 Roles and Responsibilities for Waste Management

Prior to the commencement of the Permitted Development a member of the on-site construction management staff will be assigned the role of Construction Waste Manager. The Construction Waste Manager will be in charge of the implementation of the objectives of the WMP, ensuring that all hired waste contractors have the necessary authorisations and that the waste management hierarchy is adhered to. The person nominated must have sufficient authority so that they can ensure everyone working on the Permitted Development adheres to the WMP.

3.11.6.2 Training

It is important for the Construction Waste Manager to communicate effectively with colleagues in relation to the aims and objectives of the WMP. All employees working on site during the construction phases of the project will be trained in materials management and thereby, should be able to:

- Distinguish reusable materials from those suitable for recycling;
- Ensure maximum segregation at source;
- Co-operate with site manager on the best locations for stockpiling reusable materials;
- Separate materials for recovery; and
- Identify and liaise with waste contractors and waste facility operators.

3.11.6.3 Record Keeping

The WMP will provide systems that will enable all arising, movements and treatments of construction waste to be recorded. This system will enable the contractor to measure and record the quantity of waste being generated. It will highlight the areas from which most waste occurs and allows the measurement of arising against performance targets. The WMP can then be adapted with changes that are seen through record keeping.

The fully licensed waste contractor employed to remove waste from the site will be required to provide documented records for all waste dispatches leaving the site of the Permitted Development. Each record will contain the following:

- Consignment Reference Number
- Material Type(s) and EWC Code(s)
- Company Name and Address of Site of Origin
- Trade Name and Collection Permit Ref. of Waste Carrier
- Trade Name and Licence Ref. of Destination Facility
- Date and Time of Waste Dispatch
- Registration no. of Waste Carrier vehicle
- Weight of Material
- Signature of Confirmation of Dispatch detail
- Date and Time of Waste Arrival at Destination
- Weight of Material
- Site Address of Destination Facility

3.11.7 Waste Management Plan Conclusion

The WMP will be properly adhered to by all staff involved in the project which will be outlined within the induction process for all site personnel. The waste hierarchy should always be employed when designing the plan to ensure that the least possible amount of waste is produced during the construction phase. Reuse of certain types of construction wastes will cut down on the cost and requirement of raw materials therefore further minimising waste levels.

This preliminary WMP has been prepared to outline the main objectives that are to be adhered to for the preparation of a more detailed WMP to be completed after the planning phase of the Permitted Development.

4 DRAINAGE MANAGEMENT PLAN

The drainage management plan is essential to ensure that the details submitted as part of the environmental impact statement are fully implemented on site during the construction of the development. This report incorporates a detailed silt management plan and pollution prevention plan and including appropriately drainage infrastructure including interceptor & collector drains, check dams and settlement ponds as required. A programme for drainage maintenance has been provided to ensure the drainage system operates effectively and within its capacity.

4.1 Wind Farm Drainage

4.1.1 Introduction

The drainage management plan is essential to ensure that the details submitted as part of the environmental impact statement and as part of the further information response are fully implemented on site during the construction of the development. This report incorporates a detailed silt management plan and pollution prevention plan and including appropriately-sized silt traps and/or settlement ponds as required. Detailed Drainage Design Drawings for the permitted development as prepared by Hydro Environmental Services are included in Appendix 1 of this document. The drainage design employs the various measures further described below.

The protection of the watercourses within and surrounding the site, and downstream catchments that they feed is of utmost importance in considering the most appropriate drainage proposals for the site of the development. The development's drainage design has therefore been designed specifically with the intention of having no negative impact on the water quality of the site and its associated natural watercourses, and consequently no impact on downstream catchments and ecological ecosystems. There will be no direct discharges to any natural watercourses, with all drainage waters being dispersed as overland flows or directly into artificial drainage ditches following the installation of silt traps, check dams and/or settlement ponds to these ditches. Any discharges over land, from the works areas will be made over vegetation filters maintaining a 50 metre distance from natural watercourses. Buffer zones around the existing natural drainage features have informed, wherever possible, the layout of the permitted development.

4.1.2 Existing Drainage Features

The routes of natural drainage features will not be altered as part of the development. Turbine locations have been selected to avoid natural watercourses. The wind farm development has also been designed to require only 5 no. new watercourse crossings. Some extensions to existing culverts may be required under existing roadways to manage drainage waters where road widening and upgrade is required. These will be sufficiently sized to accommodate peak flows from storm events.

There will be no direct discharges to natural watercourses. Discharges from the works areas or from interceptor drains will be made over vegetated ground at a minimum of 50 metres distance from natural watercourses in the majority of cases. There are exceptions to this where existing or new roadways traverse, or run alongside, natural watercourses and it is necessary to provide drainage measures along such sections of roadway. Discharges will be made at a minimum distance of 20 metres from artificial drainage ditches unless otherwise specified in future revisions of the drainage design.

Buffer zones around the existing natural drainage features have informed the layout of the development and are indicated on the drainage design drawings.

Where artificial drains are currently in place in the vicinity of works areas, these drains may have to be diverted around the works areas to minimise the amount of water in the vicinity of works areas. Where it may not be possible to divert artificial drains around work areas, the drains will be blocked to ensure sediment laden water from the works areas has no direct route to other watercourses. Where drains have to be blocked, the blocking will only take place after an alternative drainage system to handle the same water has been put in place.

Existing artificial drains in the vicinity of existing site roads will be maintained in their present location where possible. If it is expected that these artificial drains will receive drainage water from works areas, check dams will be added (as specified below) to control flows and sediment loads in these existing artificial drains. If road widening or improvement works are necessary along the existing roads, where possible, the works will take place on the opposite side of the road to the drain.

4.1.3 Drainage Design Principles

Drainage water from any works areas of the site will not be directed to any natural watercourses within the site. Two distinct methods will be employed to manage drainage water within the site. The first method involves keeping clean water clean by avoiding disturbance to natural drainage features, minimising any works in or around artificial drainage features, and diverting clean surface water flow around excavations and construction areas. The second method involves collecting any drainage waters from works areas within the site that might carry silt or sediment, to allow attenuation and settlement prior to controlled diffuse release.

The drainage design is intended to maximise erosion control, which is more effective than having to control sediment during high rainfall. Such a system also requires less maintenance. The area of exposed ground will be minimised. The drainage measures will prevent runoff from entering the works areas of the site from adjacent ground, to minimise the volume of sediment-laden water that has to be managed. Discoloured run-off from any construction area will be isolated from natural clean run-off.

A schematic line drawing of the drainage design is presented in Figure 4.1 below.

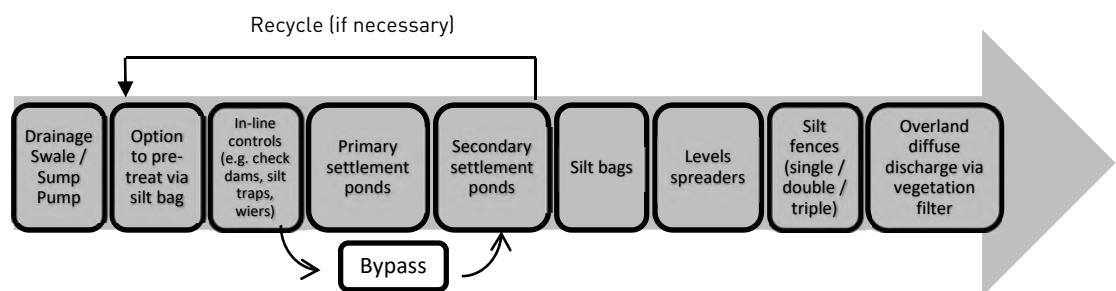


Figure 4.1 Schematic drawing of drainage design

4.1.4 Site Management & Pollution Prevention

The drainage management plan takes into account the principles of erosion and sediment control. Erosion control where runoff is prevented from flowing across exposed ground and sediment control where runoff is slowed to allow suspended sediment to settle are important elements in a drainage management plan. The drainage management plan has been prepared to provide erosion and sediment control

to prevent sediment and potentially pollutant runoff entering watercourses during the construction phase. The drainage management plan will ensure the following:

- Implement erosion control to prevent runoff flowing across exposed ground and become polluted by sediments;
- Intercept and divert clean water runoff away from construction site runoff to avoid cross contamination of clean water with soiled water;
- Implement sediment control to slow down runoff allowing suspended sediments to settle in situ particularly on roads and hardstanding areas;
- Implement the erosion and sediment controls before starting site clearance works;
- Minimise area of exposed ground by maintaining existing vegetation that would otherwise be subject to erosion in the vicinity of the wind park infrastructure and keeping excavated areas to a minimum;
- Delay clearing of peat before construction begins rather than stripping the entire site months in advance particularly during road construction;
- Designate temporary stockpiling areas located away from drains and watercourses that are protected by silt trapping apparatus such as a geotextile silt fence to prevent contaminated runoff where necessary; it is not envisaged that the stock piling areas will affect the drainage measures on site.
- Avoid working near watercourses during or after prolonged rainfall or an intense rainfall event and cease work entirely near watercourses when it is evident that pollution is occurring;
- Install a series of silt fences or other appropriate silt retention measure where there is a risk of erosion runoff to watercourses from construction related activity particularly if working during prolonged wet weather period or if working during intense rainfall event;
- Implement sediment control measures that includes for the prevention of runoff from adjacent intact ground that is for the separation of clean and 'dirty' water;
- Install appropriate silt control measures such as silt-traps, check dams and settlement ponds;
- Provide recommendations for road cleaning where needed particularly in the vicinity of watercourses; and
- Controls need to be regularly inspected and maintained otherwise a failure may result, such as a build-up of silt or tear in a fence, which could lead to water pollution. Controls must work effectively until the vegetation has re-established; inspection and maintenance is critical after prolonged or intense rainfall.

4.1.5 Pre-Construction Drainage Management

There are existing drainage features across the site, and due to the agricultural nature of the area as well as the ongoing commercial forestry operations, runoff drains relatively freely to local drains. This existing drainage system will continue to function as it is during the pre-construction phase. Prior to commencement of works in sub-catchments across the site main drain inspections will be completed to ensure ditches and streams are free from debris and blockages that may impede drainage.

The Project Hydrologist/Design Engineer will attend the site before construction commences and will assist with micro siting of drainage controls as per the mechanisms for interaction outlined in Section 5 of this CEMP. The drainage system will be excavated and constructed in conjunction with the road and hard standing construction. Drains will be excavated, and settlement ponds constructed to eliminate any suspended solids within surface water running off the site.

4.1.6 Construction Phase Drainage Management Plan

A drainage management plan is presented in this section of the CEMP to provide an overview for planning compliance and tendering purposes. This includes descriptions of the various drainage controls to be employed during the construction phase and operational phase of the wind farm development.

The early establishment of temporary drainage facilities will reduce the risk of pollution problems during construction. In addition, construction operations will adopt best working practices for drainage controls. The construction of the drainage system will start from the downstream sections and progress upstream, connecting conveyance systems with other drainage features as each development phase of the site progresses. They will therefore need to be designed with sufficient flexibility to respond to an early phase of limited incoming flow during the construction phase when sediment or other pollution may be a problem if upstream controls perform poorly, and the final phase of maximum incoming flows within the various catchments.

The implementation of a Schedule of Works Operation Record (SOWOR) will continue through the construction phase of the project. The SOWOR provides number of abandonment triggers which will ensure that site management are well informed as to the level of incident that will require the abandonment of works. The various triggers both pre-commencement and abandonment ensure best practice in terms of water quality management is maintained prior to commencement and during the various felling and construction phases.

Best practice and practical experience on other similar projects suggests that in addition to the drainage plans that are included in this CEMP, there are additional site based decisions and plans that can only be made in the field through interaction between the Site Construction Manager, the Project Hydrologist and the Project Geotechnical Engineers as per Section 5 of this CEMP.

In relation to decisions that are made on site it is important to stress that these will be implemented in line with the associated drainage controls and mitigation measures outlined in Section 7 below, and to ensure protection of all watercourses.

4.1.6.1 Drainage Design

Detailed drainage design measures are included in the site layout drawings of the development included in Appendix 1 of this report. The drainage design employs the various measures further described below.

4.1.6.1.1 Interceptor Drains

Interceptor drains will be installed upgradient of any works areas to collect surface flow runoff and prevent it reaching excavations and construction areas of the site where it might otherwise have come into contact with exposed surfaces and picked up silt and sediment. The drains will be used to divert upslope runoff around the works area to a location where it can be redistributed over the ground surface as sheet flow. This will minimise the volume of potentially silty runoff to be managed within the construction area.

The interceptor drains will be installed in advance of any main construction works commencing. The material excavated to make the drain will be compacted on the downslope edge of the drain to form a diversion dike. On completion of the construction phase works, it is envisaged that the majority of the interceptor drains could be removed. At that stage, there will be no open excavations or large areas of exposed

ground that are likely to give rise to large volumes of potentially silt-laden run off. Any areas in which works were carried out to construct roads, turbine bases or hardstands, will have been built up with large grade hardcore, which even when compacted in place, will retain sufficient void space to allow water to infiltrate the subsurface of these constructed areas. It is not anticipated that roadways or other installed site infrastructure will intercept ground-conveyed surface water runoff to any significant extent that would result in scouring or over-topping or spill over. Where the drains are to be removed, they will be backfilled with the material from the diversion dike. Interceptor drains may have to be retained in certain locations, for example where roadways are to be installed on slopes, to prevent the roadways acting as conduits for water that might infiltrate the roadway sub-base. In these cases, interceptor drains would be maintained in localised areas along the roadway with culverts under the roadway, which would allow the intercepted water to be discharged to vegetation filters downgradient of the roadway. Similarly, in localised hollows where water is likely to be funnelled at greater concentrations than on broader slopes, interceptor drains and culverts may be left in situ following construction.

Figure 4.2 shows an illustrative drawing of an interceptor drain.

The velocity of flow in the interceptor will be controlled by check dams (see Section 4.2.6.1.3 below), which will be installed at regular intervals along the drains to ensure flow in the channel is non-erosive. On steeper sections where erosion risks are greater, a geotextile membrane will be added to the channel.




Interceptor drains will be installed horizontally across slopes to run in parallel with the natural contour line of the slope. Intercepted water will travel along the interceptor drains to areas downgradient of works areas, where the drain will terminate at a level spreader (see Section 4.2.6.1.4 below). Across the entire length of the interceptor drains, the design elevation of the water surface along the route of the drains will not be lower than the design elevation of the water surface in the outlet at the level spreader.

4.1.6.1.2 Swales




Drainage swales are shallow drains that will be used to intercept and collect run off from construction areas of the site during the construction phase. Drainage swales will remain in place to collect runoff from roads and hardstanding areas of the development during the operational phase. A swale is an excavated drainage channel located along the downgradient perimeter of construction areas, used to collect and carry any sediment-laden runoff to a sediment-trapping facility and stabilised outlet. Swales are proven to be most effective when a dike is installed on the downhill side. They are similar in design to interceptor drains and collector drains described above. Figure 4.2 shows an illustrative example of a drainage swale.

Drainage swales will be installed downgradient of any works areas to collect surface flow runoff where it might have come into contact with exposed surfaces and picked up silt and sediment. Swales will intercept the potentially silt-laden water from the excavations and construction areas of the site and prevent it reaching natural watercourses.

Drainage swales will be installed in advance of any main construction works commencing. The material excavated to make the swale will be compacted on the downslope edge of the drain to form a diversion dike.

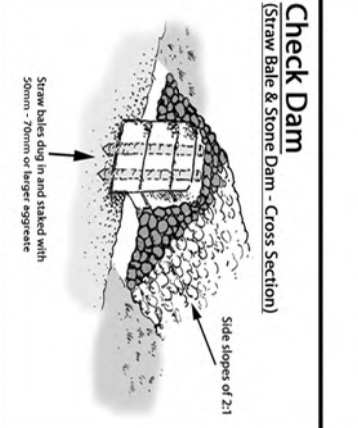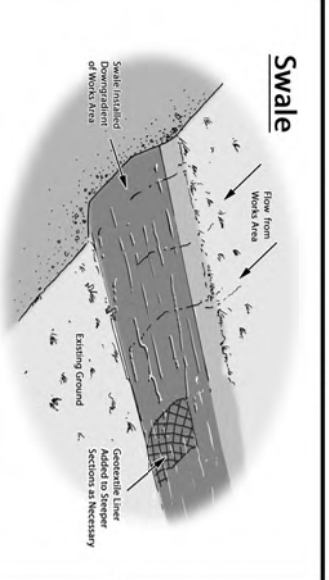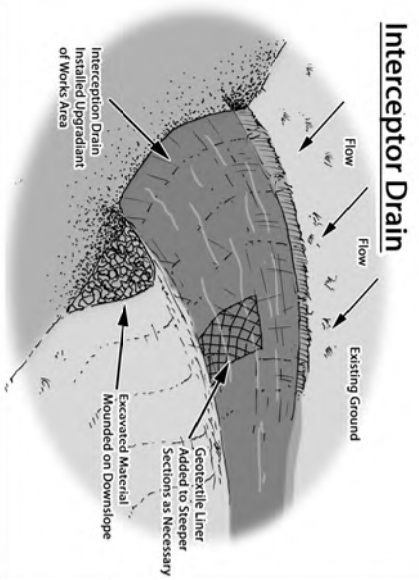

Drainage Design Measures

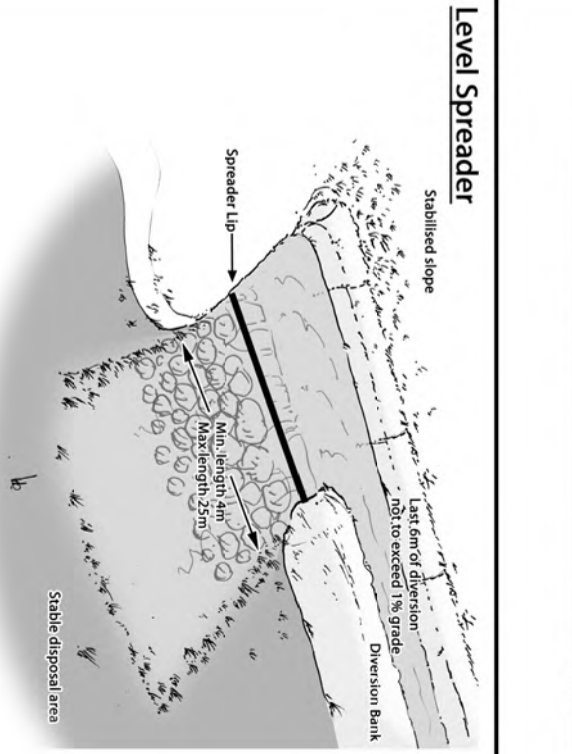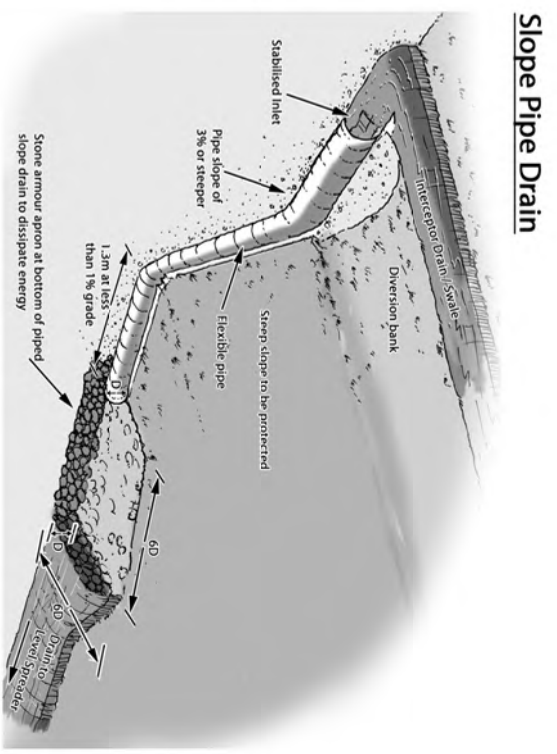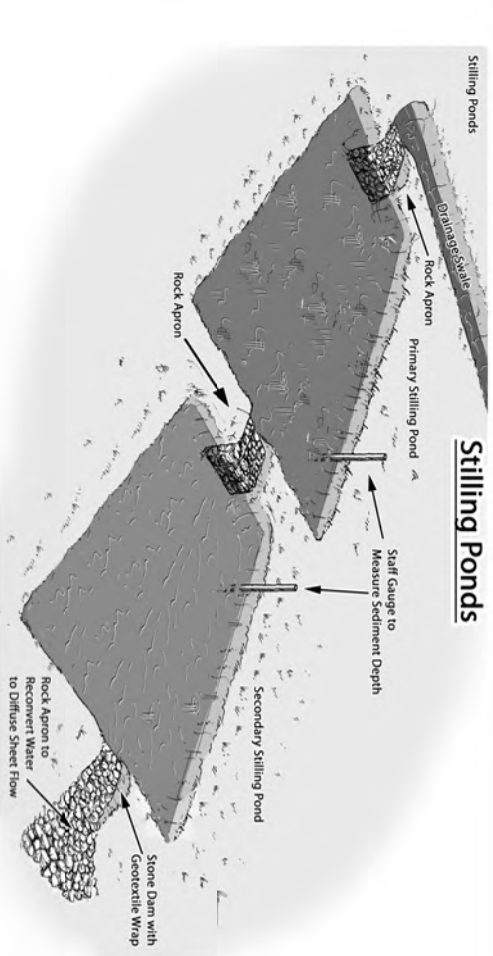

		MAP NO: Figure 4.2	SCALE: n/a
MAP TITLE: Drainage Design Measures			
PROJECT TITLE: Meenbog Wind Farm			
DRAWING BY: Owen Cahill		CHECKED BY: Michael Watson	
ISSUE NO: 160502-2018.12.18-F		DATE: 18-12-2018	
<small>McCarthy Kenille O'Sullivan Ltd., Block 1, G.F.S.C. Monaghan Road, Galway, Ireland. Email: info@mcCarthyKos.ie Tel: +353 (0)91 736611 Fax: +353 (0)91 771279</small>			
<small>Ordnance Survey Ireland Licence No. AR 0021817 © Ordnance Survey Ireland/Government of Ireland</small>			

4.1.6.1.3 Check Dams

The velocity of flow in the interceptor drains and drainage swales, particularly on sloped sections of the channel, will be controlled by check dams, which will be installed at regular intervals along the drains to ensure flow in the swale is non-erosive. Check dams will also be installed in some existing artificial drainage channels that will receive waters from works areas of the site.

Check dams will restrict flow velocity, minimise channel erosion and promote sedimentation behind the dam. The check dams will be installed as the interceptor drains are being excavated. Check dams may also be installed in some of the existing artificial drainage channels on the site, downstream of where drainage swales connect in.

The check dams will be made up of straw bales or stone, or a combination of both depending on the size of the drainage swale it is being installed in. Where straw bales are to be used, they will be secured to the bottom of the drainage swale with stakes. Clean 4-6 inch stone will be built up on either side and over the straw bale to a maximum height of 600mm over the bottom of the interceptor drain. In smaller channels, a stone check dam will be installed and pressed down into place in the bottom of the drainage swale with the bucket of an excavator.

The check dams will be installed at regular intervals along the interceptor drains to ensure the bottom elevation of the upper check dam is at the same level as the top elevation of the next down-gradient check dam in the drain. The centre of the check dam will be approximately 150mm lower than the edges to allow excess water to overtop the dam in flood conditions rather than cause upstream flooding or scouring around the dams.

Check dams will not be used in any natural watercourses, only artificial drainage channels and interceptor drains. The check dams will be left in place at the end of the construction phase to limit erosive linear flow in the drainage swales during extreme rainfall events.

Check dams are designed to reduce velocity and control erosion and are not specifically designed or intended to trap sediment, although sediment is likely to build up. If necessary, any excess sediment build up behind the dams will be removed. For this reason, check dams will be inspected and maintained regularly to insure adequate performance. Maintenance checks will also ensure the centre elevation of the dam remains lower than the sides of the dam.

4.1.6.1.4 Level Spreaders

A level spreader will be constructed at the end of each interceptor drain to convert concentrated flows in the drain, into diffuse sheet flow on areas of vegetated ground. The level spreaders will be located downgradient of any works areas in locations where they are not likely to contribute further to water ingress to construction areas of the site.

The water carried in interceptor drains will not have come in contact with works areas of the site, and therefore should be free of silt and sediment. The level spreaders will distribute clean drainage water onto vegetated areas where the water will not be re-concentrated into a flow channel immediately below the point of discharge. The discharge point will be on level or only very gently sloping ground rather than on a steep slope so as to prevent erosion. Figure 4.2 shows an illustrative example of a level spreader.

The slope in the channel leading into the spreader will be less than or equal to 1%. The slope downgradient of the spreader onto which the water will dissipate will have a grade of less than 6%. The availability of slopes with a grade of 6% or less will determine the locations of level spreaders. If a slope grade of less than 6% is not available in the immediate area downgradient of a works area at the end of a diversion drain, a piped slope drain (see Section 4.2.6.1.5 below) will be used to transfer the water to a suitable location.

The spreader lip over which the water will spill will be made of a concrete kerb, wooden board, pipe, or other similar piece of material that can create a level edge similar in effect to a weir. The spreader will be level across the top and bottom to prevent channelised flow leaving the spreader or ponding occurring behind the spreader. The top of the spreader lip will be 150mm above the ground behind it. The length of the spreader will be a minimum of four metres and a maximum length of 25 metres, with the actual length of each spreader to be determined by the size of the contributing catchment, slope and ground conditions.

Clean four-inch stone can be placed on the outside of the spreader lip and pressed into the ground mechanically to further dissipate the flow leaving the level spreader over a larger area.

4.1.6.1.5 Piped Slope Drains

Piped slope drains will be used to convey surface runoff from diversion drains safely down slopes to flat areas without causing erosion. Once the runoff reaches the flat areas it will be reconverted to diffuse sheet flow. Level spreaders will only be established on slopes of less than 6% in grade. Piped slope drains will be used to transfer water away from areas where slopes are too steep to use level spreaders.

The piped slope drains will be semi-rigid corrugated pipes with a stabilised entrance and a rock apron at the outlet to trap sediment and dissipate the energy of the water. The base of drains leading into the top of the piped slope drain will be compacted and concavely formed to channel the water into the corrugated pipe. The entrance at the top of the pipe will be stabilised with sandbags if necessary. The pipe will be anchored in place by staking at approximately 3-4 metre intervals or by weighing down with compacted soil. The bottom of the pipe will be placed on a slope with a grade of less than 1% for a length of 1.5 metres, before outflowing onto a rock apron.

The rock apron at the outlet will consist of 6-inch stone to a depth equal to the diameter of the pipe, a length six times the diameter of the pipe. The width of the rock apron will be three times the diameter of the pipe where the pipe opens onto the apron and will fan out to six times the diameter of the pipe over its length. Figure 4.2 shows a diagrammatic example of a piped slope drain and rock apron.

Piped slope drains will only remain in place for the duration of the construction phase of the project. On completion of the works, the pipes and rock aprons will be removed and all channels backfilled with the material that was originally excavated from them.

Piped slope drains will be inspected weekly and following rainfall events. Inlet and outlets will be checked for sediment accumulation and blockages. Stake anchors or fill over the pipe will be checked for settlement, cracking and stability. Any seepage holes where pipe emerges from drain at the top of the pipe will be repaired promptly.

4.1.6.1.6 Vegetation Filters

Vegetation filters are the existing vegetated areas of land that will be used to accept surface water runoff from upgradient areas. The selection of suitable areas to use as vegetation filters will be determined by the size of the contributing catchment, slope and ground conditions.

Vegetation filters will carry outflow from the level spreaders as overland sheet flow, removing any suspended solids and discharging to the groundwater system by diffuse infiltration.

Vegetation filters will not be used in isolation for waters that are likely to have higher silt loadings. In such cases, silt-bearing water will already have passed through settlement ponds prior to diffuse discharge to the vegetation filters via a level spreader.

4.1.6.1.7 Settlement Ponds

Settlement ponds will be used to attenuate runoff from works areas of the site during the construction phase and will remain in place to handle runoff from roads and hardstanding areas of the development during the operational phase. The purpose of the settlement ponds is to intercept runoff potentially laden with sediment and to reduce the amount of sediment leaving the disturbed area by reducing runoff velocity. Reducing runoff velocity will allow larger particles to settle out in the settlement ponds, before the run-off water is redistributed as diffuse sheet flow in filter strips downgradient of any works areas.

Settlement ponds will be excavated/constructed at each required location as two separate ponds in sequence, a primary pond and a secondary pond. The points at which water enters and exits the settlement ponds will be stabilised with rock aprons, which will trap sediment, dissipate the energy of the water flowing through the settlement pond system, and prevent erosion. The primary settlement pond will reduce the velocity of flows to less than 0.5 metres per second to allow settlement of silt to occur. Water will then pass from the primary pond to the secondary pond via another rock apron. The secondary settlement pond will reduce the velocity of flows to less than 0.3 metres per second. Water will flow out of the secondary settlement pond through a stone dam, partially wrapped in geo-textile membrane, which will control flow velocities and trap any sediment that has not settled out. Figure 4.2 shows an illustrative example of a settlement pond system.

Water will flow by gravity through the settlement pond system. The settlement ponds will be sized according to the size of the area they will be receiving water from but will be sufficiently large to accommodate peak flows storm events. The settlement ponds will be dimensioned so that the length to width ratio will be greater than 2:1, where the length is the distance between the inlet and the outlet. Where ground conditions allow, settlement ponds will be constructed in a wedge shape, with the inlet located at the narrow end of the wedge. Each settlement pond will be a minimum of 1-1.5 metres in depth. Deeper ponds will be used to minimise the excavation area needed for the required volume.

The embankment that forms the sloped sides of the settlement ponds will be stabilised with vegetated turves, which will have been removed during the excavation of the settlement ponds area or will be seeded after installation.

Settlement ponds will be located towards the end of swales, close to where the water will be reconverted to diffuse sheet flow. Upon exiting the settlement pond system,

water will be immediately reconverted to diffuse flow via a fan-shaped rock apron if there is adequate space and ground conditions allow. Otherwise, a swale will be used to carry water exiting the settlement pond system to a level spreader to reconvert the flow to diffuse sheet flow.

A water level indicator such as a staff gauge will be installed in each settlement pond with marks to identify when sediment is at 10% of the settlement pond capacity. Sediment will be cleaned out of the still pond when it exceeds 10% of pond capacity. Settlement ponds will be inspected weekly and following rainfall events. Inlet and outlets will be checked for sediment accumulation and anything else that might interfere with flows.

4.1.6.1.8 Dewatering Silt Bags

Dewatering silt bags are made of a high quality geotextile fabric which allow the flow of water through them while trapping any silt or sediment suspended in the water. The silt bags provide a passive non-mechanical method of removing any remaining silt contained in the potentially silt-laden water collected from works areas within the site.

Dewatering silt bags are an additional drainage measure that can be used downgradient of the settlement ponds at the end of the drainage swale channels and will be located, wherever it is deemed appropriate, throughout the site. The water will flow, via a pipe, from the settlement ponds into the silt bag. The silt bag will allow the water to flow through the geotextile fabric and will trap any of the finer silt and sediment remaining in the water after it has gone through the previous drainage measures. The dewatering silt bags will ensure that there will be no loss of peaty silt into any watercourse.

The dewatering silt bags that will be used will be approximately three metres in width by 4.5 metres (see Plate 4.1 and Plate 4.2 below) in length and will be capable of trapping approximately four tonnes of silt.



Plate 4.1 Silt Bag with water being pumped through



Plate 4.2 Silt Bag under inspection

4.1.6.1.9 Siltbuster

A "siltbuster" or similar equivalent piece of equipment will be available to filter any water pumped out of excavation areas if necessary, prior to its discharge to settlement ponds or swales.

Siltbusters are mobile silt traps that can remove fine particles from water using a proven technology and hydraulic design in a rugged unit. The mobile units are specifically designed for use on construction sites.

The unit stills the incoming water/solids mix and routes it upwards between a set of inclined plates for separation. Fine particles settle onto the plates and slide down to the base for collection, whilst treated water flows to an outlet weir after passing below a scum board to retain any floating material. The inclined plates dramatically increase the effective settling area of the unit giving it a very small footprint on site and making it highly mobile. Figure 4.3 below shows an illustrative diagram of the Siltbuster.

The Siltbuster units are now considered best practice for the management of dirty water pumped from construction sites. The UK Environment Agency and the Scottish Environmental Protection Agency have all recommended/specified the use of *Siltbuster* units on construction projects.

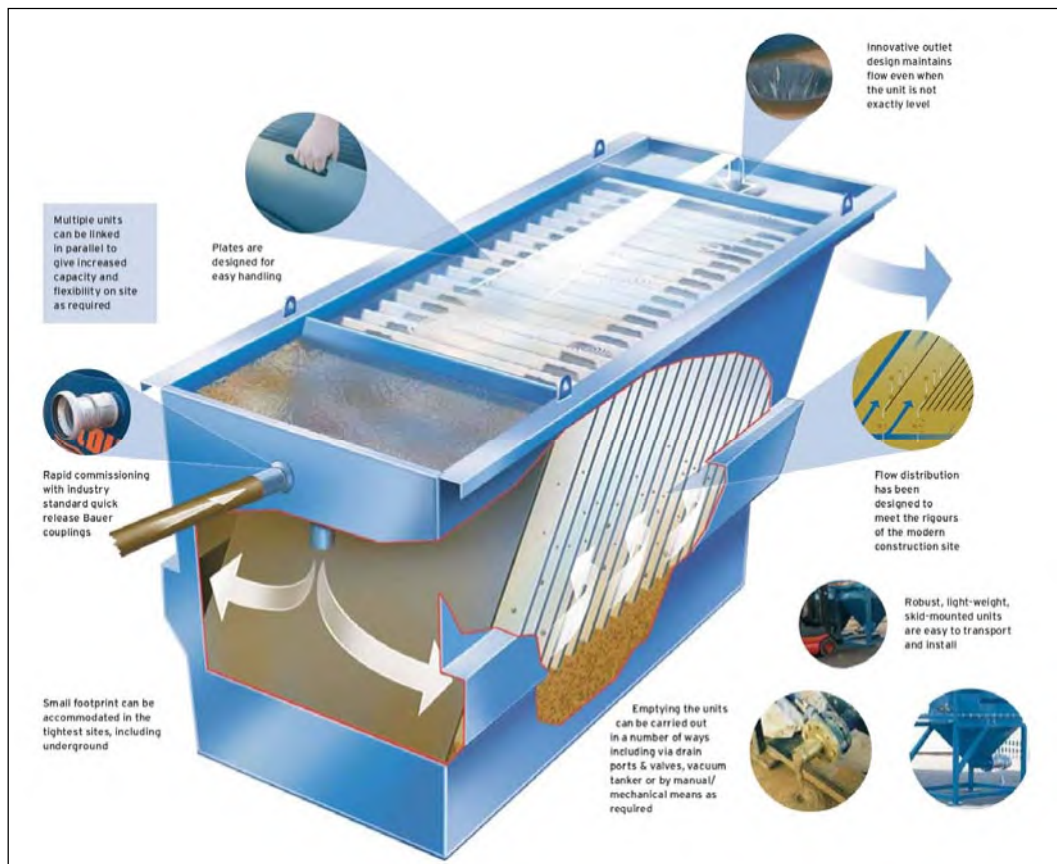


Figure 4.3 Siltbuster

4.1.6.1.10 Culverts

Where any new culverts of existing watercourses crossing are to be installed, they will be the subject of consent applications to the Office of Public Works under Section 50 of the Arterial Drainage Act, 1945. Some culverts may be installed to manage drainage waters from works areas of the development, particularly where the waters have to be taken from one side of an existing roadway to the other for discharge. The size of culverts will be influenced by the depth of the track or road sub-base. In some cases, two, or more, smaller diameter culverts may be used where this depth is limited, though this will be avoided as they will have a higher associated risk of blockage than a single, larger pipe. In all cases, culverts will be oversized to allow mammals to pass through the culvert.

Culverts will be installed with a minimum internal gradient of 1% (1 in 100). Smaller culverts will have a smooth internal surface. Larger culverts may have corrugated

surfaces which will trap silt and contribute to the stream ecosystem. Depending on the management of water on the downstream side of the culvert, large stone may be used to interrupt the flow of water. This will help dissipate its energy and help prevent problems of erosion. Smaller water crossings will simply consist of an appropriately sized pipe buried in the sub-base of the road at the necessary invert level to ensure ponding or pooling doesn't occur above or below the culvert and water can continue to flow as necessary.

All culverts will be inspected regularly to ensure they are not blocked by debris, vegetation or any other material that may impede conveyance.

4.1.6.1.11 Silt Fences

Silt fences will be installed as an additional water protection measure around existing watercourses in certain locations, particularly where works are proposed within the 50-metre buffer zone from natural watercourses, which is inevitable where existing roads in proximity to watercourses are to be upgraded as part of the development. These areas include around existing culverts, around the headwaters of watercourses, and the proposed locations are indicated on the site layout drawings included in Appendix 1.

Silt fences will be installed as single, double or a series of triple silt fences, depending on the space available and the anticipated sediment loading. The silt fence designs follow the technical guidance document *'Control of Water Pollution from Linear Construction Projects'* published by CIRIA [Ciria, No. C648, 1996]. Up to three silt fences may be deployed in series as outlined in Figure 4.4.

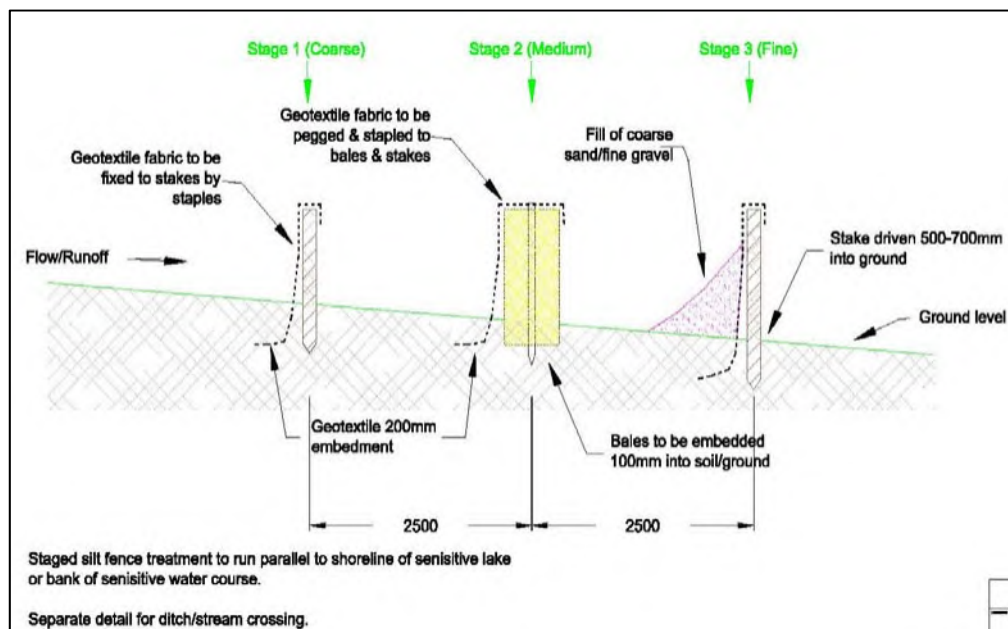


Figure 4.4 Silt Fence Detail

The Stage 1 (Coarse) silt fence will consist of a geotextile fabric such as Terram 1000 attached by staples to fixed stakes. The Terram sheets will be folded in an L shape with one metre extending horizontally in towards the works area. This horizontal section will be buried at a distance of approximately 150mm beneath a clean stone surface. Terram 1000 is a permeable fabric through which water can pass, but through which

sediment particles cannot. It does however, impede water flow and can lead to the backing up of water and sediment, which reduce its effectiveness.

The Stage 2 (Medium) silt fence will consist of straw bales, embedded 100mm into the soil/ground and fixed in place with stakes. A geotextile fabric will be pegged and stapled to the straw bales and stakes.

The Stage 3 (Fine) silt fence will be similar to the Stage 1 fence, with the addition of a course sand and/or fine gravel at the base of the geotextile.

In the case of all three types of fence, the geotextile fabric will be embedded at least 150mm below the ground surface.

In a small number of locations around the site where space between the works areas and watercourses may be limited, silt fence designs will be combined to increase their effectiveness. For example, a straw bale silt fence (Stage 2) may be double wrapped with geotextile fabric (Stage 1) and course sand/fine gravel added on the upgradient side (Stage 3). See Figure 4.4. The most suitable type, number or combination of silt fences will be determined on a location specific basis for the various parts of the site. Site fences will be inspected regularly to ensure water is continuing to flow through the Terram, and the fence is not coming under strain from water backing up behind it.

4.1.6.2 Construction Compound Drainage

Surface water run-off from the construction compound will be controlled via a single outlet that will be installed at the edge of the compound. The single outfall point will be constructed to handle runoff from the compound and its immediate surrounds. Interceptor drains will already have been installed upgradient of the compound area before any excavation begins.

Run off from the single outlet point will be diverted via a drainage swale and on to a settlement pond prior to discharge over an area of vegetated ground.

4.1.6.3 Borrow Pit Drainage

While surface water will be contained in the borrow pit area, the design proposal is to control the level of water in the borrow pit area by creating a single point outlet from the basin-like area that will ensure the water does not overtop the pit area. Run-off from the borrow pit areas will be controlled via a single outlet that will be installed at the edge of the borrow pit. The single outfall point will be constructed to handle runoff from the borrow pit and its immediate surrounds. Interceptor drains will already have been installed upgradient of the borrow pit area before any extraction begins.

Run off from the single outlet point will be diverted via a drainage swale to a series of settlement ponds and onwards to a level spreader, which will convert concentrated flows in the drain, into diffuse sheet flow on areas of vegetated ground. The management of surface runoff from the peat disposal area by converting it to diffuse sheet flow removes the risk of contamination of surface water drains and removes the requirement for silt traps leading from this particular area.

During the construction phase of the project, it will be necessary to keep the borrow pit area free of standing water while rock is still being extracted. This will be achieved by using a mobile pump, which will pump water into the same series of drains, settlement ponds and level spreader, which will receive the water from the single outlet.

4.1.6.4 Tree Felling Drainage Controls

Mitigation measures which will reduce the risk of entrainment of suspended solids and nutrient release in surface watercourses comprise best practice methods which are set out as follows:

- Machine combinations will be chosen which are most suitable for ground conditions at the time of felling and to minimise soils disturbance;
- Use of buffer zones for aquatic zones (see Table 4.1 below);
- Checking and maintenance of roads and culverts will be on-going through any felling operation. No tracking of vehicles through watercourses will occur, as vehicles will use road infrastructure and existing watercourse crossing points. Where possible, existing drains will not be disturbed during felling works;
- Ditches which drain from the area to be felled towards existing surface watercourses will be blocked, and temporary silt traps will be constructed. No direct discharge of such ditches to watercourses will occur. Drains and sediment traps should be installed during ground preparation. Collector drains will be excavated at an acute angle to the contour (~0.3%-3% gradient), to minimise flow velocities. Main drains to take the discharge from collector drains will include water drops and rock armour, as required, where there are steep gradients, and should avoid being placed at right angles to the contour;
- Sediment traps will be sited outside of buffer zones and will have no direct outflow into the aquatic zone. Machine access will be maintained to enable the accumulated sediment to be excavated. Sediment will be carefully disposed of away from all aquatic zones. Where possible, all new silt traps will be constructed on even ground and not on sloping ground;
- In areas, particularly sensitive to erosion, it may be necessary to install double or triple sediment traps. This measure will be reviewed on site during construction;
- All drainage channels will taper out before entering the aquatic buffer zone. This ensures that discharged water gently fans out over the buffer zone before entering the aquatic zone, with sediment filtered out from the flow by ground vegetation within the zone. On erodible soils, silt traps will be installed at the end of the drainage channels, to the outside of the buffer zone;
- Drains and silt traps will be maintained throughout all felling works, ensuring that they are clear of sediment build-up and are not severely eroded. Correct drain alignment, spacing and depth will ensure that erosion and sediment build-up are minimised and controlled;
- Brash mats will be used to support vehicles on soft ground, reducing peat and mineral soils erosion and avoiding the formation of rutted areas, in which surface water ponding can occur. Brash mat renewal should take place when they become heavily used and worn. Provision should be made for brash mats along all off-road routes, to protect the soil from compaction and rutting. Where there is risk of severe erosion occurring, extraction should be suspended during periods of high rainfall;
- Timber should be stacked in dry areas, and outside a local 50m stream buffer zone. Straw bales and check dams to be emplaced on the down gradient side of timber storage/processing sites;
- Works should be carried out during periods of no, or low rainfall, in order to minimise entrainment of exposed sediment in surface water run-off;
- Checking and maintenance of roads and culverts will be on-going through the felling operation;
- Refuelling or maintenance of machinery will not occur within 50m of an aquatic zone. Dedicated refuelling areas will be used during the felling works; and,

- Branches, logs or debris will not be allowed to build up in aquatic zones. All such material will be removed when harvesting operations have been completed, but care will be taken to avoid removing natural debris deflectors.

Table 4.1 Minimum Buffer Zone Widths (Forest Service, 2000)

Average slope leading to the aquatic zone		Buffer zone width on either side of the aquatic zone	Buffer zone width for highly erodible soils
Moderate	(0 – 15%)	10 m	15 m
Steep	(15 – 30%)	15 m	20 m
Very steep	(>30%)	20 m	25 m

The majority of the felling will be within and around the development footprint of turbine bases and access roads.

Best practice methods related to water incorporated into the forestry management and water quality protection measures will be derived from:

- Forestry Commission (2011): Forests and Water Guidelines, Fifth Edition. Publ. Forestry Commission, Edinburgh;
- Coillte (2013) Forest Operations & Water Protection Guidelines;
- DAFM (2017). Felling and Reforestation Policy;
- Coillte (2009) Methodology for Clear Felling Harvesting Operations;
- Forest Service (2000): Forestry and Water Quality Guidelines. Forest Service, DAF, Johnstown Castle Estate, Co. Wexford; and,
- Forest Service, (2000): Code of Best Forest Practice – Ireland. Forest Service, DAF, Johnstown Castle Estate, Co. Wexford.

4.1.6.5 Cable Trench Drainage

Cable trenches are typically developed in short sections, thereby minimising the amount of ground disturbed at any one time and minimising the potential for drainage runoff to pick up silt or suspended solids. Each short section of trench is excavated, ducting installed and bedded, and backfilled with the appropriate materials, before work on the next section commences.

To efficiently control drainage runoff from cable trench works areas, excavated material is stored on the upgradient side of the trench. Should any rainfall cause runoff from the excavated material, the material is contained in the downgradient cable trench. Excess subsoil is removed from the cable trench works area immediately upon excavation, and in the case of the development, would be transported to one of the on-site borrow pit disposal areas or used for landscaping and reinstatements of other areas elsewhere on site.

On steeper slopes, silt fences, as detailed in Section 4.2.6.1.11 above will be installed temporarily downgradient of the cable trench works area, or on the downhill slope below where excavated material is being temporarily stored to control run-off.

4.1.7 Drainage Maintenance

Drainage performance will form part of the civil works contract requirements. During the construction phase the effectiveness of drainage measures designed to minimise runoff entering works areas and capture and treatment of potentially silt-laden water from the works areas will be monitored periodically (daily, weekly, and event based monitoring, *i.e.* after heavy rainfall events as summarised in Section 5.2 below) by the

ECoW and/or the Project Hydrologist. The ECoW will respond to changing weather and drainage conditions on the ground as the project proceeds, to ensure the effectiveness of the drainage design is maintained.

The abandonment triggers as set out in the SOWOR will be adopted as part of drainage inspections to ensure that any of the conditions prescribed under any abandonment trigger does not exist at the locations under inspection.

Regular inspections of all existing and installed drainage systems will be undertaken, especially after heavy rainfall, to check for blockages, and ensure there is no build-up of standing water within the system. Any excess build-up of silt levels at check dams, the settlement ponds, or any other drainage features that may decrease the effectiveness of the drainage feature, will be removed. For this reason, check dams will be inspected and maintained weekly during the construction phase of the project to insure adequate performance. Maintenance checks will also ensure the centre elevation of the dam remains lower than the sides of the dam.

Check dams will also be inspected weekly during the construction phase of the project and following rainfall events to ensure the structure of the dam is still effective in controlling flow. Any scouring around the edges of the check dams or overtopping of the dam in normal flow conditions will be rectified by reinforcement of the check dam. Drainage swales will be regularly inspected for evidence of erosion along the length of the swale. If any evidence of erosion is detected, additional check dams will be installed to limit the velocity of flow in the channel and reduce the likelihood of erosion occurring in the future.

A water level indicator such as a simple staff gauge or level marker will be installed in each settlement pond with marks to identify when sediment is at 50% of the pond's capacity. Sediment will be cleaned out of the settlement pond when it exceeds 50% of capacity. Settlement ponds will be inspected weekly during the construction phase of the project and following rainfall events. Inlet and outlets will be checked for sediment accumulation and anything else that might interfere with flows.

On completion of the civil and excavations works at the site, the frequency of inspections and monitoring of the drainage infrastructure will reduce to monthly as deemed appropriate by the ECoW.

4.1.8 Operational Phase Drainage Management

The project hydrologist will inspect and review the drainage system after construction has been completed to provide guidance on the requirements of an operational phase drainage system. This operational phase drainage system will have been installed during the construction phase in conjunction with the road and hardstanding construction work as described below:

- Interceptor drains will be maintained up-gradient of all infrastructure to collect clean surface runoff, in order to minimise the amount of runoff reaching areas where suspended sediment could become entrained. It will then be directed through a series of in-line treatments prior to discharge;
- Swales/road side drains will be maintained to intercept and collect runoff from access roads and hardstanding areas of the site, likely to have entrained suspended sediment, and channel it to settlement ponds for sediment settling;
- Check dams will be maintained at regular intervals along interceptor drains and swales/roadside drains in order to reduce flow velocities and therefore minimise erosion within the system during storm rainfall events; and,

- Settlement ponds, emplaced downstream of swales and roadside drains, will buffer volumes of runoff discharging from the drainage system during periods of high rainfall, by retaining water until the storm hydrograph has receded, thus reducing the hydraulic loading to watercourses.

In operational phase of the wind farm, the reliance on the drainage system summarised above will become reduced as areas naturally revegetate. Once areas revegetate, this will result in a resumption of the natural drainage management that will have existed prior to any construction.


5 ENVIRONMENTAL MANAGEMENT IMPLEMENTATION

5.1 Roles and Responsibilities

The Site Supervisor/Construction Manager and/or Environmental Clerk of Works (ECoW) are the project focal point relating to construction-related environmental issues.

In general, the ECoW will maintain responsibility for monitoring the works and Contractors/Sub-contractors from an environmental perspective. The ECoW will act as the regulatory interface on environmental matters by reporting to and liaising with Donegal County Council and other statutory bodies as required.

The ECoW will report directly to the Site Supervisor/Wind Farm Construction Manager. A Project Ecologist, Project Hydrologist and Project Geotechnical engineer will visit the site regularly and report to site management. This structure provides a “triple lock” review/interaction by external specialists. An organogram structure for the construction stage is as follows:

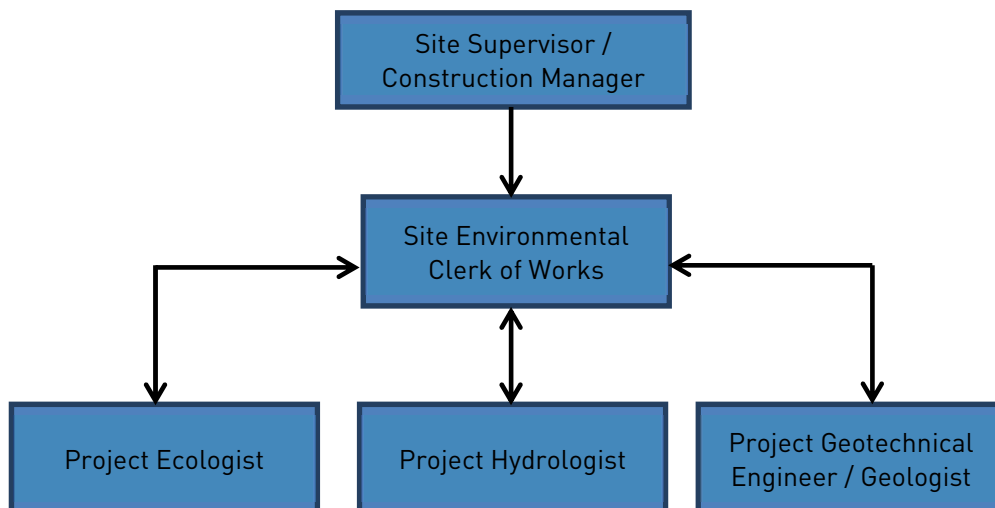

Any requirement of favourable planning permission decision, for the works to be supervised by an engineer with professional indemnity insurance, who upon completion of the works, including site stability, shall certify the said works, will be adhered to. Such an engineer will be appointed to oversee and supervise the construction phase of the project.

5.1.1 Wind Farm Construction Manager/Site Supervisor

The Site Supervisor/Construction Manager will have overall responsibility for the organisation and execution of all related environmental activities as appropriate, in accordance with regulatory and project environmental requirements. The duties and responsibilities of the Site Supervisor/Construction Manager will include:

- Ensure that all works are completed safely and with minimal environmental risk;
- Approve and implement the Project CEMP and supporting environmental documentation, and ensure that all environmental standards are achieved during the construction phase of the project;

- Take advice from the ECoW on legislation, codes of practice, guidance notes and good environmental working practice relevant to their work;
- Ensure compliance through audits and management site visits;
- Ensure timely notification of environmental incidents; and,
- Ensure that all construction activities are planned and performed such that minimal risk to the environment is introduced.

5.1.2 Site Environmental Clerk of Works

The main contractor will be required to engage a qualified Environmental Engineer, Environmental Scientist, or equivalent, with experience in wind farm construction to fulfil the role of Site Environmental Clerk of Works (ECoW), and to monitor all site works and to ensure that methodologies and mitigation are followed throughout construction to avoid negatively impacting on the receiving environment.

The ECoW will report to the Construction Manager. The responsibilities and duties of the ECoW will include the following:

- Preparation of the CEMP and supporting environmental documentation and review/approval of contractor method statements;
- Undertake inspections and reviews to ensure the works are carried out in compliance with the CEMP;
- Monitor the implementation of the CEMP, particularly all proposed/required Environmental Monitoring;
- Generate environmental reports as required to show environmental data trends and incidents and ensure environmental records are maintained throughout the construction period;
- Advise site management/contractor/sub-contractors on:
 - Prevention of environmental pollution and improvement to existing working methods;
 - Changes in legislation and legal requirements affecting the environment;
 - Suitability and use of plant, equipment and materials to prevent pollution;
 - Environmentally sound methods of working and systems to identify environmental hazards;
- Ensure proper mitigation measures are initiated and adhered to during the construction phase;
- Liaise with Project Ecologist, Project Hydrologist and Project Geotechnical Engineer to ensure regular site visits and audits/inspections are completed;
- Ensure adequate arrangements are in place for site personnel to identify potential environmental incidents;
- Ensure that details of environmental incidents are communicated in a timely manner to the relevant regulatory authorities, initially by phone and followed up as soon as is practicable by e-mail;
- Support the investigation of incidents of significant, potential or actual environmental damage, and ensure corrective actions are carried out, recommend means to prevent recurrence and communicate incident findings to relevant parties; and,
- Identify environmental training requirements and arrange relevant training for all levels of site-based staff/workers.
- The level, detail and frequency of reporting expected from the ECoW for the Construction Manager, developer's project manager, and any Authorities or other Agencies, will be agreed by all parties prior to commencement of

construction, and may be further adjusted as required during the course of the project.

5.1.3 Project Ecologist

The Project Ecologist will report to the ECoW and is responsible for the protection of sensitive habitats and species encountered during the construction phase of the wind farm. The Project Ecologist will not be full time on site but will visit the site at least once a month during construction.

The responsibilities and duties of the Project Ecologist will include the following:

- Review and input to the final construction phase CEMP in respect of ecological matters;
- In liaison with ECoW, oversee and provide advice on all relevant ecology mitigation measures set out in EIAR;
- Regular inspection and monitoring of the development, through all phases of construction/operation and provide ecological advice as required;
- Carry out ecological monitoring and survey work as may be required by the planning authority.
- Complete a pre-commencement invasive species survey at the site

5.1.4 Project Hydrologist

The Project Hydrologist will report to the ECoW and is responsible for inspection and review of drainage and water quality aspects associated with construction of the wind farm. The Project Hydrologist will not be full time on site but will visit the site at least once a month during construction.

The responsibilities and duties of the Project Hydrologist will include the following:

- Assist in compiling a detailed drainage design before construction commences and attend the site to set out and assist with micro siting of drainage controls. This will be completed over several site visits at the start of the construction phase;
- Review and input to the final construction phase CEMP in respect of drainage and water quality management;
- Following the initial stage of drainage construction regular site visits will be required, at least once a month, to complete hydrological and water quality audits and reviews and report any issues noted to the Site Supervisor/Construction Manager; and,
- Complete ongoing inspection and monitoring of the development, particularly in areas of drainage control, through all phases of construction (including pre, during and post construction) and ensure construction is carried out as specified in the EIAR.

5.1.5 Project Geotechnical Engineer / Geologist

The Geotechnical Engineer or Project Geologist will report to the ECoW and is responsible for inspection and review of geotechnical aspects associated with construction of the wind farm. The Geotechnical Engineer will not be full time on site but will visit site at least once a month during construction phase.

The responsibilities and duties of the Geotechnical Engineer or Geologist will include the following:

- Visit site regularly, or at least once a month during the construction phase, to complete geotechnical audits and reviews and report any issues to the Site Supervisor/Construction Manager;
- Ensuring that identified hazards are listed in the Geotechnical Risk Register and that these are subject to ongoing monitoring;
- Set up and review the readings of the peat stability monitoring system and,
- Ongoing inspection and monitoring of the development, particularly in areas of peatland and at the borrow pit areas through all phases of construction (including pre, during and post construction) and ensure construction is carried out as specified in the EIAR.

5.2 Monitoring of Surface Water Quality

The surface water quality monitoring programme combines the use of laboratory analysis, water quality monitoring instrumentation and visual inspection to develop a comprehensive schedule of monitoring of all watercourse that exist both at the site and the surrounding area. The information collected by this schedule of water monitoring, particularly the continuous turbidity monitoring will inform the pre-commencement triggers in the SOWOR before works commence in an area. The turbidity monitors both upstream and downstream of the site will provide instant data on the quality of water in which they are deployed and will be equipped with an alarm system to alert site management if a peak in turbidity occurs as set out in the SOWOR.

The water monitoring programme was prepared in accordance with the following legislation:

- Planning and Development Acts 2000-2017;
- Planning and Development Regulations, 2001 (as amended);
- S.I. No. 94 of 1997: European Communities (Natural Habitats) Regulations, resulting from EU Directives 92/43/EEC on the conservation of natural habitats and of wild fauna and flora (the Habitats Directive) and 79/409/EEC on the conservation of wild birds (the Birds Directive);
- S.I. No. 293 of 1988: Quality of Salmon Water Regulations, resulting from EU Directive 78/659/EEC on the Quality of Fresh Waters Needing Protection or Improvement in order to Support Fish Life;
- S.I. No. 272 of 2009: European Communities Environmental Objectives (Surface Waters) Regulations 2009 and S.I. No. 722 of 2003 European Communities (Water Policy) Regulations which implement EU Water Framework Directive (2000/60/EC) and provide for implementation of 'daughter' Groundwater Directive (2006/118/EC). Since 2000 water management in the EU has been directed by the Water Framework Directive (WFD). The key objectives of the WFD are that all water bodies in member states achieve (or retain) at least 'good' status by 2015. Water bodies comprise both surface and groundwater bodies, and the achievement of 'Good' status for these depends also on the achievement of 'good' status by dependent ecosystems. Phases of characterisation, risk assessment, monitoring and the design of programmes of measures to achieve the objectives of the WFD have either been completed or are ongoing. In 2015 it will fully replace a number of existing water related directives, which are successively being repealed, while implementation of other Directives (such as the Habitats Directive 92/43/EEC) will form part of the achievement of implementation of the objectives of the WFD;
- S.I. No. 41 of 1999: Protection of Groundwater Regulations, resulting from EU Directive 80/68/EEC on the protection of groundwater against pollution caused by certain dangerous substances (the Groundwater Directive);

- S.I. No. 249 of 1989: Quality of Surface Water Intended for Abstraction (Drinking Water), resulting from EU Directive 75/440/EEC concerning the quality required of surface water intended for the abstraction of drinking water in the Member States (repealed by 2000/60/EC in 2007);
- S.I. No. 439 of 2000: Quality of Water intended for Human Consumption Regulations and S.I. No. 278 of 2007 European Communities (Drinking Water No. 2) Regulations, arising from EU Directive 98/83/EC on the quality of water intended for human consumption (the Drinking Water Directive) and WFD 2000/60/EC (the Water Framework Directive);
- S.I. No. 272 of 2009: European Communities Environmental Objectives (Surface Waters) Regulations 2009;
- S.I. No. 9 of 2010: European Communities Environmental Objectives (Groundwater) Regulations 2010; and,
- S.I. No. 296 of 2009: European Communities Environmental Objectives (Freshwater Pearl Mussel) Regulations 2009.

Relevant Northern Irish legislation were also reviewed and considered during the assessment of trans-border hydrological impacts.

This water monitoring programme will be the subject of independent review by the supervising hydrologist who will provide the necessary guidance on the monitoring requirements. The water monitoring programme is outlined in the following sections.

5.2.1 Pre-Construction Drainage Inspection and Monitoring

There is an existing drainage network across the site and runoff drains relatively freely to local watercourses and streams. This existing drainage system will continue to function as it is during the pre-construction phase.

However, prior to commencement of works in sub-catchments across the site main drain inspections will be completed to ensure ditches and streams are free from debris and blockages that may impede drainage. These inspections will be done on a catchment by catchment basis as the construction works develop across the site, as works in all areas will not commence simultaneously.

Monthly Laboratory Analysis Sampling: Baseline laboratory analysis for the parameters listed below with relevant regulatory limits and Environmental Quality Standards (EQSs) will be undertaken for each watercourse *e.g.* at SW1 – SW3 as outlined in Figure 5.1. This will not be restricted to just these three locations and further sampling points will be added as deemed necessary by the ECoW in consultation with the project hydrologist.


5.2.2 Construction Phase Drainage Inspection and Monitoring:

Inspection sheets and photographic records will be kept on site. Inspection points will include the in-situ field monitoring point locations and the laboratory analysis sampling points. Inspection points will depend on works being completed within the catchment upstream of the identified monitoring locations. Visual inspections will also be completed after major rainfall events, *i.e.* after events of >25mm rainfall in any 24-hour period and data including photographs will be collected by visual inspections and independently assessed by the supervising hydrologist who will monitor and advise on the records being received.

The following periodic inspection regime will be implemented:

Map Legend

- ▭ Site Location
- Turbine Locations
- - - Grid Connection
- ◆ Surface Water Sampling Location
- ▭ Glendergan River Catchment
- ▭ Mourne Beg River Catchment
- ▭ Lowerymore River Catchment
- Sonde Locations
- Wind Farm Infrastructure
- River/Stream

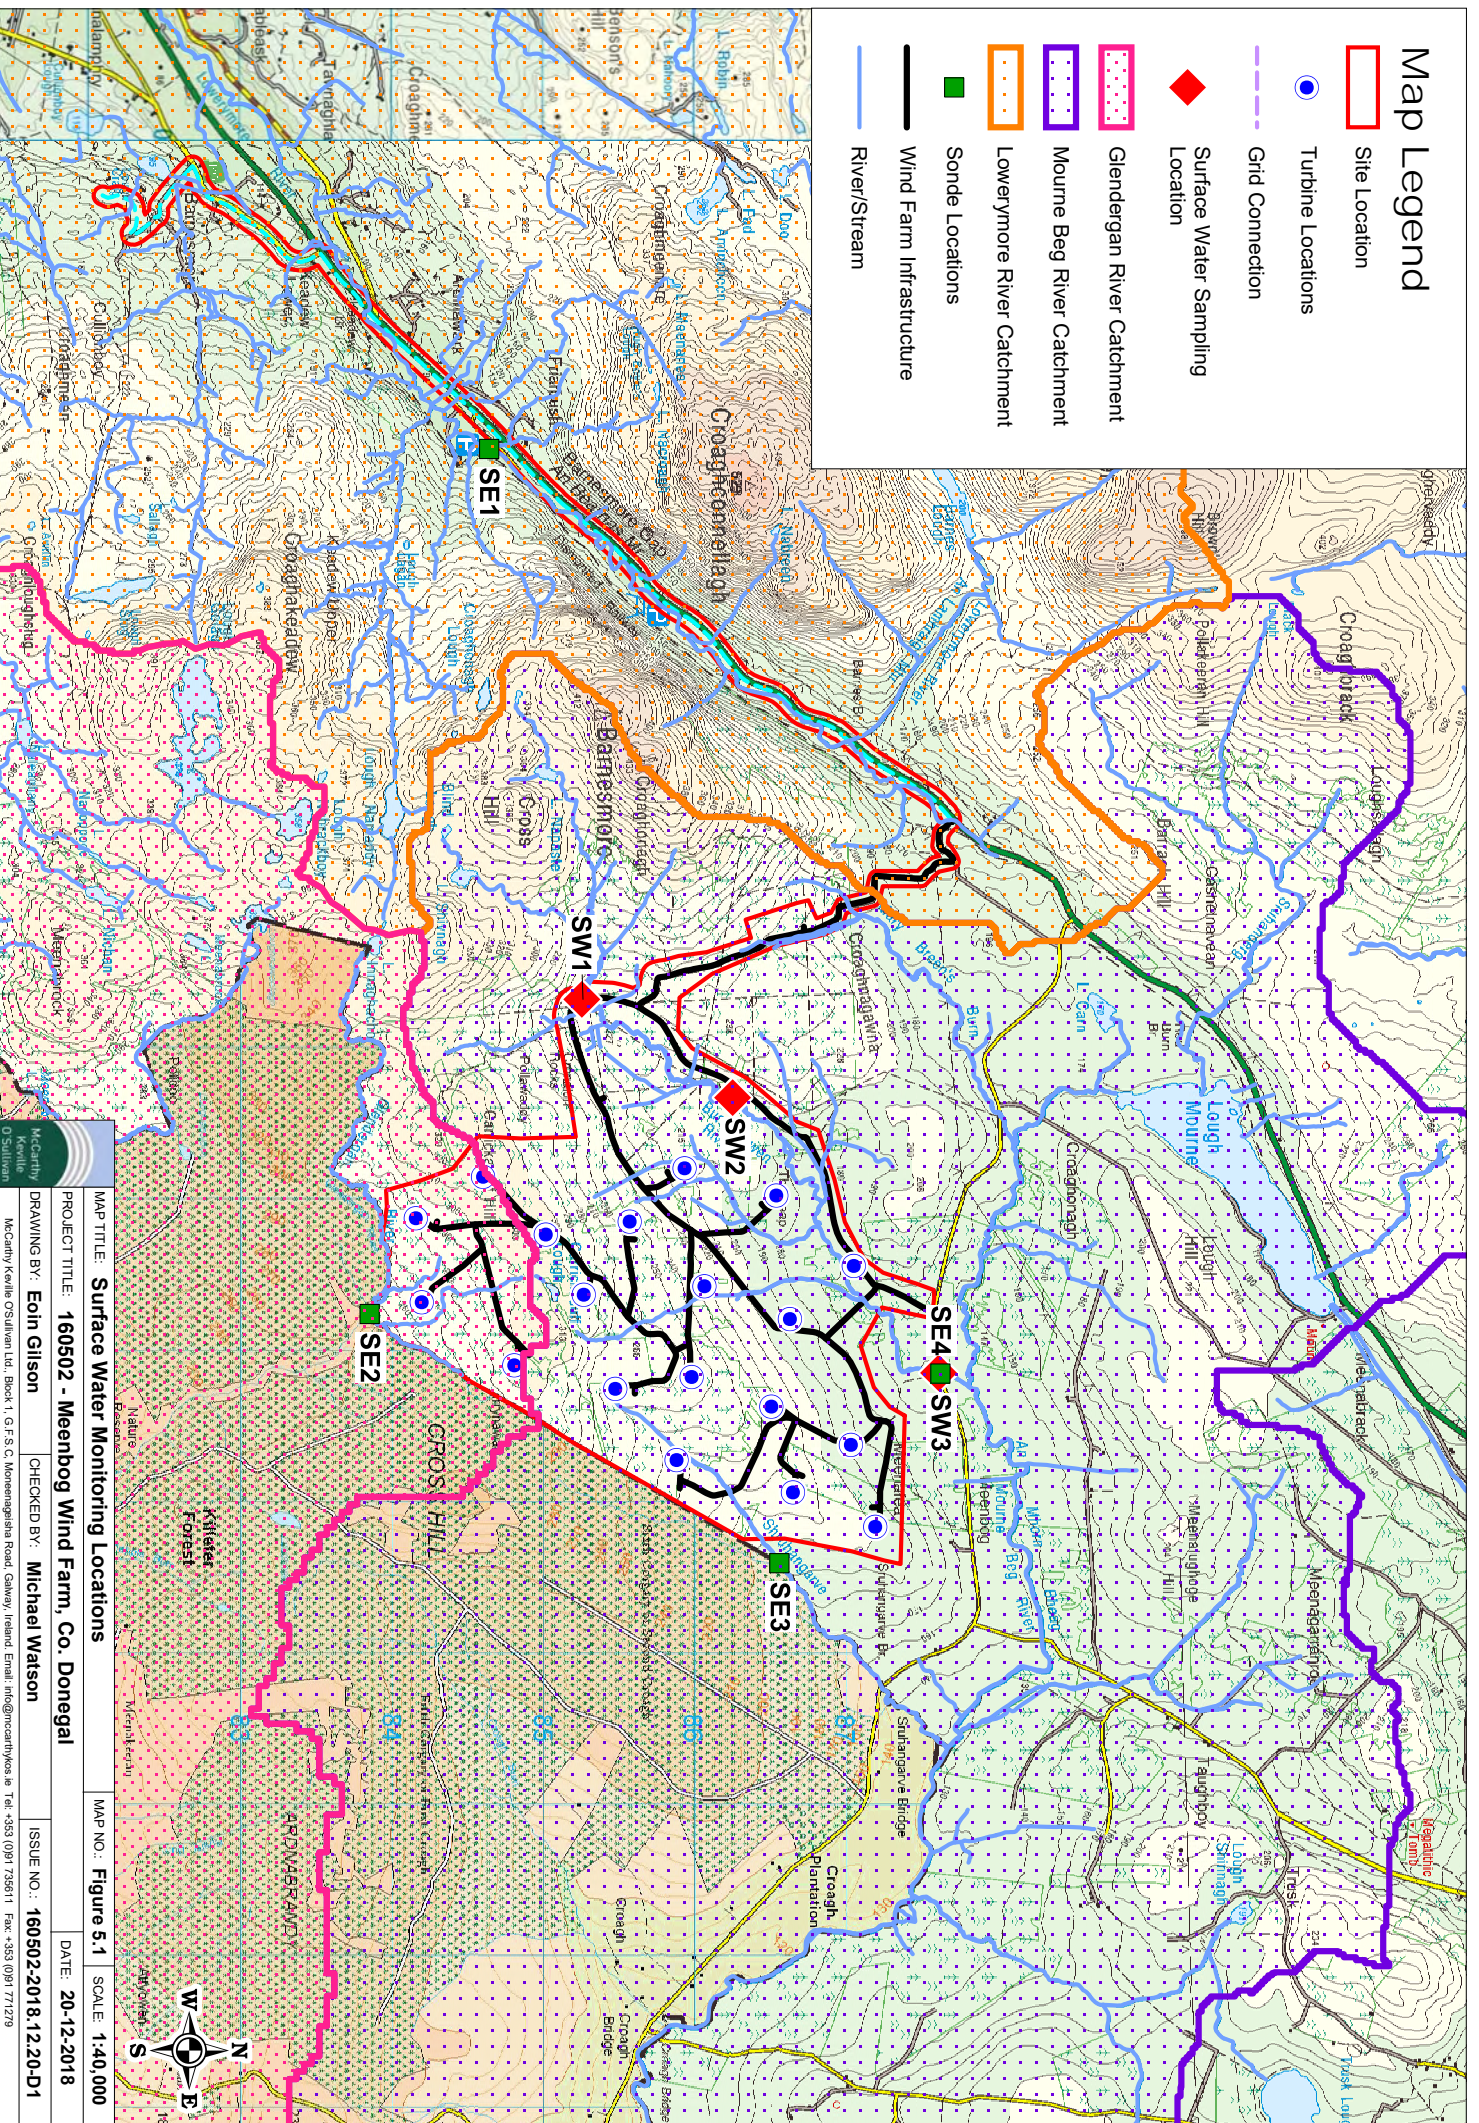

	MAP TITLE: Surface Water Monitoring Locations	MAP NO.: Figure 5.1	SCALE: 1:40 000
	PROJECT TITLE: 160502 - Meenbog Wind Farm, Co. Donegal	CHECKED BY: Michael Watson	ISSUE NO.: 160502-2018.12.20-D1
DRAWING BY: Eoin Gilson		DATE: 20-12-2018	
Ordnance Survey Ireland Licence No. AR 0021815 © Ordnance Survey Ireland/Government of Ireland			

- Daily general visual inspections of site operations and inspections of all watercourses within the site and in the surrounding area by the ECoW or a suitably qualified and competent person as delegated by the ECoW;
- Inspections to include all elements of drainage infrastructure to ensure the system is operating correctly and to identify and maintenance that is required. Any changes, such as discolouration, odour, oily sheen or litter should be noted and corrective action should be implemented. High risk locations such as settlement ponds will be inspected daily. Daily inspections checks will be completed on plant and equipment, and whether materials such as straw bales or oil absorbent materials need replacement;
- Event based inspections by the ECoW as follows:
 - >10 mm/hr (*i.e.* high intensity localised rainfall event);
 - >25 mm in a 24-hour period (heavy frontal rainfall lasting most of the day); or,
 - Rainfall depth greater than monthly average in 7 days (prolonged heavy rainfall over a week).
- Monthly site inspections by the Project Hydrologist/ ECoW during construction phase;
- Quarterly site inspections by the Project Hydrologist/ ECoW after construction for a period of one year following the construction phase; and,
- A written record will be maintained or available on-site within this Construction Environmental Management Plan (CEMP) which will be maintained on-site during the construction phase.

5.2.2.1 In-situ field monitoring:

Field chemistry measurements of unstable parameters, (pH, conductivity, dissolved oxygen and temperature) will be taken at all monitoring locations outlined in Figure 5.1. These analyses will be carried out by either the ECoW or the Project Hydrologist. In-situ field monitoring will be completed on a weekly basis. In-situ field monitoring will also be completed after major rainfall events, *i.e.* after events of >25mm rainfall in any 24-hour period. The supervising hydrologist will monitor and advise on the readings collected by in-situ field monitoring.

5.2.2.2 Monthly Laboratory Analysis Sampling

Laboratory analysis of a range of parameters with relevant regulatory limits and EQSs will continue throughout the construction phase for each monitoring location as outlined in Figure 5.1. All samples will be sent for analysis to an independent laboratory. This sampling will also be completed on an event based basis, *i.e.* after major rainfall events (>25mm rainfall in any 24-hour period). The supervising hydrologist will monitor and advise on the readings being received from the testing laboratory.

5.2.2.3 Continuous Turbidity Monitoring

Turbidity monitors or sondes will be installed at locations surrounding the wind farm site as outlined in Figure 5.1. The sondes will provide continuous readings for turbidity levels in the watercourse. This equipment will be supplemented by daily visual monitoring at their locations as outlined in the sections below.

5.2.2.4 Monitoring Parameters

The analytical determinants of the monitoring programme (including limits of detection and frequency of analysis) will be as per S.I. No. 272 of 2009 European Communities Environmental Objectives (Surface Waters) Regulations, S.I. No. 722 of 2003 European Communities (Water Policy) Regulations and European Communities Environmental

Objectives (Freshwater Pearl Mussel) Regulations 2009. The likely suite of parameters will include:

- pH (field measured)
- Electrical Conductivity (field measured)
- Temperature (field measured)
- Dissolved Oxygen (field measured)
- Turbidity (NTU) (sonde measured)
- Total Suspended Solids (mg/l)
- Ammoniacal Nitrogen as NH₃ (mg/l)
- Ammoniacal Nitrogen as NH₄ (mg/l)
- Nitrite (NO₂) (mg/l)
- Ortho-Phosphate (P) (mg/l)
- Nitrate (NO₃) (mg/l)
- Phosphorus (unfiltered) (mg/l)
- Chloride (mg/l)
- Biochemical Oxygen Demand (BOD) (mg/l)

5.2.3 Surface Water Monitoring Reporting

Visual inspection and laboratory analysis results of water quality monitoring shall assist in determining requirements for any necessary improvements in drainage controls and pollution prevention measures implemented on site.

It will be the responsibility of the Environmental Clerk of Works to present the ongoing results of water quality and weather monitoring at or in advance of regular site meetings.

Reports on water quality will consider all field monitoring and visual inspections, and results of laboratory analysis completed for that period. Reports will describe how the results compare with baseline data as well as previous reports on water quality. The reports will also describe whether any deterioration or improvement in water quality that has been observed, whether any effects are attributable to construction activities and what remedial measures or corrective actions have been implemented.

All water monitoring reports will be available to Donegal County Council on request at any stage during the construction phase

5.2.4 Post-Construction Monitoring

Monthly sampling for laboratory analysis for a range of parameters as adopted during pre-commencement and construction phases will continue for six months after construction is complete. The supervising hydrologist will monitor and advise on the readings being received from the testing laboratory.

5.3 Environmental Awareness and Training

5.3.1 Environmental Induction

The Environmental Induction will be integrated into the general site induction on a case by case basis for each member of staff employed on-site depending on their assigned roles and responsibilities on site. Where necessary, the Environmental Induction will as a minimum include:

- A copy of the Environmental Management Site Plans and discussion of the key environmental risks and constraints;

- An outline of the CEMP structure;
- A discussion of the applicable Works Method Statement;
- The roles and responsibilities of staff, including contractors, in relation to environmental management; and,
- An outline of the Environmental Incident Management Procedure.

5.3.2 Toolbox Talks

Tool box talks would be held by the ECoW or Construction Manager at the commencement of each day, or at the commencement of new activities. The aims of the tool box talks are to identify the specific work activities that are scheduled for that day or phase of work. In addition, the necessary work method statements and sub plans would be identified and discussed prior to the commencement of the day's activities.

Site meetings would be held on a regular basis involving all site personnel. The objectives of site meetings is to discuss the coming weeks activities and identify the relevant work method statements and sub plans that will be relevant to that weeks activities. Additionally, any non-compliance identified during the previous week would also be discussed with the aim to reduce the potential of the same non-compliance reoccurring.

6 EMERGENCY RESPONSE PLAN

An Emergency Response Plan is presented in this section of the CEMP. It provides details of procedures to be adopted in the event of an emergency in terms of site health and safety and environmental protection.

6.1 Emergency Response

The Emergency Response Plan (ERP) is presented in this section of the CEMP. It provides details of procedures to be adopted in the event of an emergency. The site ERP includes details on the response required and the responsibilities of all personnel in the event of an emergency. The ERP will require updating and submissions from the contractor/PSCS and suppliers as the project progresses. Where sub-contractors that are contracted on site are governed by their own emergency response procedure a bridging arrangement will be adopted to allow for inclusion of the sub-contractor's ERP within this within this document.

This is a working document that requires updating throughout the various stages of the project.

6.1.1 Roles and Responsibilities

The chain of command during an emergency response sets out who is responsible for coordinating the response. The Site Manager will lead the emergency response which makes him responsible for activating and coordinating the emergency response procedure. The other site personnel who can be identified at this time who will be delegated responsibilities during the emergency response are presented in Figure 6.1. In a situation where the Site Manager is unavailable or incapable of coordinating the emergency response, the responsibility will be transferred to the next person in the chain of command outlined in Figure 6.1. This will be updated throughout the various stages of the project.

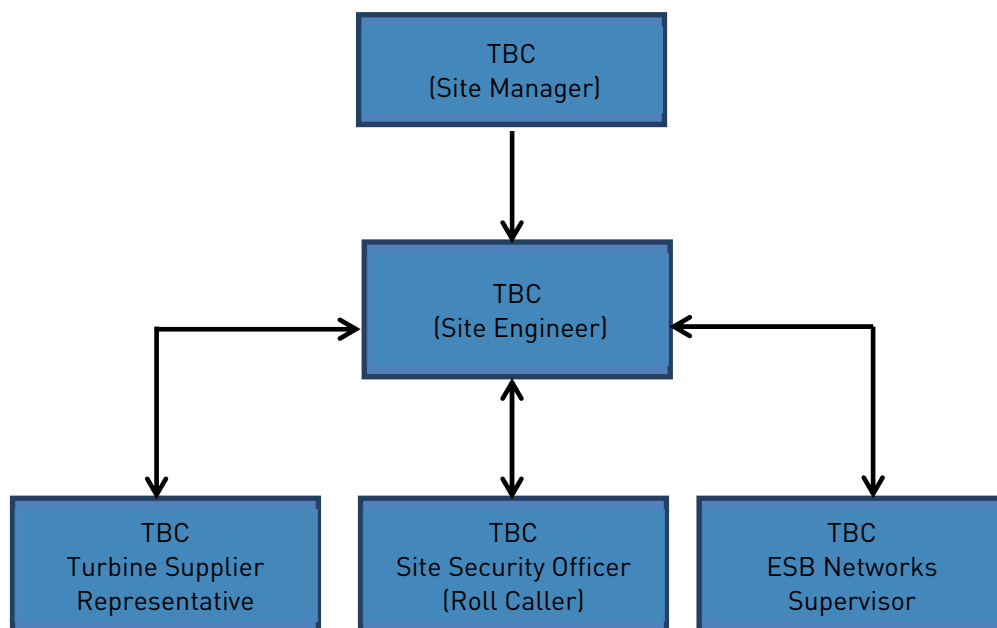


Figure 6.1 Emergency Response Procedure Chain of Command

6.1.2 Initial Steps

In order to establish the type and scale of potential emergencies that may occur, the following hazards have been identified as being potential situations that may require an emergency response in the event of an occurrence.

Table 6.1 Hazards associated with potential emergency situations

Hazard	Emergency Situation
Construction Vehicles: Dump trucks, tractors, excavators, cranes etc.	Collision or overturn which has resulted in operator or third-party injury.
Abrasive wheels/Portable Tools	Entanglement, amputation or electrical shock associated with portable tools
Contact with services	Electrical shock or gas leak associated with an accidental breach of underground services
Fire	Injury to operative through exposure to fire
Falls from heights including falls from scaffold towers, scissor lifts, and ladders	Injury to operative after a fall from a height
Sickness	Illness unrelated to site activities of an operative e.g. heart attack, loss of consciousness, seizure

In the event of an emergency situation associated with, but not restricted to, the hazards outlined in Table 6.1 the Site Manager will carry out the following:

- Establish the scale of the emergency situation and identify the number of personnel, if any, have been injured or are at risk of injury.
- Where necessary, sound the emergency siren/fog horn that activates an emergency evacuation on the site. The Site Manager must proceed to the assembly point if the emergency poses any significant threat to their welfare **and if there are no injured personnel at the scene that require assistance.** The Site Manager will be required to use his own discretion at that point. In the case of fire, the emergency evacuation of the site should proceed, without exception. The site evacuation procedure is outlined in Section 6.1.3.
- Make safe the area if possible and ensure that there is no identifiable risk exists with regard to dealing with the situation e.g. if a machine has turned over, ensure that it is in a safe position so as not to endanger others before assisting the injured.
- Contact the required emergency services or delegate the task to someone if he is unable to do so. If delegating the task, ensure that they follow the procedures for contacting the emergency services as set out in Section 6.3.
- Take any further steps that are deemed necessary to make safe or contain the emergency incident e.g. cordon off an area where an incident associated with electrical issues has occurred.
- Contact any regulatory body or service provider as required e.g. ESB Networks the numbers for which as provided in Section 6.3.2.
- Contact the next of kin of any injured personnel where appropriate. The procedure for this is outlined in Section 6.3.3.

6.1.3 Site Evacuation/Fire Drill

A site evacuation/fire drill procedure will provide basis for carrying out the immediate evacuation of all site personnel in the event of an emergency. The following steps will be taken:

- Notification of the emergency situation. Provision of a siren or fog horn to notify all personnel of an emergency situation.
- An assembly point will be designated in the construction compound area and will be marked with a sign. All site personnel will assemble at this point.
- A roll call will be carried out by the Site Security Officer to account for all personnel on site.
- The Site Security Officer will inform the Site Manager when all personnel have been accounted for. At this time, the Site Manager will decide the next course of action which be determined by the situation that exists at that time. The Site Manager will advise all personnel accordingly.

All personnel will be made aware of the evacuation procedure during site induction. The Fire Services Acts of 1981 and 2003 require the holding of fire safety evacuation drills at specified intervals and the keeping of records of such drills.

6.1.4 Excessive Peat Movement

Where there is excessive peat movement or continuing peat movement recorded at a monitoring location or identified at any location within the site but no apparent signs of distress to the peat (e.g. cracking, surface rippling) then the following shall be carried out.

1. All construction activities shall cease within the affected area.
2. Increased monitoring at the location shall be carried out. The area will be monitored, as appropriate, until such time as movements have ceased.
3. Re-commencement of limited construction activity shall only start following a cessation of movement and the completion of a geotechnical risk assessment by a geotechnical engineer.

6.1.5 Onset of Peat Slide

Where there is the onset or actual detachment of peat (e.g. cracking, surface rippling) then the following shall be carried out.

1. On alert of a peat slide incident, all construction activities will cease and all available resources will be diverted to assist in the required mitigation procedures.
2. Where considered possible, action will be taken to prevent a peat slide reaching any watercourse. This will take the form of the construction of check barrages on land. Due to the terrain, the possible short run-out length to watercourses, speed of movement and the inability to predict locations it may not be possible to implement any on-land prevention measures, in this case a watercourse check barrage will be implemented.
3. For localised peat slides that do not represent a risk to a watercourse and have essentially come to rest, the area will be stabilised initially by rock infill, if required. The failed area and surrounding area will then be assessed by the engineering staff and stabilisation procedures implemented. The area will be monitored, as appropriate, until such time as movements have ceased.

6.1.6 Spill Control Measures

Every effort will be made to prevent an environmental incident during the construction and operational phase of the project. Oil/Fuel spillages are one of the main environmental risks that will exist at the site which will require an emergency response procedure. The importance of a swift and effective response in the event of such an incident occurring cannot be over emphasised. The following steps provide the procedure to be followed in the event of such an incident.

- Stop the source of the spill and raise the alarm to alert people working in the vicinity of any potential dangers.
- If applicable, eliminate any sources of ignition in the immediate vicinity of the incident
- Contain the spill using the spill control materials, track mats or other material as required. Do not spread or flush away the spill.
- If possible, cover or bund off any vulnerable areas where appropriate such as drains, watercourses or sensitive habitats.
- If possible, clean up as much as possible using the spill control materials.
- Contain any used spill control material and dispose of used materials appropriately using a fully licensed waste contractor with the appropriate permits so that further contamination is limited.
- Notify the ECoW immediately giving information on the location, type and extent of the spill so that they can take appropriate action.
- The ECoW will inspect the site and ensure the necessary measures are in place to contain and clean up the spill and prevent further spillage from occurring.
- The ECoW will notify the appropriate regulatory body such as Donegal County Council, Department of Communications, Climate Action and Environment (DCCAE), if deemed necessary.

Environmental incidents are not limited to just fuel spillages. Therefore, any environmental incident must be investigated in accordance with the following steps.

- The ECoW must be immediately notified.
- If necessary, the ECoW will inform the appropriate regulatory authority. The appropriate regulatory authority will depend on the nature of the incident.
- The details of the incident will be recorded on an Environmental Incident Form which will provide information such as the cause, extent, actions and remedial measures used following the incident. The form will also include any recommendations made to avoid reoccurrence of the incident.
- If the incident has impacted on an ecologically sensitive receptor, such as a sensitive habitat, protected species or designated conservation site (pSPA or cSAC), the ECoW will liaise with the Project Ecologist.
- If the incident has impacted on a sensitive receptor such as an archaeological feature the ECoW will liaise with the Project Archaeologist.
- A record of all environmental incidents will be kept on file by the ECoW and the Main Contractor. These records will be made available to the relevant authorities such as Donegal County Council and DCCAE, if required.

The ECoW will be responsible for any corrective actions required as a result of the incident e.g. an investigative report, formulation of alternative construction methods or environmental sampling, and will advise the Main Contractor as appropriate.

6.2 Contacting the Emergency Services

6.2.1 Emergency Communications Procedure

In the event of requiring the assistance of the emergency services the following steps should be taken:

Stay calm. It's important to take a deep breath and not get excited. Any situation that requires 999/112 is, by definition, is an emergency. The dispatcher or call-taker knows that and will try to move things along quickly, but under control.

Know the location of the emergency and the number you are calling from. This may be asked and answered a couple of times but don't get frustrated. Even though many emergency call centres have enhanced capabilities meaning they are able to see your location on the computer screen they are still required to confirm the information. If for any reason you are disconnected, at least emergency crews will know where to go and how to call you back.

Wait for the call-taker to ask questions, then answer clearly and calmly. If you are in danger of assault, the dispatcher or call-taker will still need you to answer quietly, mostly "yes" and "no" questions.

If you reach a recording, listen to what it says. If the recording says your call cannot be completed, hang up and try again. If the recording says all call takers are busy, *WAIT*. When the next call-taker or dispatcher is available to take the call, it will transfer you.

Let the call-taker guide the conversation. He or she is typing the information into a computer and may seem to be taking forever. There's a good chance, however, that emergency services are already being sent while you are still on the line.

Follow all directions. In some cases, the call-taker will give you directions. Listen carefully, follow each step exactly, and *ask for clarification* if you don't understand.

Keep your eyes open. You may be asked to describe victims, suspects, vehicles, or other parts of the scene.

Do not hang up the call until directed to do so by the call taker.

Due to the remoteness of the site it may be necessary to liaise with the emergency services on the ground in terms of locating the site. This may involve providing an escort from a designated meeting point that may be located more easily by the emergency services. This should form part of the site induction to make new personnel and sub-contractors aware of any such arrangement or requirement if applicable.

6.2.2 Contact Details

A list of emergency contacts is presented in Table 5.2. A copy of these contacts will be included in the Site Safety Manual and in the site offices and the various site welfare facilities.

Table 5.2 Emergency Contacts

Contact	Telephone no.
Emergency Services – Ambulance, Fire, Gardaí	999/112
Doctor – Milbrae Surgery Ballybofey	074 913 1023
Hospital – Letterkenny University Hospital	074 912 5888
ESB Emergency Services	1850 372 999
Bord Gáis Emergency	1850 20 50 50
Gardaí –Local Garda Station TBC	TBC
Health and Safety Co-ordinator - Health & Safety Services	TBC
Health and Safety Authority	1890 289 389
Project Supervisor Construction Stage (PSCS): TBC	TBC
Project Supervisor Design Stage (PSDS):	TBC
Client –	Planree Ltd

6.2.3 Procedure for Personnel Tracking

All operatives on site without any exception will have undergone a site induction where they will be required to provide personal contact details which will include contact information for the next of kin.

In the event of a site operative becoming in an emergency situation where serious injury has occurred and hospitalisation has taken place, it will be the responsibility of the Site Manager or next in command if unavailable to contact the next of kin to inform them of the situation that exists.

6.3 Induction Checklist

Table 5.3 provides a list of items highlighted in this ERP which must be included or obtained during the mandatory site induction of all personnel that will work on the site. This will be updated throughout the various stages of the project.

Table 5.3 Emergency Response Plan Items Applicable to the Site Induction Process

ERP Items to be included in Site Induction	Status
All personnel will be made aware of the evacuation procedure during site induction	
Due to the remoteness of the site it may be necessary to liaise with and assist the emergency services on the ground in terms of locating the site. This may involve providing an escort from a designated meeting point that may be located more easily by the emergency services. This should form part of the site induction to make new personnel and sub-contractors aware of any such arrangement or requirement if applicable.	
All operatives on site without any exception will have undergone a site induction where they will be required to provide personal contact details which will include contact information for the next of kin.	

7 MITIGATION PROPOSALS

All mitigation measures relating to the pre-commencement, construction and operational phases of the Permitted Development were set out in the various sections of the Environmental Impact Assessment Report (EIAR) prepared as part of the planning permission application to An Bord Pleanála.

This section of the CEMP groups together all of the mitigation measures presented in the EIAR. The Mitigation Measures are presented in the following pages.

By presenting the mitigation proposals in the below format, it is intended to provide an easy to audit list that can be reviewed and reported on during the future phases of the project. The tabular format in which the below information is presented, can be further expanded upon during the course of future project phases to provide a reporting template for site compliance audits.

Table 7.1 Site preparation and Mitigation Measures

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
Pre-Commencement Phase				
MM1	EIAR Section 7	It is proposed that construction works will commence outside the bird nesting season (1 st of April to 31 st of July inclusive).		
MM2	EIAR Section 4	The removal and disposal of wastewater from the site will be carried out by a fully permitted waste collector holding valid Waste Collection Permits as issued under the Waste Management (Collection Permit) Regulations, 2007. Information on the appointed permitted contractor and evidence of a maintenance contract will be submitted to the Planning Authority prior to any construction works taking place.		
MM3	EIAR Section 4	All site activities will be provided for in a Construction Environmental Management Plan, prepared prior to the commencement of any operations onsite. The CEMP will set out all measures necessary to ensure works are carried out in accordance with the mitigation measures set out in the EIAR and will set out the monitoring and inspections procedures and frequencies.		
MM4	EIAR Section 4 CEMP Section 4	An ECoW will oversee the site works and implementation of the Environmental Management Plan and provide on-site advice on the mitigation measures as necessary to ensure the project proceeds as intended. The level, detail and frequency of reporting expected from the ECoW for the Construction Manager, developer's project manager, and any Authorities or other Agencies, will be agreed by all parties prior to commencement of construction, and may be further adjusted as required during the course of the project.		
MM5	EIAR Section 4	The arrangements for concrete deliveries to the site will be discussed with suppliers before work starts, agreeing routes, prohibiting on-site washout and discussing emergency procedures.		
MM6	EIAR Section 4	Drainage swales will be installed in advance of any construction works commencing.		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
MM7	CEMP Section 3 EIA Section 4 CEMP Section 2	Borrow pits will be secured with stock proof fencing to prevent access to these areas. Appropriate health and safety signage will be erected on the fencing prior to construction works commencing.		
MM8	EIA Section 4 CEMP Section 2	Culverts will be installed at locations where streams or natural drainage channels cross the new access track route. All works involving culverts, whether they are new, upgraded or extended, will be carried out to follow a method statement to be agreed with Inland Fisheries Ireland.		
MM9	EIA Section 4 CEMP Section 3	All materials and equipment necessary to implement the drainage mitigation measures will be brought on-site in advance of any works commencing. The drainage measures outlined in the EIA will be installed prior to, or at the same time as the works they are intended to drain. An adequate amount of straw bales, clean stone, terram, stakes, etc. will be kept on site at all times to implement the drainage design measures as necessary.		
MM10	EIA Section 4 CEMP Section 3	The works programme for the ground works part of the construction phase of the project will also take account of weather forecasts and predicted rainfall in particular.		
MM11	EIA Section 4 CEMP Section 3, 7	The effectiveness of drainage measures designed to minimise runoff entering works areas and capture and treat silt-laden water from the works areas, will be monitored as part of the water quality and monitoring programme set out in Section 7 of the CEMP. The ECoW or supervising hydrologist will respond to changing weather, ground or drainage conditions on the ground as the project proceeds, to ensure the effectiveness of the drainage design is maintained in so far as is possible. This may require the installation of additional check dams, interceptor drains or swales as deemed necessary on-site.		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
MM12	EIAR Section 4 CEMP Section 7	An inspection and maintenance plan for the drainage system on site will be prepared in advance of commencement of any works. Regular inspections of all installed drainage systems will be necessary, especially after heavy rainfall, to check for blockages, and ensure there is no build-up of standing water at parts of the systems where it is not intended. The inspection of the drainage system will be the responsibility of the ECoW or the supervising hydrologist.		
MM13	EIAR Section 9 CEMP Section 3	A 50-metre buffer zone will be maintained around watercourses during the windfarm construction. With the exception of road crossings of streams and associated culvert construction, no development infrastructure, vehicle or plant movement, construction activity or stock-piling of construction materials or construction waste will take place within this zone, and no vegetation will be removed from within this zone.		
MM14	EIAR Section 9 CEMP Section 3	A 20-metre buffer zone will be maintained around existing artificial drainage points for the duration of the construction phase.		
MM15	EIAR Section 7	No felling of conifers, individual trees or bushes will be carried out during the general bird breeding season. (the 1st of April to the 31st of July inclusive).		
MM16	EIAR Section 6	An Invasive Species Management Plan will be developed following a preconstruction invasive survey. The report will describe the best practice measures that will be followed to ensure that works associated with the permitted wind farm development do not result in the spread or proliferation of invasive species.		
MM17	EIAR Section 6	A pre-construction mammal survey will be undertaken to identify evidence of protected mammals within the works areas associated with the Permitted Development.		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
MM18	EIAR Section 14	A pre-commencement condition survey of roads associated with the Permitted Development will be carried out prior to commencement of construction activities.		
MM19	EIAR Section 4 CEMP Section 9	The procedures for the implementation of the mitigation measures outlined in such an CEMP and their effectiveness and completion is typically audited by way of an Environmental Management Plan Audit Report. The CEMP Audit Report effectively lists all mitigation measures prescribed in any of the planning documentation, all conditions attached to the grant of planning permission and any further mitigation measures proposed during the detailed design stage and allows them to be audited on a systematic and regular basis.		
Construction Phase				
Construction Management				
MM20	EIAR Section 4 CEMP Section 3	On-site refuelling will be carried out at dedicated refuelling locations using a mobile double skinned fuel bowser. The fuel bowser, a double-axel custom-built refuelling trailer will be re-filled off site and will be towed around the site by a 4x4 jeep to where machinery is located. It is not practical for all vehicles to travel back to a single refuelling point, given the size of the cranes, excavators, etc. that will be used during the construction of the permitted wind farm development. The 4x4 jeep will also carry fuel absorbent material and pads in the event of any accidental spillages. The fuel bowser will be parked on a level area in the construction when not in use. Only designated trained and competent operatives will be authorised to refuel plant on site. Mobile measures such as drip trays, spill kits and fuel absorbent mats will be used during all refuelling operations.		
MM21	EIAR Section 4	No batching of wet-cement products will occur on site. Ready-mixed supply of wet concrete products and where possible, emplacement of pre-cast elements, will take place. Only ready-mixed concrete will be used during the construction phase, with all ready-mixed concrete being delivered from local batching plants in sealed concrete delivery trucks.		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
MM22	EIAR Section 4	No washing out of any plant used in concrete transport or concreting operations will be carried out onsite. When concrete is delivered to site, only the chute of the delivery truck will be cleaned, using the smallest volume of water necessary, before leaving the site. Concrete trucks will be directed back to their batching plant for washout.		
MM23	EIAR Section 4	No concrete will be transported around the site in open trailers or dumpers so as to avoid spillage while in transport.		
MM24	EIAR Section 4	Clearly visible signs in prominent locations will be placed close to concrete pour areas specifically stating washout of concrete lorries is not permitted on the site.		
MM25	EIAR Section 4	All concrete used in the construction of turbine bases will be poured directly into the shuttered formwork from the delivery truck. If this is not practical, the concrete will be poured from the delivery truck into a hydraulic concrete pump or into the bucket of an excavator, which will transfer the concrete to the location where it is needed.		
MM26	EIAR Section 4	Main pours will be planned days or weeks in advance. Large pours will be avoided when prolonged periods of heavy rain are forecast.		
MM27	EIAR Section 4	Concrete pumps and machine buckets will be restricted from slewing over watercourses while placing concrete.		
MM28	EIAR Section 4	Excavations will be sufficiently dewatered before concreting begins. Dewatering will continue while concrete sets.		
MM29	EIAR Section 4	Covers will be available for freshly placed concrete to avoid the surface washing away in heavy rain.		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
MM30	EIAR Section 4	Surplus concrete after completion of a pour will be used elsewhere at suitable locations around the site where it is required.		
MM31	EIAR Section 4 CEMP Section 3	If necessary, water will be taken from settlement ponds in the site's drainage system and will be pumped into a bowser or water spreader to dampen down haul roads and site compounds to prevent the generation of dust. Silty or oily water will not be used for dust suppression.		
MM32	CEMP Section 3	All construction related traffic will have speed restrictions on un-surfaced roads to 20 kph.		
MM33	EIAR Section 4	A road sweeper will be available if any section of the public roads were to be dirtied by trucks associated with the Permitted Development.		
MM34	EIAR Section 4	During construction of the Permitted Development, all staff will be made aware of and adhere to the Health & Safety Authority's <i>'Guidelines on the Procurement, Design and Management Requirements of the Safety, Health and Welfare at Work (Construction) Regulations 2006'</i> . This will encompass the use of all necessary Personal Protective Equipment and adherence to the site Health and Safety Plan.		
MM35	EIAR Section 4	Any area where excavations are planned will be surveyed and all existing services will be identified prior to commencement of any works. Liaison will be held with the relevant sections of the Local Authority including all the relevant area engineers to ensure all services are identified. Excavation permits will be completed and all plant operators and general operatives will be inducted and informed as to the location of any services.		
Drainage Design and Management				
MM36	EIAR Section 4	Swales will be used to intercept and collect run off from construction areas of the site during the construction phase, and channel it to stilling ponds for sediment attenuation.		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
MM37	CEMP Section 3 EiAR Section 4 CEMP Section 3	Interceptor drains will be installed upgradient of any works areas to collect surface flow runoff and prevent it reaching excavations and construction areas of the site. It will then be directed to areas where it can be re-distributed over the ground as sheet flow.		
MM38	EiAR Section 4 CEMP Section 3	Check dams will not be used in any natural watercourses, only artificial drainage channels and interceptor drains. The check dams will be left in place when the interceptor drains are backfilled at the end of the construction phase to limit linear flow in the backfilled drain. The check dams will be installed at regular intervals along interceptor drains to restrict flow velocity, minimise channel erosion and promote sedimentation behind the dam. The check dams will be installed as the interceptor drains are being excavated. The spacing and frequency of the check dams will be dependent on the gradient of the interceptor drain or swale in which they are being installed.		
MM39	EiAR Section 4 CEMP Section 3	A level spreader will be constructed at the end of each interceptor drain to convert concentrated flows in the drain into diffuse sheet flow on areas of vegetated ground. The levels spreaders will be located downgradient of any works areas in locations where they are not likely to contribute further to water ingress to construction areas of the site. They will also be emplaced at end of swales carrying discharge from settlement ponds. The level spreaders will distribute clean drainage water onto vegetated areas where the water will not be reconcentrated into a flow channel immediately below the point of discharge. The discharge point will be on level or only very gently sloping ground rather than on a steep slope so as to prevent erosion. No drains will discharge directly to surface waters.		
MM40	EiAR Section 4 CEMP Section 3	Piped slope drains will be used to convey surface runoff from diversion drains safely down slopes to flat areas without causing erosion. Once the runoff reaches the flat areas it will be reconverted to diffuse sheet flow. Level spreaders will only be established on slopes of less than 6% in grade. Piped slope drains will be used to transfer water away from areas		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
		where slopes are too steep to use level spreaders. Piped slope drains will only remain in place for the duration of the construction phase of the project. On completion of the works, the pipes and rock aprons will be removed and all channels backfilled with the material that was originally excavated from them.		
MM41	EIAR Section 4 CEMP Section 3	Vegetation filters, that is areas of existing vegetation, accepting drainage water issuing from level spreaders as sheet flow, will remove any suspended sediment from water channelled via interceptor drains or any remaining sediment in waters channelled via swales and stilling ponds.		
MM42	EIAR Section 4 CEMP Section 3	Stilling ponds will be used to attenuate runoff from works areas of the site during the construction phase and will remain in place to handle runoff from roads and hardstanding areas of the Permitted Development during the operational phase. Stilling ponds will be excavated/constructed at each required location as two separate ponds in sequence, a primary pond and a secondary pond. The stilling ponds will be sized according to the size of the area they will be receiving water from but will be sufficiently large to accommodate peak flows storm events. The stilling ponds will be dimensioned so that the length to width ratio will be greater than 2:1, where the length is the distance between the inlet and the outlet. Where ground conditions allow, stilling ponds will be constructed in a wedge shape, with the inlet located at the narrow end of the wedge. Each stilling pond will be a minimum of 1-1.5 metres in depth. Deeper ponds will be used to minimise the excavation area needed for the required volume. The embankment that forms the sloped sides of the stilling ponds will be stabilised with vegetated turves, which will have been removed during the excavation of the stilling ponds area.		
MM43	EIAR Section 4 CEMP Section 3	A siltbuster or similar equivalent piece of equipment will be available if required to filter any water pumped out of excavation areas, prior to its discharge to settlement ponds or swales. This includes turbine base excavations and borrow pit excavations. This water is		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
		likely to have a high sediment load and will be directed via swales to settlement ponds after treatment in the unit.		
MM44	EIAR Section 4 CEMP Section 3	Culverts will be installed at locations where streams or natural drainage channels cross the new access track route. All works involving culverts, whether they are new, upgraded or extended, will be carried out to follow a method statement to be agreed with Inland Fisheries Ireland.		
MM45	EIAR Section 4 EIAR Section 9 CEMP Section 3	Silt fences will be installed along the routes of existing watercourses or drainage ditches where site roads pass over the watercourses, immediately downstream of the construction area. Silt fences will be installed along a level contour so water does not pond more than 400 mm at any point. The silt fence will be trenched at least 100 mm into the ground and will be stretched tight between the posts. The fences will not be allowed to sag or break away from the fence posts. Silt fences will be installed as single, double or a series of triple silt fences, depending on the space available and the anticipated sediment loading. During the near stream construction work double silt fences will be emplaced immediately down-gradient of the construction area for the duration of the construction phase.		
MM46	EIAR Section 9 CEMP Section 3	Mitigation measures which will reduce the risk of entrainment of suspended solids and nutrient release in surface watercourses comprise best practice methods which are set out above in Section 3.4.		
MM47	EIAR Section 4 CEMP Section 3	The works programme for the groundworks part of the construction phase of the project will also take account of weather forecasts and predicted rainfall in particular.		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
MM48	EIAR Section 4 CEMP Section 3, 4 & 7	The effectiveness of drainage measures designed to minimise runoff entering works areas and capture and treat silt-laden water from the works areas, will be monitored continuously by the ECoW or supervising hydrologist on-site. The ECoW or supervising hydrologist will respond to changing weather, ground or drainage conditions on the ground as the project proceeds, to ensure the effectiveness of the drainage design is maintained in so far as is possible. This may require the installation of additional check dams, interceptor drains or swales as deemed necessary on-site.		
MM49	EIAR Section 4	Material excavated to create the working area will be stored locally for later reuse in backfilling the working area around the turbine foundation. The excavated material will be covered with polythene sheets and surrounded by silt fences to ensure sediment-laden run-off does not occur.		
Flora and Fauna				
MM50	EIAR Section 9 CEMP Section 3	Best practice Forestry Service Guideline mitigation measures will reduce the risk of entrainment of suspended solids and nutrient release in surface watercourses as outlined in the EIAR.		
MM51	Condition 16 CCS Section 10 Bird Monitoring Programme	If any hen harrier breeding activity is identified, surveys will focus on establishing the location of the nest site and no works shall be permitted within a 500m buffer of the nest (Forestry Commission Scotland 2006). Works will not be permitted to recommence within the buffer zone until it can be demonstrated that that hen harrier are no longer reliant on the nest site. All site staff and subcontractors will be made aware of any restrictions to be imposed by means of a toolbox talk and a map of the 'no-works zone' will be made available to all construction staff. The restricted area will also be marked off using hazard-tape fencing to alert all persons on site to the suspension of works within that area.		
Peat, Subsoils and Bedrock				

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
MM52	CEMP Section 3	General recommendation for good construction practice to minimise the risk of construction activity causing potential peat instability are outlined in Section 3.6 of the CEMP.		
MM53	EIAR Section 8	Peat removed from turbine locations will be transported to the designated borrow pit areas.		
MM54	EIAR Section 8	Any excess mounded peat in temporary placement areas for long periods will be digger-bucket sealed and covered with polyethylene sheets or reseeded at the earliest opportunity.		
MM55	EIAR Section 8	In order to minimise runoff during the construction phase, stripping of peat should not take place during excessively dry weather (to prevent dust generation) or extremely wet periods (to prevent increased silt rich runoff).		
MM56	EIAR Section 9	Brash mats will be used where necessary to support vehicles on soft ground, reducing peat and mineral soils erosion and avoiding the formation of rutted areas, in which surface water ponding can occur. Brash mat renewal should take place when they become heavily used and worn. Provision should be made for brash mats along all off-road routes, to protect the soil from compaction and rutting.		
MM57	EIAR Section 8 CEMP Section 3	<p>The following issues incorporated into the construction phase of the project will assist in the management of the risks for this site (AGEC, 2017):</p> <ul style="list-style-type: none"> ▪ Appointment of experienced and competent contractors; ▪ The site should be supervised by experienced and qualified personnel; ▪ Allocate sufficient time for the project (be aware that decreasing the construction time has the potential to increase the risk of initiating a peat movement); ▪ Prevent undercutting of slopes and unsupported excavations; ▪ Maintain a managed robust drainage system; ▪ Prevent placement of loads/overburden on marginal ground; ▪ Set up, maintain and report findings from monitoring systems; 		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
Air Quality/Dust				
MM58	EIAR Section 4 CEMP Section 3 EIAR Section 10	<ul style="list-style-type: none"> ▪ Ensure construction method statements are followed or where agreed modified/ developed; and, ▪ Revise and amend the Geotechnical Risk Register as construction progresses. 		
		<ul style="list-style-type: none"> ▪ Revise and amend the Geotechnical Risk Register as construction progresses. ▪ Truck wheels will be washed to remove mud and dirt before leaving the site. ▪ All plant and materials vehicles shall be stored in the dedicated compound area. ▪ Areas of excavation will be kept to a minimum, and stockpiling will be minimised by coordinating excavation, spreading and compaction. ▪ Construction traffic will be restricted to defined routes and a speed limit will be implemented. ▪ Water misting or bowsers will operate on-site as required to mitigate dust in dry weather conditions. ▪ The transport of soils or other material, which has significant potential to cause dust, will be undertaken in tarpaulin-covered vehicles where necessary. ▪ The agreed haul route roads adjacent to the site will be regularly inspected for cleanliness and cleaned as necessary. 		
MM59	EIAR Section 10	All construction machinery will be maintained in good operational order while on-site, minimising any emissions that are likely to arise.		
MM60	EIAR Section 10	In periods of extended dry weather, dust suppression may be necessary along haul roads and around the borrow pit area to ensure dust does not cause a nuisance. If necessary, water will be taken from stilling ponds in the site's drainage system and will be pumped into a bowser or water spreader to dampen down haul roads and site compounds to prevent the generation of dust. Silty or oily water will not be used for dust suppression, because this would transfer the pollutants to the haul roads and generate polluted runoff		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
		or more dust. Water bowser movements will be carefully monitored, as the application of too much water may lead to increased runoff.		
Noise				
MM61	EIAR Section 4 & 11	Equipment will be sensitively located, taking account of local topography and natural screening.		
MM62	EIAR Section 4 & 11	All construction work will be restricted to the specified working hours. Any construction work carried out outside of these hours shall be restricted to activities that will not generate noise of a level that may cause a nuisance.		
MM63	EIAR Section 4 & 11	Plant will be selected taking account of the characteristics of noise emissions from each item. All plant and machinery used on the site shall comply with E.U. and Irish legislation in relation to noise emissions. The timing of on- and off-site movements of plant near occupied properties will be controlled.		
MM64	EIAR Section 11	<p>The contract documents will clearly specify that the Contractor undertaking the construction of the works will be obliged to adhere to the following noise abatement measures:</p> <ul style="list-style-type: none"> ▪ No plant used on site will be permitted to cause an on-going public nuisance due to noise. ▪ The best means practicable, including proper maintenance of plant, will be employed to minimise the noise produced by on site operations. ▪ All vehicles and mechanical plant will be fitted with effective exhaust silencers and maintained in good working order for the duration of the contract. ▪ Compressors will be attenuated models fitted with properly lined and sealed acoustic covers which will be kept closed whenever the machines are in use and all ancillary pneumatic tools shall be fitted with suitable silencers. 		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
MM65	EIAR Section 11	<p>The following mitigation measures will be employed to control the impact of vibration during blasting activities:</p> <ul style="list-style-type: none"> ▪ Trial blasts will be undertaken to obtain scaled distance analysis; ▪ Appropriate burden to avoid over or under confinement of the charge; ▪ Accurate setting out and drilling; ▪ Appropriate charging; ▪ Appropriate stemming with appropriate material such as sized gravel or stone chipping; ▪ Delay detonation to ensure small maximum instantaneous charges; ▪ Decked charges and in-hole delays; ▪ Blast monitoring to enable adjustment of subsequent charges; ▪ Good blast design to maximise efficiency and reduce vibration; ▪ Avoid using exposed detonating cord on the surface; and ▪ During the course of the construction programme, supervision of the works will include ensuring compliance with the limits detailed in Table 11-2. 		
		<ul style="list-style-type: none"> ▪ Machinery that is used intermittently will be shut down or throttled back to a minimum during periods when not in use. ▪ Any plant, such as generators or pumps, which is required to operate near any sensitive receptors before 07:00hrs or after 19:00hrs will be surrounded by an acoustic enclosure or portable screen. ▪ Diesel generators will be enclosed in sound proofed containers to minimise the potential for noise impacts. ▪ Residents will be notified in advance of all blasting schedules. ▪ During the course of the construction programme, supervision of the works will include ensuring compliance with the limits detailed in Table 11.1 of the EIAR using methods outlined in British Standard BS 5228-1:2009+A1:2014 <i>Code of practice for noise and vibration control on construction and open sites – Noise</i>. 		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
MM66	EIAR Section 4, 10 & 11	All construction operations shall comply with guidelines set out in British Standard documents <i>BS 5338: Code of Practice for Noise Control on Construction and Demolition Sites</i> and <i>BS5228: Part 1: 1997: Noise & Vibration Control on Construction and Open Sites</i> .		
Cultural Heritage				
MM67	EIAR Section 13	Archaeological monitoring of ground works (to include roads, substation, turbine hardstands, bases and cable trenching) will be undertaken at the construction phase of the development.		
MM68	EIAR Section 13	DG085-005 Site of Megalithic Structure – The excavation of the grid connection route at this location should be archaeologically monitored during construction. This is in order to ensure that no damage takes place to any sub-surface archaeological features relating to the recorded monument that may be present beneath the surface of the road. A report on the monitoring will be undertaken and submitted to the relevant authorities on completion of the work.		
MM69	EIAR Section 13	40909424 Road Bridge - Archaeological monitoring of ground works during construction where they extend past the road bridge. A report on the results of the monitoring will be compiled and submitted to the relevant authorities on completion of the work.		
MM70	EIAR Section 13	40909423 Milestone - Archaeological monitoring of ground works during construction where they extend past the monument. A report on the results of the monitoring will be compiled and submitted to the relevant authorities on completion of the work.		
Traffic				
MM71	EIAR Section 14	All of the deliveries comprising abnormally large loads will be made outside the normal peak traffic periods to avoid disruption to work and school related traffic.		

Reference No.	Reference	Mitigation Measure	Audit Result	Action Required
MM72	EIAR Section 14	A programme of deliveries will be submitted to Donegal County Council in advance of deliveries of turbine components to site.		
Operational Phase				
MM73	EIAR Section 4	The removal and disposal of wastewater from the site will be carried out by a fully permitted waste collector holding valid Waste Collection Permits as issued under the Waste Management (Collection Permit) Regulations, 2007. Information on the appointed permitted contractor and evidence of a maintenance contract having been submitted to the Planning Authority prior to any construction works taking place.		

8 MONITORING PROPOSALS

All monitoring proposals relating to the pre-commencement, construction and operational phases of the Permitted Development were set out in various sections of the EIAR prepared as part of the planning permission application to An Bord Pleanála.

This section of the Construction and Environment Management Plan groups together all of the monitoring proposals presented in the EIAR. The monitoring proposals are presented in the following pages.

By presenting the monitoring proposals in the below format, it is intended to provide an easy to audit list that can be reviewed and reported on during the future phases of the project. The tabular format in which the below information is presented, can be further expanded upon during the course of future project phases to provide a reporting template for site compliance audits.

Table 8.1 Schedule of Monitoring Measures

Ref. No.	Reference	Survey/Monitoring Measure	Frequency	Reporting Measures	Responsibility
Pre-Commencement Phase					
MX1	ELAR Section 9	An inspection and maintenance plan for the on-site drainage system will be prepared in advance of commencement of any works.	On going	Monthly	EC&W
MX2	ELAR Section 9	Water sampling will be completed before, during and after the felling activity. The 'before' sampling should be conducted within 4 weeks of the felling activity, preferably in medium to high water flow conditions.	As Required	Monthly	Project Hydrologist
MX3	ELAR Section 13	Pre-construction archaeological testing of all turbine bases, hardstands, substation site, site compound, borrow pits and new roads will take place. A report on the archaeological testing will be submitted to the planning authority and the Department of Arts Heritage and the Gaeltacht.	Once	As required	Project Archaeologist
MX4	ELAR Section 7 Condition 16 CCS Section 10 Bird Monitoring Programme	Where construction works run into the subsequent breeding season following commencement, pre-construction bird surveys will be undertaken to confirm the absence of breeding Hen Harrier. If breeding activity is identified, the nest site will be located and no works shall be undertaken within a 500m buffer. No works within the buffer zone shall be permitted until it can be demonstrated that Hen Harrier are no longer reliant on the nest site. Should pre-construction monitoring be required, the findings of these surveys will be incorporated into a report for submission to the planning authority before the end of the year in which surveys were completed.	As required	As required	Project Ornithologist
MX5	Condition 5 CCS Appendix 2	Vegetation sampling: A number of fixed relevé sites (i.e. permanent quadrats) will be set up in areas where active management is proposed of previously forested areas. Baseline data will be recorded prior to the commencement of habitat management activities set out in this outline plan. The character of each relevé will be recorded (e.g. species proportions present using Domin scale,	As required	As required	Project Ecologist

Ref. No.	Reference	Survey/Monitoring Measure	Frequency	Reporting Measures	Responsibility
MX6	Condition 5 CCS Appendix 2	vegetation structure) and photographs will be taken of each relevé from a fixed point. Hydrological monitoring: Water levels within areas where drains are blocked will be recorded quarterly for two years. A number of phreatic stand pipes will be installed (prior to restoration) to allow monitoring of water levels within the restoration area and outside the restoration area in. In this way, any positive impacts on the local hydrology can be verified and quantified.	Prior to commencement	As required	Project Ecologist
MX7	Condition 15 CCS	Plant Species: Surveys for Irish Ladies tresses can only be conducted between early August and early September (NRA 2009). Surveys for Globeflower can be conducted between June and August. Surveys will only be required where works traverse potential suitable habitat as identified in Figure 3.4 of the EIAR. Works can proceed outside the identified areas.	Prior to commencement	As required	Project Ecologist
MX8	EIAR Section 6 Condition 15 CCS	Otter A pre-construction otter survey will be undertaken to identify evidence of otter within the works areas associated with the development	Prior to commencement	As required	Project Ecologist
Construction Phase					
MX9	EIAR Section 9	Daily monitoring of excavations by a suitably qualified person will occur during the construction phase. If high levels of seepage inflow occur, excavation work should immediately be stopped and a geotechnical assessment undertaken.	Daily	As required	ECoW
MX10	CEMP Section 3	Haul route will be condition monitored and maintained if necessary.	As required	As required	ECoW
MX11	EIAR Section 4	A system of peat monitoring will be implemented under the supervision of the project geotechnical engineer. This will include movement monitoring posts the findings of which will be reviewed by the geotechnical engineer.	Monthly or more frequently as required by construction programme	Monthly	Project Geotechnical Engineer

Ref. No.	Reference	Survey/Monitoring Measure	Frequency	Reporting Measures	Responsibility
MX12	EIAR Section 4	Check dams will be inspected and maintained regularly to insure adequate performance. Maintenance checks will also ensure the centre elevation of the dam remains lower than the sides of the dam.	As Required	As Necessary	ECoW
MX13	EIAR Section 4	Piped slope drains will be inspected weekly and following rainfall events. Inlet and outlets will be checked for sediment accumulation and blockages. Stake anchors or fill over the pipe will be checked for settlement, cracking and stability. Any seepage holes where pipe emerges from drain at the top of the pipe will be repaired promptly.	Weekly	As Necessary	ECoW
MX14	EIAR Section 4	Inspection and maintenance of all stilling ponds will be ongoing through the construction period. A water level indicator such as a staff gauge will be installed in each stilling pond with marks to identify when sediment is at 10% of the settlement pond capacity. Sediment will be cleaned out of the still pond when it exceeds 10% of pond capacity.	As Required	As Necessary	ECoW
MX15	EIAR Section 4	All culverts will be inspected regularly to ensure they are not blocked by debris, vegetation or any other material that may impede conveyance.	Weekly / Monthly	As Necessary	ECoW
MX16	EIAR Section 4 CEMP Section 3	The effectiveness of drainage measures designed to minimise runoff entering works areas and capture and treat silt-laden water from the works areas, will be monitored continuously by the ECoW or supervising hydrologist on-site. The ECoW or supervising hydrologist will respond to changing weather, ground or drainage conditions on the ground as the project proceeds, to ensure the effectiveness of the drainage design is maintained in so far as is possible. This may require the installation of additional check dams, interceptor drains or swales as deemed necessary on-site.	As Required	As Necessary	ECoW / Project Hydrologist

Ref. No.	Reference	Survey/Monitoring Measure	Frequency	Reporting Measures	Responsibility
MX17	EIAR Section 8, 9 CEMP Section 3	The plant used should be regularly inspected for leaks and fitness for purpose.	Daily	As Necessary	Plant Operators / ECoW
MX18	EIAR Section 9	Drains and silt traps will be maintained throughout all felling works, ensuring that they are clear of sediment build-up and are not severely eroded. Correct drain alignment, spacing and depth will ensure that erosion and sediment build-up are minimised and controlled.	Weekly/ Monthly	As Necessary	ECoW
MX19	EIAR Section 9	Regular inspections of all installed drainage systems will be undertaken, especially after heavy rainfall, to check for blockages, and ensure there is no build-up of standing water in parts of the systems where it is not intended. Inspections will also be undertaken after tree felling.	Weekly Monthly	As Necessary	ECoW
MX20	EIAR Section 9	During the construction phase field testing and laboratory analysis of a range of parameters with relevant regulatory limits and EQSs should be undertaken for each primary watercourse, and specifically following heavy rainfall events (i.e. weekly, monthly and event based).	Weekly, monthly & event based	As Necessary	ECoW / Project Hydrologist
MX21	EIAR Section 9	Sampling will be completed before, during and after the felling activity. The “during” sampling will be undertaken once a week or after rainfall events. The ‘after’ sampling should comprise as many samplings as necessary to demonstrate that water quality has returned to pre-activity status (i.e. where an impact has been shown).	As Required	Monthly	ECoW / Project Hydrologist
MX22	EIAR Section 5 CEMP Section 3	Training and supervision of drivers to ensure smooth machinery operation/driving, and to minimise unnecessary noise generation.	As Required	As Necessary	ECoW

Ref. No.	Reference	Survey/Monitoring Measure	Frequency	Reporting Measures	Responsibility
MX23	CEMP Section 3	Daily inspection of construction sites to examine dust measures and their effectiveness.	Daily	As Necessary	ECOW
MX24	EIAR Section 13	Archaeological monitoring of ground works during construction.	As Required	As Required	Project Archaeologist
MX25	EIAR Section 6	A detailed habitat enhancement management plan (HEMP) will be prepared for all areas that are subject to restoration. Ongoing monitoring to assess the effectiveness of the measures proposed and employed during habitat replacement. The monitoring measures will include vegetation sampling and hydrological monitoring.	As Required	Years 1, 2, 3, 5, 10, 15 and 25 following commencement of the plan.	Project Ecologist
Operational Phase					
MX26	EIAR Section 7	To take account of both short-term and long-term effects on bird populations, post-construction monitoring should be conducted during the bird breeding season in years 1, 2, 3, 4, 5, 10 and 15 of the life of a wind farm. Ideally, post-construction monitoring will include ongoing breeding bird/activity surveys and a programme of regular corpse searching (at least as regularly as once per month) at the wind turbine sites in the same years to find the corpses of birds and bats that may be struck by the operating turbines.	Years 1, 2, 3, 4, 5, 10 and 15 for the period April - July	Annually at the end of years where surveys are completed	Project Ecologist
MX27	Condition 16 CCS Section 10 Bird Monitoring Programme	Hen harrier will be monitored in years 1,2,3,5,10 and 15 of wind farm operation by means of Vantage Point (VP) surveys	Years 1, 2, 3, 4, 5, 10 and 15 for the period April - July	Annually at the end of years where surveys are completed	Project Ecologist
MX28	Condition 16	Breeding raptor surveys in the breeding season (mid-March/April-July) and hen harrier roost surveys in the winter season.	Years 1, 2, 3, 4, 5, 10 and 15 for	Annually at the end of	Project Ecologist

Ref. No.	Reference	Survey/Monitoring Measure	Frequency	Reporting Measures	Responsibility
	CCS Section 10 Bird Monitoring Programme		the period April - July	years where surveys are completed	
MX29	EIAR Section 7	Hen Harrier Roost Surveys	Years 1, 2, 3, 4, 5, 10 and 15 for the period October – March	Annually at the end of years where surveys are completed	Project Ecologist
MX30	EIAR Section 7	Autumn Migration/Wintering Birds Survey	Years 1, 2, 3, 4, 5, 10 and 15 for the period September – March	Annually at the end of years where surveys are completed	Project Ecologist
MX31	EIAR Section 7	Corpse Searches (Bird Casualties) for birds that may potentially collide with operating turbines during the operational phase of the wind farm project will be implemented. Prior to the commencement of monthly surveys, a searcher efficiency test to allow monthly results to be calibrated according to the ability of the dog to detect carcasses and a carcass removal trial to assess the scavenger removal rate at the site will be undertaken. An annual report summarising the findings of the bird monitoring surveys at and in the vicinity of the permitted wind farm will be submitted to the Planning Authority following monitoring in years 1,2,3,5,10 and 15 of operation at the permitted wind farm	Monthly in years 1, 2, 3, 4, 5, 10 and 15 for the period	Annually at the end of years where surveys are completed	Project Ecologist
MX32	EIAR Section 9	Any excess build-up of silt levels at dams, the settlement pond, or any other drainage features that may decrease the effectiveness of the drainage feature, will be removed.	As Required	As Required	ECoW

Ref. No.	Reference	Survey/Monitoring Measure	Frequency	Reporting Measures	Responsibility
		This drainage infrastructure will remain in place until natural vegetation filters have regenerated.			
MX33	ELAR Section 11	Post commissioning operational noise monitoring is recommended to ensure compliance with the relevant planning noise condition.	As Required	As Required	Project Noise Consultant
MX34	Condition 5 CCS Appendix 2	The fixed relevees sites will then be re-examined during years 1, 2, 3, 5, 10, 15 and 25 following commencement of the plan in place in order to establish the extent of habitat improvement resulting from management practices. The finalised HEMP will contain the locations of the releves.	As required	As required	Project Ecologist
MX35	Condition 5 CCS Appendix 2	The efficacy of the habitat rehabilitation and enhancement measures employed will be reviewed in years 1, 2, 3, 5, 10, 15 and 25 following commencement of the plan on the basis of the results of vegetation sampling and water level readings from the managed areas. Analysis of the data collected will be the basis for a review of the measures and techniques employed. Should any adjustments to the plan will deemed necessary or advisable, these will be the subject of consultation with the NPWS prior to any alterations to the plan.	As required	As required	Project Ecologist
MX36	Condition 9 CCS Section 5	<ul style="list-style-type: none"> ▪ Following commissioning of the permitted wind farm, a shadow flicker analysis will be produced using the as-built co-ordinates and the installed turbine technology on site. ▪ If exceedances of the limits set by Condition no. 9 are predicted to occur, each of the potentially affected properties will be assessed to review orientation, landscaping and identify if there are any mitigating circumstances at the properties. Field investigations will also be carried out at the affected properties to allow the theoretical modelling of shadow flicker to be compared to actual occurrences. Field investigations will involve site visits which will be targeted at times when actual forecasted conditions required for shadow flicker are predicted. 	As Required on completion of construction	As Required	ECoW

Ref. No.	Reference	Survey/Monitoring Measure	Frequency	Reporting Measures	Responsibility
		<ul style="list-style-type: none"> ▪ The timing and extent of field investigation and monitoring will be based on the findings of the Shadow Flicker Model and will be scheduled to coincide with the relevant periods of predicated shadow flicker occurrence. The field investigations will be based on a minimum of three site visits at each receptor and will be fully informed by weather conditions. 			

9 PROGRAMME OF WORKS

The construction phase will take approximately 12-18 months to complete from starting on site to the commissioning of the electrical system and export of electricity from site.

The EIAR stipulated that in the interest of breeding birds, construction would not commence during the breeding bird season, which runs from April to July. The EIAR stipulated that construction may commence between August to the end of March, so that construction activities are ongoing by the time the next breeding bird season comes around and can continue throughout the next breeding season.

The phasing and scheduling main construction task items are outlined in Figure 8.1 below, where 1st February 2019 has been selected as an arbitrary start date for construction activities.

ID	Task Name	Task Description	Q1 19			Q2 19			Q3 19			Q4 19			Q1 20			Q2 20			Q3 20		
			Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	
1	Site Health & Safety		[Blue bar spanning from Feb 2019 to Aug 2020]																				
2	Site Compound	Site Compound, Site Access, Fencing, Gates	[Blue bar]																				
3	Site Roads	Excavate/upgrade roads; Install drainage measures; Install culvert; Install water protection measures;	[Blue bar]																				
4	Turbine Hardstands	Excavate base; construct hardstanding areas	[Blue bar]																				
5	Turbine Foundations	Fix steel; Erect shuttering; Concrete pour	[Blue bar]																				
6	Substation Construction & Electrical Works	Construct Substation; Underground cabling between turbines;	[Blue bar]																				
7	Backfilling & Landscaping														[Blue bar]								
8	Bolts/Cans Delivery														[Blue bar]								
9	Turbine Delivery & Erection														[Blue bar]								
10	Substation Commissioning														[Blue bar]								
11	Turbine Commissioning														[Blue bar]								

Figure 8.1 Indicative Construction Schedule

10 COMPLIANCE AND REVIEW

10.1 Site Inspections and Environmental Audits

Routine inspections of construction activities will be carried out on a daily and weekly basis by the ECoW and the Construction Manager to ensure all controls to prevent environmental impact, relevant to the construction activities taking place at the time, are in place.

Environmental inspections will ensure that the works are undertaken in compliance with this CEMP and all other planning application documents. Only suitably trained staff will undertake environmental site inspections.

10.2 Auditing

Environmental audits will be carried out during the construction phase of the project. In contrast to monitoring and inspection activities, audits are designed to shed light on the underlying causes of non-compliance, and not merely detect the non-compliance itself. In addition, audits are the main means by which system and performance improvement opportunities may be identified. Environmental audits will be carried out by contractor staff or alternatively by external personnel acting on their behalf. It is important that an impartial and objective approach is adopted. Environmental audits will be conducted at planned intervals to determine whether the CEMP is being properly implemented and maintained. The results of environmental audits will be provided to project management personnel.

10.3 Environmental Compliance

The following definitions shall apply in relation to the classification of Environmental Occurrences during construction of the wind farm:

Environmental Near Miss: An occurrence which if not controlled or due to its nature could lead to an Environmental Incident.

Environmental Incident: Any occurrence which has potential, due to its scale and nature, to migrate from source and have an environmental impact beyond the site boundary.

Environmental Exceedance Event: An environmental exceedance event occurs when monitoring results indicate that limits for a particular environmental parameter (as indicated in the Environmental Monitoring Programme) has been exceeded.

An exceedance will immediately trigger an investigation into the reason for the exceedance occurring and the application of suitable mitigation where necessary.

Exceedance events can be closed out on achieving a monitoring result below the assigned limit for a particular environmental parameter.

Environmental Non-Compliance: Non-fulfilment of a requirement and includes any deviations from established procedures, programs and other arrangements related to the EMP.

10.4 Corrective Action Procedure

A corrective action is implemented to rectify an environmental problem on-site. Corrective actions will be implemented by the Construction Manager, as advised by the Site ECoW. Corrective actions may be required as a result of the following;

- Environmental Audits;
- Environmental Inspections and Reviews;
- Environmental Monitoring;
- Environmental Incidents; and,
- Environmental Complaints.

A Corrective Action Notice will be used to communicate the details of the action required to the main contractor. A Corrective Action Notice is a form that describes the cause and effect of an environmental problem on site and the recommended corrective action that is required. The Corrective Action Notice, when completed, will include details of close out and follow up actions.

If an environmental problem occurs on site that requires immediate attention direct communications between the Construction Manager and the ECoW will be conducted. This in turn will be passed down to the site staff involved. A Corrective Action Notice will be completed at a later date.

10.5 Construction Phase Plan Review

This CEMP will be updated and reviewed prior to commencement of construction, and also every six months thereafter during the construction phase of the project.

Appendix 1

Site Layout Drawings

Project Design Drawing Notes

1. Drawings are for specific purposes only.
2. Drawings are to be used for the conditions stated.
3. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the express written consent of McCarthy Keville O'Sullivan Ltd.
4. The user of this drawing is deemed to have agreed that any errors or omissions should be taken of this drawing. All dimensions in millimetres unless otherwise stated.
5. The user of this drawing is deemed to have agreed that any errors or omissions should be taken of this drawing. All dimensions in millimetres unless otherwise stated.
6. The user of this drawing is deemed to have agreed that any errors or omissions should be taken of this drawing. All dimensions in millimetres unless otherwise stated.
7. The user of this drawing is deemed to have agreed that any errors or omissions should be taken of this drawing. All dimensions in millimetres unless otherwise stated.
8. Final levels may vary depending on local ground conditions.
9. Internal electrical cable trench may be installed on either side of the roads.


Drawing Legend

- Planning Application Site Boundary
- Existing Road to be Upgraded
- Existing Floating Road to be Upgraded
- Proposed Road
- Proposed Floating Road
- Internal Electrical Cable Trench
- Proposed Underground Grid Connection Cabling Route
- Directionally Drilled Cabling Route Section Under NTS
- Works Area
- Soft Levelled Area
- Crane Pad Handstanding Area
- Turbine Foundation
- Turbine Sweep Area
- Borrow Pit
- Proposed Amenity Track
- Passing Bay



**Site Layout (1:5,000)
Key Plan**

DRAWING TITLE		PROJECT TITLE	
Site Layout (1:5,000) Key Plan		Meerbog Wind Farm, Co. Donegal	
DRAWING NO.		PROJECT NO.	
0502 - 03		0502 - 03	
DRAWN BY		CHECKED BY	
Joseph O'Brien		Michael Watson	
SCALE		DATE	
1:20,000 @ A1		14.12.2017	
<p>McCarthy Keville O'Sullivan Ltd. Block 1, Financial Services Centre, Monaghan Road, Galway, Ireland. email: info@coarthyos.ie www.coarthyos.ie Tel: +353 91 735611 Fax: +353 91 771279</p>			

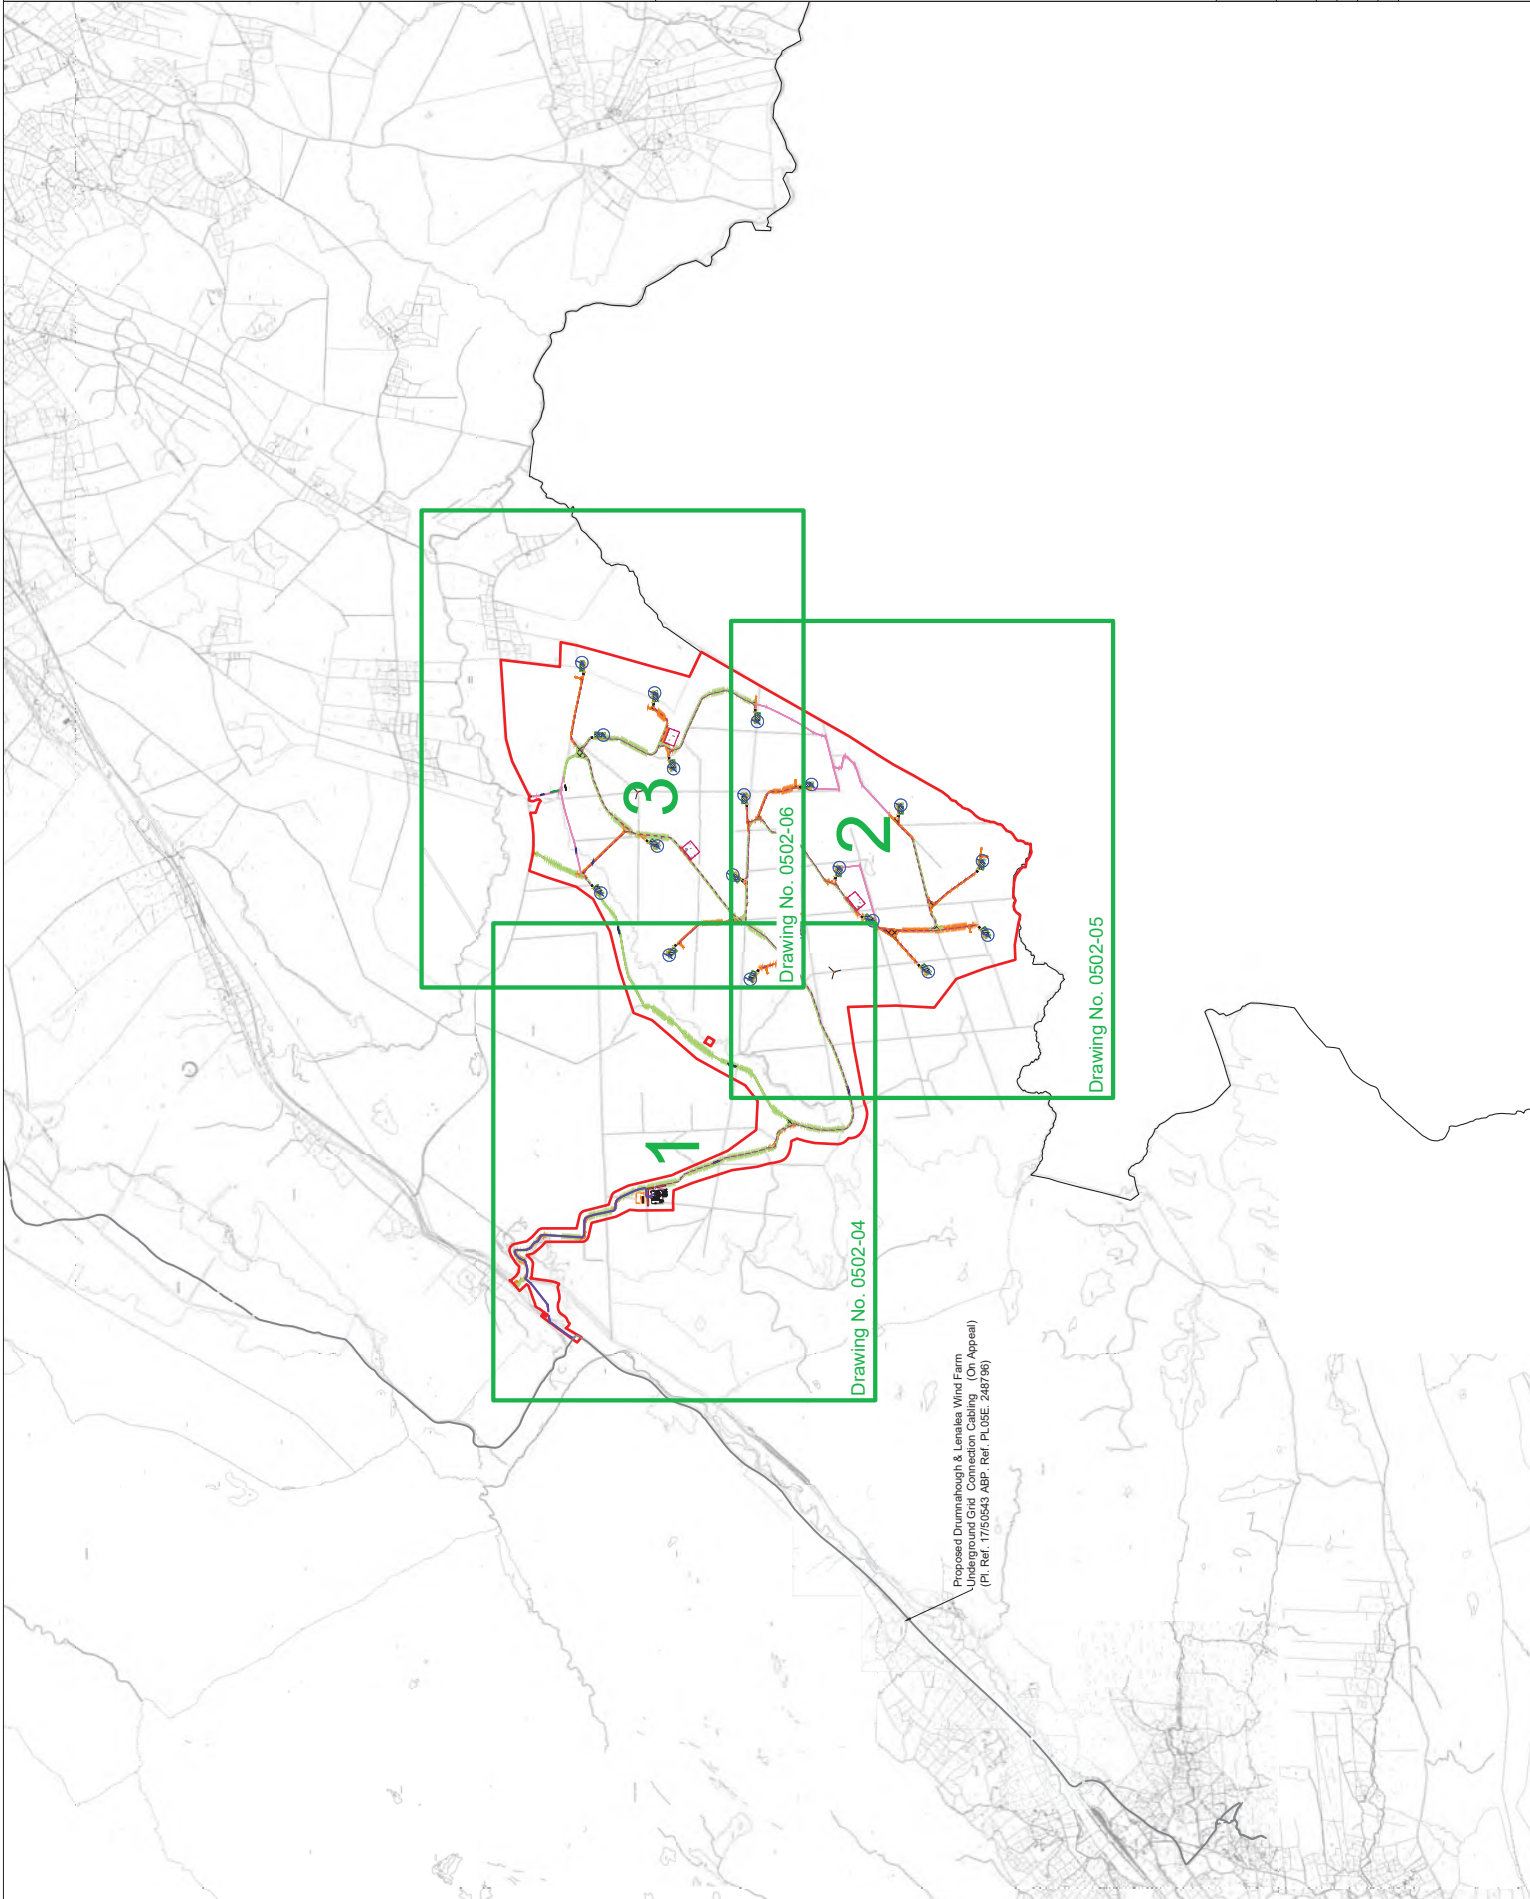


Proposed Drumsborough & Lonsdale Wind Farm
Underground Grid Connection Cabling (On Approval)
(Pl. Ref. 17/5/0543 ABP, Ref. PL.05E.2487/96)

Drawing No. 0502-04

Drawing No. 0502-06

Drawing No. 0502-05

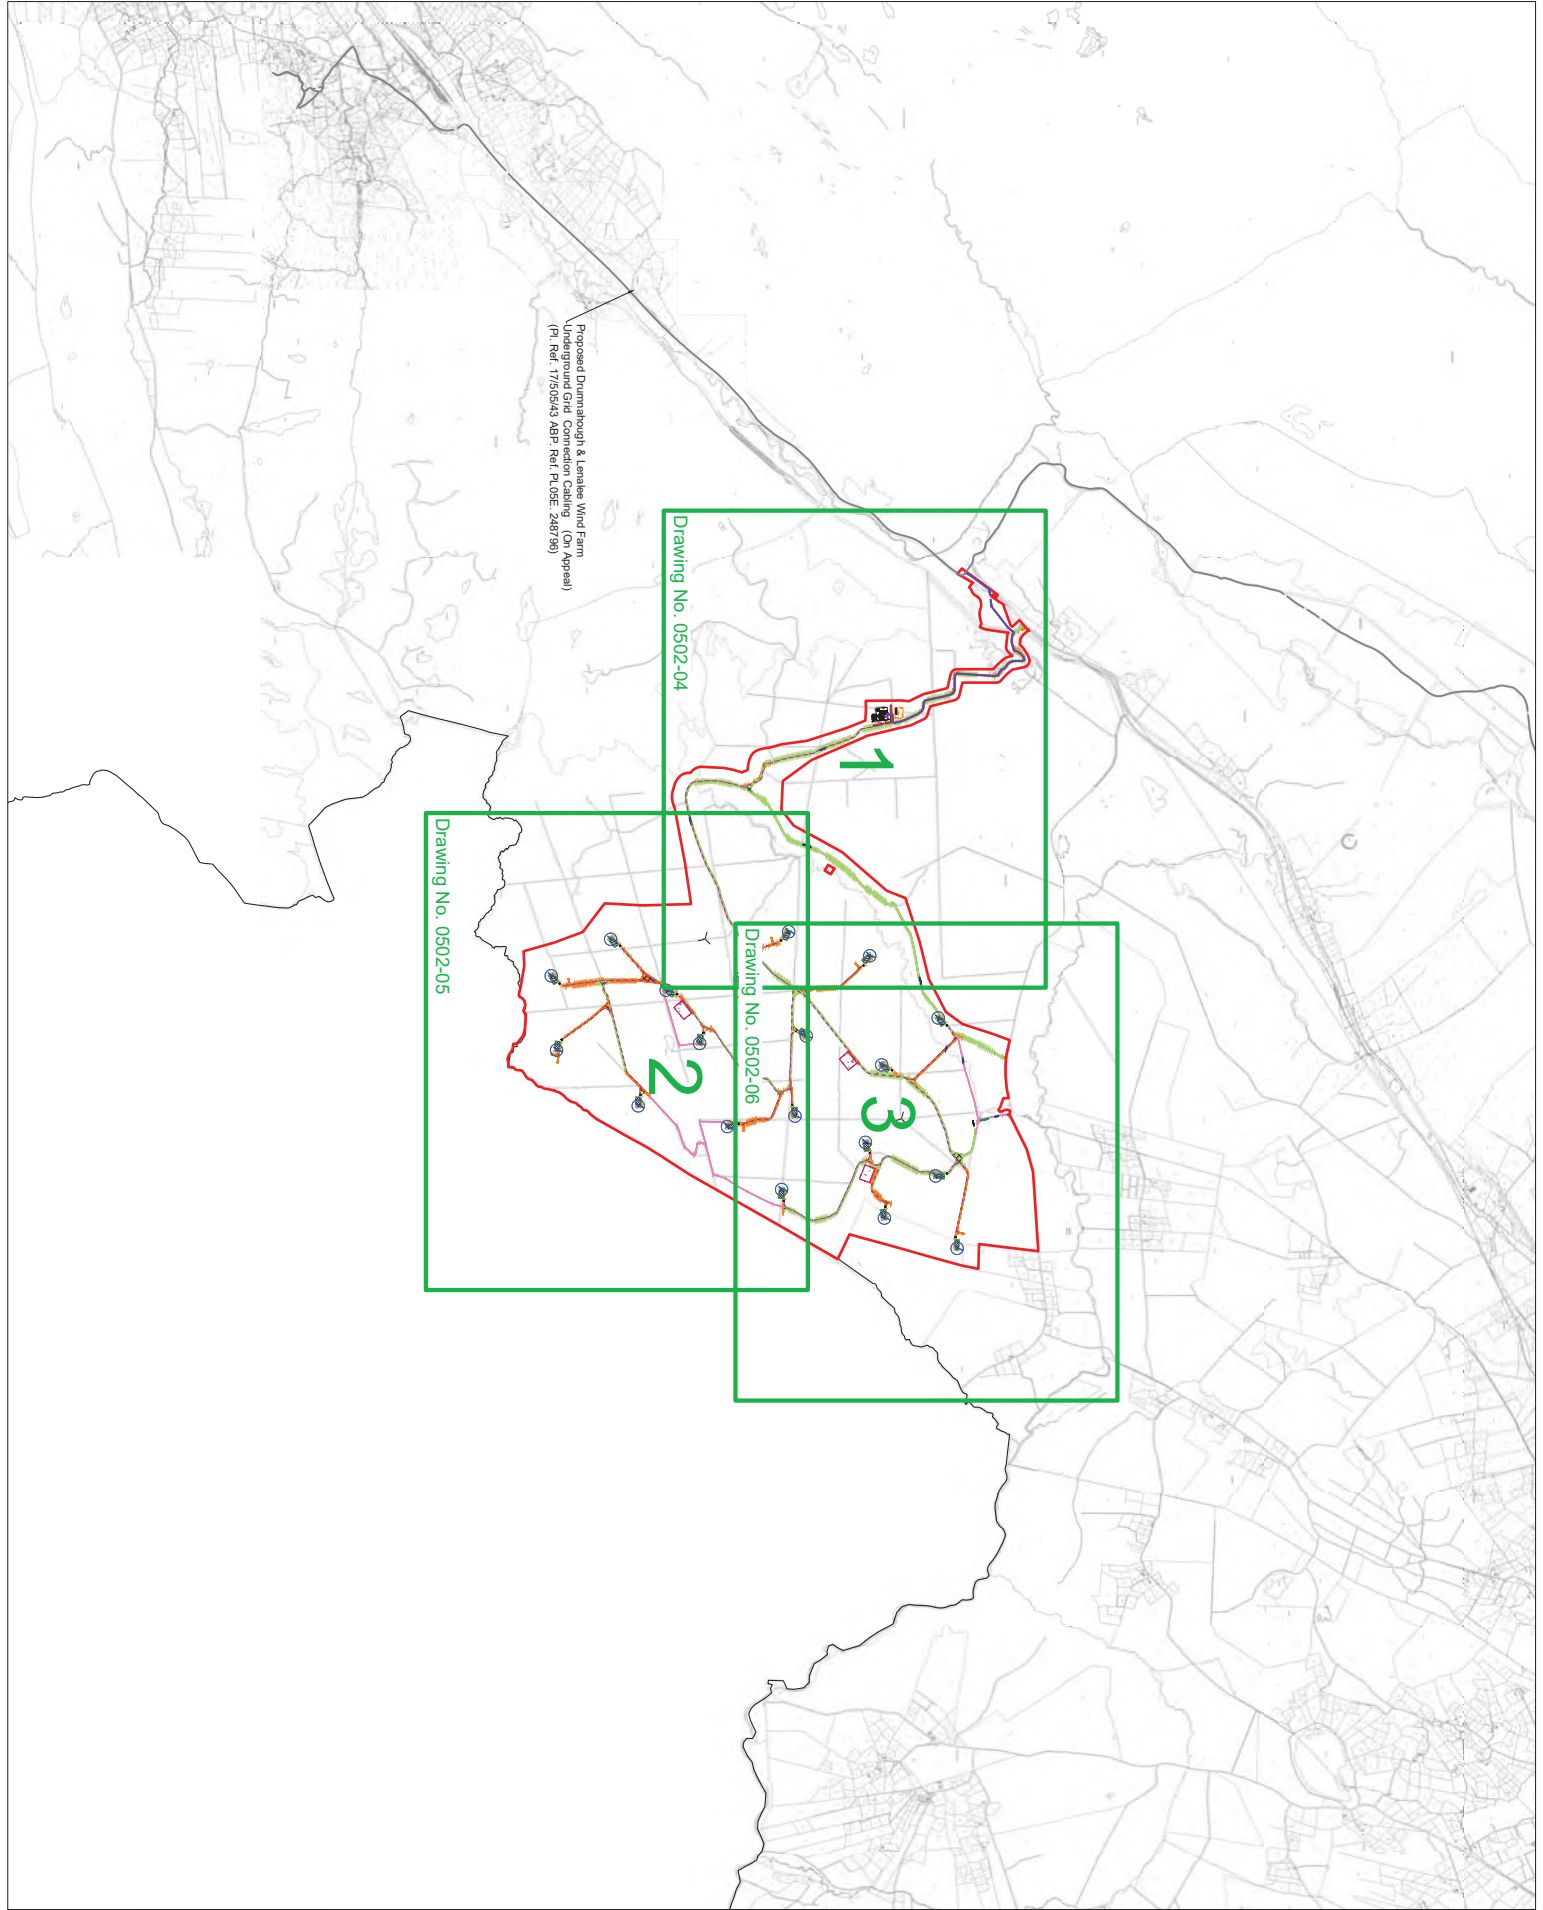

Proposed Dunmabagh & Lamlash Wind Farm
 Planning Application (P/A) Ref: 17/0504/3 ABP Ref: P/05E/24/7/95

Drawing No. 0502-04

Drawing No. 0502-05

Drawing No. 0502-06

- Proposed Design Drawings Notes**
1. Drawings should not be printed, reproduced, copied or otherwise used in any way without the prior written consent of the copyright owner, McCarthy Keville O'Sullivan Ltd.
 2. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior written consent of the copyright owner, McCarthy Keville O'Sullivan Ltd.
 3. The use of or reliance upon the drawing shall be deemed to be a warranty, such warranty agreement to be sought from and issued by the copyright holder to the user or reliance upon this drawing.
 4. The use of or reliance upon the drawing shall be deemed to be a warranty, such warranty agreement to be sought from and issued by the copyright holder to the user or reliance upon this drawing.
 5. The use of or reliance upon the drawing shall be deemed to be a warranty, such warranty agreement to be sought from and issued by the copyright holder to the user or reliance upon this drawing.
 6. Final levels may vary depending on local ground conditions.
 7. Internal electrical cable trench may be installed on either side of the roads.

Drawing Legend

- Planning Application Site Boundary
- Existing Road to be Upgraded
- Existing Footing Road to be Upgraded
- Proposed Road
- Proposed Footing Road
- Internal Electrical Cable Trench
- Proposed Underground Grid Connection
- Proposed Cable Trench
- Directional Drilled Casing Road Sweeps Under NIS
- Works Area
- Soft Levelled Area
- Crane Pad Handstanding Area
- Turbine Foundation
- Turbine Sweeps Area
- Borrow Pit
- Proposed Amenity Track
- Passing Bay



**Site Layout (1:5,000)
Key Plan**

PROJECT TITLE		Meenbog Wind Farm, Co. Donegal	
DRAWN BY	DESIGNED BY		
Joseph O'Brien	Michiel Watson		
PROJECT NO.	DRAWING NO.		
160502	0502-03		
SCALE	DATE		
1:20,000 @ A1	13.12.2017		
<p>McCarthy Keville O'Sullivan Ltd. Planning & Environmental Consultants Block 1, Industrial Services Centre, Monaghan Road, Galway, Ireland. email: info@cmk-os.com Tel: +353 91 735611 Fax: +353 91 771279</p>			

Project Design Drawing Notes

1. Drawings are for planning purposes only. They are not to be used for construction.
2. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior written consent of McCarthy Kevin O'Sullivan Ltd.
3. The use of or reliance upon this drawing shall be deemed to be a warranty of accuracy by McCarthy Kevin O'Sullivan Ltd. unless otherwise stated.
4. Dimensions are given in metres unless otherwise stated.
5. All dimensions are to be checked and checked any and all dimensions and levels that relate to the works.
6. The use of or reliance upon this drawing shall be deemed to be a warranty of accuracy by McCarthy Kevin O'Sullivan Ltd. unless otherwise stated.
7. All dimensions are to be checked and checked any and all dimensions and levels that relate to the works.
8. Final levels may vary depending on local ground conditions.
9. Internal electrical cable trench may be installed on either side of site roads.

Drawing Legend

	Planning Application Site Boundary
	Existing Road to be Upgraded
	Existing Floating Road to be Upgraded
	Proposed Road
	Proposed Floating Road
	Proposed Paving Road
	Internal Electrical Cable Trench
	Proposed Underground Grid Connection Cabling Route
	Directional Drilling Route Section Under N12
	River/Stream
	River/Stream 50m Buffer
	Lakes
	Lakes 50m Buffer
	Works Area
	Soft Levelled Area
	Crane Pad Handstanding Area
	Turbine Foundation
	Turbine Sweep Area
	Borrow Pit
	Cut
	Fill
	Passing Bay
	Berm

N

**Site Layout Plan
Sheet 1 of 3**

PROJECT TITLE
Meerbog Wind Farm, Co. Donegal

DESIGNED BY
Joseph O'Brien

CHECKED BY
Michael Watson


PROJECT NO.
160502

DRAWING NO.
0502 - 04


SCALE
1:5,000 @ A1

DATE
14.12.2017

McCarthy Kevin O'Sullivan Ltd.
Planning & Environmental Consultants
Block 1, Financial Services Centre,
Menaghagha Road,
Galway, Ireland.
email: info@mcCarthyKevinO'Sullivan.ie
Tel: +353 91 735611
Fax: +353 91 771279

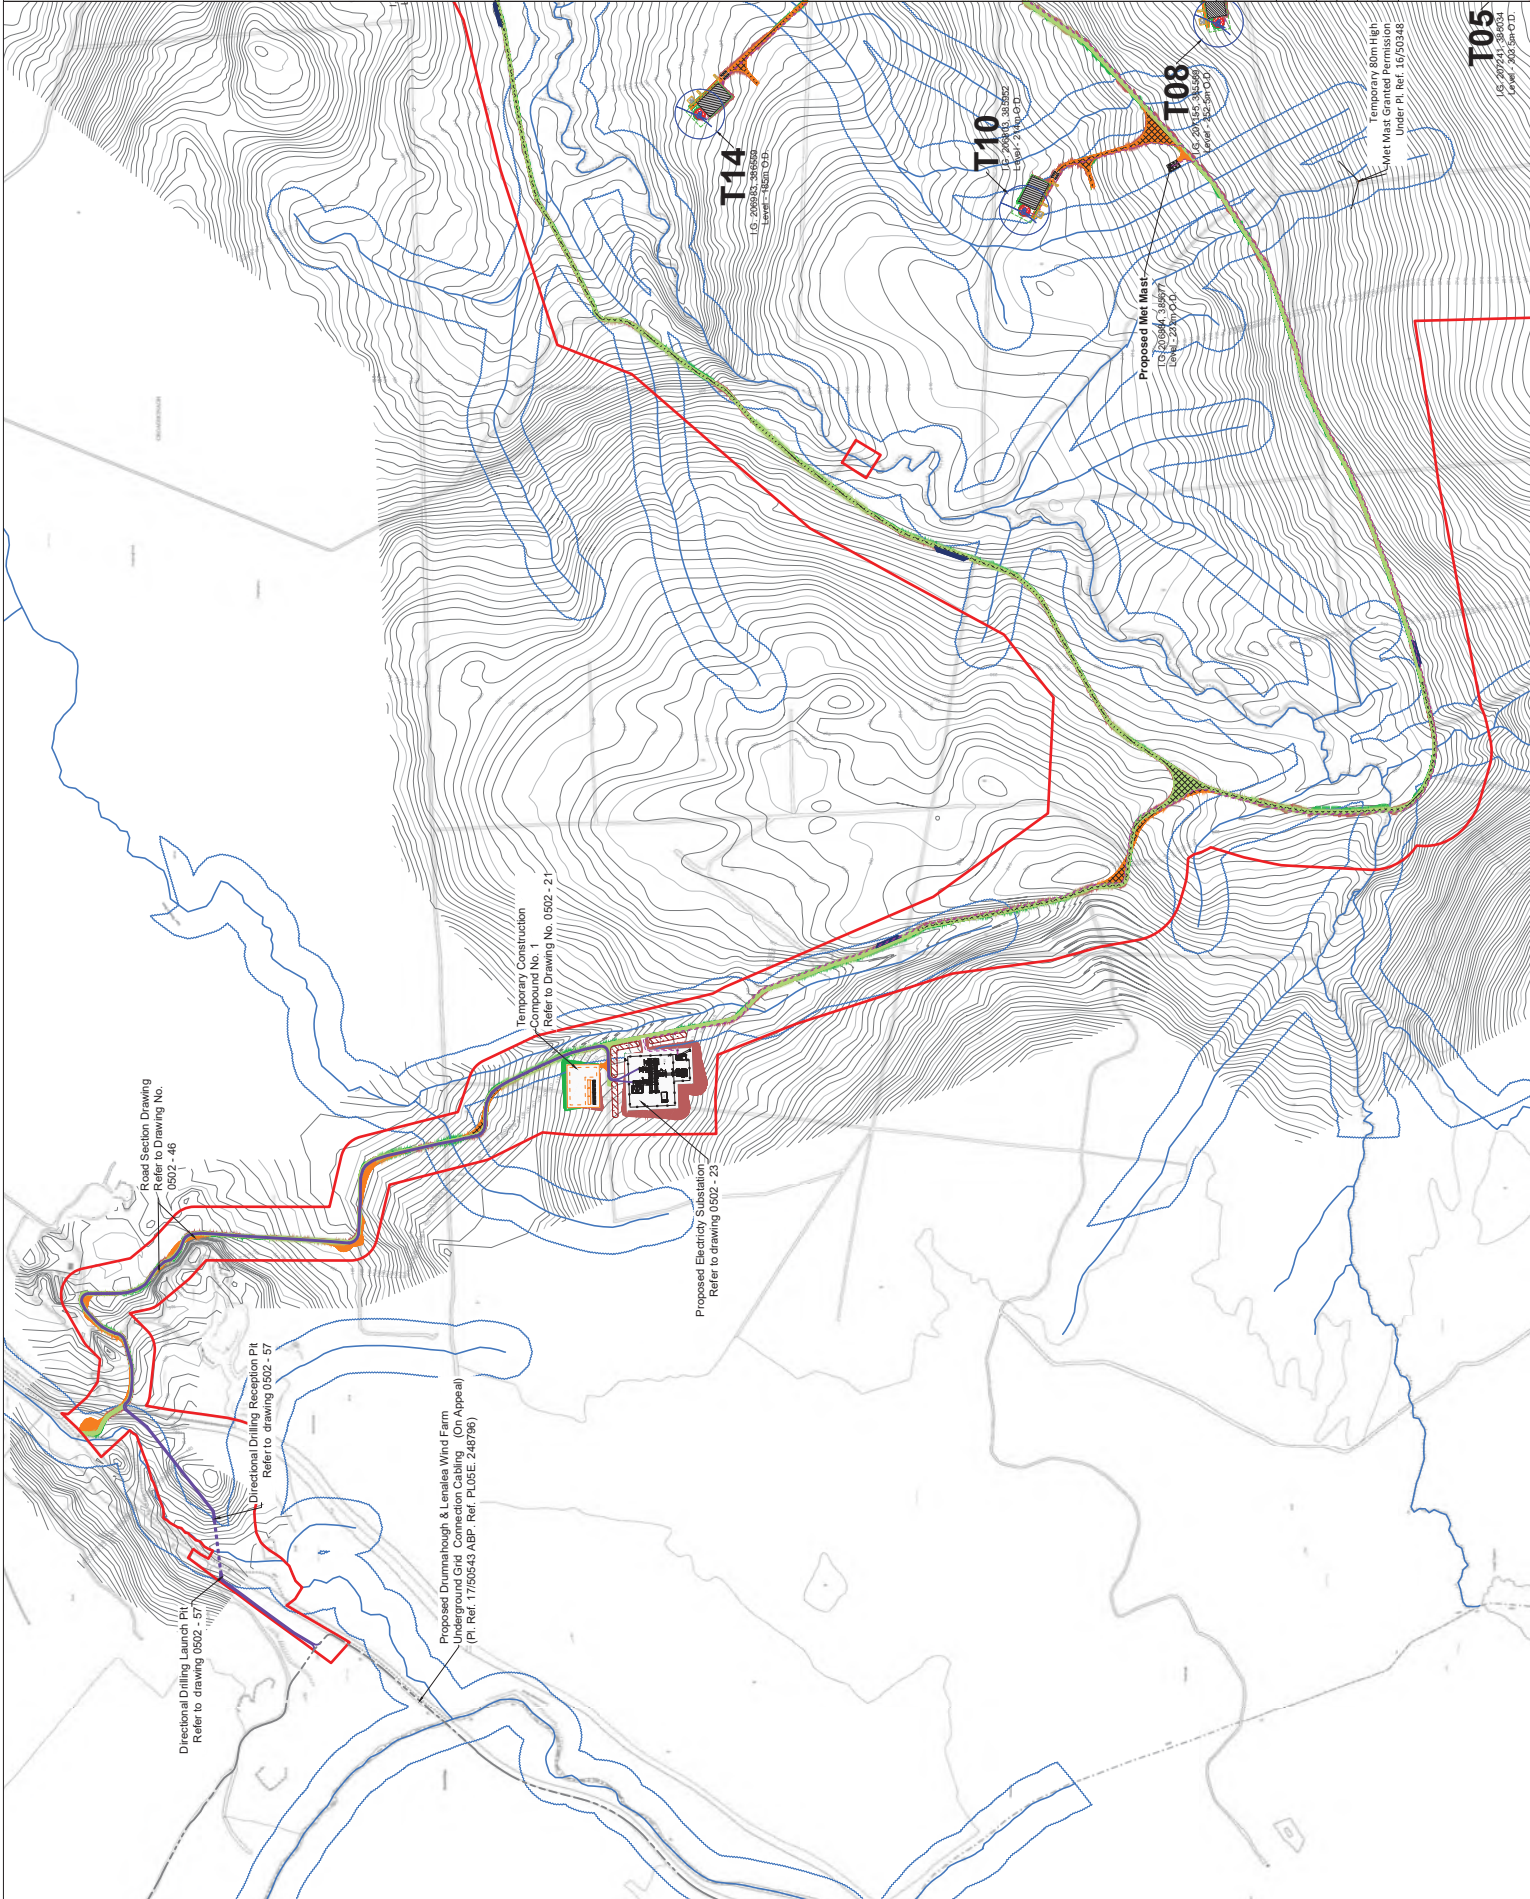

T05
1:5,000 @ A1
14.12.2017

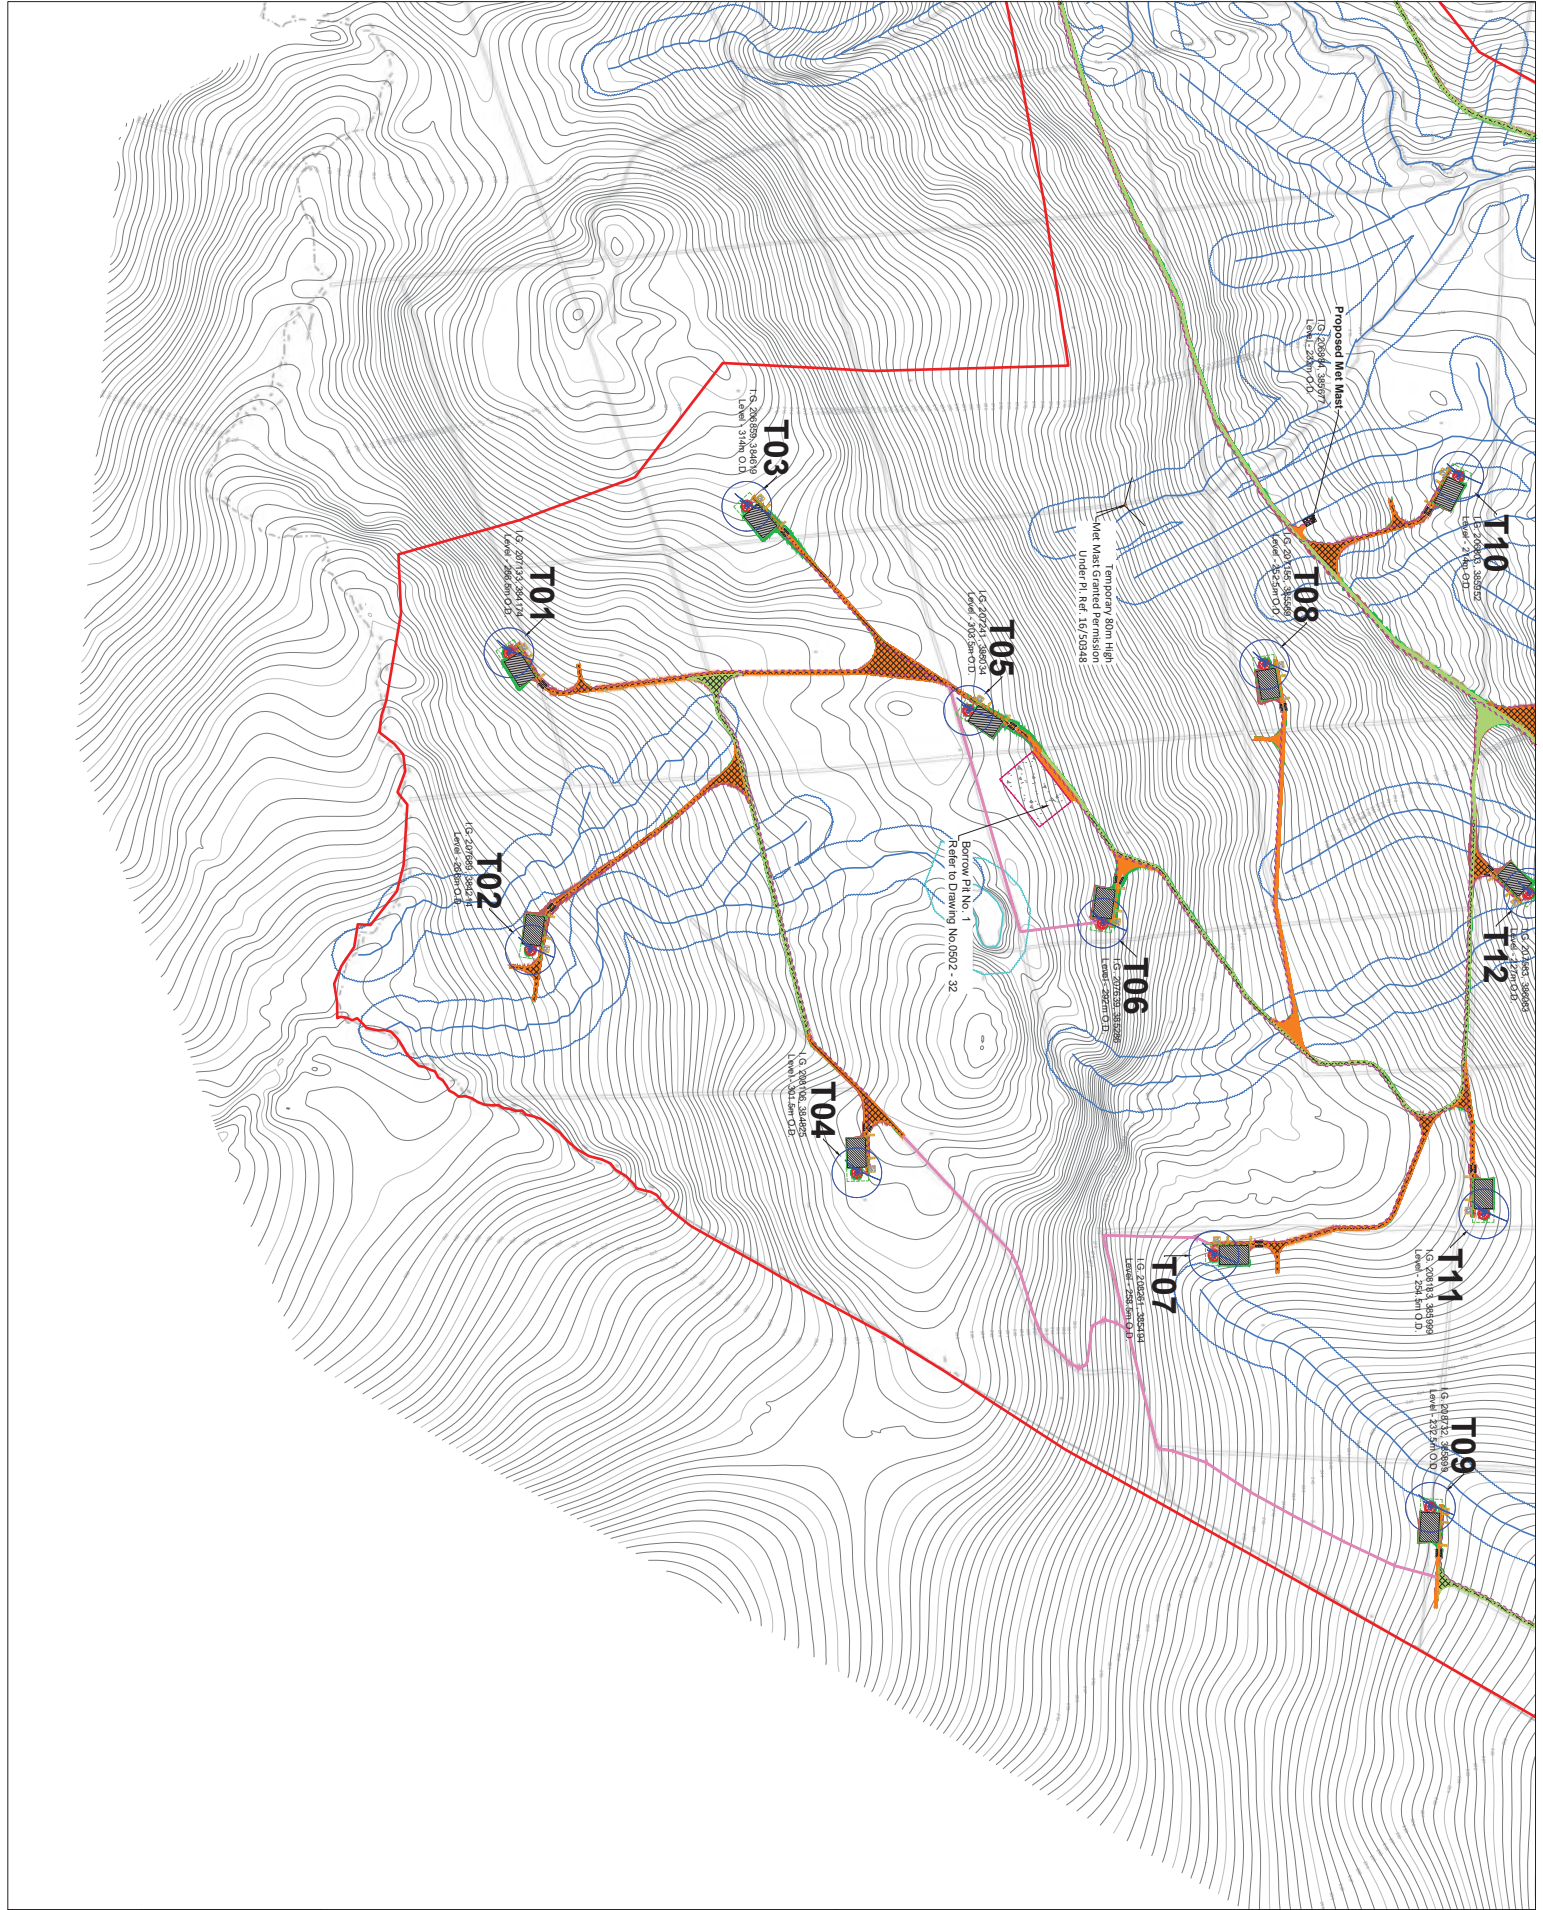

Project Design Drawing Notes

1. Drawings issued are for planning application purposes only.
2. The information contained in this drawing is for information only and does not constitute an offer of any services or products.
3. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior consent of the copyright owner McCarthy Keville O'Sullivan Ltd.
4. The information contained in this drawing is for information only and should be taken of this drawing. All dimensions in millimetres unless otherwise stated.
5. The use of reference symbols for levels and elevations, and the dimensions and levels that relate to the works.
6. The use of reference symbols in drawings shall be deemed to be the same as the information for levels and elevations, and the dimensions and levels that relate to the works.
7. The use of reference symbols in drawings shall be deemed to be the same as the information for levels and elevations, and the dimensions and levels that relate to the works.
8. Final levels may vary depending on local ground conditions.
9. All vertical electrical cable trench may be installed on either side of the roads.

Drawing Legend

	Planning Application Site Boundary
	Existing Road to be Upgraded
	Existing Footing Road to be Upgraded
	Proposed Road
	Proposed Footing Road
	Internal Electrical Cable Trench
	River/Stream
	River/Stream 50m Buffer
	Lakes
	Lakes 50m Buffer
	Works Area
	Soft Levelled Area
	Crane Pad Handstanding Area
	Turbine Foundation
	Turbine Sweeps Area
	Borrow Pit
	Cut
	Fill
	Proposed Amenity Track

Site Layout Plan Sheet 2 of 3

PROJECT TITLE: Meenbog Wind Farm, Co. Donegal

DRAWN BY: Joseph O'Brien

CHECKED BY: Michiel Watson

SCALE: 1:5,000 @ A1

DATE: 13.12.2017

PROJECT NO: 160502

DRAWING NO: 0502 - 05

McCarthy Keville O'Sullivan Ltd.
 Planning & Environmental Consultants
 Block 1, Commercial Services Centre,
 Moynebeghna Road,
 Galway, Ireland.
 email: info@cmko.ie
 Tel: +353 91 725611
 Fax: +353 91 771279

Ordnance Survey Ireland Licence No. AR0021817 © Ordnance Survey Ireland/Government of Ireland

Project Design Drawing Notes

1. Drawings are for planning application purposes only.
2. No part of this drawing is to be copied or reproduced in any form without the prior written consent of McCarthy Keville O'Sullivan Ltd.
3. Copyright, all rights reserved. No part herein may be copied or reproduced partially or wholly in any form whatsoever without the prior written consent of McCarthy Keville O'Sullivan Ltd.
4. The use of any copyright material in this drawing is acknowledged and should be taken of this drawing. All dimensions in millimetres unless otherwise stated.
5. The use of any copyright material in this drawing is acknowledged and should be taken of this drawing. All dimensions in millimetres unless otherwise stated.
6. The use of any copyright material in this drawing is acknowledged and should be taken of this drawing. All dimensions in millimetres unless otherwise stated.
7. The use of any copyright material in this drawing is acknowledged and should be taken of this drawing. All dimensions in millimetres unless otherwise stated.
8. Final levels may vary depending on local ground conditions.
9. Internal electrical cable trench may be installed on either side of site roads.

Drawing Legend

- Planning Application Site Boundary
- Existing Road to be Upgraded
- Existing Floating Road to be Upgraded
- Proposed Road
- Proposed Floating Road
- Internal Electrical Cable Trench
- River/Stream
- River/Stream 50m Buffer
- Works Area
- Soil Levelled Area
- Crane Pad/Retaining Area
- Turbine Foundation
- Turbine Sweeps Area
- Borrow Pit
- Cut
- Fill
- Proposed Amenity Track
- Passing Bay

Ordnance Survey Ireland Licence No. AR00217 © Ordnance Survey Ireland/Government of Ireland

Site Layout Plan Sheet 3 of 3


PROJECT TITLE: Meerbog Wind Farm, Co. Donegal


DESIGNED BY: Joseph O'Brien | Michael Watson

PROJECT NO: 160502 | 0502 - 06

SCALE: 1:5,000 @ A1 | DATE: 13.12.2017

McCarthy Keville O'Sullivan Ltd.
 Planning & Environmental Consultants
 Black T, Financial Services Centre,
 Monaghan Road,
 Galway, Ireland.
 email: info@coarwyn.ie
 www.coarwyn.ie
 Tel: +353 91 735611
 Fax: +353 91 771279

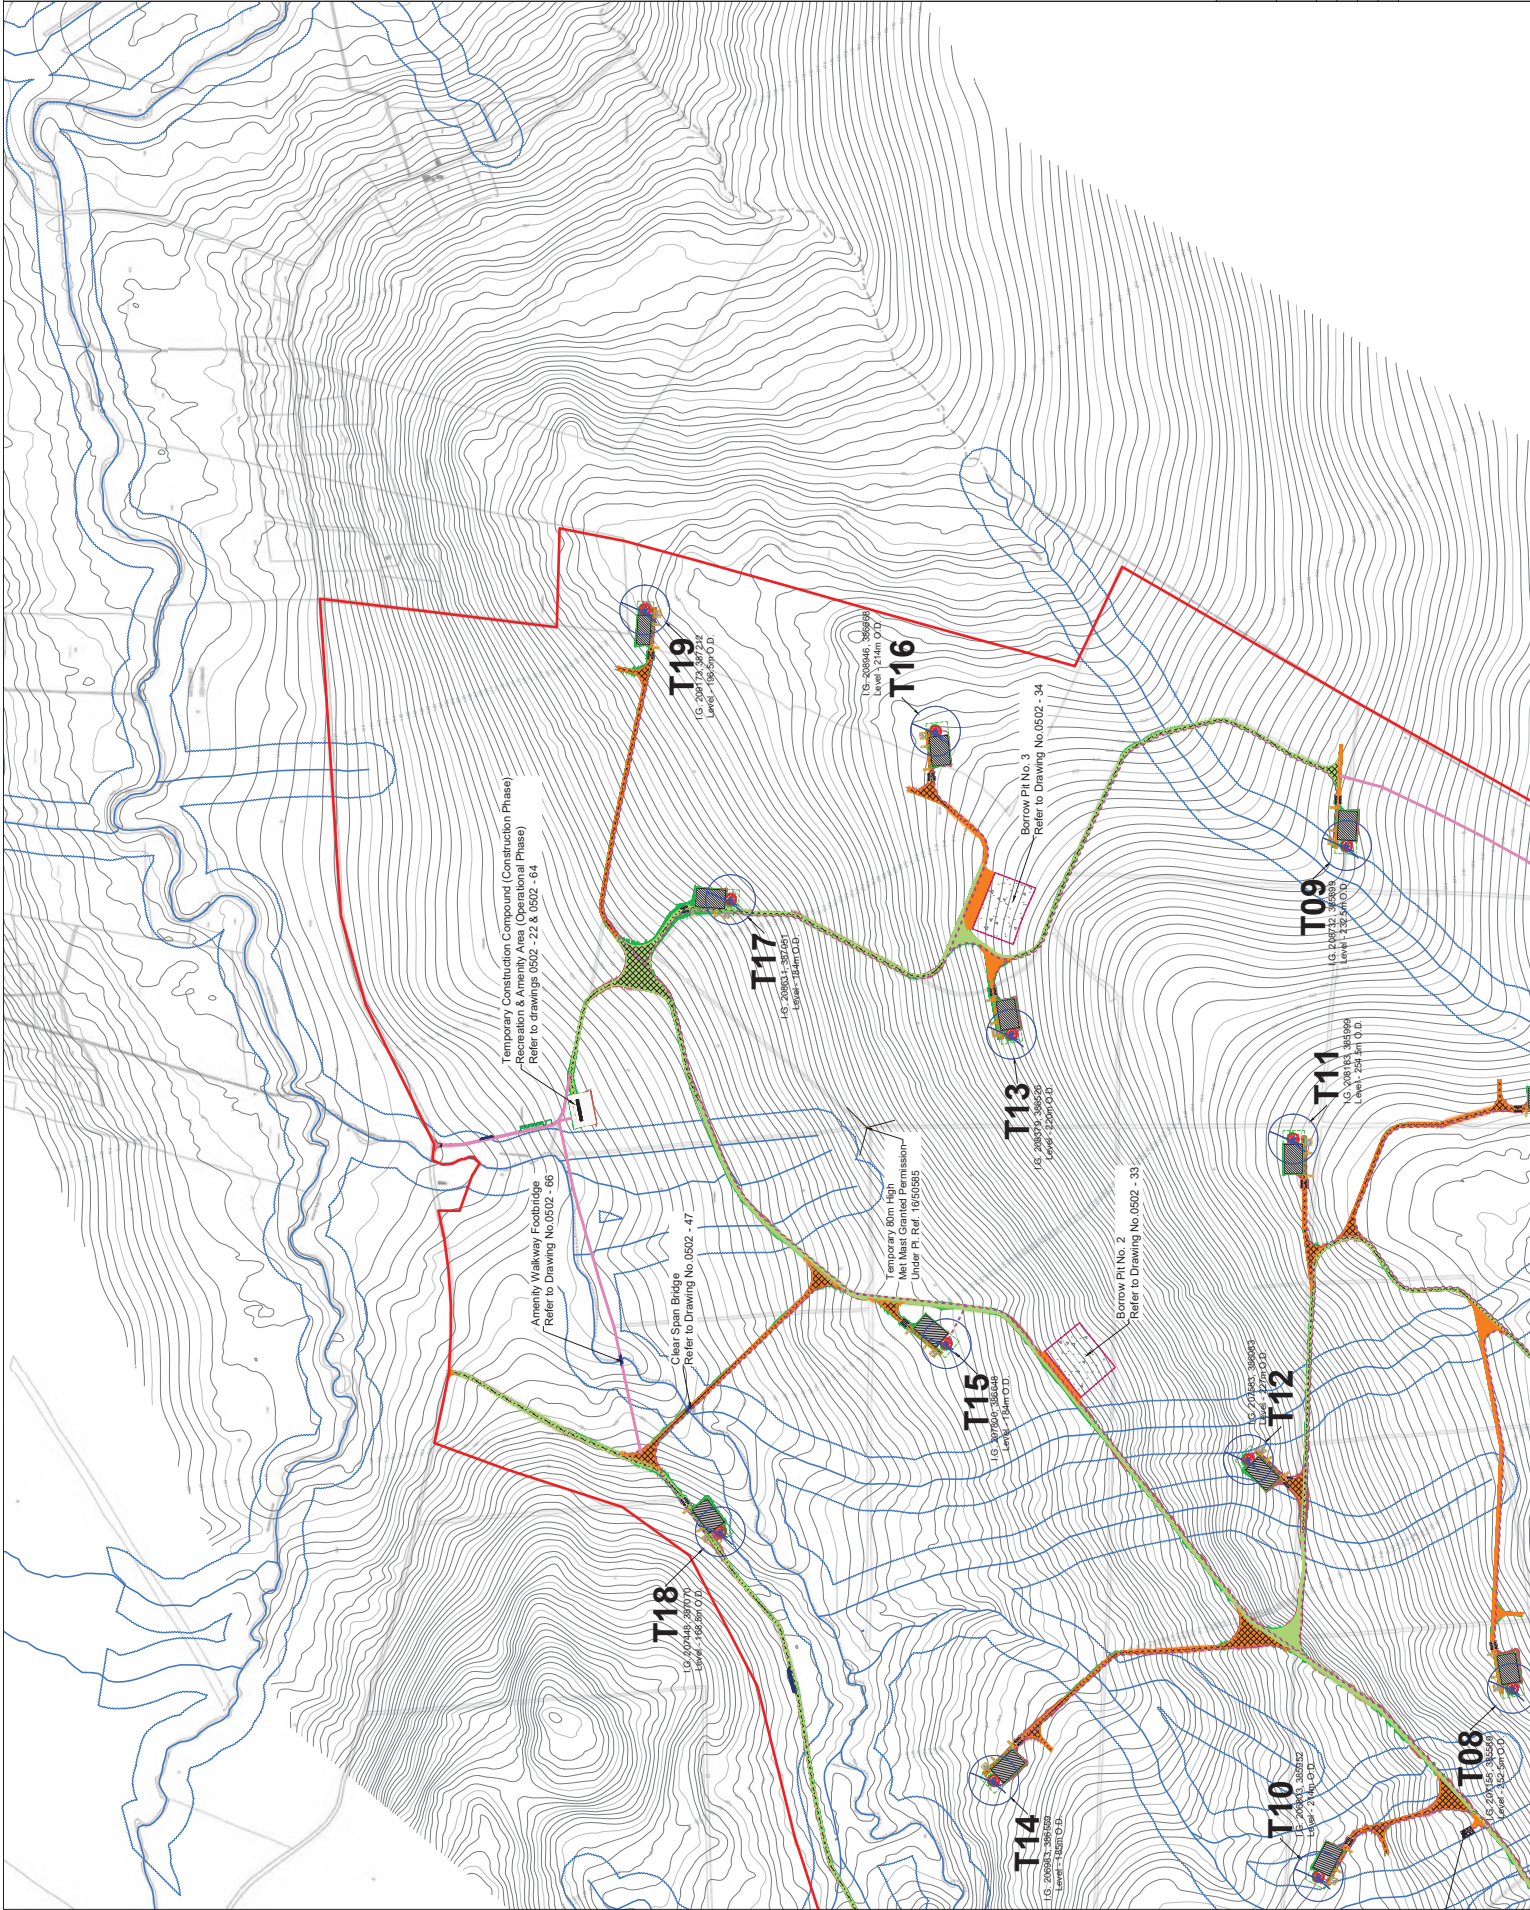

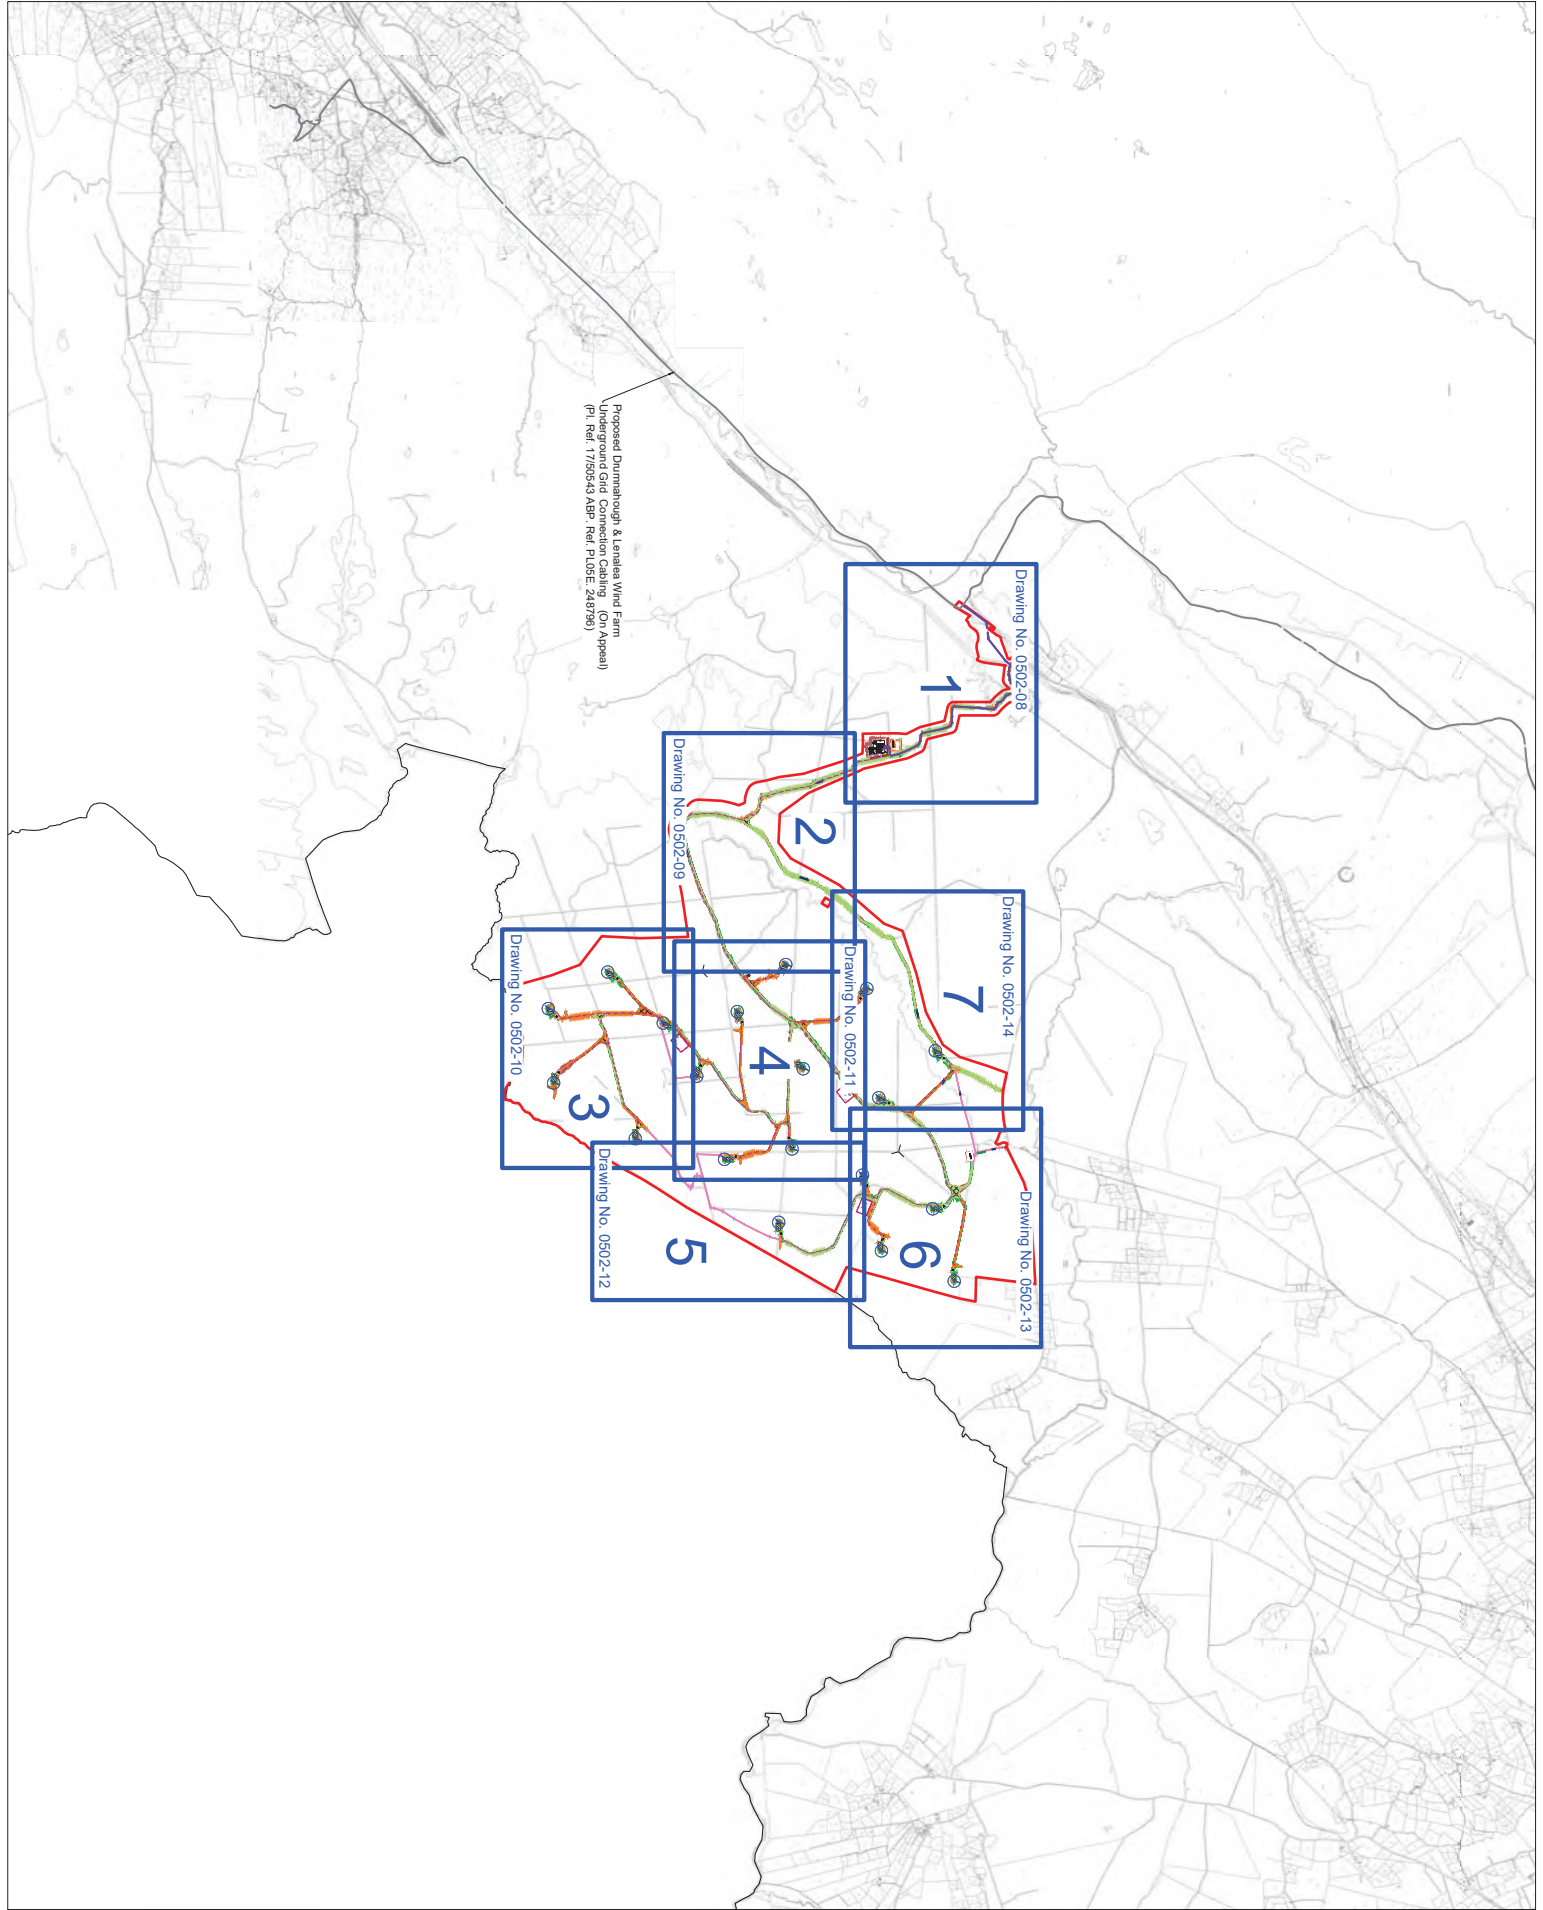

Proposed Durnathough & Lenalee Wind Farm
 Underground Grid Connection Cabling (OJ Appeal)
 (PJ Ref: 17/05/543 ABP Ref PJ.05E.248795)

Drawing No. 0502-08

Drawing No. 0502-09

Drawing No. 0502-14

Drawing No. 0502-11

Drawing No. 0502-10

Drawing No. 0502-12

Drawing No. 0502-13

Project Design Drawing Notes

1. Drawings should not be printed, reproduced, copied, or otherwise used without the written consent of the copyright owner.
2. Copyright in all rights reserved. No part hereof may be copied or reproduced in any form or by any means without the prior written consent of the copyright owner.
3. Copyright in all rights reserved. No part hereof may be copied or reproduced in any form or by any means without the prior written consent of the copyright owner.
4. Copyright in all rights reserved. No part hereof may be copied or reproduced in any form or by any means without the prior written consent of the copyright owner.
5. Copyright in all rights reserved. No part hereof may be copied or reproduced in any form or by any means without the prior written consent of the copyright owner.
6. The use of or reliance upon the drawings shall be deemed to be a warranty by the copyright owner that the drawings are true and correct and are intended to be used as a guide only and are not intended to be used as a basis for any construction or other work.
7. The use of or reliance upon the drawings shall be deemed to be a warranty by the copyright owner that the drawings are true and correct and are intended to be used as a guide only and are not intended to be used as a basis for any construction or other work.
8. Final levels may vary depending on local ground conditions.
9. Internal electrical cable trench may be installed on either side of the roads.

Drawing Legend

- Planning Application Site Boundary
- Existing Road to be Upgraded
- Existing Footpath Road to be Upgraded
- Existing Road
- Proposed Footpath Road
- Proposed Footpath Road
- Proposed Underground Grid Connection Cabling Route
- Directionally Oriented Cabling Route Sections Under N15
- Internal Electrical Cable Trench
- Works Area
- Soft Levelled Area
- Crane Pad Hardstanding Area
- Turbine Foundation
- Turbine Sweeep Area
- Borrow Pit
- Proposed Armey Track
- Passing Bay



**Site Layout (1:2,500)
Key Plan**

PROJECT TITLE		Meebrog Wind Farm, Co. Donegal	
DRAWN BY	DESIGNED BY	MICHAEL WATSON	
PROJECT NO.	DRAWING NO.	0502 - 07	
SCALE	DATE	1:250,000 @ A1 14.12.2017	
McCarthy O'Sullivan Ltd. Planning & Environmental Consultants Block 1, Industrial Services Centre, Monaghan Road, Galway, Ireland. email: info@mcCarthyOSullivan.ie Tel: +353 91 735611 Fax: +353 91 771279			

Project Design Drawing Notes

- Drawings are for planning purposes only. They are not to be used for construction.
- Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior written consent of McCarthy Keville O'Sullivan Ltd.
- The use of any information contained in this drawing is at the user's own risk. The user shall be responsible for ensuring that the drawing is suitable for the intended use and for any consequences arising therefrom.
- The user shall be responsible for ensuring that the drawing is suitable for the intended use and for any consequences arising therefrom.
- The user shall be responsible for ensuring that the drawing is suitable for the intended use and for any consequences arising therefrom.
- The user shall be responsible for ensuring that the drawing is suitable for the intended use and for any consequences arising therefrom.
- The user shall be responsible for ensuring that the drawing is suitable for the intended use and for any consequences arising therefrom.
- The user shall be responsible for ensuring that the drawing is suitable for the intended use and for any consequences arising therefrom.
- The user shall be responsible for ensuring that the drawing is suitable for the intended use and for any consequences arising therefrom.
- The user shall be responsible for ensuring that the drawing is suitable for the intended use and for any consequences arising therefrom.

Drawing Legend

- Planning Application Site Boundary
- Existing Road to be Upgraded
- Proposed Road
- Proposed Floating Road
- Internal Electrical Cable Trench
- Proposed Underground Grid Connection
- Directionally Drilled Cabling Route See Drawing 0502 - 20
- Under NTS
- River/Stream
- River/Stream 50m Buffer
- Cut
- Fill

Ordnance Survey Ireland Licence No. A70021817 © Ordnance Survey Ireland

Site Layout Plan Sheet 1 of 7

PROJECT TITLE: Meerbog Wind Farm, Co. Donegal

DESIGNED BY: Joseph O'Brien


DRAWN BY: Michael Watson


PROJECT NO: 160502

DATE: 14.12.2017

SCALE: 1:2,500 @ A1

McCarthy Keville O'Sullivan Ltd.
 Planning & Environmental Consultants
 Black T, Financial Services Centre,
 Monaghan Road,
 Galway, Ireland.
 email: info@mcortwo.ie
 Tel: +353 91 735611
 Fax: +353 91 771279

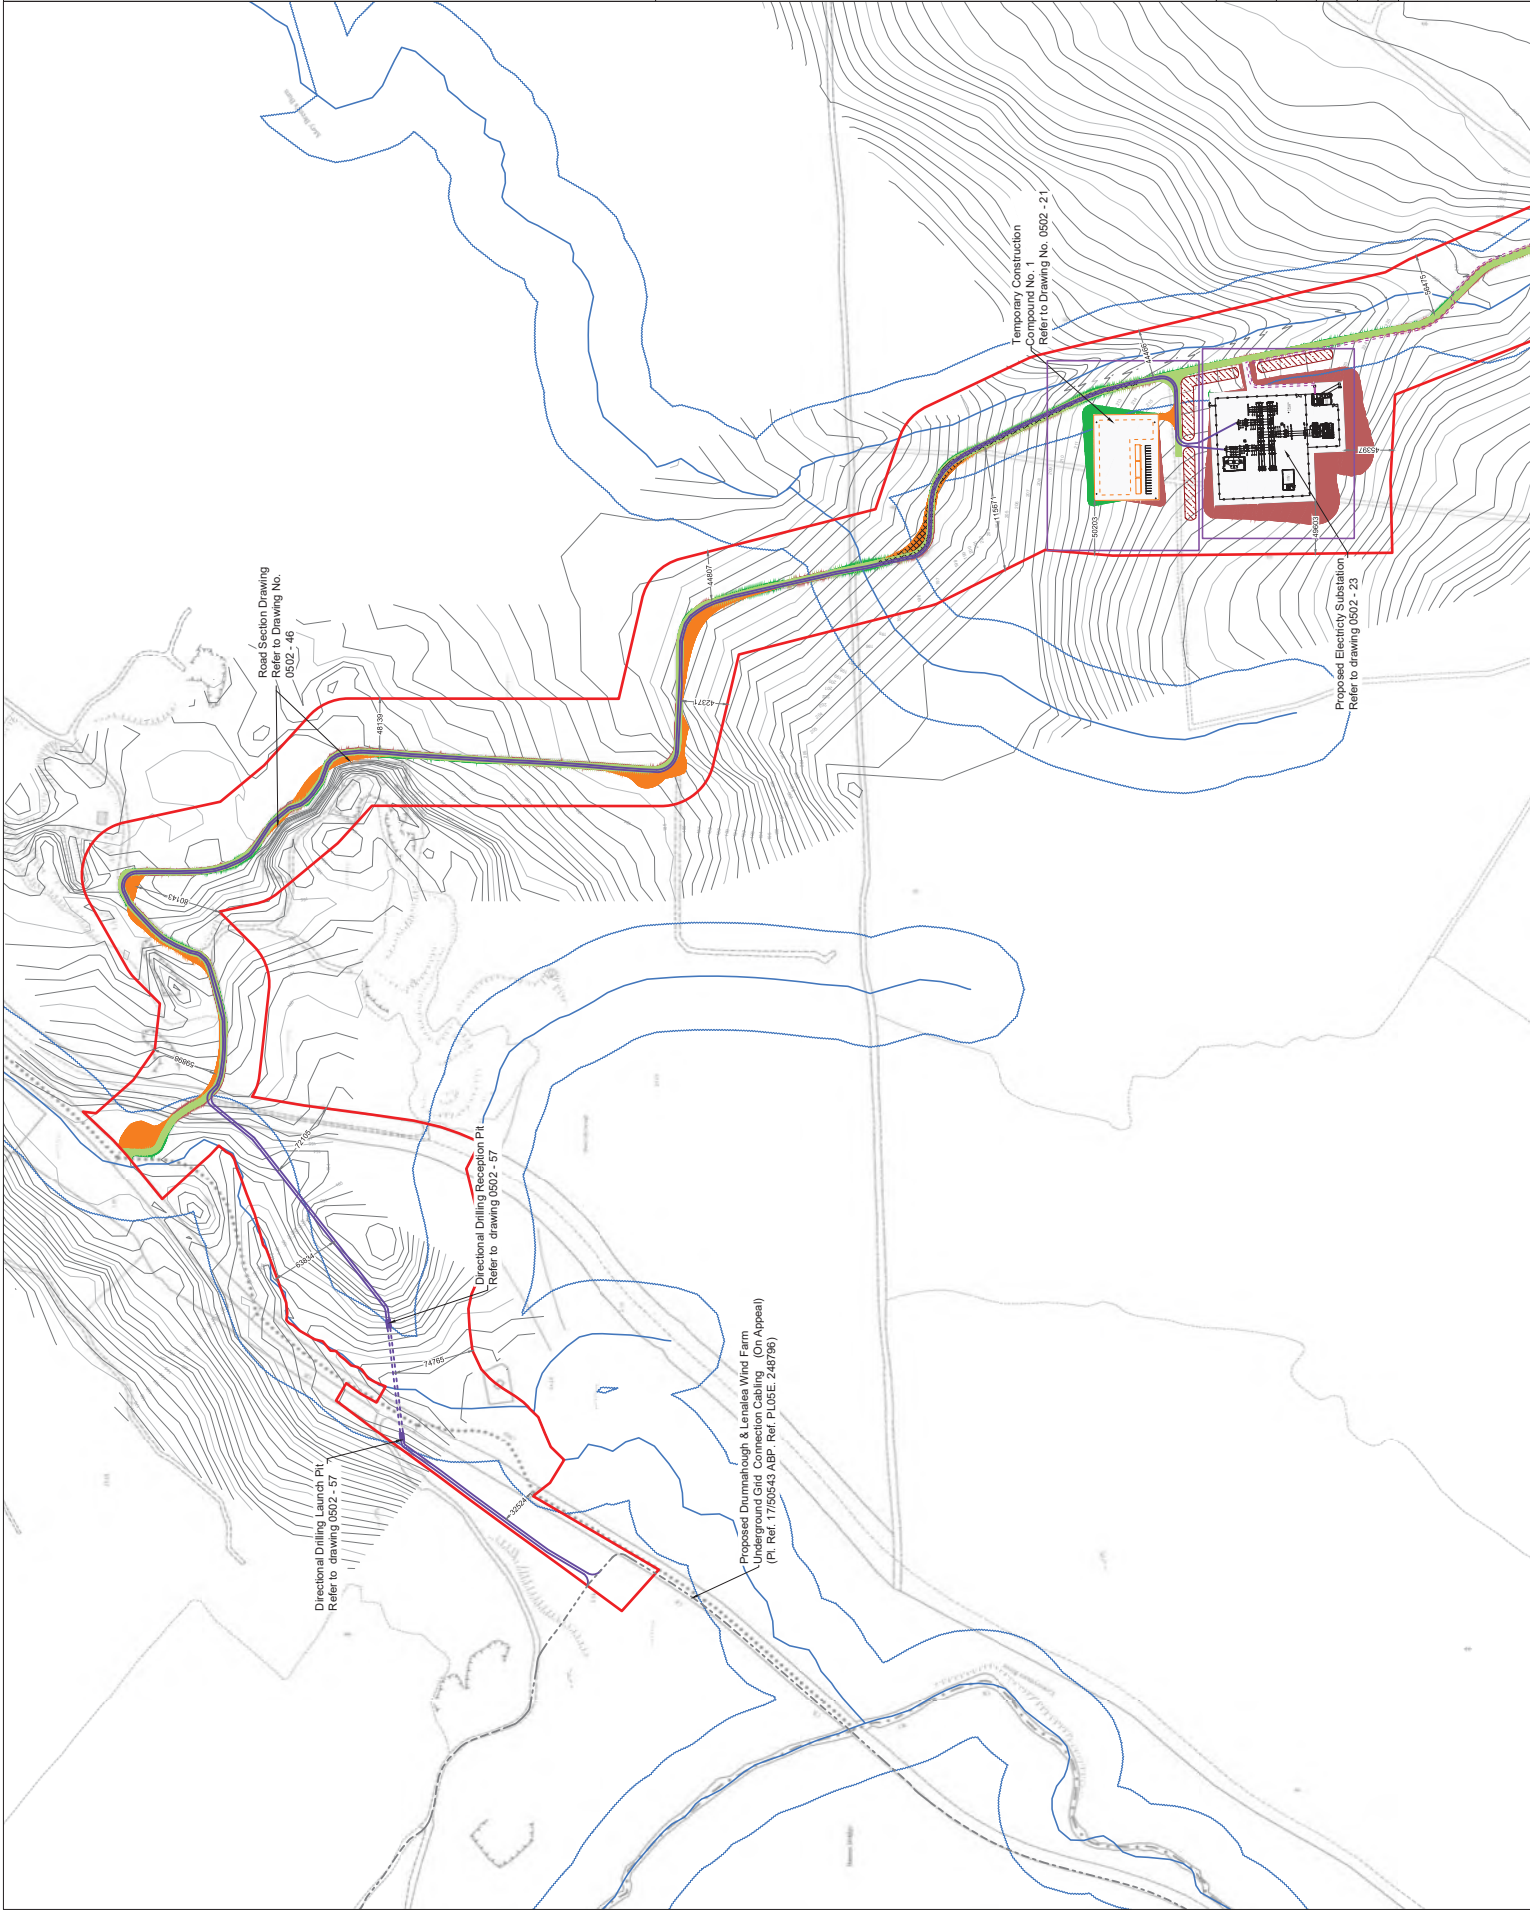

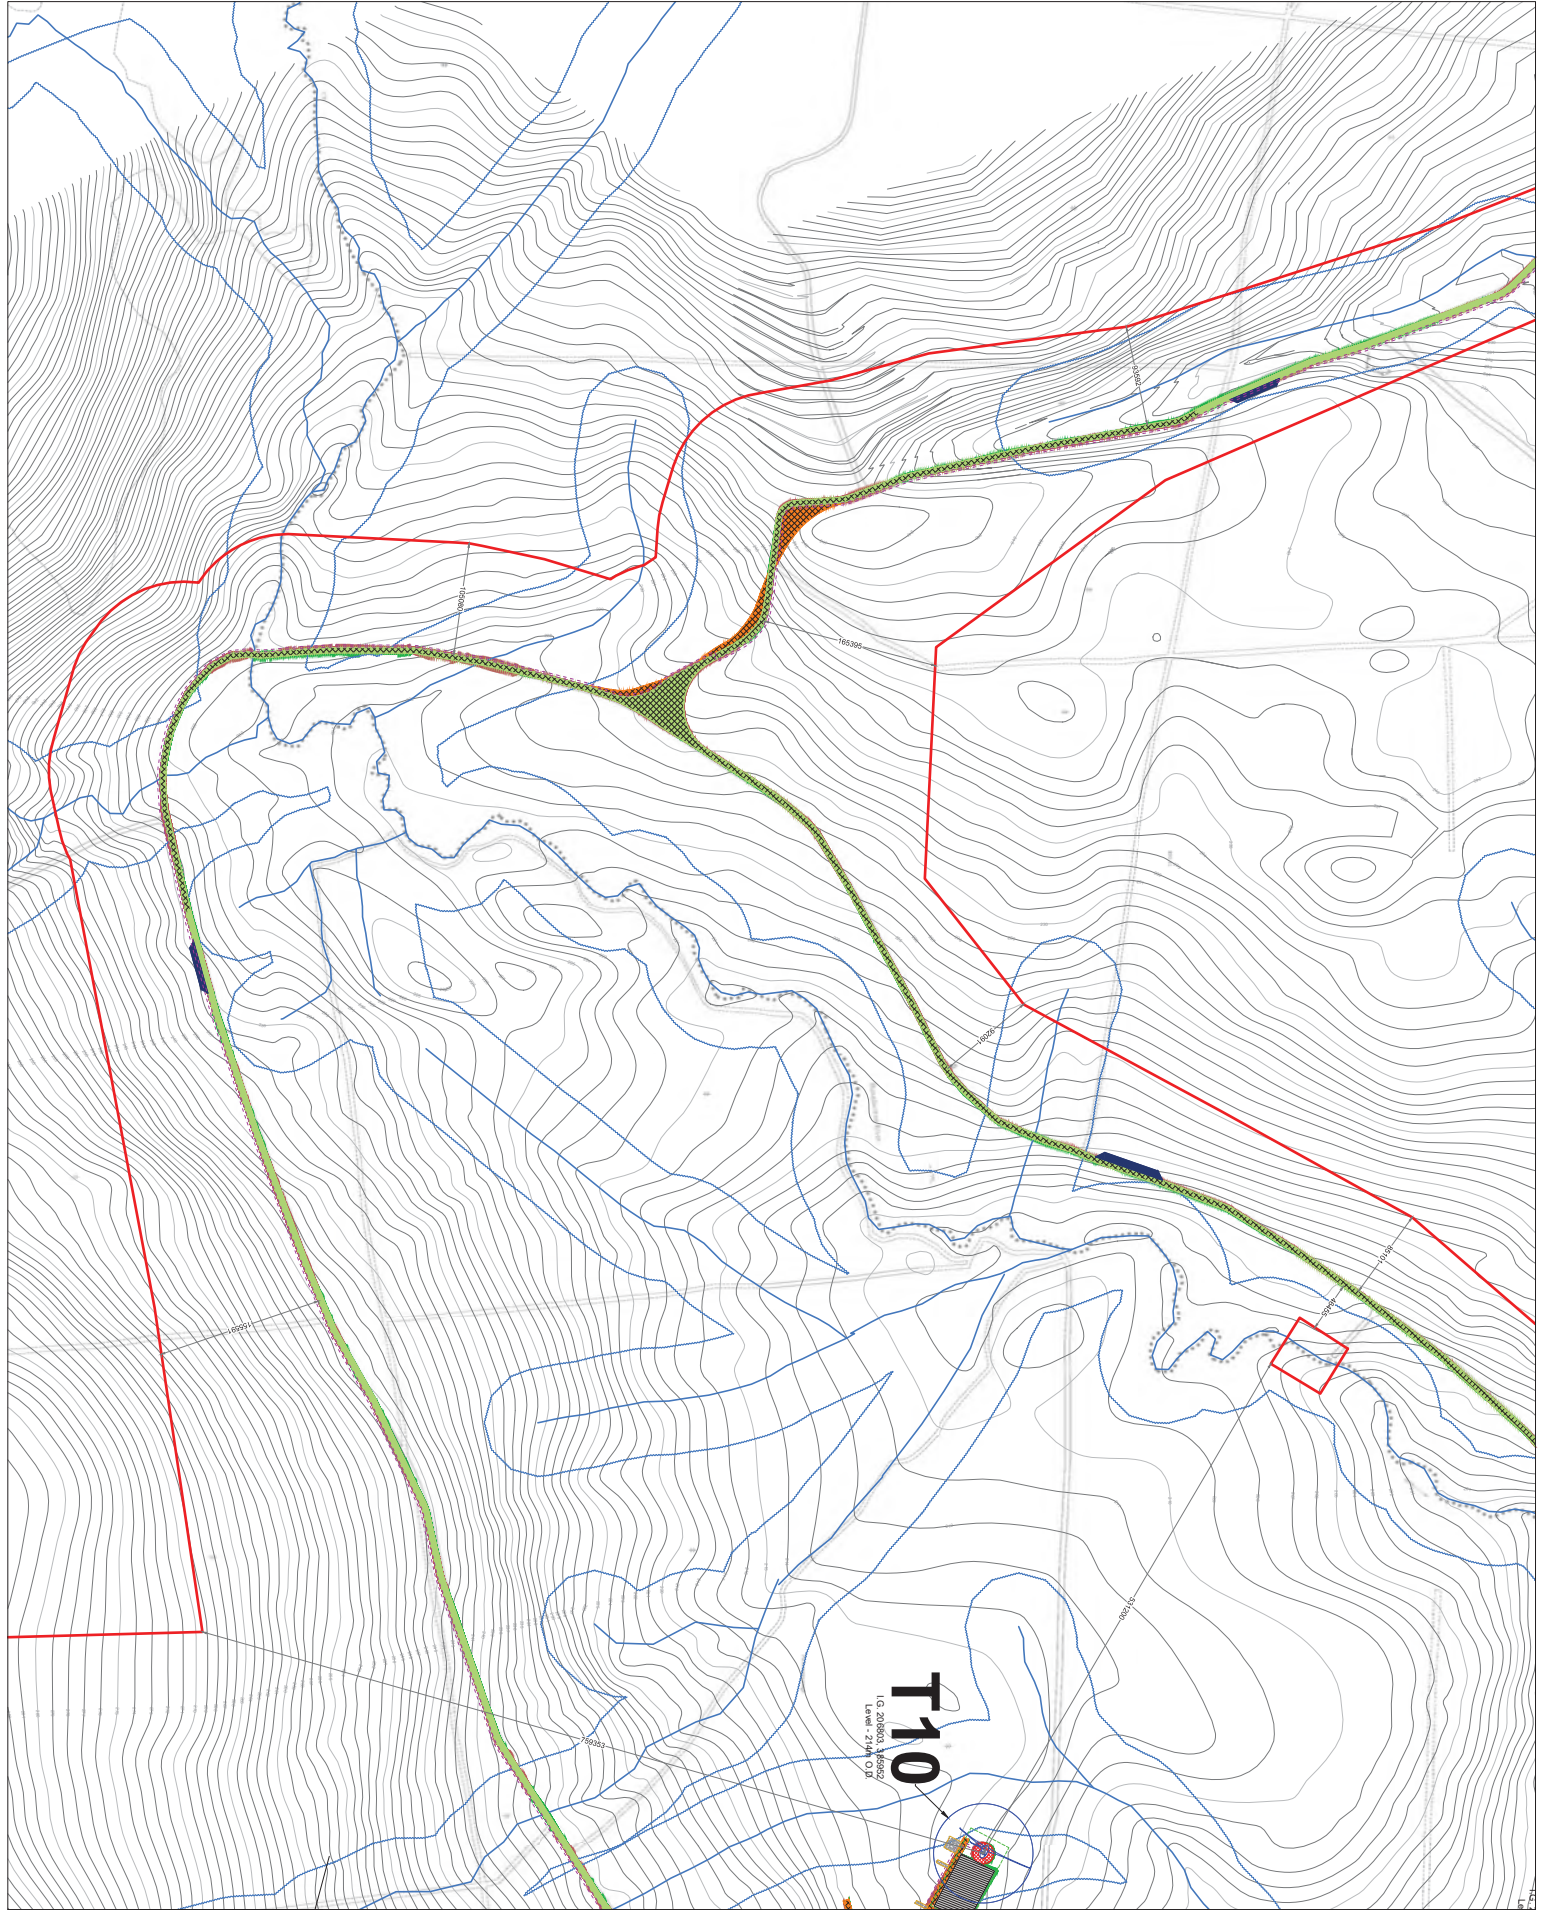

T110
 LG 201803, 180202/
 Volume 2 of 7 (0/1)

- Project Design Drawing Notes**
1. Drawings should not be prepared for specific purposes only.
 2. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior consent of the copyright owner McCarthy Service of Sullivan Ltd.
 3. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior consent of the copyright owner McCarthy Service of Sullivan Ltd. should be taken of this drawing. All dimensions in millimetres unless otherwise stated.
 4. The use of or reliance upon the drawing shall be deemed to be the use of or reliance upon the information contained therein and the drafter and user are responsible for making and checking any and all dimensions and levels that relate to the works.
 5. The use of or reliance upon the drawing shall be deemed to be the use of or reliance upon the information contained therein and the drafter and user are responsible for making and checking any and all dimensions and levels that relate to the works.
 6. The use of or reliance upon the drawing shall be deemed to be the use of or reliance upon the information contained therein and the drafter and user are responsible for making and checking any and all dimensions and levels that relate to the works.
 7. Final levels may vary depending on local ground conditions.
 8. Internal electrical cable trench may be installed on either side of the road.

Drawing Legend

- Planning Application Site Boundary
- Existing Road to be Upgraded
- Existing Footing Road to be Upgraded
- Proposed Road
- Proposed Footing Road
- Internal Electrical Cable Trench
- River/Stream
- River/Stream Open Buffer
- Works Area
- Soft Levelled Area
- Crane Pad Handwashing Area
- Turbine Foundation
- Turbine Sweep Area
- Fill
- Cut
- Passing Bay



Ordnance Survey Ireland Licence No. AR0021817 © Ordnance Survey Ireland/Government of Ireland

**Site Layout Plan
 Sheet 2 of 7**

PROJECT TITLE
 Meenbog Wind Farm, Co. Donegal

DRAWN BY
 Joseph O'Brien

CHECKED BY
 Michail Watson

SCALE
 1:2,500 @ A1

PROJECT NO.
 160502

DATE
 13.12.2017

PROJECT LOCATION
 Block 1, Meenbog Wind Farm, Co. Donegal


DRAWING NO.
 160502-09

DATE
 13.12.2017

McCarthy Service of Sullivan Ltd.
 Planning & Environmental Consultants
 Block 1, Meenbog Wind Farm, Co. Donegal
 Meenbog Wind Farm, Co. Donegal
 Galway, Ireland
 email: info@mcshill.com
 Tel: +353 91 738541
 Fax: +353 91 771279

Project Design Drawing Notes

1. Drawings are for planning application purposes only.
2. All dimensions are to be taken from the proposed construction coordinates.
3. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the express written consent of McCarthy Keville O'Sullivan Ltd.
4. The use of any copyright material without the express written consent of McCarthy Keville O'Sullivan Ltd. should be taken of this drawing. All dimensions in millimetres unless otherwise stated.
5. All dimensions to be taken to the centre of the turbine tower and are responsible for taking and checking any and all dimensions and levels that relate to the works.
6. The use of or reliance upon the drawing shall be deemed to be a warranty, such written agreement to be sought from and issued by the copyright holder to the user or reliance upon this drawing.
7. Levels shown upon turbine tower diameter are per turbine drawing.
8. Final levels may vary depending on local ground conditions.
9. Internal electrical cable trench may be installed on either side of site roads.

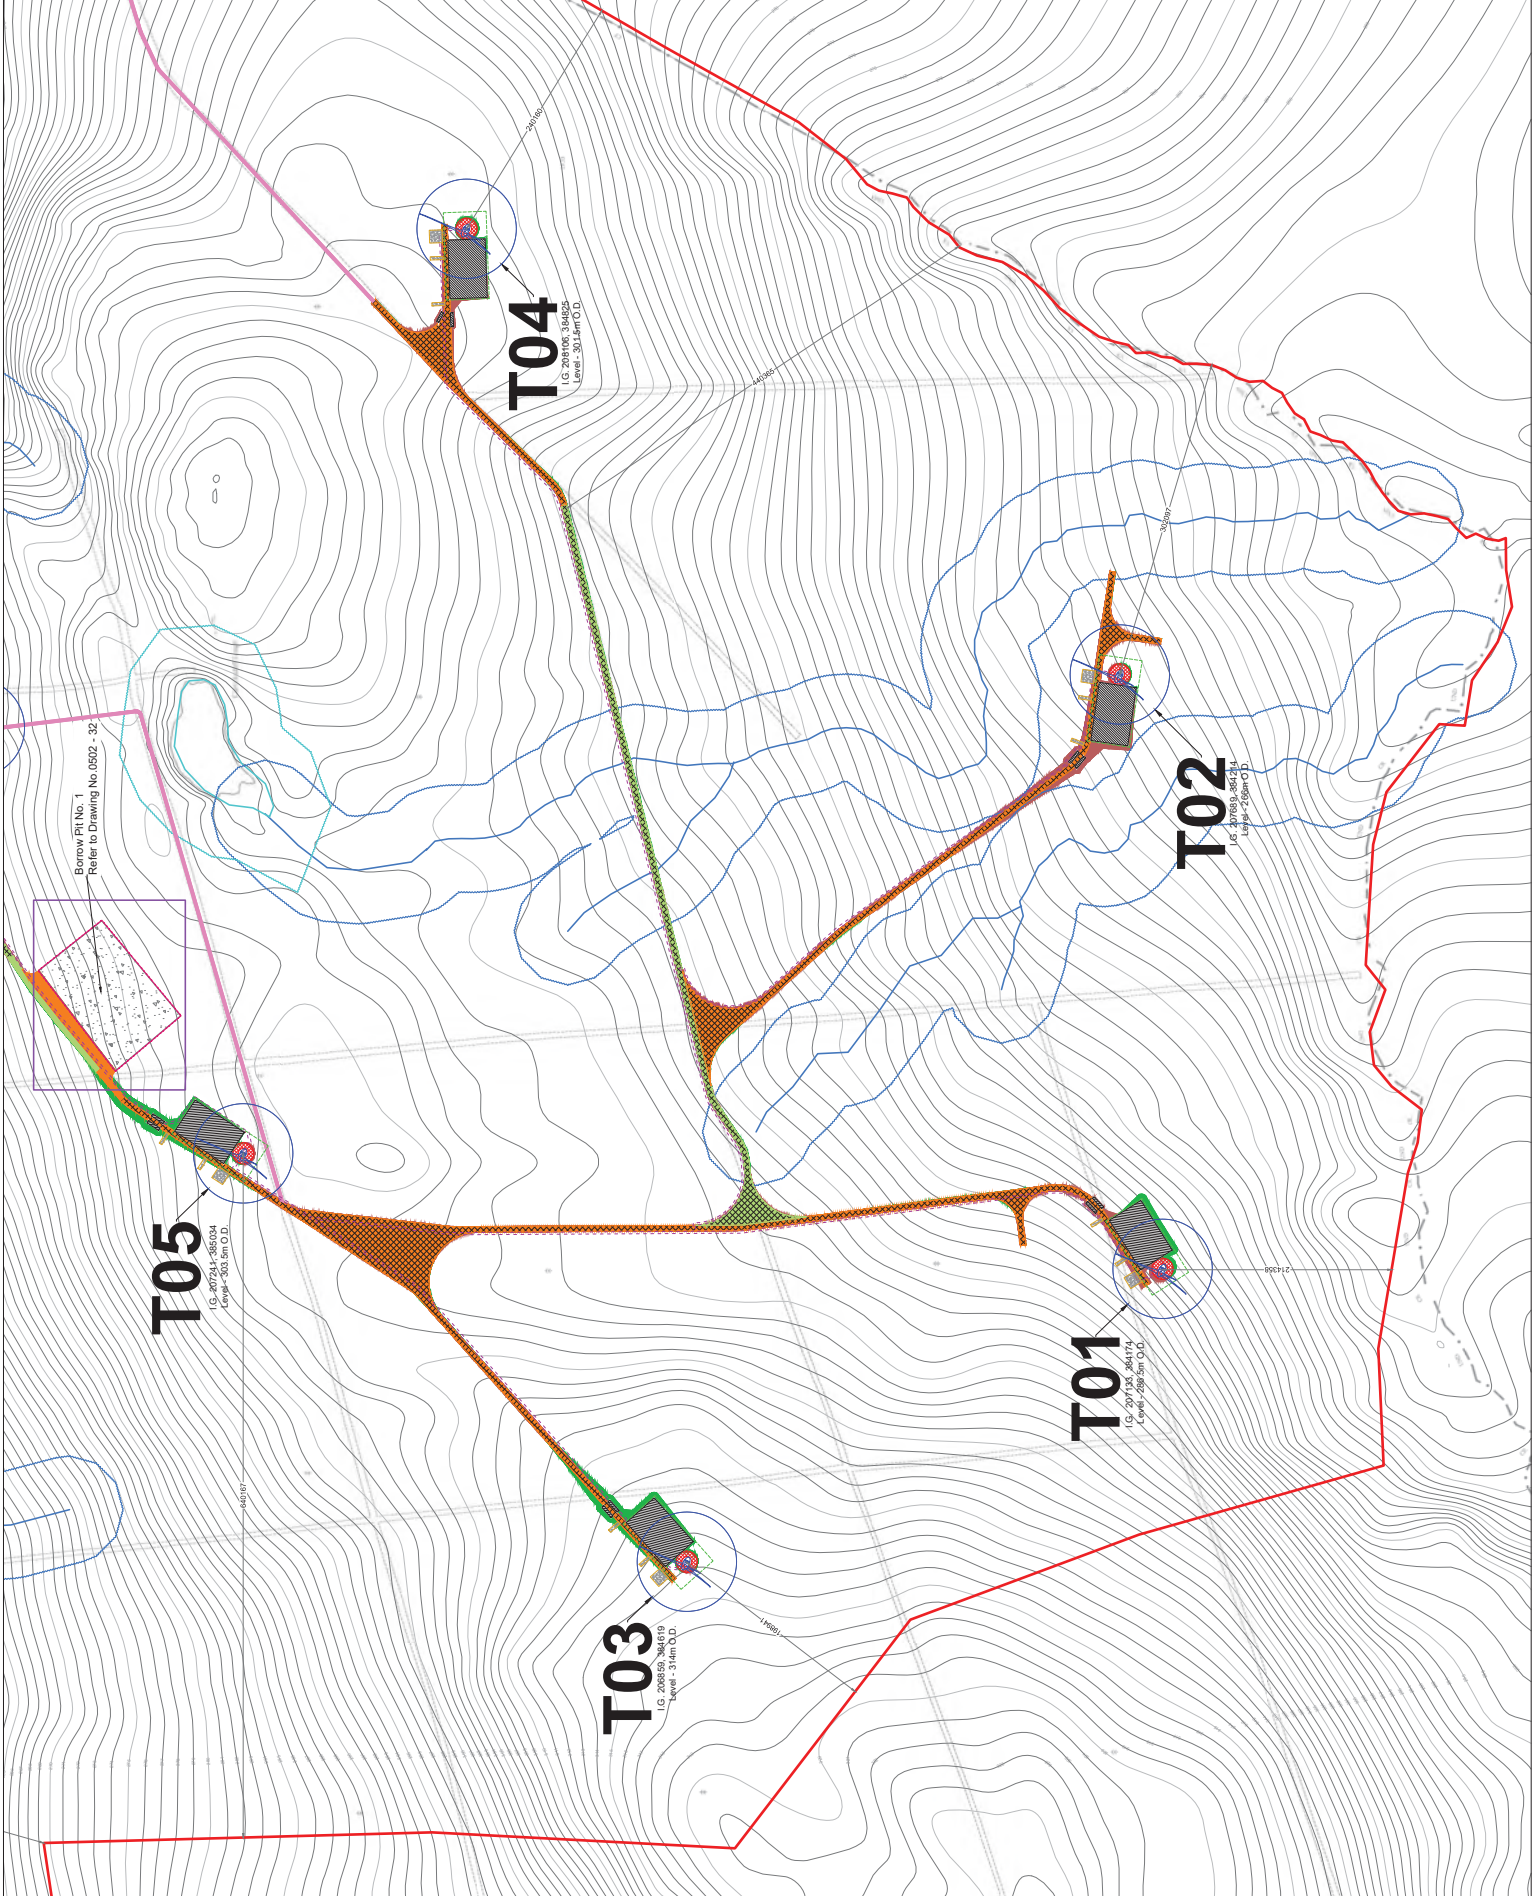

Drawing Legend

- Planning Application Site Boundary
- Existing Road to be Upgraded
- Proposed Road
- Internal Electrical Cable Trench
- River/Stream
- River/Stream 50m Buffer
- Lakes
- Lakes 50m Buffer
- Works Area
- Soft Levelled Area
- Crane Pad Headstaying Area
- Turbine Foundation
- Turbine Sweep Area
- Borrow Pit
- Cut
- Fill
- Proposed Amenity Track



**Site Layout Plan
Sheet 3 of 7**

DRAWING TITLE
Meerbog Wind Farm, Co. Donegal

PROJECT TITLE
Meerbog Wind Farm, Co. Donegal

DESIGNED BY
Michael Watson

DRAWN BY
Joseph O'Brien

PROJECT NO.
0502 - 10


SCALE
1:2,500 @ A1

DATE
13.12.2017

CHECKED BY
Michael Watson

DATE
13.12.2017

McCarthy Keville O'Sullivan Ltd.
Planning & Environmental Consultants
Block 1, Financial Services Centre,
Menaghassagh Road,
Galway, Ireland.
email: info@coarthyos.ie
www.coarthyos.ie
Tel: +353 91 735611
Fax: +353 91 771779

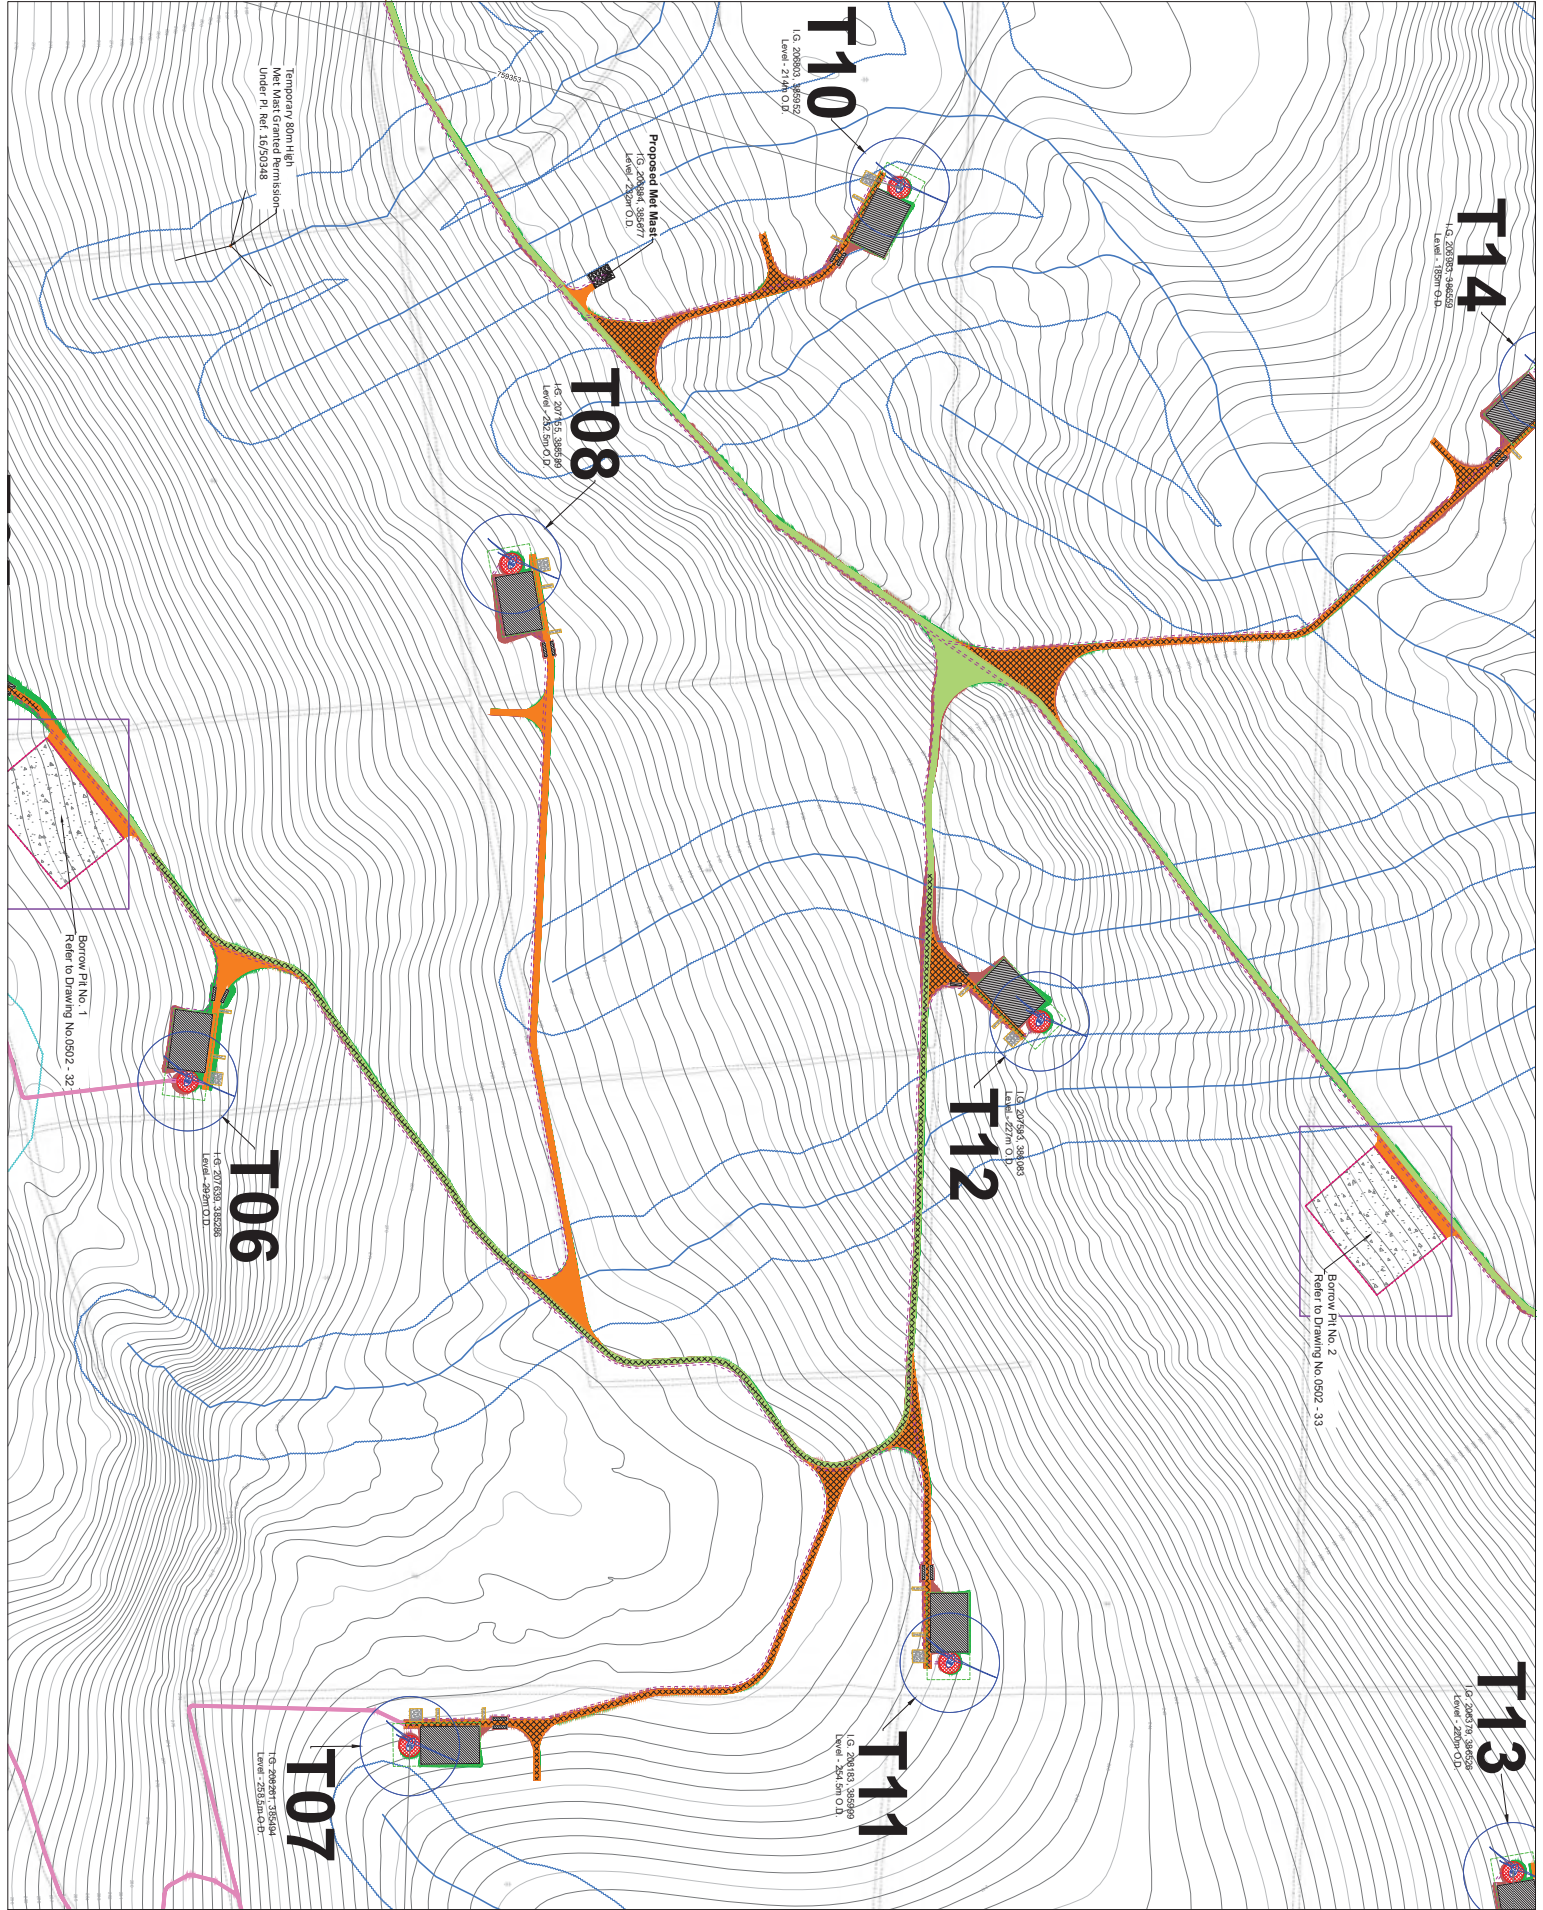

Plotted Design Drawings Notes

1. Drawings issued are for planning application purposes only.
2. All dimensions are in metres unless otherwise stated.
3. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior consent of the copyright owner McCarthy O'Sullivan Ltd. Any reproduction without the prior consent of McCarthy O'Sullivan Ltd. should be taken at the drafter's risk. All dimensions in millimetres unless otherwise stated.
4. The use of reference symbols on drawings shall be deemed to be the use of the same as on the drawings of the same project and the drafter and any other person responsible for making and checking any and all drawings shall be deemed to be responsible for ensuring that the dimensions and levels that relate to the works.
5. The use of reference symbols on drawings shall be deemed to be the use of the same as on the drawings of the same project and the drafter and any other person responsible for making and checking any and all drawings shall be deemed to be responsible for ensuring that the dimensions and levels that relate to the works.
6. The use of reference symbols on drawings shall be deemed to be the use of the same as on the drawings of the same project and the drafter and any other person responsible for making and checking any and all drawings shall be deemed to be responsible for ensuring that the dimensions and levels that relate to the works.
7. Final levels may vary depending on local ground conditions.
8. Internal electrical cable trench may be installed on either side of the roads.

Drawing Legend

	Planning Application Site Boundary
	Existing Road to be Upgraded
	Existing Finishing Road to be Upgraded
	Proposed Road
	Proposed Finishing Road
	Internal Electrical Cable Trench
	River/Stream
	River/Stream 50m Buffer
	Works Area
	Soft Levelled Area
	Caree Pad Handwashing Area
	Turbine Foundation
	Turbine Sweeep Area
	Borrow Pit
	Fill
	Cut
	Proposed Armey Track

Site Layout Plan
Sheet 4 of 7

ORDNANCE SURVEY IRELAND LICENCE NO. AR0021817 © ORDNANCE SURVEY IRELAND/GOVERNMENT OF IRELAND

PROJECT TITLE: Meenbog Wind Farm, Co. Donegal

DRAWN BY: Joseph O'Brien

CHECKED BY: Michael Wilson

PROJECT NO.: 160502


DRAWING NO.: 0502 - 11

SCALE: 1:2,500 @ A1

DATE: 13.12.2017

CLIENT: McCarthy O'Sullivan

ADDRESS: McCarthy O'Sullivan Ltd.
Planning & Environmental Consultants
Block 1, Industrial Services Centre,
Moneenagh Road,
Galway, Ireland.
email: info@mcosullivan.ie
Tel: +353 91 736541
Fax: +353 91 717179

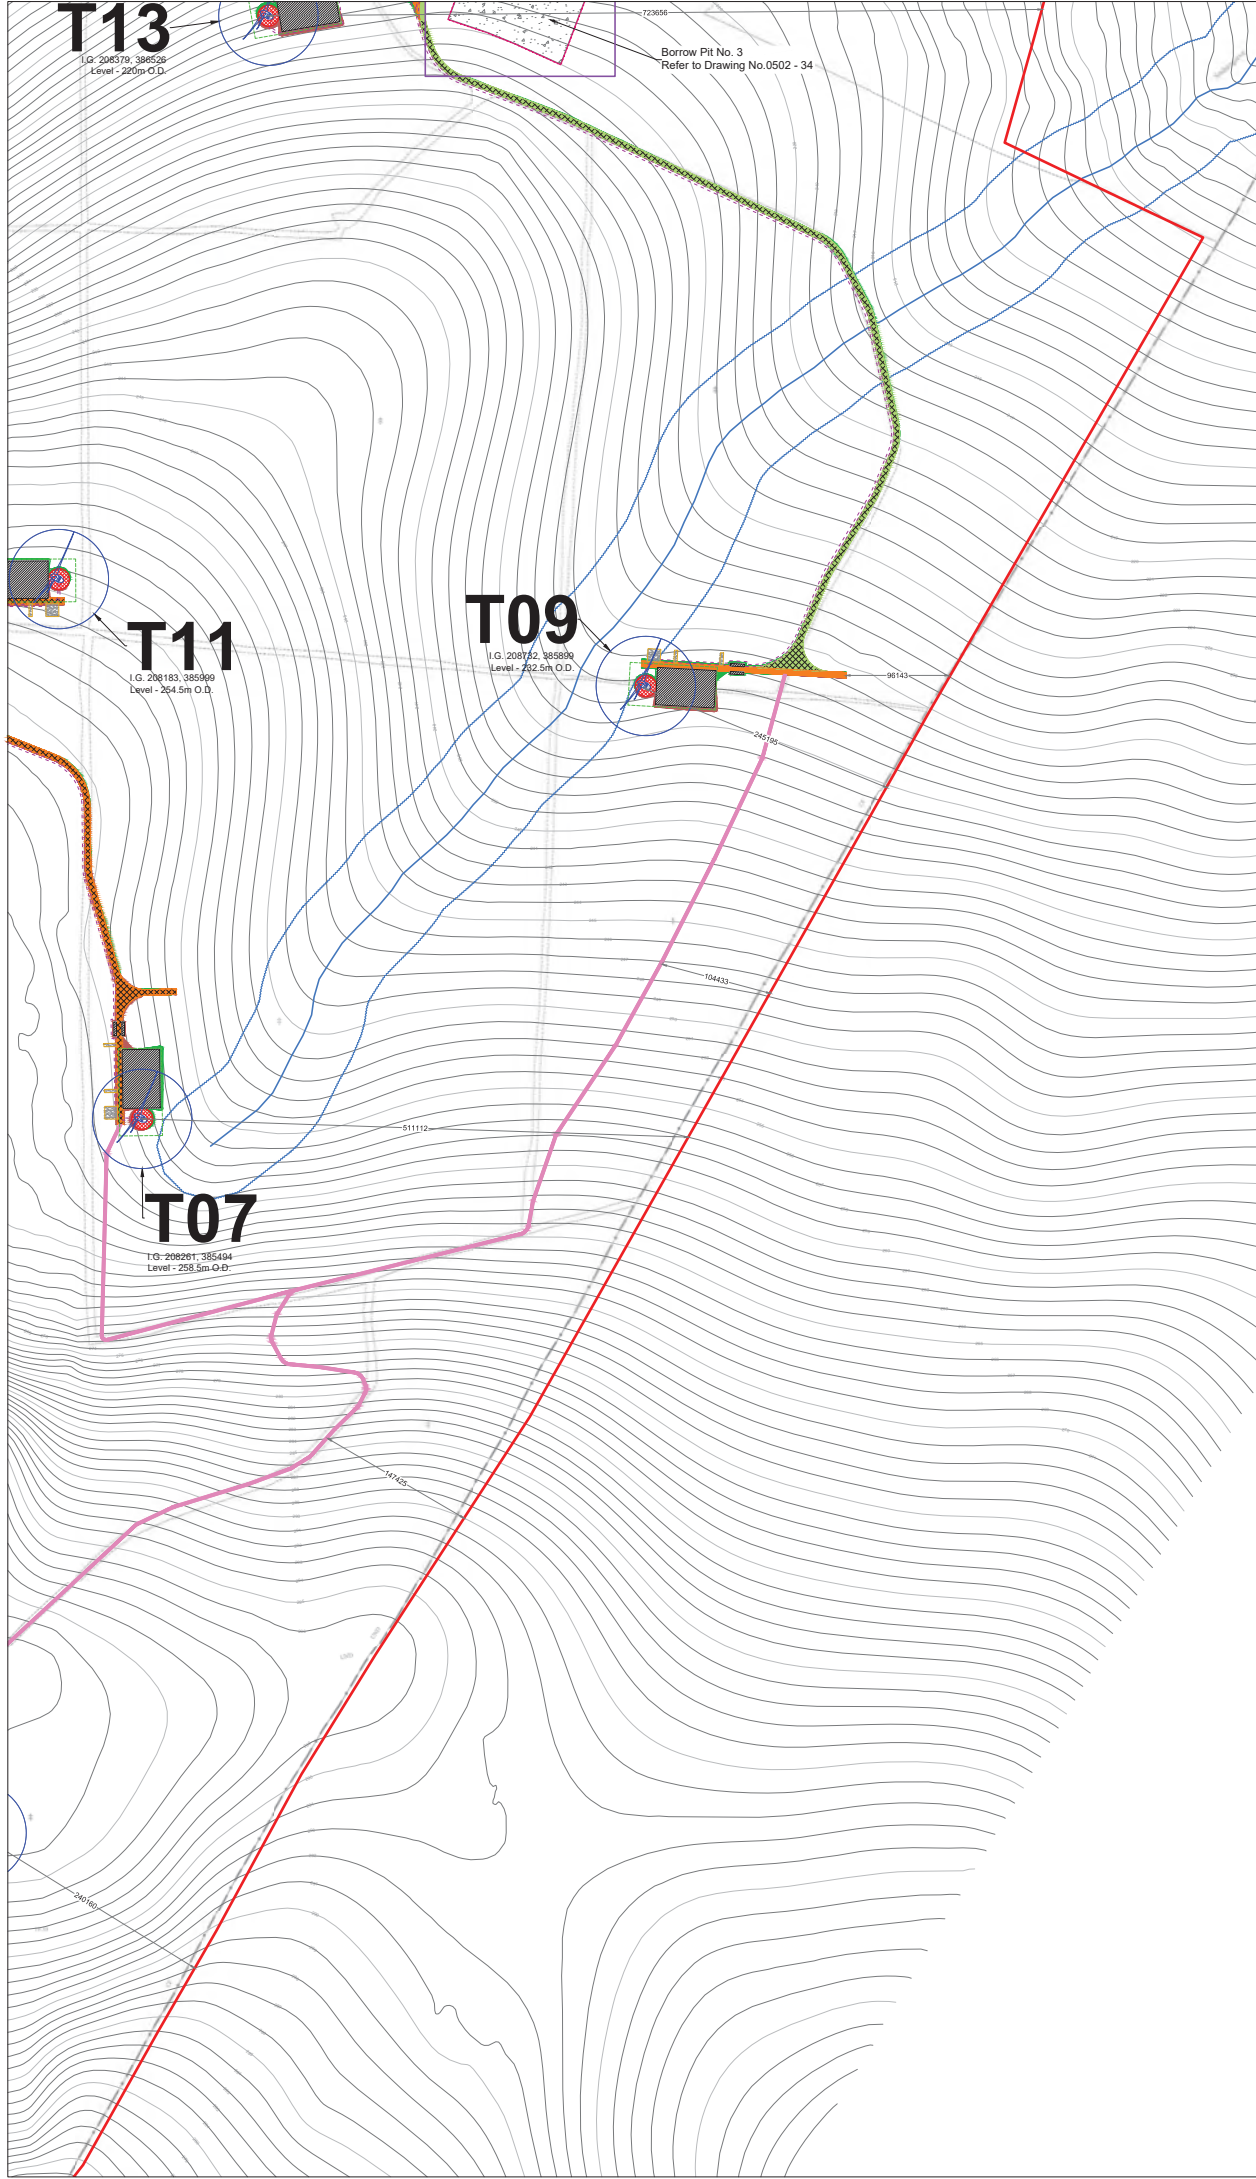

Borrow Pit No. 3
Refer to Drawing No.0502 - 34

Project Design Drawing Notes
 1. Drawings issued are for planning application purposes only.
 2. Drawings not to be used for construction/contract conditions.
 3. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior notice of the copyright owner McCarthy Keville O'Sullivan Ltd.
 4. Do not scale off this drawing. Figured metric dimensions only should be taken off this drawing. All dimensions in millimeters unless otherwise stated.
 5. All contractors, whether main or sub-contractors, must visit the site and are responsible for taking and checking any and all dimensions and levels that relate to the works.
 6. The use of or reliance upon this drawing shall be deemed to be acceptance of these conditions of use unless otherwise agreed in writing, such written agreement to be sought from and issued by the copyright holder to the use or reliance upon this drawing.
 7. Layout plans show typical Turbine rotor diameter as per turbine drawing.
 8. Final levels may vary depending on local ground conditions.
 9. Internal electrical cable trench may be installed on either side of site roads.

Drawing Legend


- Planning Application Site Boundary
- Existing Floating Road to be Upgraded
- Proposed Road
- Proposed Floating Road
- Internal Electrical Cable Trench
- River/Stream
- River/Stream 50m Buffer
- Works Area
- Soft Levelled Area
- Crane Pad Hardstanding Area
- Turbine Foundation
- Turbine Sweep Area
- Cut
- Fill

**Site Layout Plan
Sheet 5 of 7**

PROJECT TITLE:
Meenbog Wind Farm, Co. Donegal

DRAWING BY: Joseph O'Brien	CHECKED BY: Michael Watson
PROJECT NO: T60502	DRAWING NO: 0502 - 12
SCALE: 1:2,500 @ A1	DATE: 13.12.2017

OS SHEET No. 9027 0000, 9099 0000, 9101 0000, 9102 0000, 9103 0000, 9104 0000, 9105 0000, 9106 0000, 9107 0000, 9108 0000, 9109 0000, 9110 0000, 9111 0000, 9112 0000, 9113 0000, 9114 0000, 9115 0000, 9116 0000, 9117 0000, 9118 0000, 9119 0000, 9120 0000, 9121 0000, 9122 0000, 9123 0000, 9124 0000, 9125 0000, 9126 0000, 9127 0000, 9128 0000, 9129 0000, 9130 0000, 9131 0000, 9132 0000, 9133 0000, 9134 0000, 9135 0000, 9136 0000, 9137 0000, 9138 0000, 9139 0000, 9140 0000, 9141 0000, 9142 0000, 9143 0000, 9144 0000, 9145 0000, 9146 0000, 9147 0000, 9148 0000, 9149 0000, 9150 0000, 9151 0000, 9152 0000, 9153 0000, 9154 0000, 9155 0000, 9156 0000, 9157 0000, 9158 0000, 9159 0000, 9160 0000, 9161 0000, 9162 0000, 9163 0000, 9164 0000, 9165 0000, 9166 0000, 9167 0000, 9168 0000, 9169 0000, 9170 0000, 9171 0000, 9172 0000, 9173 0000, 9174 0000, 9175 0000, 9176 0000, 9177 0000, 9178 0000, 9179 0000, 9180 0000, 9181 0000, 9182 0000, 9183 0000, 9184 0000, 9185 0000, 9186 0000, 9187 0000, 9188 0000, 9189 0000, 9190 0000, 9191 0000, 9192 0000, 9193 0000, 9194 0000, 9195 0000, 9196 0000, 9197 0000, 9198 0000, 9199 0000, 9200 0000, 9201 0000, 9202 0000, 9203 0000, 9204 0000, 9205 0000, 9206 0000, 9207 0000, 9208 0000, 9209 0000, 9210 0000, 9211 0000, 9212 0000, 9213 0000, 9214 0000, 9215 0000, 9216 0000, 9217 0000, 9218 0000, 9219 0000, 9220 0000, 9221 0000, 9222 0000, 9223 0000, 9224 0000, 9225 0000, 9226 0000, 9227 0000, 9228 0000, 9229 0000, 9230 0000, 9231 0000, 9232 0000, 9233 0000, 9234 0000, 9235 0000, 9236 0000, 9237 0000, 9238 0000, 9239 0000, 9240 0000, 9241 0000, 9242 0000, 9243 0000, 9244 0000, 9245 0000, 9246 0000, 9247 0000, 9248 0000, 9249 0000, 9250 0000, 9251 0000, 9252 0000, 9253 0000, 9254 0000, 9255 0000, 9256 0000, 9257 0000, 9258 0000, 9259 0000, 9260 0000, 9261 0000, 9262 0000, 9263 0000, 9264 0000, 9265 0000, 9266 0000, 9267 0000, 9268 0000, 9269 0000, 9270 0000, 9271 0000, 9272 0000, 9273 0000, 9274 0000, 9275 0000, 9276 0000, 9277 0000, 9278 0000, 9279 0000, 9280 0000, 9281 0000, 9282 0000, 9283 0000, 9284 0000, 9285 0000, 9286 0000, 9287 0000, 9288 0000, 9289 0000, 9290 0000, 9291 0000, 9292 0000, 9293 0000, 9294 0000, 9295 0000, 9296 0000, 9297 0000, 9298 0000, 9299 0000, 9300 0000, 9301 0000, 9302 0000, 9303 0000, 9304 0000, 9305 0000, 9306 0000, 9307 0000, 9308 0000, 9309 0000, 9310 0000, 9311 0000, 9312 0000, 9313 0000, 9314 0000, 9315 0000, 9316 0000, 9317 0000, 9318 0000, 9319 0000, 9320 0000, 9321 0000, 9322 0000, 9323 0000, 9324 0000, 9325 0000, 9326 0000, 9327 0000, 9328 0000, 9329 0000, 9330 0000, 9331 0000, 9332 0000, 9333 0000, 9334 0000, 9335 0000, 9336 0000, 9337 0000, 9338 0000, 9339 0000, 9340 0000, 9341 0000, 9342 0000, 9343 0000, 9344 0000, 9345 0000, 9346 0000, 9347 0000, 9348 0000, 9349 0000, 9350 0000, 9351 0000, 9352 0000, 9353 0000, 9354 0000, 9355 0000, 9356 0000, 9357 0000, 9358 0000, 9359 0000, 9360 0000, 9361 0000, 9362 0000, 9363 0000, 9364 0000, 9365 0000, 9366 0000, 9367 0000, 9368 0000, 9369 0000, 9370 0000, 9371 0000, 9372 0000, 9373 0000, 9374 0000, 9375 0000, 9376 0000, 9377 0000, 9378 0000, 9379 0000, 9380 0000, 9381 0000, 9382 0000, 9383 0000, 9384 0000, 9385 0000, 9386 0000, 9387 0000, 9388 0000, 9389 0000, 9390 0000, 9391 0000, 9392 0000, 9393 0000, 9394 0000, 9395 0000, 9396 0000, 9397 0000, 9398 0000, 9399 0000, 9400 0000, 9401 0000, 9402 0000, 9403 0000, 9404 0000, 9405 0000, 9406 0000, 9407 0000, 9408 0000, 9409 0000, 9410 0000, 9411 0000, 9412 0000, 9413 0000, 9414 0000, 9415 0000, 9416 0000, 9417 0000, 9418 0000, 9419 0000, 9420 0000, 9421 0000, 9422 0000, 9423 0000, 9424 0000, 9425 0000, 9426 0000, 9427 0000, 9428 0000, 9429 0000, 9430 0000, 9431 0000, 9432 0000, 9433 0000, 9434 0000, 9435 0000, 9436 0000, 9437 0000, 9438 0000, 9439 0000, 9440 0000, 9441 0000, 9442 0000, 9443 0000, 9444 0000, 9445 0000, 9446 0000, 9447 0000, 9448 0000, 9449 0000, 9450 0000, 9451 0000, 9452 0000, 9453 0000, 9454 0000, 9455 0000, 9456 0000, 9457 0000, 9458 0000, 9459 0000, 9460 0000, 9461 0000, 9462 0000, 9463 0000, 9464 0000, 9465 0000, 9466 0000, 9467 0000, 9468 0000, 9469 0000, 9470 0000, 9471 0000, 9472 0000, 9473 0000, 9474 0000, 9475 0000, 9476 0000, 9477 0000, 9478 0000, 9479 0000, 9480 0000, 9481 0000, 9482 0000, 9483 0000, 9484 0000, 9485 0000, 9486 0000, 9487 0000, 9488 0000, 9489 0000, 9490 0000, 9491 0000, 9492 0000, 9493 0000, 9494 0000, 9495 0000, 9496 0000, 9497 0000, 9498 0000, 9499 0000, 9500 0000, 9501 0000, 9502 0000, 9503 0000, 9504 0000, 9505 0000, 9506 0000, 9507 0000, 9508 0000, 9509 0000, 9510 0000, 9511 0000, 9512 0000, 9513 0000, 9514 0000, 9515 0000, 9516 0000, 9517 0000, 9518 0000, 9519 0000, 9520 0000, 9521 0000, 9522 0000, 9523 0000, 9524 0000, 9525 0000, 9526 0000, 9527 0000, 9528 0000, 9529 0000, 9530 0000, 9531 0000, 9532 0000, 9533 0000, 9534 0000, 9535 0000, 9536 0000, 9537 0000, 9538 0000, 9539 0000, 9540 0000, 9541 0000, 9542 0000, 9543 0000, 9544 0000, 9545 0000, 9546 0000, 9547 0000, 9548 0000, 9549 0000, 9550 0000, 9551 0000, 9552 0000, 9553 0000, 9554 0000, 9555 0000, 9556 0000, 9557 0000, 9558 0000, 9559 0000, 9560 0000, 9561 0000, 9562 0000, 9563 0000, 9564 0000, 9565 0000, 9566 0000, 9567 0000, 9568 0000, 9569 0000, 9570 0000, 9571 0000, 9572 0000, 9573 0000, 9574 0000, 9575 0000, 9576 0000, 9577 0000, 9578 0000, 9579 0000, 9580 0000, 9581 0000, 9582 0000, 9583 0000, 9584 0000, 9585 0000, 9586 0000, 9587 0000, 9588 0000, 9589 0000, 9590 0000, 9591 0000, 9592 0000, 9593 0000, 9594 0000, 9595 0000, 9596 0000, 9597 0000, 9598 0000, 9599 0000, 9600 0000, 9601 0000, 9602 0000, 9603 0000, 9604 0000, 9605 0000, 9606 0000, 9607 0000, 9608 0000, 9609 0000, 9610 0000, 9611 0000, 9612 0000, 9613 0000, 9614 0000, 9615 0000, 9616 0000, 9617 0000, 9618 0000, 9619 0000, 9620 0000, 9621 0000, 9622 0000, 9623 0000, 9624 0000, 9625 0000, 9626 0000, 9627 0000, 9628 0000, 9629 0000, 9630 0000, 9631 0000, 9632 0000, 9633 0000, 9634 0000, 9635 0000, 9636 0000, 9637 0000, 9638 0000, 9639 0000, 9640 0000, 9641 0000, 9642 0000, 9643 0000, 9644 0000, 9645 0000, 9646 0000, 9647 0000, 9648 0000, 9649 0000, 9650 0000, 9651 0000, 9652 0000, 9653 0000, 9654 0000, 9655 0000, 9656 0000, 9657 0000, 9658 0000, 9659 0000, 9660 0000, 9661 0000, 9662 0000, 9663 0000, 9664 0000, 9665 0000, 9666 0000, 9667 0000, 9668 0000, 9669 0000, 9670 0000, 9671 0000, 9672 0000, 9673 0000, 9674 0000, 9675 0000, 9676 0000, 9677 0000, 9678 0000, 9679 0000, 9680 0000, 9681 0000, 9682 0000, 9683 0000, 9684 0000, 9685 0000, 9686 0000, 9687 0000, 9688 0000, 9689 0000, 9690 0000, 9691 0000, 9692 0000, 9693 0000, 9694 0000, 9695 0000, 9696 0000, 9697 0000, 9698 0000, 9699 0000, 9700 0000, 9701 0000, 9702 0000, 9703 0000, 9704 0000, 9705 0000, 9706 0000, 9707 0000, 9708 0000, 9709 0000, 9710 0000, 9711 0000, 9712 0000, 9713 0000, 9714 0000, 9715 0000, 9716 0000, 9717 0000, 9718 0000, 9719 0000, 9720 0000, 9721 0000, 9722 0000, 9723 0000, 9724 0000, 9725 0000, 9726 0000, 9727 0000, 9728 0000, 9729 0000, 9730 0000, 9731 0000, 9732 0000, 9733 0000, 9734 0000, 9735 0000, 9736 0000, 9737 0000, 9738 0000, 9739 0000, 9740 0000, 9741 0000, 9742 0000, 9743 0000, 9744 0000, 9745 0000, 9746 0000, 9747 0000, 9748 0000, 9749 0000, 9750 0000, 9751 0000, 9752 0000, 9753 0000, 9754 0000, 9755 0000, 9756 0000, 9757 0000, 9758 0000, 9759 0000, 9760 0000, 9761 0000, 9762 0000, 9763 0000, 9764 0000, 9765 0000, 9766 0000, 9767 0000, 9768 0000, 9769 0000, 9770 0000, 9771 0000, 9772 0000, 9773 0000, 9774 0000, 9775 0000, 9776 0000, 9777 0000, 9778 0000, 9779 0000, 9780 0000, 9781 0000, 9782 0000, 9783 0000, 9784 0000, 9785 0000, 9786 0000, 9787 0000, 9788 0000, 9789 0000, 9790 0000, 9791 0000, 9792 0000, 9793 0000, 9794 0000, 9795 0000, 9796 0000, 9797 0000, 9798 0000, 9799 0000, 9800 0000, 9801 0000, 9802 0000, 9803 0000, 9804 0000, 9805 0000, 9806 0000, 9807 0000, 9808 0000, 9809 0000, 9810 0000, 9811 0000, 9812 0000, 9813 0000, 9814 0000, 9815 0000, 9816 0000, 9817 0000, 9818 0000, 9819 0000, 9820 0000, 9821 0000, 9822 0000, 9823 0000, 9824 0000, 9825 0000, 9826 0000, 9827 0000, 9828 0000, 9829 0000, 9830 0000, 9831 0000, 9832 0000, 9833 0000, 9834 0000, 9835 0000, 9836 0000, 9837 0000, 9838 0000, 9839 0000, 9840 0000, 9841 0000, 9842 0000, 9843 0000, 9844 0000, 9845 0000, 9846 0000, 9847 0000, 9848 0000, 9849 0000, 9850 0000, 9851 0000, 9852 0000, 9853 0000, 9854 0000, 9855 0000, 9856 0000, 9857 0000, 9858 0000, 9859 0000, 9860 0000, 9861 0000, 9862 0000, 9863 0000, 9864 0000, 9865 0000, 9866 0000, 9867 0000, 9868 0000, 9869 0000, 9870 0000, 9871 0000, 9872 0000, 9873 0000, 9874 0000, 9875 0000, 9876 0000, 9877 0000, 9878 0000, 9879 0000, 9880 0000, 9881 0000, 9882 0000, 9883 0000, 9884 0000, 9885 0000, 9886 0000, 9887 0000, 9888 0000, 9889 0000, 9890 0000, 9891 0000, 9892 0000, 9893 0000, 9894 0000, 9895 0000, 9896 0000, 9897 0000, 9898 0000, 9899 0000, 9900 0000, 9901 0000, 9902 0000, 9903 0000, 9904 0000, 9905 0000, 9906 0000, 9907 0000, 9908 0000, 9909 0000, 9910 0000, 9911 0000, 9912 0000, 9913 0000, 9914 0000, 9915 0000, 9916 0000, 9917 0000, 9918 0000, 9919 0000, 9920 0000, 9921 0000, 9922 0000, 9923 0000, 9924 0000, 9925 0000, 9926 0000, 9927 0000, 9928 0000, 9929 0000, 9930 0000, 9931 0000, 9932 0000, 9933 0000, 9934 0000, 9935 0000, 9936 0000, 9937 0000, 9938 0000, 9939 0000, 9940 0000, 9941 0000, 9942 0000, 9943 0000, 9944 0000, 9945 0000, 9946 0000, 9947 0000, 9948 0000, 9949 0000, 9950 0000, 9951 0000, 9952 0000, 9953 0000, 9954 0000, 9955 0000, 9956 0000, 9957 0000, 9958 0000, 9959 0000, 9960 0000, 9961 0000, 9962 0000, 9963 0000, 9964 0000, 9965 0000, 9966 0000, 9967 0000, 9968 0000, 9969 0000, 9970 0000, 9971 0000, 9972 0000, 9973 0000, 9974 0000, 9975 0000, 9976 0000, 9977 0000, 9978 0000, 9979 0000, 9980 0000, 9981 0000, 9982 0000, 9983 0000, 9984 0000, 9985 0000, 9986 0000, 9987 0000, 9988 0000, 9989 0000, 9990 0000, 9991 0000, 9992 0000, 9993 0000, 9994 0000, 9995 0000, 9996 0000, 9997 0000, 9998 0000, 9999 0000, 10000 0000, 10001 0000, 10002 0000, 10003 0000, 10004 0000, 10005 0000, 10006 0000, 10007 0000, 10008 0000, 10009 0000, 10010 0000, 10011 0000, 10012 0000, 10013 0000, 10014 0000, 10015 0000, 10016 0000, 10017 0000, 10018 0000, 10019 0000, 10020 0000, 10021 0000, 10022 0000, 10023 0000, 10024 0000, 10025 0000, 10026 0000, 10027 0000, 10028 0000, 10029 0000, 10030 0000, 10031 0000, 10032 0000, 10033 0000, 10034 0000, 10035 0000, 10036 0000, 10037 0000, 10038 0000, 10039 0000, 10040 0000, 10041 0000, 10042 0000, 10043 0000, 10044 0000, 10045 0000, 10046 0000, 10047 0000, 10048 0000, 10049 0000, 10050 0000, 10051 0000, 10052 0000, 10053 0000, 10054 0000, 10055 0000, 10056 0000, 10057 0000, 10058 0000, 10059 0000, 10060 0000, 10061 0000, 10062 0000, 10063 0000, 10064 0000, 10065 0000, 10066 0000, 10067 0000, 10068 0000, 10069 0000, 10070 0000, 10071 0000, 10072 0000, 10073 0000, 10074 0000, 10075 0000, 10076 0000, 10077 0000, 10078 0000, 10079 0000, 10080 0000, 10081 0000, 10082 0000, 10083 0000, 10084 0000, 10085 0000, 10086 0000, 10087 0000, 10088 0000, 10089 0000, 10090 0000, 10091 0000, 10092 0000, 10093 0000, 10094 0000, 10095 0000, 10096 0000, 10097 0000, 10098 0000, 10099 0000, 10100 0000, 10101 0000, 10102 0000, 101

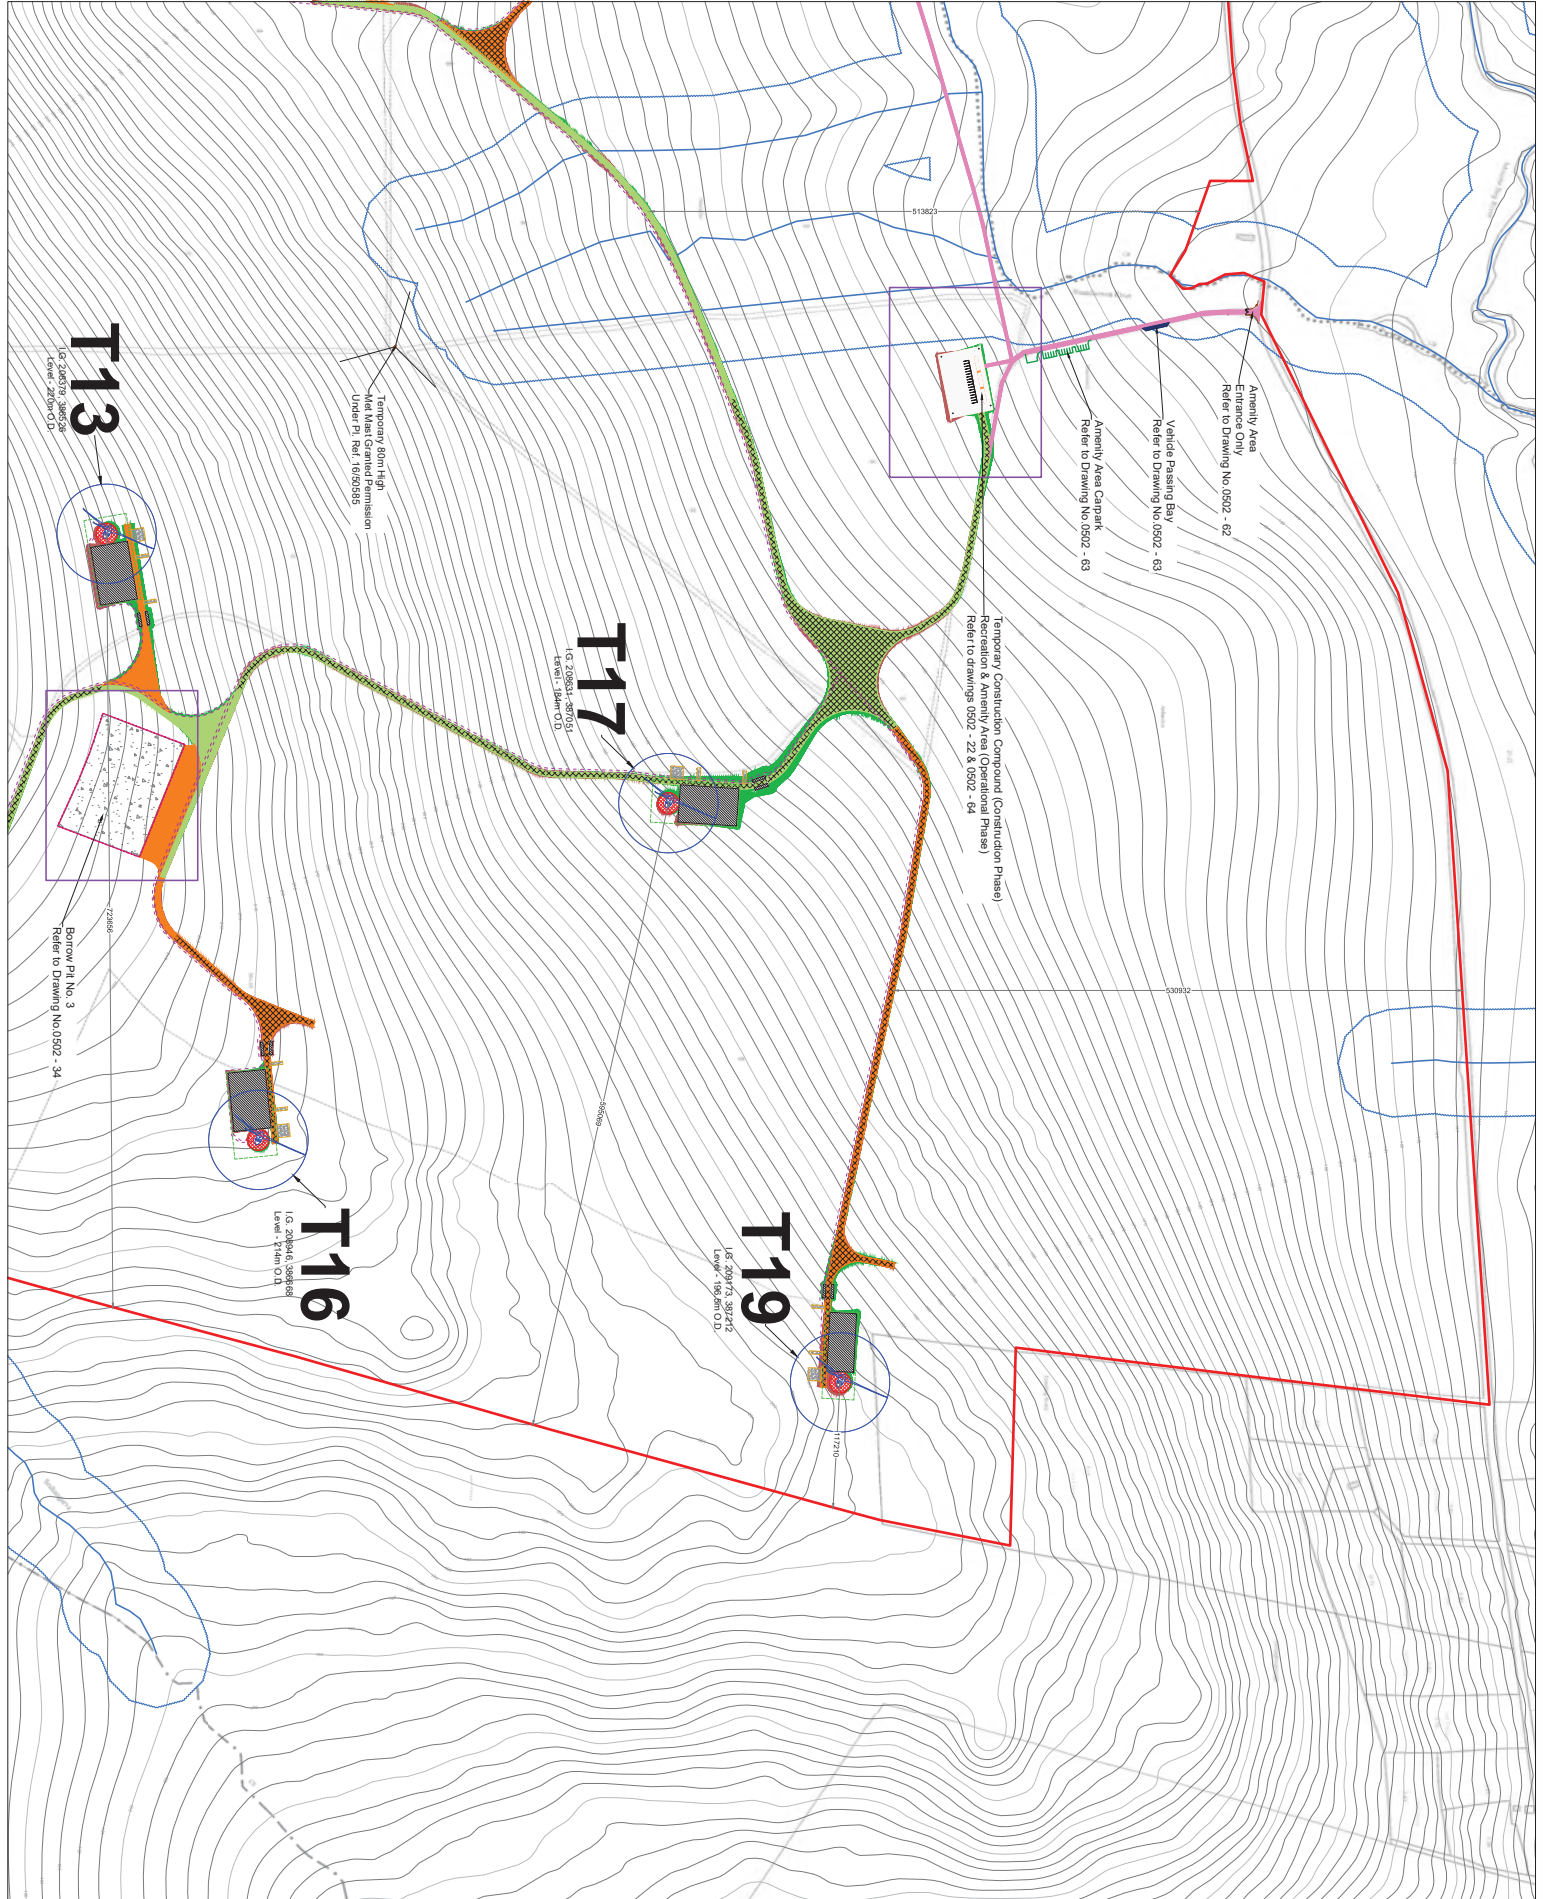

Project Design Drawings Notes

1. Drawings issued are for planning application purposes only.
2. The drawings are not to be used for any other purpose without the written consent of the Designer.
3. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior consent of the copyright owner (McCarthy Keville O'Sullivan Ltd).
4. The drawings are the property of McCarthy Keville O'Sullivan Ltd and should be taken of this drawing. All dimensions in millimetres unless otherwise stated.
5. The use of reference to a drawing shall be deemed to be the use of the drawing as shown on the drawing and not the site and are not responsible for misinterpretation of any and all dimensions and levels that relate to the works.
6. The use of reference to a drawing shall be deemed to be the use of the drawing as shown on the drawing and not the site and are not responsible for misinterpretation of any and all dimensions and levels that relate to the works.
7. The use of reference to a drawing shall be deemed to be the use of the drawing as shown on the drawing and not the site and are not responsible for misinterpretation of any and all dimensions and levels that relate to the works.
8. Final levels may vary depending on local ground conditions.
9. Internal electrical cables which may be installed on either side of the roads.

Drawing Legend

	Planning Application Site Boundary
	Existing Road to be Upgraded
	Existing Footing Road to be Upgraded
	Proposed Road
	Proposed Footing Road
	Internal Electrical Cable Trench
	River/Stream
	River/Stream Gorn Butler
	Works Area
	Soft Levelled Area
	Crane Pad Handstanding Area
	Turbine Foundation
	Turbine Sweep Area
	Borrow Pit
	Cut
	Fill
	Proposed Amenity Track
	Passing Bay

Site Layout Plan Sheet 6 of 7

PROJECT TITLE: Meenbog Wind Farm, Co. Donegal

DESIGNED BY: Joseph O'Brien

CHECKED BY: Michael Wilson

SCALE: 1:2,500 @ A1

DATE: 13.12.2017

PROJECT NO: 160502

DRAWING NO: 0502 - 13

McCarthy Keville O'Sullivan Ltd
 Planning & Environmental Consultants
 Block 1, Riverside Park,
 Galway, Ireland.
 email: info@cmko.ie
 Tel: +353 91 735611
 Fax: +353 91 771279

Ordnance Survey Ireland Licence No. AR0021817 © Ordnance Survey Ireland/Government of Ireland

Project Design Drawing Notes

1. Drawings are for planning application purposes only. They are not to be used for construction purposes.
2. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior written consent of McCarthy Geomatics & Environmental Ltd.
3. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior written consent of McCarthy Geomatics & Environmental Ltd.
4. Dimensions are in millimetres unless otherwise stated.
5. Final levels may vary depending on local ground conditions and are responsible for taking and checking any and all dimensions and levels that relate to the works.
6. The use of or reliance upon the drawing shall be deemed to be a warranty, such written agreement to be sought from and issued by the copyright holder to the use or reliance upon this drawing.
7. Plans show typical turbine rotor diameter as per turbine drawing.
8. Final levels may vary depending on local ground conditions and are responsible for taking and checking any and all dimensions and levels that relate to the works.
9. Internal electrical cable trench may be installed on either side of site roads.

CROAGHONAGH

Drawing Legend

- Planning Application Site Boundary
- Existing Road to be Upgraded
- Existing Floating Road to be Upgraded
- Proposed Road
- Proposed Floating Road
- Internal Electrical Cable Trench
- River/Stream
- River/Stream 50m Buffer
- Works Area
- Soft Levelled Area
- Crane Pad/Handlanding Area
- Turbine Foundation
- Turbine Sweep Area
- Borrow Pit
- Cut
- Fill
- Passing Bay



Site Layout Plan Sheet 7 of 7

PROJECT TITLE: Meerbog Wind Farm, Co. Donegal

DESIGNED BY: Joseph O'Brien

CHECKED BY: Michael Watson

PROJECT NO: 100502


UNIVERSITY NO: 0502 - 14

SCALE: 1:2,500 @ A1


DATE: 13.12.2017

ISSUED FOR: Planning Application


McCarthy Geomatics & Environmental Ltd.
 Block 1, Financial Services Centre,
 Monaghan Road,
 Galway, Ireland.
 email: info@mcgeoenv.ie
 Tel: +353 91 735611
 Fax: +353 91 771729

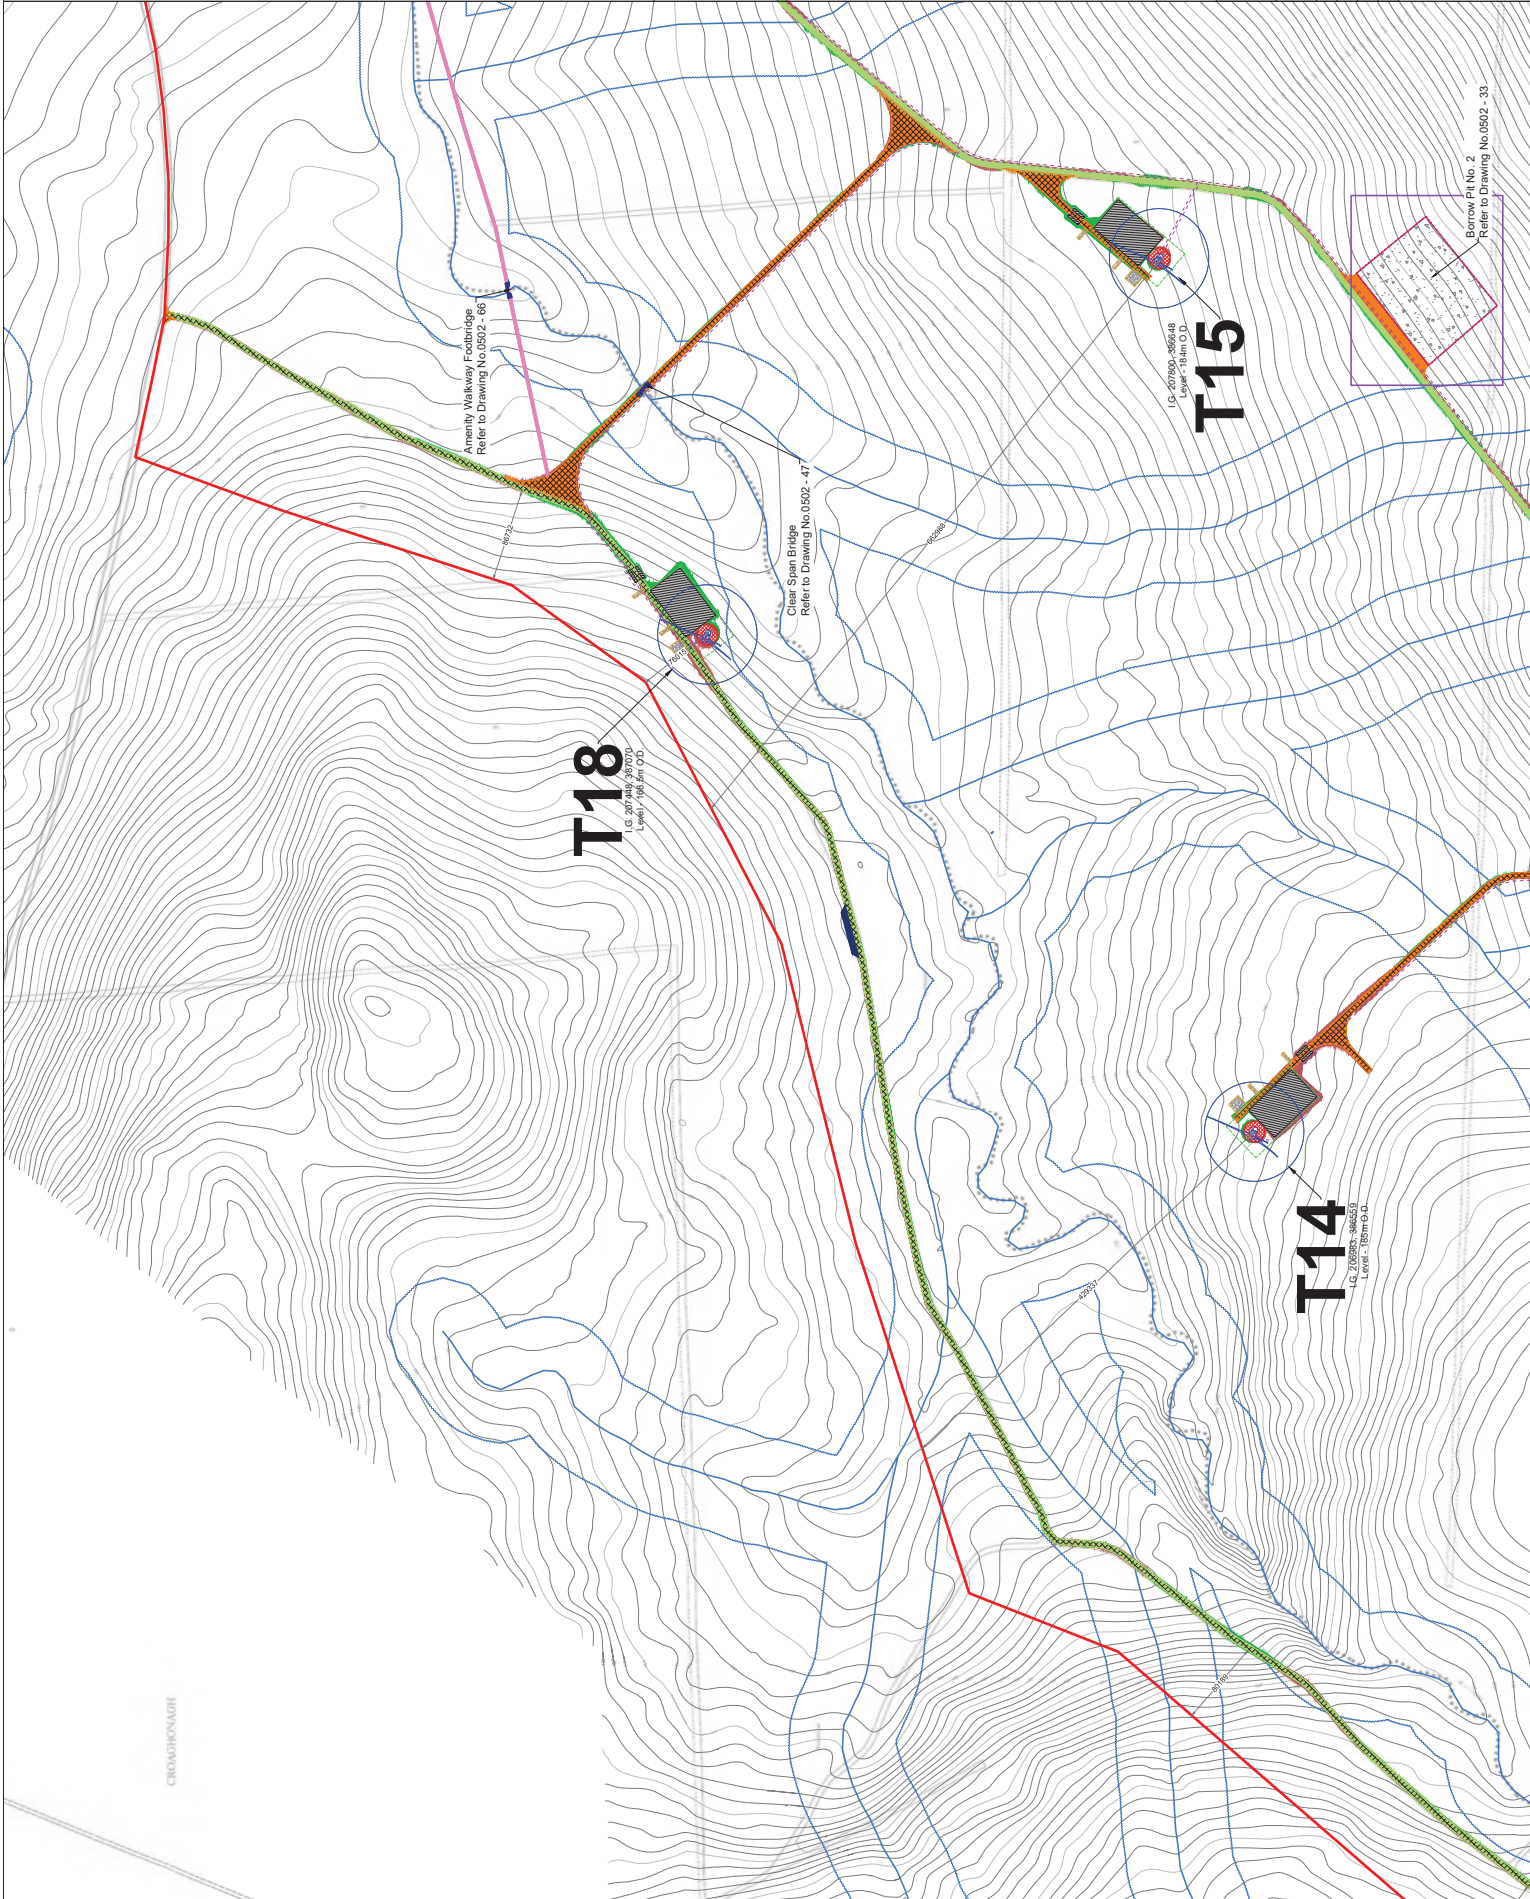

Borrow Pit No. 2
 Refer to Drawing No.0502 - 33

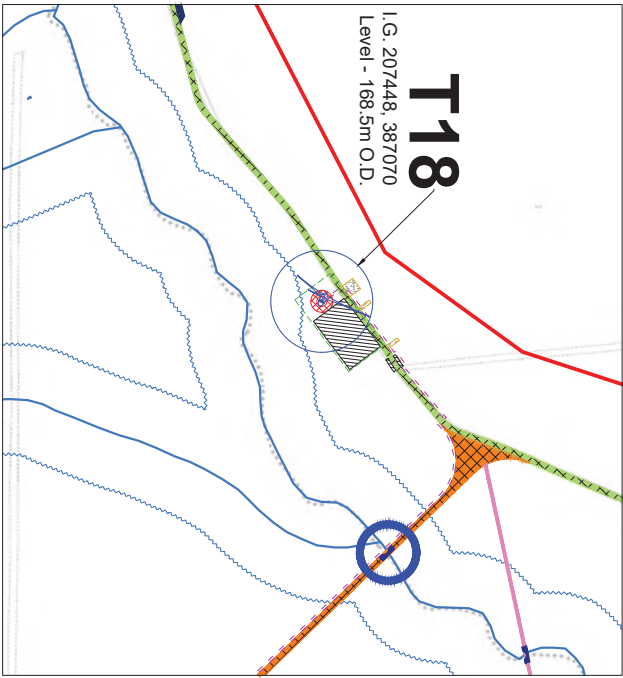

1:5,000 Location on Context Map

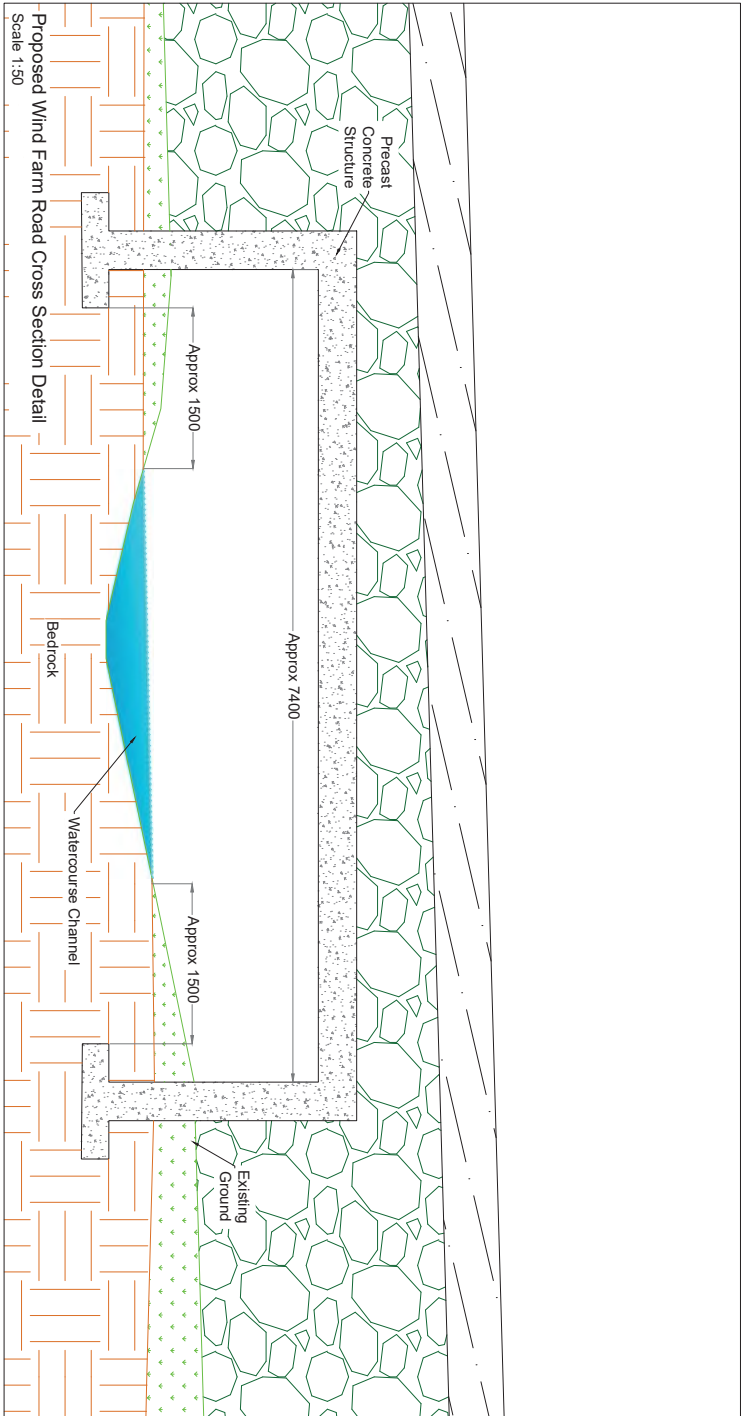

Typical Clear Span Bridge

Meenbrog Wind Farm, Co. Donegal

DESIGNED BY: **Joseph O Briain**

CHECKED BY: **Michael Watson**

PROJECT NO: **168502**

SCALE: **As Shown @A3**

DATE: **13.12.2017**


PROJECT NO: **0502 - 47**

DATE: **13.12.2017**

PROJECT NO: **0502 - 47**





DATE: **13.12.2017**

McCarthy Keville O'Sullivan Ltd
 Planning & Environmental Consultants
 Black 'T' Financial Services Centre,
 Gateway Enterprise Park,
 Galway, Ireland.
 email: info@mcCarthyKevilleO'Sullivan.ie
 website: www.mccarthyKevilleO'Sullivan.ie
 Fax: +353 91 772719

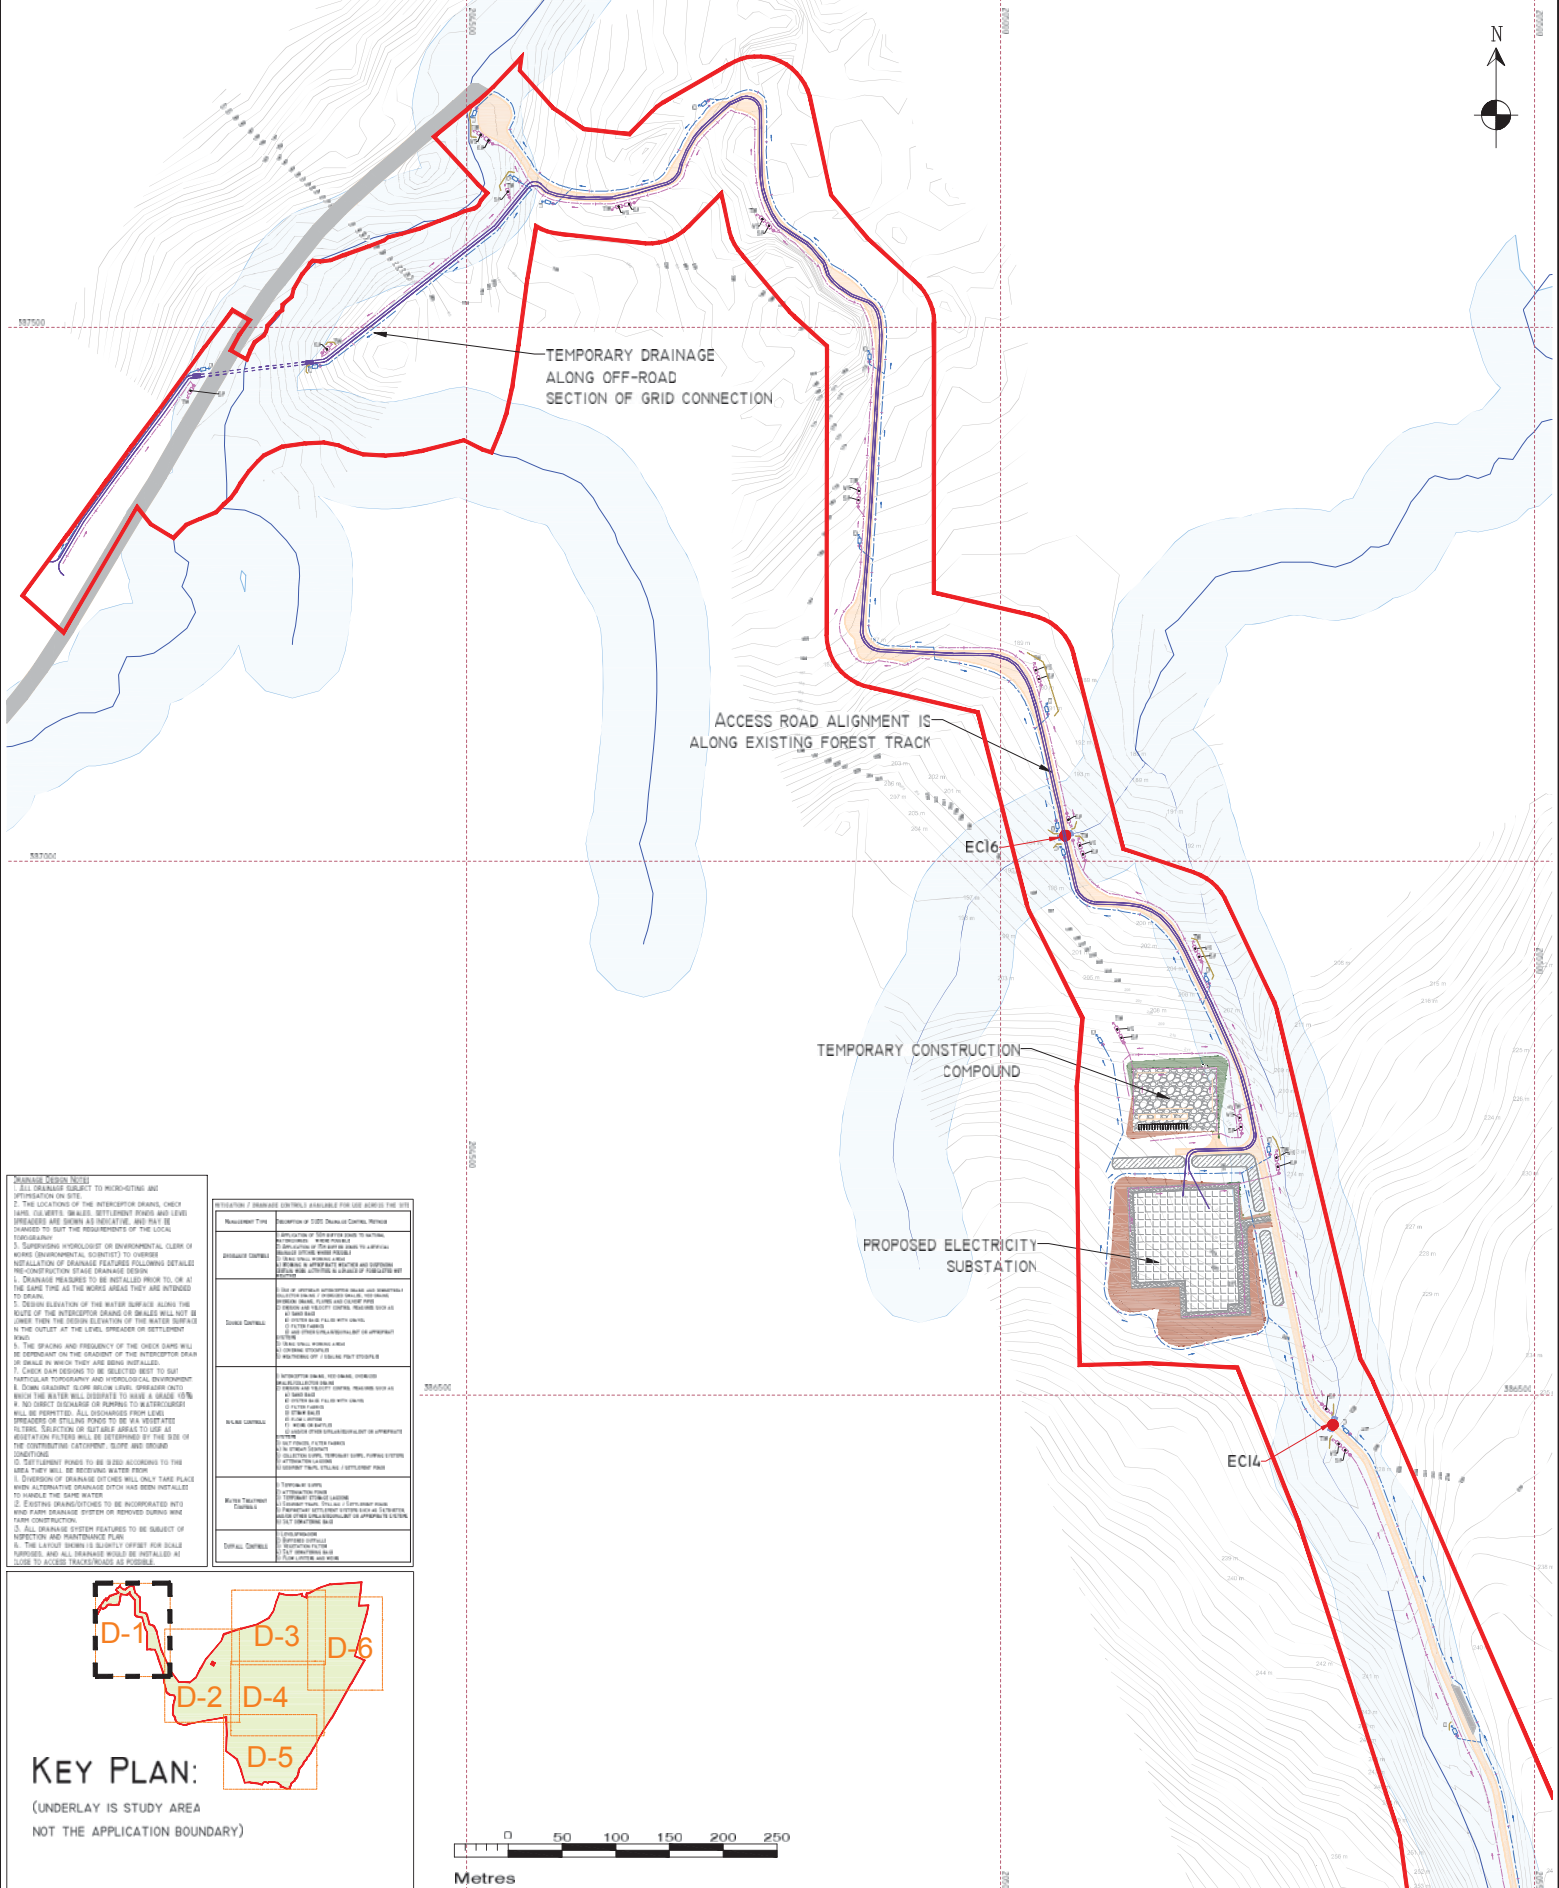

- DRAINAGE DESIGN NOTES**
1. ALL DRAINAGE SUBJECT TO MICRO-SITING AND INFORMATION ON SITE.
 2. THE LOCATIONS OF THE INTERCEPTOR DRAIN, CHECK DAMS, CHECK DAMS, SETTLEMENT PONDS AND LEVEL SPREADERS ARE SHOWN AS INDICATIVE, AND MAY BE CHANGED TO SUIT THE REQUIREMENTS OF THE LOCAL SINGLESIDE.
 3. SURVEILING HYDROLOGIST OR ENVIRONMENTAL CLERK OF RECORD (ENVIRONMENTAL SCIENTIST) TO OVERSEE INSTALLATION OF DRAINAGE FEATURES FOLLOWING DETAILED PRE-CONSTRUCTION STAGE DRAINAGE DESIGN.
 4. DRAINAGE FEATURES TO BE INSTALLED PRIOR TO, OR AT THE SAME TIME AS THE WORKS ARE BEING INTRODUCED TO DRAIN.
 5. CHECK DAM ELEVATION OF THE WATER SURFACE ALONG THE ROUTE OF THE INTERCEPTOR DRAIN OR SPREADER WILL NOT BE LOWER THAN THE DESIGN ELEVATION OF THE WATER SURFACE IN THE OUTLET AT THE LEVEL SPREADER OR SETTLEMENT POND.
 6. THE SPACING AND FREQUENCY OF THE CHECK DAMS WILL BE DETERMINED ON THE BASIS OF THE INTERCEPTOR DRAIN OR SPREADER IN WHICH THEY ARE BEING INSTALLED.
 7. CHECK DAM DESIGN TO BE SUBJECT TO SUIT PARTICULAR TOPOGRAPHY AND HYDROLOGICAL ENVIRONMENT.
 8. DOWN GRASSING SLOPE BELOW LEVEL SPREADERS OR CHECK DAMS THE WATER WILL DISSEPERATE TO HAVE A GRADE 10%.
 9. NO DIRECT DISCHARGE OF RUNOFF TO WATERCOURSES WILL BE PERMITTED. ALL DISCHARGES FROM LEVEL SPREADERS OR CHECK DAMS TO BE VIA VEGETATED FILTERS. SELECTION OF SUEYABLE AREAS TO USE AS VEGETATED FILTERS WILL BE DETERMINED BY THE SIZE OF THE CONTRIBUTING CATCHMENT, SLOPE AND SOIL CONDITIONS.
 10. SETTLEMENT POND TO BE SIZED ACCORDING TO THIS AREA THEY WILL BE RECEIVING WATER FROM.
 11. DIVERSION OF DRAINAGE OFFICES WILL ONLY TAKE PLACE TO HANDLE THE SAME WATER.
 12. EXISTING DRAINAGE TO BE INCORPORATED INTO NEW DRAINAGE SYSTEM OR REMOVED ENTIRELY WITH CONSTRUCTION.
 13. ALL DRAINAGE SYSTEM FEATURES TO BE SUBJECT OF INSPECTION AND MAINTENANCE PLAN.
 14. THE LAYOUT DESIGN IS SUITABLE SUBJECT FOR SCALE PURPOSES, AND ALL DRAINAGE WOULD BE INSTALLED AT CLOSE TO ACCESS TO ACCESS AS POSSIBLE.

Requirement Type	Description or CODE Details Control, Notice
DRAINAGE CONTROL	Application of the proposed drains to factors: <ul style="list-style-type: none"> 1. TOPOGRAPHY 2. SOIL TYPE 3. VEGETATION 4. CLIMATE 5. ADJACENT AREAS 6. EXISTING DRAINAGE 7. ACCESSIBILITY 8. MAINTENANCE 9. COST
SOILS CONTROL	<ul style="list-style-type: none"> 1. Soil of proposed interceptors shall not be saturated. 2. Proposed drains shall be installed on a minimum of 10% slope. 3. Proposed drains shall be installed on a minimum of 10% slope. 4. Proposed drains shall be installed on a minimum of 10% slope. 5. Proposed drains shall be installed on a minimum of 10% slope. 6. Proposed drains shall be installed on a minimum of 10% slope. 7. Proposed drains shall be installed on a minimum of 10% slope. 8. Proposed drains shall be installed on a minimum of 10% slope. 9. Proposed drains shall be installed on a minimum of 10% slope. 10. Proposed drains shall be installed on a minimum of 10% slope.
WATER CONTROL	<ul style="list-style-type: none"> 1. Proposed drains shall be installed on a minimum of 10% slope. 2. Proposed drains shall be installed on a minimum of 10% slope. 3. Proposed drains shall be installed on a minimum of 10% slope. 4. Proposed drains shall be installed on a minimum of 10% slope. 5. Proposed drains shall be installed on a minimum of 10% slope. 6. Proposed drains shall be installed on a minimum of 10% slope. 7. Proposed drains shall be installed on a minimum of 10% slope. 8. Proposed drains shall be installed on a minimum of 10% slope. 9. Proposed drains shall be installed on a minimum of 10% slope. 10. Proposed drains shall be installed on a minimum of 10% slope.
Water Treatment Controls	<ul style="list-style-type: none"> 1. Proposed drains shall be installed on a minimum of 10% slope. 2. Proposed drains shall be installed on a minimum of 10% slope. 3. Proposed drains shall be installed on a minimum of 10% slope. 4. Proposed drains shall be installed on a minimum of 10% slope. 5. Proposed drains shall be installed on a minimum of 10% slope. 6. Proposed drains shall be installed on a minimum of 10% slope. 7. Proposed drains shall be installed on a minimum of 10% slope. 8. Proposed drains shall be installed on a minimum of 10% slope. 9. Proposed drains shall be installed on a minimum of 10% slope. 10. Proposed drains shall be installed on a minimum of 10% slope.
General Controls	<ul style="list-style-type: none"> 1. Proposed drains shall be installed on a minimum of 10% slope. 2. Proposed drains shall be installed on a minimum of 10% slope. 3. Proposed drains shall be installed on a minimum of 10% slope. 4. Proposed drains shall be installed on a minimum of 10% slope. 5. Proposed drains shall be installed on a minimum of 10% slope. 6. Proposed drains shall be installed on a minimum of 10% slope. 7. Proposed drains shall be installed on a minimum of 10% slope. 8. Proposed drains shall be installed on a minimum of 10% slope. 9. Proposed drains shall be installed on a minimum of 10% slope. 10. Proposed drains shall be installed on a minimum of 10% slope.

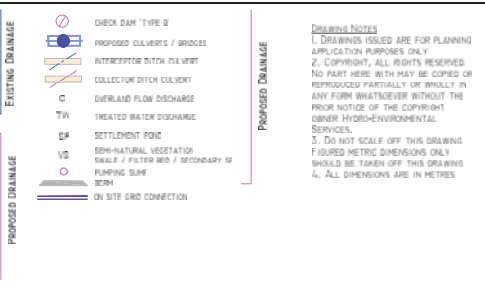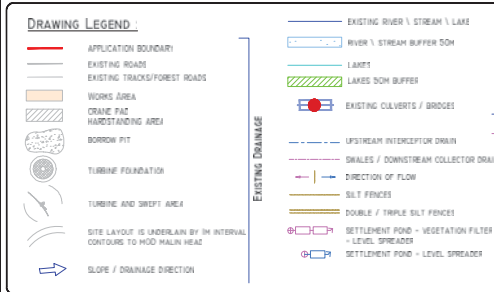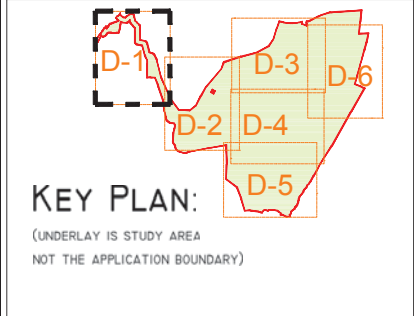

Ordnance Survey Ireland Licence No. EN 0044717
© Ordnance Survey Ireland/Geomatics of Ireland

Client: MCCARTHY KEVILLE AND O'SULLIVAN

Job: MEENBOG WIND FARM, CO. DONEGAL

13.12.17 Planning MG MG
Date Description Chkd Signed


Revisions

HYDRO ENVIRONMENTAL SERVICES
22 Lower Main St
Dungarvan
Co. Waterford
Ireland

tel: +353 (0) 58-44122
tel: +353 (0) 58-44244
email: info@hydroenvironmental.ie
web: www.hydroenvironmental.ie

Figure No: D101 (0502-15)

Drawing No: P1249-2-1217-A1-D101 (0502-15)-00A
Sheet Size: A1 Project No.: P1249-2
Scale: 1:2,500 (A1) Drawn By: MG/GD
Date: 13/12/2017 Checked By: MG




KEY PLAN:

(UNDERLAY IS STUDY AREA
NOT THE APPLICATION BOUNDARY)

ATTENTION / DRAINAGE CONTROL AVAILABLE FOR USE ABOVE THE SITE

Measurement Time	Description of SITE DRAINAGE CONTROL MEASURE
Pre-Construction	Application of top soil or straw to surface; mulch; geotextiles; silt fences; sedimentation ponds and levels; spreaders are shown as indicative and may be changed to suit the requirements of the local topography
Construction	1. SURROUNDING HYDROLOGIST OR ENVIRONMENTAL CLERK OF WORKS (ENVIRONMENTAL SCIENTIST) TO OVERSEE PRE-CONSTRUCTION OF BASE DRAINAGE DESIGN 2. CHANGE MEASURES TO BE INSTALLED PRIOR TO, OR AT THE SAME TIME AS THE WORKS ARE INTENDED TO BE DONE 3. DESIGN ELEVATION OF THE WATER SURFACE ALONG THE ROUTE OF THE INTERCEPTION DRAIN OR CHANNEL WILL NOT BE LOWER THAN THE DESIGN ELEVATION OF THE WATER SURFACE IN THE COLLECTOR AT THE LEVEL SPREADER OR SETTLEMENT POND 4. THE DESIGN AND FREQUENCY OF THE CHECK DAMS WILL BE DEPENDANT ON THE GRADIENT OF THE INTERCEPTION DRAIN OR CHANNEL IN WHICH THEY ARE BEING INSTALLED 5. CHECK DAMS SHOULD BE SITED TO SUIT NATURAL TOPOGRAPHY AND HYDROLOGICAL ENVIRONMENT 6. DOWN GRADIENT SLOPE BELOW LEVEL SPREADER CANE WHICH THE WATER WILL DISCHARGE TO LAKES OR LAGOONS 7. NO DIRECT DISCHARGE OR PUMPING TO WATERCOURSE WHICH WILL BE INSTALLED. ALL DISCHARGES FROM LEVEL SPREADERS OR SETTLING PONDS TO BE VIA VEGETATED FILTER STRIP, SLOTTED OR SIFTABLE AREA TO USE AS ISOLATION FILTERS WILL BE CONTROLLED BY THE SIZE OF THE CONTRIBUTING CATCHMENT, SLOPE AND GROUND CONDITIONS 8. SETTLEMENT PONDS TO BE SITED ACCORDING TO THE AREA THEY WILL BE RECEIVING WATER FROM 9. DIVERSION OF DRAINAGE LINES WILL ONLY TAKE PLACE WHEN ALTERNATIVE DRAINAGE OPTION HAS BEEN INSTALLED TO HANDLE THE SAME WATER 10. CLEARING OPERATIONS TO BE INCORPORATED INTO WIND FARM DRAINAGE SYSTEM OR FINISHED DURING WIND FARM CONSTRUCTION 11. ALL DRAINAGE SYSTEM FEATURES TO BE SUBJECT OF INSPECTION AND MAINTENANCE PLANS 12. THIS LAYOUT SHOULD BE SUBJECT OF OFFER FOR SCALE PURCHASES AND ALL DRAINAGE MEASURES TO BE INSTALLED AS PLANNED TO AVOID TRANSDUCTIONS AS POSSIBLE

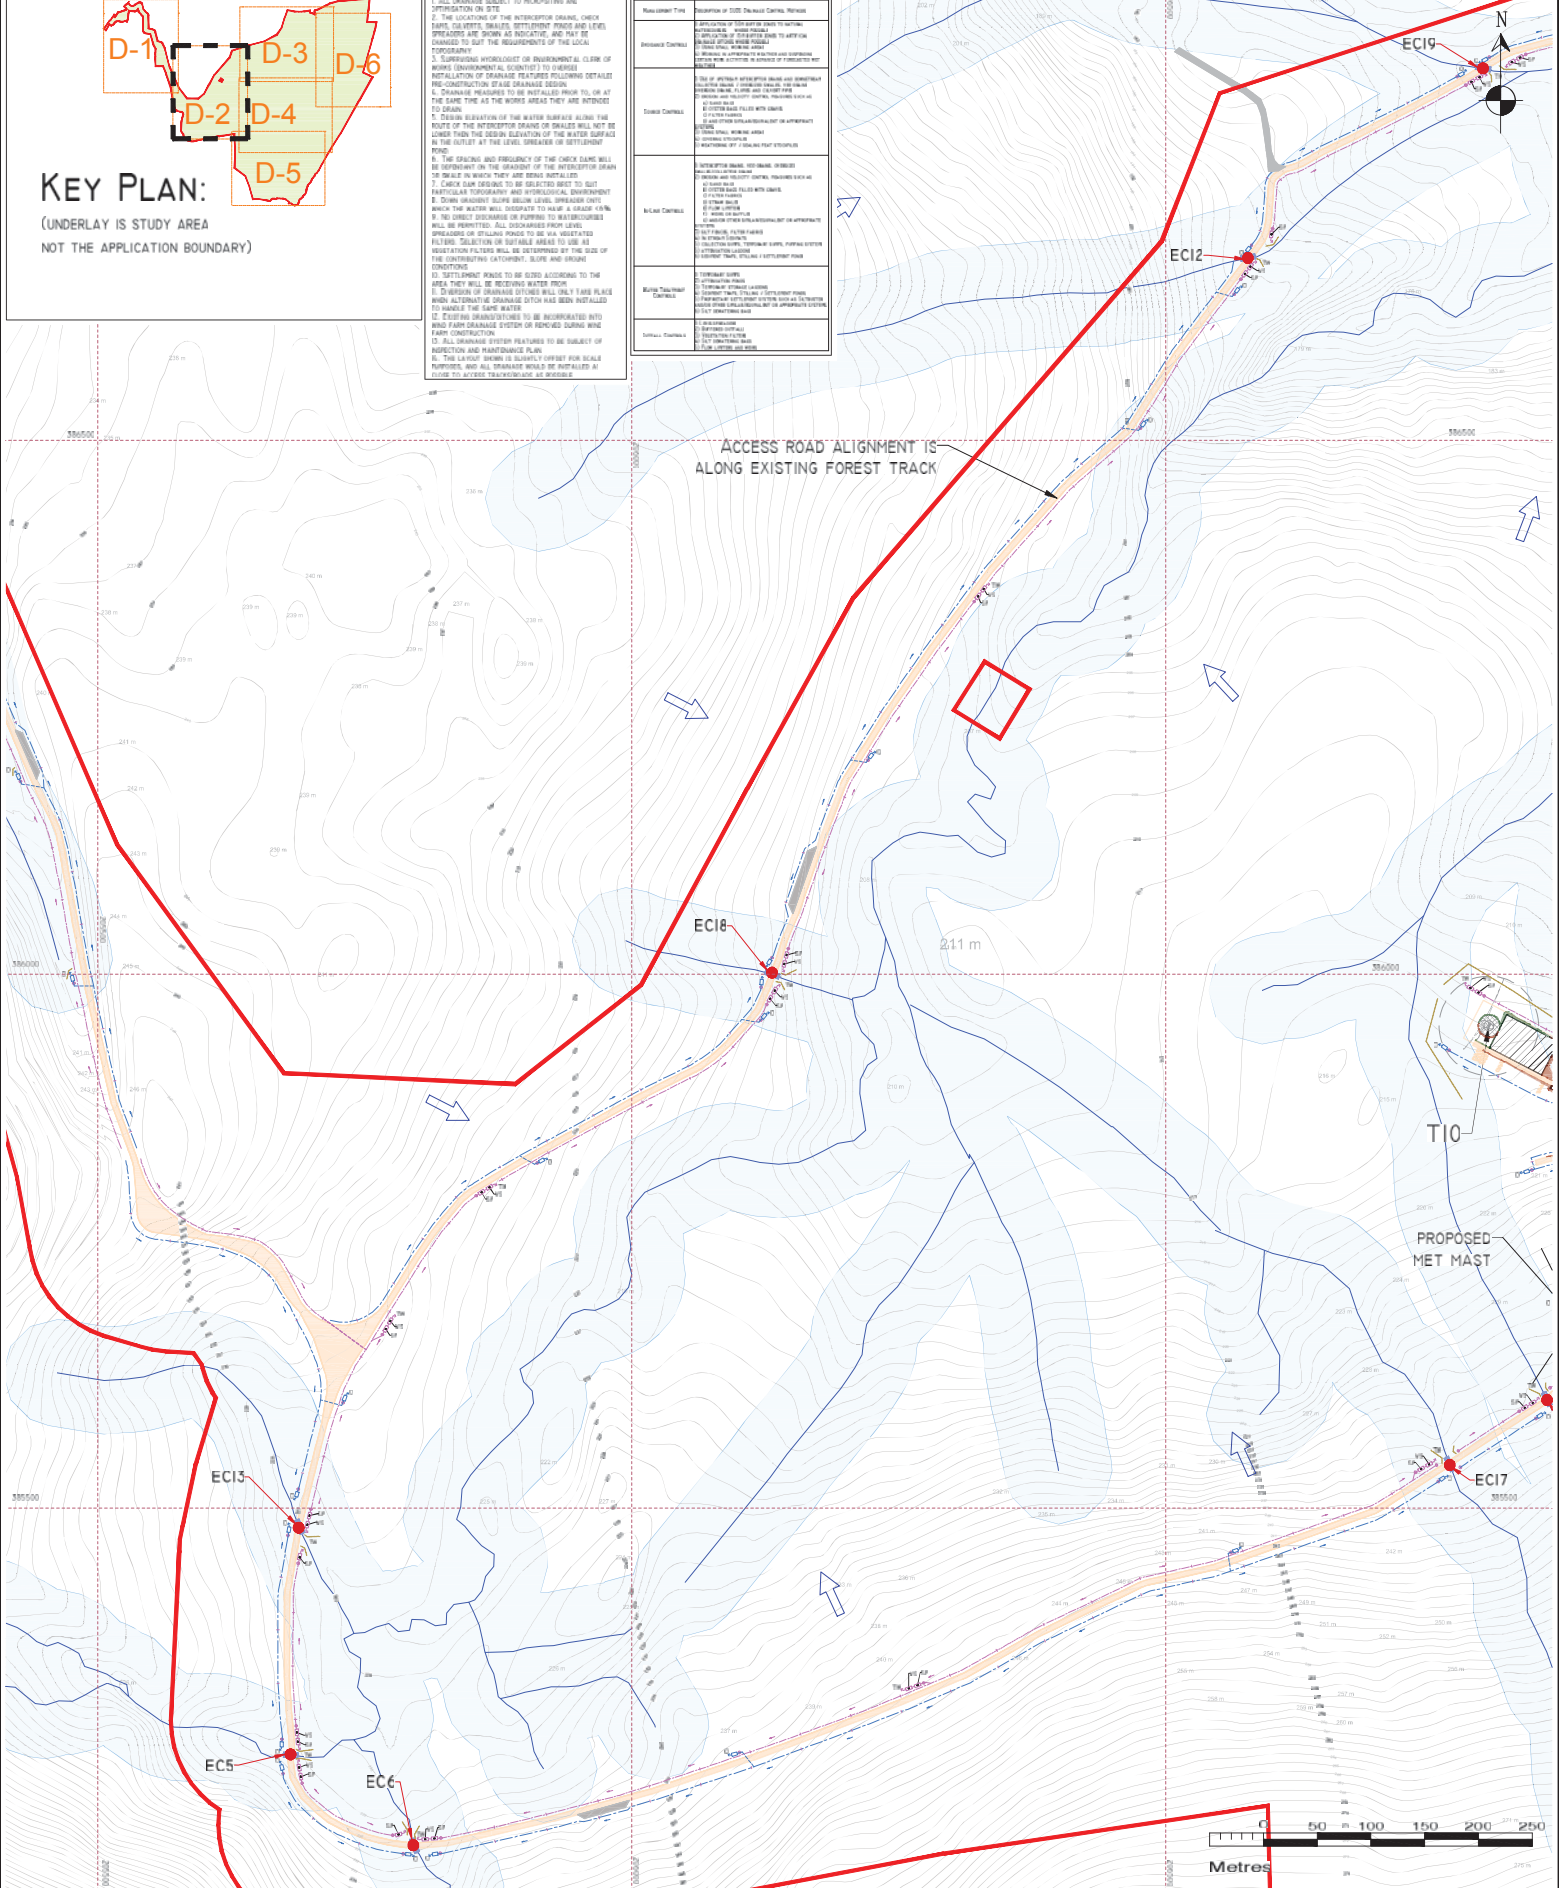

DRAWING LEGEND




<ul style="list-style-type: none"> APPLICATION BOUNDARY EXISTING ROADS EXISTING TRACKS/FOREST ROADS WORKS AREA CRANE PAD HANDSTANDING AREA BORROW PIT TURBINE FOUNDATION TURBINE AND SWEPT AREA SITE LAYOUT IS UNDERLAIN BY 1M INTERVAL CONTOURS TO SHOW MAIN HEAD SLOPE / DRAINAGE DIRECTION 	<ul style="list-style-type: none"> EXISTING RIVER / STREAM / LAKE RIVER / STREAM BUFFER 50M LAKES LAKES 50M BUFFER EXISTING CULVERTS / BRIDGES UPSTREAM INTERCEPTION DRAIN DIAPHRAGM / DOWNSTREAM COLLECTOR DRAIN DIRECTION OF FLOW SILT FENCES DOUBLE / TRIPLE SILT FENCES SETTLEMENT POND - VEGETATION FILTER - LEVEL SPREADER SETTLEMENT POND - LEVEL SPREADER 	<ul style="list-style-type: none"> CHECK DAM TYPE B PROPOSED CULVERTS / BRIDGES INTERCEPTOR DITCH CULVERT COLLECTOR DITCH CULVERT OVERLAND FLOW DISCHARGE TW TREATED WATER DISCHARGE CFP SETTLEMENT POND SEMI-NATURAL VEGETATION SWALE / FILTER BED / SECONDARY SP PUMPING SUMP BSOM ON SITE GRID CONNECTION 	<p>DRAWING NOTES</p> <ol style="list-style-type: none"> DRAWINGS ISSUED ARE FOR PLANNING APPLICATION PURPOSES ONLY COPYRIGHT, ALL RIGHTS RESERVED. NO PART HERE WITH MAY BE COPIED OR REPRODUCED PARTIALLY OR WHOLLY IN ANY FORM WHATSOEVER WITHOUT THE PRIOR NOTICE OF THE COPYRIGHT OWNER HYDRO-ENVIRONMENTAL SERVICES DO NOT SCALE OFF THIS DRAWING FIGURED METRIC DIMENSIONS ONLY SHOULD BE TAKEN OFF THIS DRAWING ALL DIMENSIONS ARE IN METRES
--	---	--	--

Ordnance Survey Ireland Licence No. EN 0044717 © Ordnance Survey Ireland/Department of Transport			Client:	
			MCCARTHY KEVILLE AND O'SULLIVAN	
			Job:	
			MEENBOG WIND FARM, CO. DONEGAL	
			Title:	
			DRAINAGE LAYOUT SHEET 2 OF 6	
			Figure No:	
			D102 (0502-16)	
			Drawing No:	
			P1249-2-1217-A1-D102(0502-16)-00A	
			Sheet Size:	
			A1	
			Project No.:	
			P1249-2	
			Scale:	
			1:2,500 (A1)	
			Drawn By:	
			MG/GD	
			Date:	
			13/12/2017	
			Checked By:	
			MG	

HYDRO ENVIRONMENTAL SERVICES

22 Lower Main St
Dungannon
Co. Waterford
Ireland

tel: +353 (0) 58-44122
tel: +353 (0) 58-44244
email: info@hydroenvironmental.ie
web: www.hydroenvironmental.ie

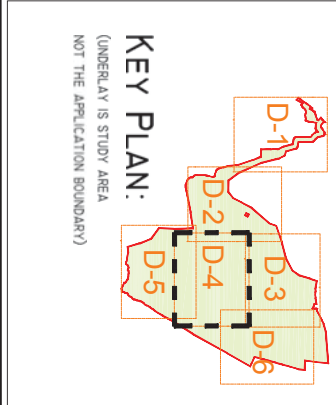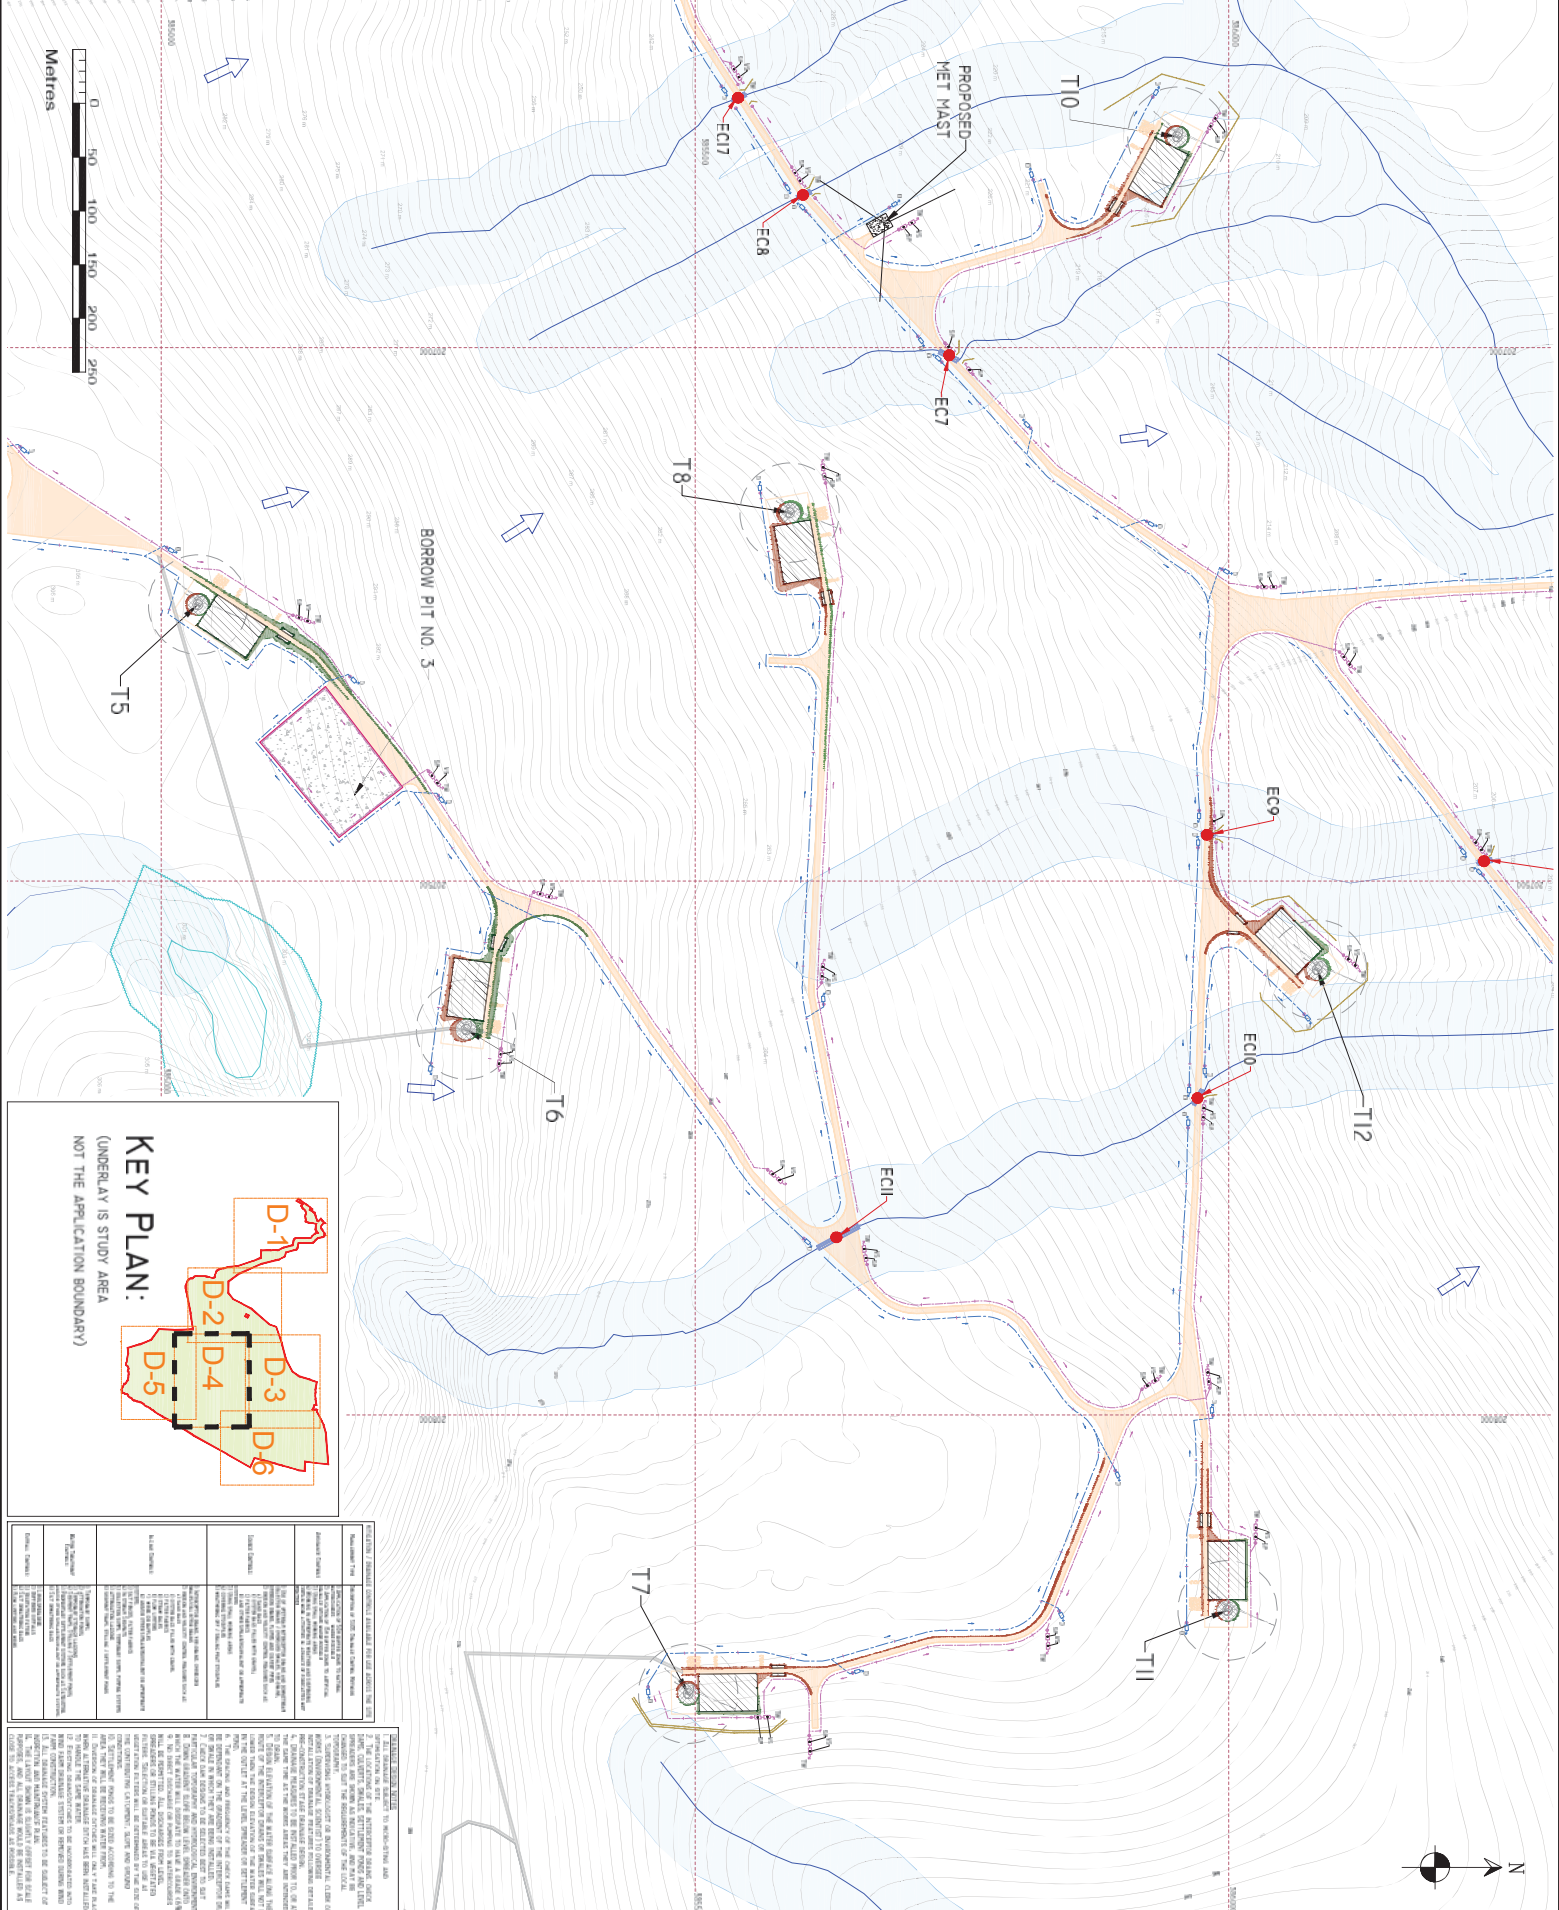

Symbol	Description
[Symbol]	PROPOSED DRAINAGE
[Symbol]	EXISTING DRAINAGE
[Symbol]	PROPOSED STRUCTURE
[Symbol]	EXISTING STRUCTURE
[Symbol]	PROPOSED ROAD
[Symbol]	EXISTING ROAD
[Symbol]	PROPOSED LOT
[Symbol]	EXISTING LOT
[Symbol]	PROPOSED BOUNDARY
[Symbol]	EXISTING BOUNDARY

PROPOSED DRAINAGE

- PROPOSED DRAINAGE
- PROPOSED STRUCTURE
- PROPOSED ROAD
- PROPOSED LOT
- PROPOSED BOUNDARY

Revisions	Date	Description	By	Checked
1	1/17/2017	WORKING	MJC	MJC

HYDRO ENVIRONMENTAL SERVICES
 27 Dover Lane 2
 Danvers MA 01923
 Tel: +508.584.4177
 Fax: +508.584.4144
 CA: 661444
 www.hydroenv.com

NEIGHBORING WIND FARM, CO. DOWEGAL
 SHEET 4 OF 6
 DRAWING NO. P129-2
 SCALE: 1:2500 (A1)
 DATE: 1/17/2017
 CHECKED BY: MJC

PROPOSED DRAINAGE

- PROPOSED DRAINAGE
- PROPOSED STRUCTURE
- PROPOSED ROAD
- PROPOSED LOT
- PROPOSED BOUNDARY

EXISTING DRAINAGE

- EXISTING DRAINAGE
- EXISTING STRUCTURE
- EXISTING ROAD
- EXISTING LOT
- EXISTING BOUNDARY

DRAINAGE LEGEND:

- PROPOSED DRAINAGE
- EXISTING DRAINAGE
- PROPOSED STRUCTURE
- EXISTING STRUCTURE
- PROPOSED ROAD
- EXISTING ROAD
- PROPOSED LOT
- EXISTING LOT
- PROPOSED BOUNDARY
- EXISTING BOUNDARY

DRAWING LEGEND

[Symbol]	APPLICATION BOUNDARY
[Symbol]	EXISTING ROAD
[Symbol]	EXISTING INTERDRYNESS DRAIN
[Symbol]	WORKING AREA
[Symbol]	HIGHWAY/ROAD AREA
[Symbol]	WORKING PIT
[Symbol]	TURBINE FOUNDATION
[Symbol]	TURBINE AND SHUT AREA
[Symbol]	SOFT EXISTING OR TO BE CONSTRUCTED IN INTERNAL CHANNELS TO ROAD PAVEMENT
[Symbol]	SLOPE / DRAINAGE DIRECTION
[Symbol]	EXISTING DRAINAGE / CREEK / LAKE
[Symbol]	WORKING LAKE BUFFER 50m
[Symbol]	LAKE
[Symbol]	LAKE SLOPE BUFFER
[Symbol]	EXISTING COLLECTOR / BRIDGE
[Symbol]	UPSTREAM INTERCEPTION DRAIN
[Symbol]	DRAINAGE / DOWNSTREAM COLLECTOR DRAIN
[Symbol]	DRAINAGE / DRAINAGE DIRECTION
[Symbol]	SOFT FINISH
[Symbol]	DOUBLE / TRIPLE OUT FINISHES
[Symbol]	SETTLEMENT POND - VEGETATION FILTER
[Symbol]	LEVEL SPREADER
[Symbol]	SOFT FINISH POND / LEVEL SPREADER
[Symbol]	CHECK DAM "TYPE 1"
[Symbol]	CHECK DAM "TYPE 2"
[Symbol]	INTERCEPTOR COLLECTOR / BRIDGE
[Symbol]	INTERCEPTOR DRAIN COLLECTOR
[Symbol]	COLLECTOR DRAIN COLLECTOR
[Symbol]	TREATED WATER DISCHARGE
[Symbol]	T1
[Symbol]	T2
[Symbol]	GETTLEMENT POND
[Symbol]	SEMI-NATURAL VEGETATION
[Symbol]	EXISTING DRAINAGE / BRIDGE / STRENGTH OF
[Symbol]	RAMPING SLOPE
[Symbol]	IN SITE GRID CONNECTION

PROCESS DRAINAGE



1. DRAINAGE DESIGN IS FOR PLANNING APPLICATION PURPOSES ONLY. THE DESIGNER ASSUMES NO LIABILITY FOR THE ACCURACY OF THE INFORMATION PROVIDED IN THIS DRAWING. THE CLIENT MUST OBTAIN NECESSARY PERMITS FROM THE LOCAL AUTHORITIES FOR THE CONSTRUCTION OF THE DRAINAGE SYSTEM. THE CLIENT MUST OBTAIN NECESSARY PERMITS FROM THE LOCAL AUTHORITIES FOR THE CONSTRUCTION OF THE DRAINAGE SYSTEM. THE CLIENT MUST OBTAIN NECESSARY PERMITS FROM THE LOCAL AUTHORITIES FOR THE CONSTRUCTION OF THE DRAINAGE SYSTEM.

HYDRO ENVIRONMENTAL SERVICES

27 Lower Maung Rd
Dunedin
New Zealand
Ph: +63 512 544172
Fax: +63 512 544244
www.hydroenvironmental.co.nz

Client: MCCLARTY KEVILLE AND O'SULLIVAN
Job: MEENOG WING FARM, CO. DONEGAL
Title: DRAINAGE LAYOUT SHEET 5 OF 6
Figure No: D105 (05/02/19)
Drawing No: P1249-2/17-A1-D105(02/19)00A
Sheet Size: A1
Scale: 1:2,500 (A1)
Drawn By: MCS/DSD
Date: 13/12/2017
Checked By: MCS

Date	Description	Checked	Signed
13/12/17	Final	[Signature]	[Signature]

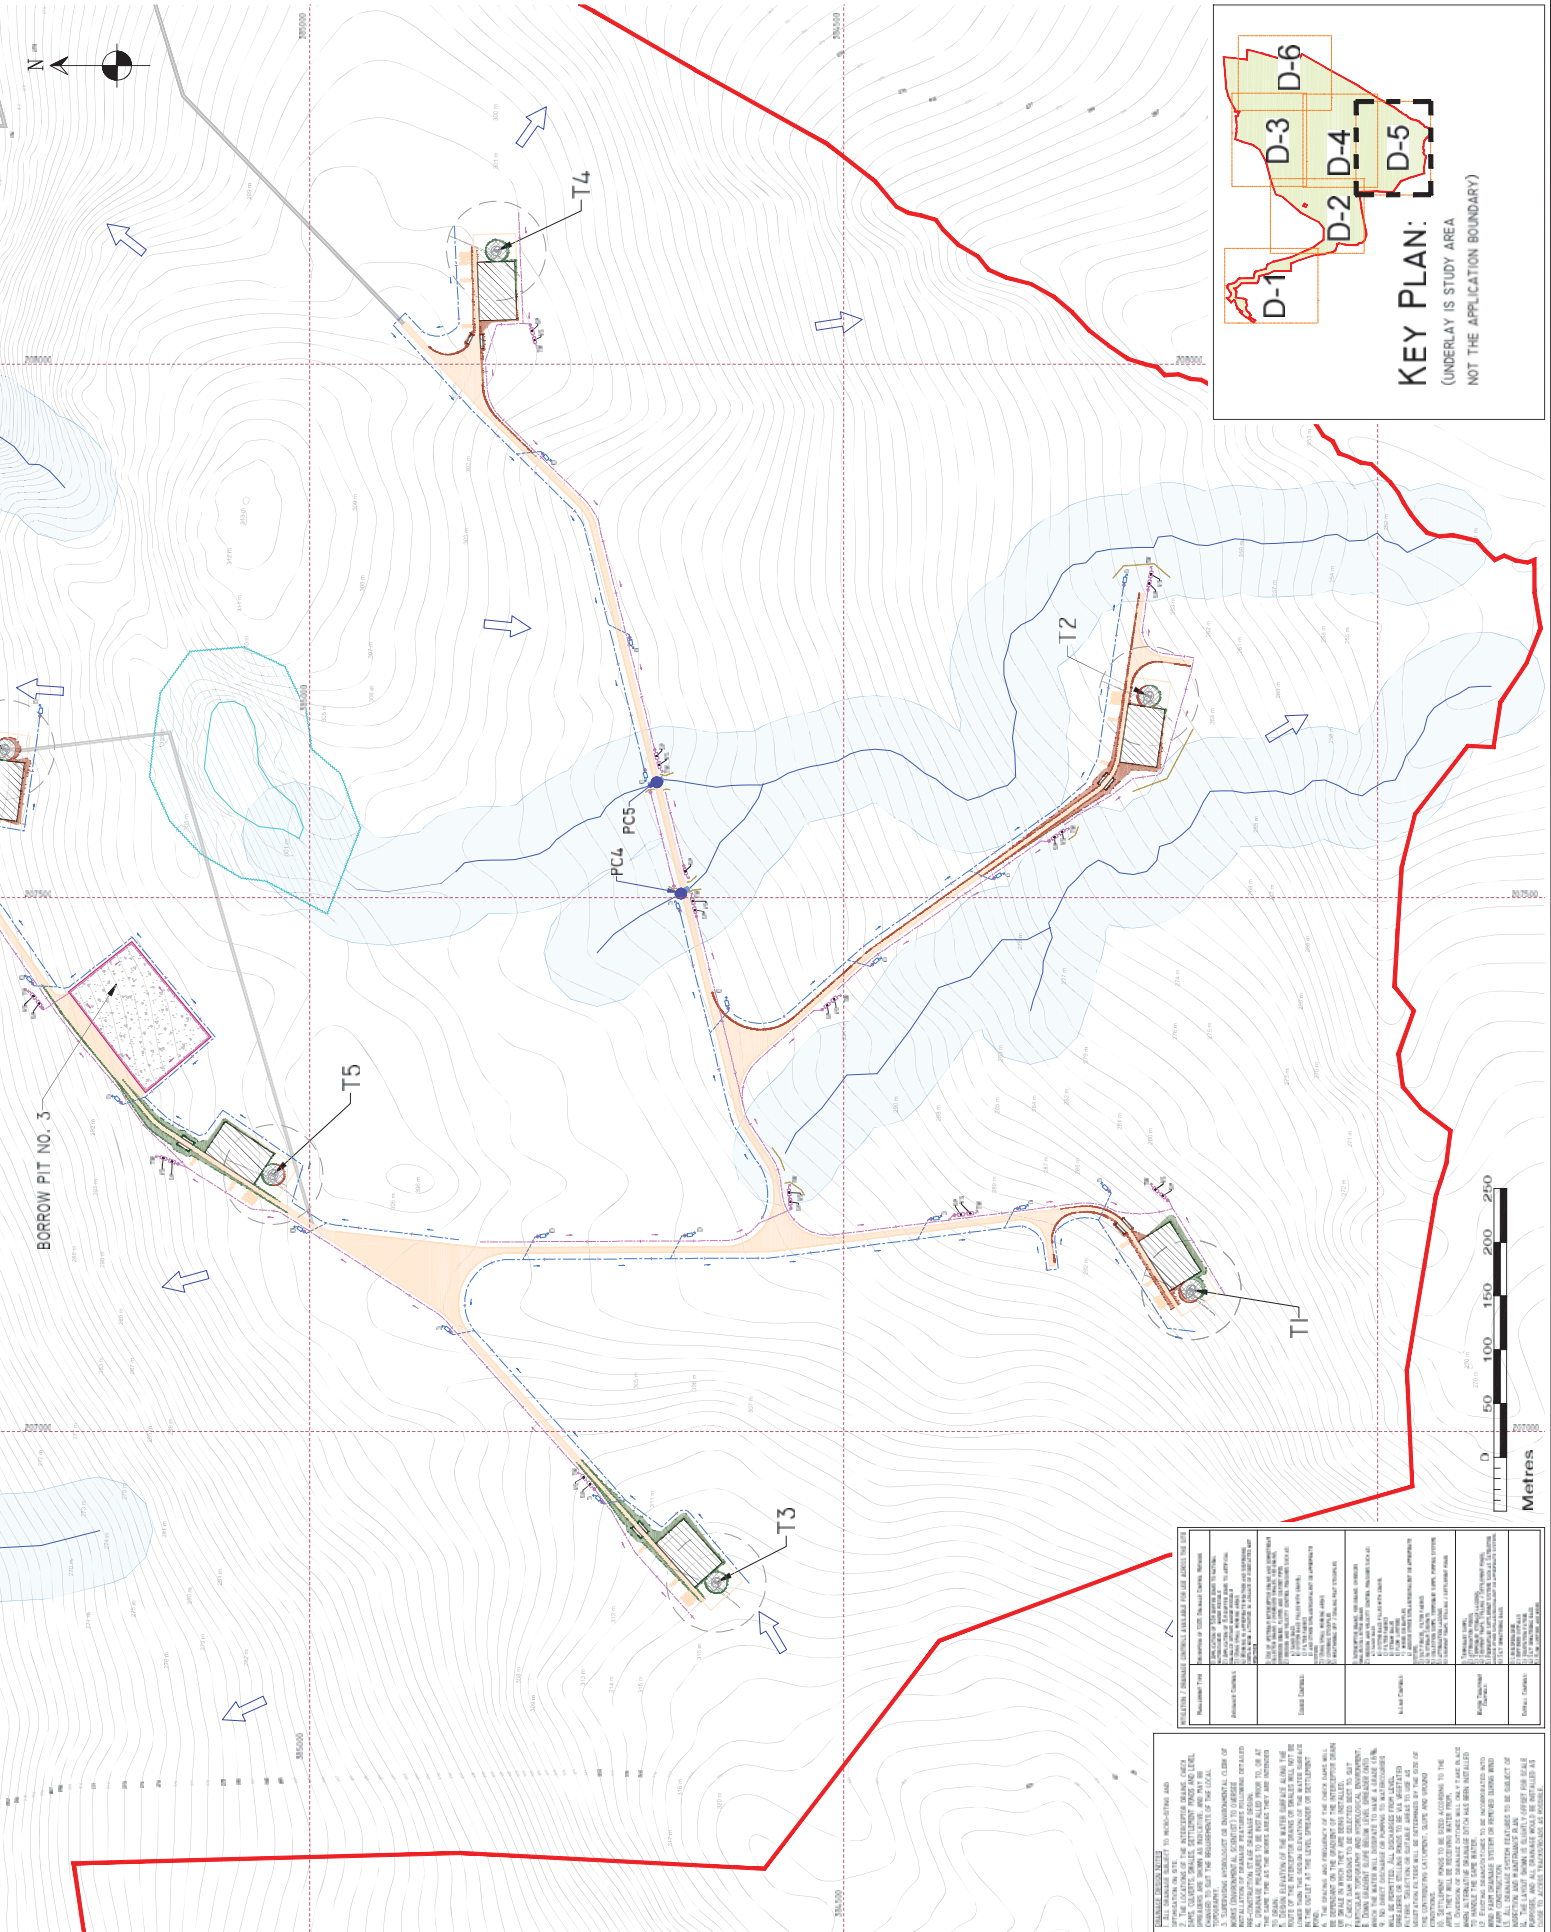

WORKING AREA

1. THE WORKING AREA IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE WORKING AREA IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE WORKING AREA IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED.

WORKING PIT

1. THE WORKING PIT IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE WORKING PIT IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE WORKING PIT IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED.

LAKE

1. THE LAKE IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE LAKE IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE LAKE IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED.

LAKE SLOPE BUFFER

1. THE LAKE SLOPE BUFFER IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE LAKE SLOPE BUFFER IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE LAKE SLOPE BUFFER IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED.

EXISTING COLLECTOR / BRIDGE

1. THE EXISTING COLLECTOR / BRIDGE IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE EXISTING COLLECTOR / BRIDGE IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE EXISTING COLLECTOR / BRIDGE IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED.

UPSTREAM INTERCEPTION DRAIN

1. THE UPSTREAM INTERCEPTION DRAIN IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE UPSTREAM INTERCEPTION DRAIN IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE UPSTREAM INTERCEPTION DRAIN IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED.

DRAINAGE / DOWNSTREAM COLLECTOR DRAIN

1. THE DRAINAGE / DOWNSTREAM COLLECTOR DRAIN IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE DRAINAGE / DOWNSTREAM COLLECTOR DRAIN IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE DRAINAGE / DOWNSTREAM COLLECTOR DRAIN IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED.

DRAINAGE / DRAINAGE DIRECTION

1. THE DRAINAGE / DRAINAGE DIRECTION IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE DRAINAGE / DRAINAGE DIRECTION IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE DRAINAGE / DRAINAGE DIRECTION IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED.

SOFT FINISH

1. THE SOFT FINISH IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE SOFT FINISH IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE SOFT FINISH IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED.

BORROW PIT NO. 3

1. THE BORROW PIT NO. 3 IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE BORROW PIT NO. 3 IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE BORROW PIT NO. 3 IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED.

T5

1. THE TURBINE T5 IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE TURBINE T5 IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE TURBINE T5 IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED.

T4

1. THE TURBINE T4 IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE TURBINE T4 IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE TURBINE T4 IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED.

PC4 PC5

1. THE POINTS PC4 AND PC5 ARE THE AREAS WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE POINTS PC4 AND PC5 ARE THE AREAS WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE POINTS PC4 AND PC5 ARE THE AREAS WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED.

T3



1. THE TURBINE T3 IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE TURBINE T3 IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE TURBINE T3 IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED.

T2

1. THE TURBINE T2 IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE TURBINE T2 IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE TURBINE T2 IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED.

T1

1. THE TURBINE T1 IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE TURBINE T1 IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED. THE TURBINE T1 IS THE AREA WHERE THE DRAINAGE SYSTEM IS TO BE CONSTRUCTED.



SCALE

1:2,500 (A1)

DRAWING NO.

D105 (05/02/19)

CLIENT

MCCLARTY KEVILLE AND O'SULLIVAN

JOB

MEENOG WING FARM, CO. DONEGAL

TITLE

DRAINAGE LAYOUT SHEET 5 OF 6

FIGURE NO.

D105 (05/02/19)

DRAWING NO.

P1249-2/17-A1-D105(02/19)00A

SHEET SIZE

A1

SCALE

1:2,500 (A1)

DRAWN BY

MCS/DSD

DATE

13/12/2017

CHECKED BY

MCS

DATE

13/12/2017

SCALE

1:2,500 (A1)

DRAWN BY

MCS/DSD

DATE

13/12/2017

CHECKED BY

MCS

DATE

13/12/2017

CHECKED BY

MCS

DATE

13/12/2017

CHECKED BY


MCS

DATE

13/12/2017

CHECKED BY



MCS

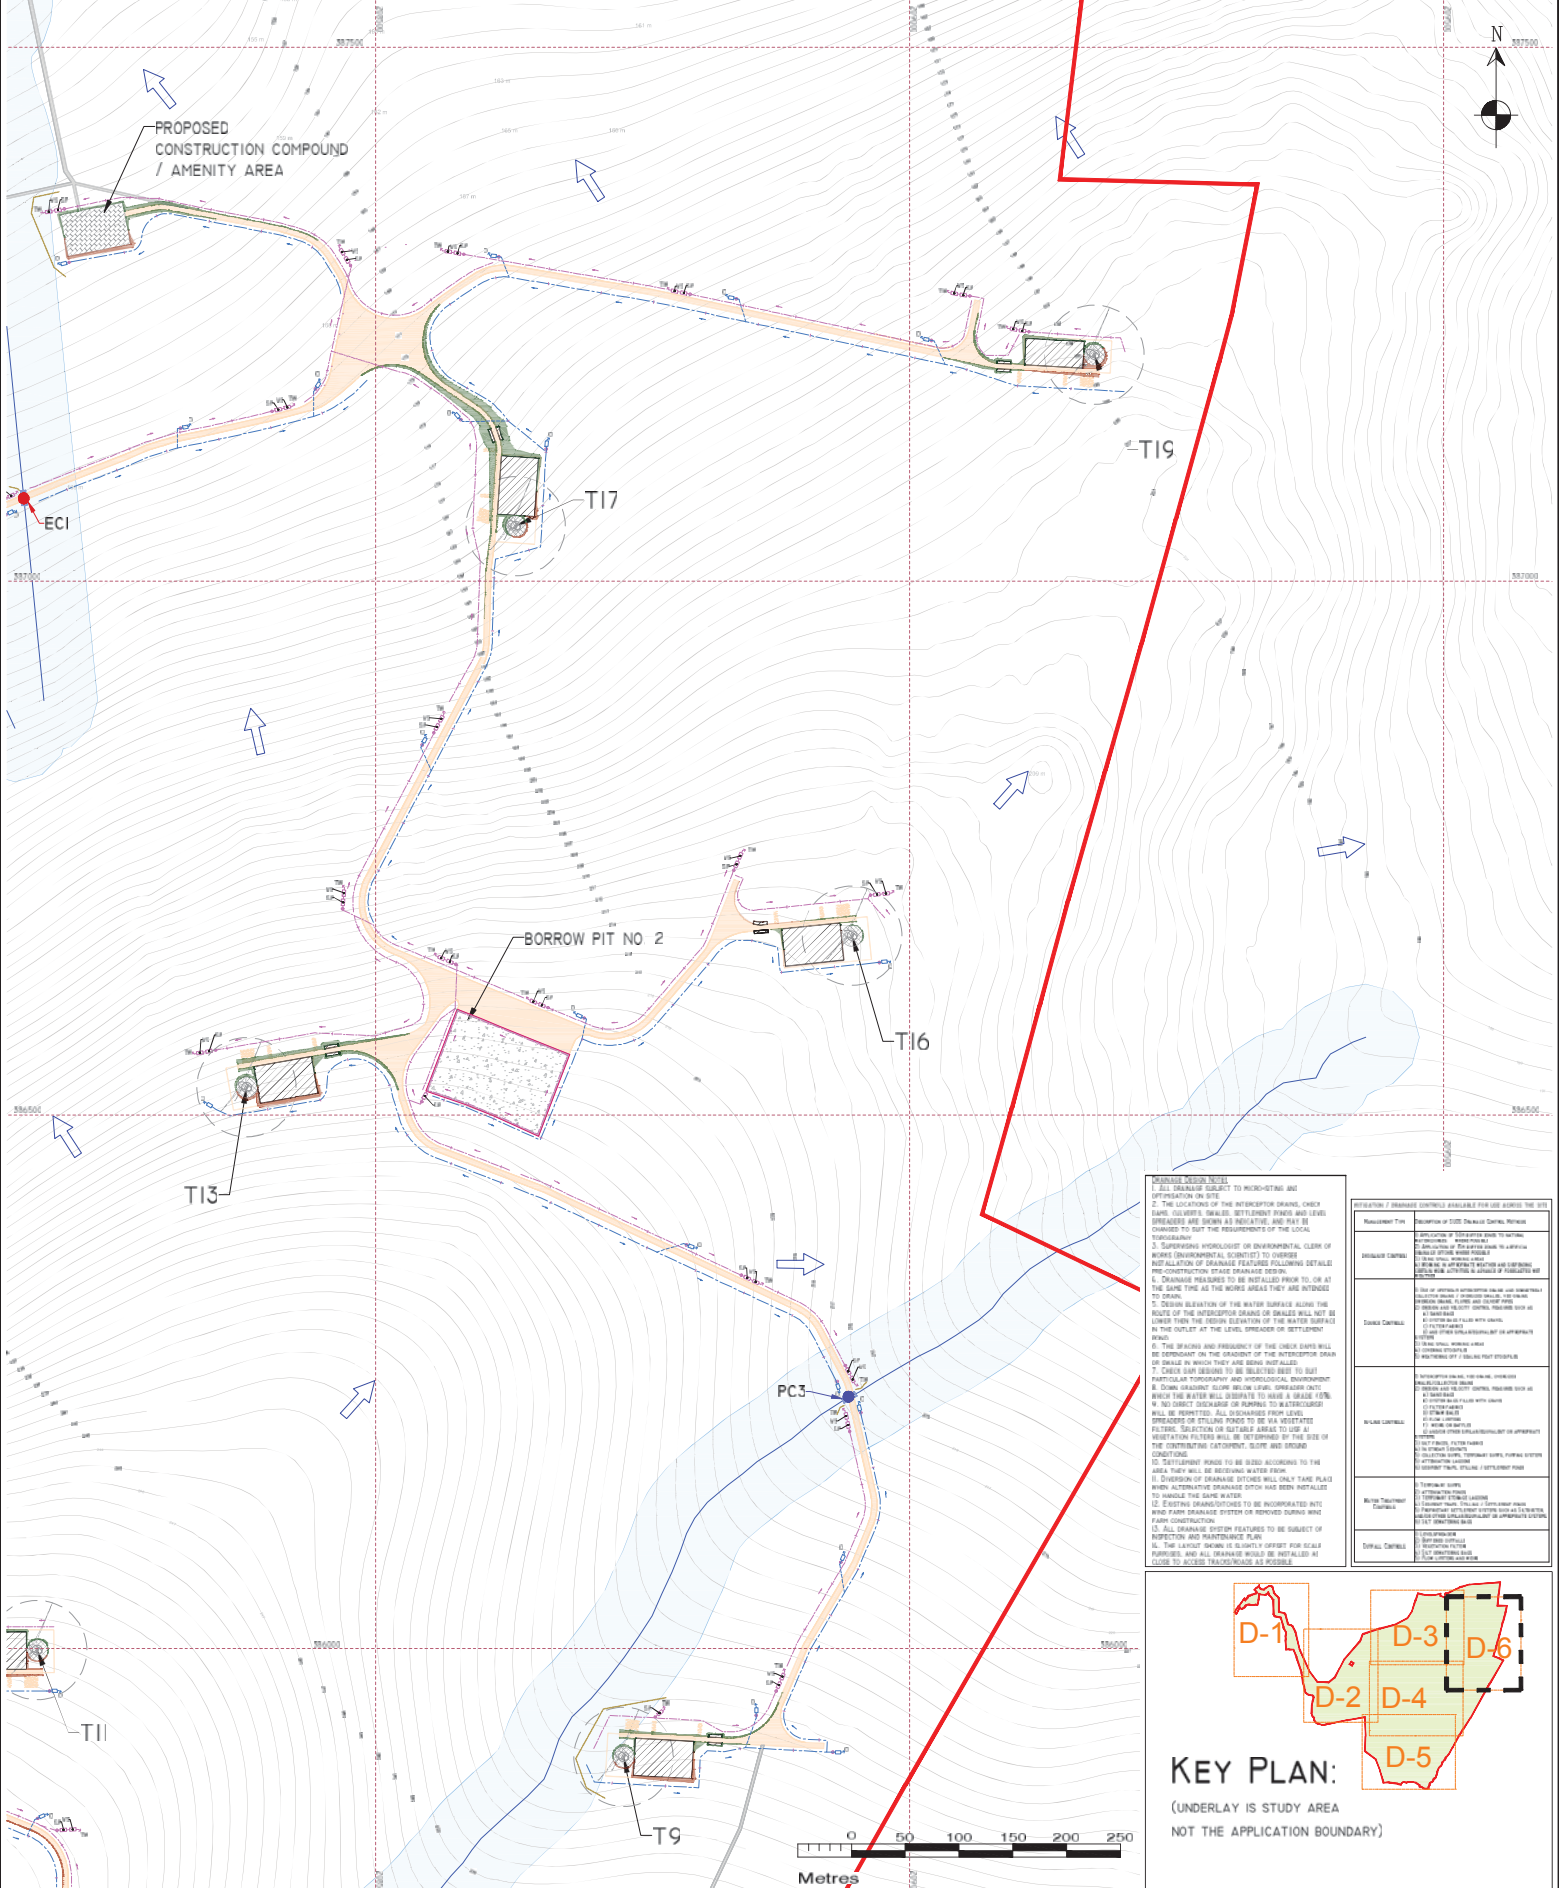

DRAINAGE DESIGN NOTES

1. ALL DRAINAGE SUBJECT TO MICRO-STAGS AND UP-TOPOGRAPHY ON SITE.
2. THE LOCATIONS OF THE INTERCEPTOR DRAINS, CHECK DAMS, SWALES, SETTLEMENT PONDS AND LEVEL SPREADERS ARE SHOWN AS RELATIVE, AND MAY BE CHANGED TO SUIT THE REQUIREMENTS OF THE LOCAL TOPOGRAPHY.
3. SUFFICIENT HYDROLOGICAL OR ENVIRONMENTAL CLEARANCE OF WORKS (ENVIRONMENTAL SCIENTIST) TO OVERSEE AND VALIDATE ALL DRAINAGE RELATED FOLLOWING DETAILED PRE-CONSTRUCTION STAGE DRAINAGE DESIGN.
4. DRAINAGE FEATURES TO BE INSTALLED PRIOR TO, OR AT THE SAME TIME AS THE WORK AREAS THEY ARE INTENDED TO DRAIN.
5. DRAINAGE ELEVATION OF THE WATER SURFACE ALONG THE ROUTE OF THE INTERCEPTOR DRAINS WILL NOT BE LOWER THAN THE DESIGN ELEVATION OF THE WATER SURFACE AT THE OUTLET AT THE LEVEL SPREADER OR SETTLEMENT POND.
6. THE SPACING AND FREQUENCY OF THE CHECK DAMS WILL BE DEPENDANT ON THE GRADIENT OF THE INTERCEPTOR DRAIN OF DRAIN IN WHICH THEY ARE BEING INSTALLED.
7. CHECK DAMS SHOULD BE SO SITED AS TO SUIT PARTICULAR TOPOGRAPHY AND HYDROLOGICAL ENVIRONMENT.
8. DOWN STREAM SLOPE BEHIND CHECK DAMS SHOULD BE SUCH THAT WATER WILL DISPERSE TO SUIT A GRADE WITHIN 10% NO DIRECT DISCHARGE OF RUNOFF TO WATERCOURSE WILL BE PERMITTED. ALL DISCHARGES FROM LEVEL SPREADERS OR SETTLING PONDS TO BE VIA WATERCOURSE FILTER. SELECTION OF FILTERABLE MATERIAL TO USE IN VEGETATION FILTERS WILL BE DETERMINED BY THE SIZE OF THE CONTRIBUTING CATCHMENT, SOILS AND GROUND CONDITIONS.
9. SETTLEMENT PONDS TO BE SITED ACCORDING TO THE AREA THEY ARE BEING DESIGNED TO RECEIVE WATER FROM.
10. DIVERSION OF DRAINAGE DITCHES WILL ONLY TAKE PLACE TO HANDLE THE SAME WATER.
11. EXISTING DRAINAGE DITCHES TO BE INCORPORATED INTO WORKS DRAINAGE SYSTEM OF PROPOSED DRAINAGE WORKS.
12. ALL DRAINAGE SYSTEM FEATURES TO BE SUBJECT OF INSPECTION AND MAINTENANCE PLAN.
13. THE LAYOUT SHOWN IS QUANTITY OFFSET FOR SCALAR PURPOSES, AND ALL DRAINAGE SHOULD BE INSTALLED AT CLOSE TO ACCESS, MAINTENANCE AS POSSIBLE.

Revision / Feature	Description of Change / Details
1	Issue of application for planning permission to the planning authority.
2	Issue of application for planning permission to the planning authority.
3	Issue of application for planning permission to the planning authority.
4	Issue of application for planning permission to the planning authority.
5	Issue of application for planning permission to the planning authority.
6	Issue of application for planning permission to the planning authority.
7	Issue of application for planning permission to the planning authority.
8	Issue of application for planning permission to the planning authority.
9	Issue of application for planning permission to the planning authority.
10	Issue of application for planning permission to the planning authority.
11	Issue of application for planning permission to the planning authority.
12	Issue of application for planning permission to the planning authority.
13	Issue of application for planning permission to the planning authority.
14	Issue of application for planning permission to the planning authority.
15	Issue of application for planning permission to the planning authority.
16	Issue of application for planning permission to the planning authority.
17	Issue of application for planning permission to the planning authority.
18	Issue of application for planning permission to the planning authority.
19	Issue of application for planning permission to the planning authority.
20	Issue of application for planning permission to the planning authority.

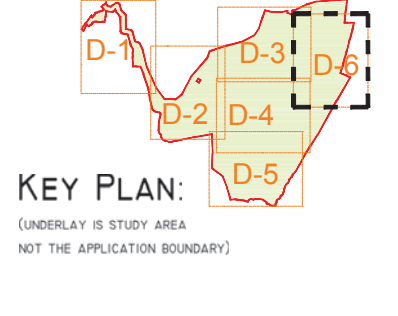

DRAWING LEGEND

	APPLICATION BOUNDARY		EXISTING RIVER / STREAM / LAKE		CHECK DAM TYPE B
	EXISTING ROADS		RIVER / STREAM BUFFER 50M		PROPOSED OLIVERTS / BRIDGES
	EXISTING TRACKS/FOREST ROADS		LAKES		INTERCEPTOR DITCH OLIVERT
	WORKS AREA		LAKES 50M BUFFER		COLLECTOR DITCH OLIVERT
	CRANE PAD		EXISTING OLIVERTS / BRIDGES		OVERLAND FLOW DISCHARGE
	HARDSTANDING AREA		UPSTREAM INTERCEPTOR DRAIN		TREATED WATER DISCHARGE
	BORROW PIT		SWALES / DOWNSTREAM COLLECTOR DRAIN		SETTLEMENT POND
	TURBINE FOUNDATION		DICTION OF FLOW		SWALE / FILTER BED / SECONDARY SW
	TURBINE AND SHEFT AREA		SILT FENCES		PUMPING SLUMP
	SITE LAYOUT IS UNDERLAIN BY 1M INTERVAL CONTOURS TO SHOW MAIN HEAD		DOUBLE / TRIPLE SILT FENCES		ON SITE GRID CONNECTION
	SLOPE / DRAINAGE DIRECTION		SETTLEMENT POND - VEGETATION FILTER + LEVEL SPREADER		
			SETTLEMENT POND - LEVEL SPREADER		

DRAINAGE NOTES

1. DRAWINGS ISSUED ARE FOR PLANNING APPLICATION PURPOSES ONLY.
2. COPYRIGHT, ALL RIGHTS RESERVED. NO PART HERE WITH MAY BE COPIED OR REPRODUCED PARTIALLY OR WHOLLY IN ANY FORM WITHOUT THE WRITTEN NOTICE OF THE COPYRIGHT OWNER.
3. DO NOT SCALE OFF THIS DRAWING. FIGURED METRIC DIMENSIONS ONLY SHOULD BE TAKEN OFF THIS DRAWING.
4. ALL DIMENSIONS ARE IN METRES.

Ordnance Survey Ireland Licence No. EN 0044717
© Ordnance Survey Ireland Government of Ireland

13.12.17	Planning	MG	MG
Date	Description	Chkd	Signed
Revisions			

HYDRO ENVIRONMENTAL SERVICES

22 Lower Main St
Dunganan
Co. Waterford
Ireland

tel: +353 (0) 58-44122
tel: +353 (0) 58-44244
email: info@hydroenvironmental.ie
web: www.hydroenvironmental.ie

Client: MCCARTHY KEVILLE AND O'SULLIVAN

Job: MEENBOG WIND FARM, CO. DONEGAL

Title: DRAINAGE LAYOUT SHEET 6 OF 6

Figure No: DI06 (0502-20)

Drawing No: P1249-2-1217-A1-D106(0502-20)-00A

Sheet Size: A1
Scale: 1:2,500 (A1)
Date: 13/12/2017

Project No: P1249-2
Drawn By: MG/GD
Checked By: MG


Project Design Drawing Notes

1. Drawings are for planning application purposes only. They are not to be used for construction.
2. Copyright. All rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior written consent of McCarthy Keville O'Sullivan Ltd.
3. The use of any information contained in this drawing is at the user's own risk. McCarthy Keville O'Sullivan Ltd. shall not be liable for any loss or damage, whether direct or indirect, arising from the use of this drawing. All dimensions are in millimetres unless otherwise stated.
4. The user is responsible for checking and verifying any and all dimensions and levels that relate to the works.
5. The use of or reliance upon the drawing shall be deemed to be a warranty of the user or reliance upon the drawing. McCarthy Keville O'Sullivan Ltd. shall not be liable for any loss or damage, whether direct or indirect, arising from the use of this drawing.
6. Final levels may vary depending on local ground conditions.
7. Internal electrical cable trench may be installed on either side of site roads.

Drawing Legend

- Planning Application Site Boundary
- - - - - Underground Cabling Routes
- Proposed Drummaibough & Lissala Wind Farm
Proposed Drummaibough & Lissala Wind Farm
Cabling (On Appeal)
(Pt. Ref. 17/56943/ABP Ref. PL/06 2/67/86)
- Route of Meenbog Wind Farm
Independent Grid Connection Cabling

Ordnance Survey Ireland Licence No. A90221617 © Ordnance Survey Ireland/Government of Ireland



DRAWING TITLE
**Grid Connection
(1:2,500) Key Plan**

PROJECT TITLE
Meenbog Wind Farm, Co. Donegal


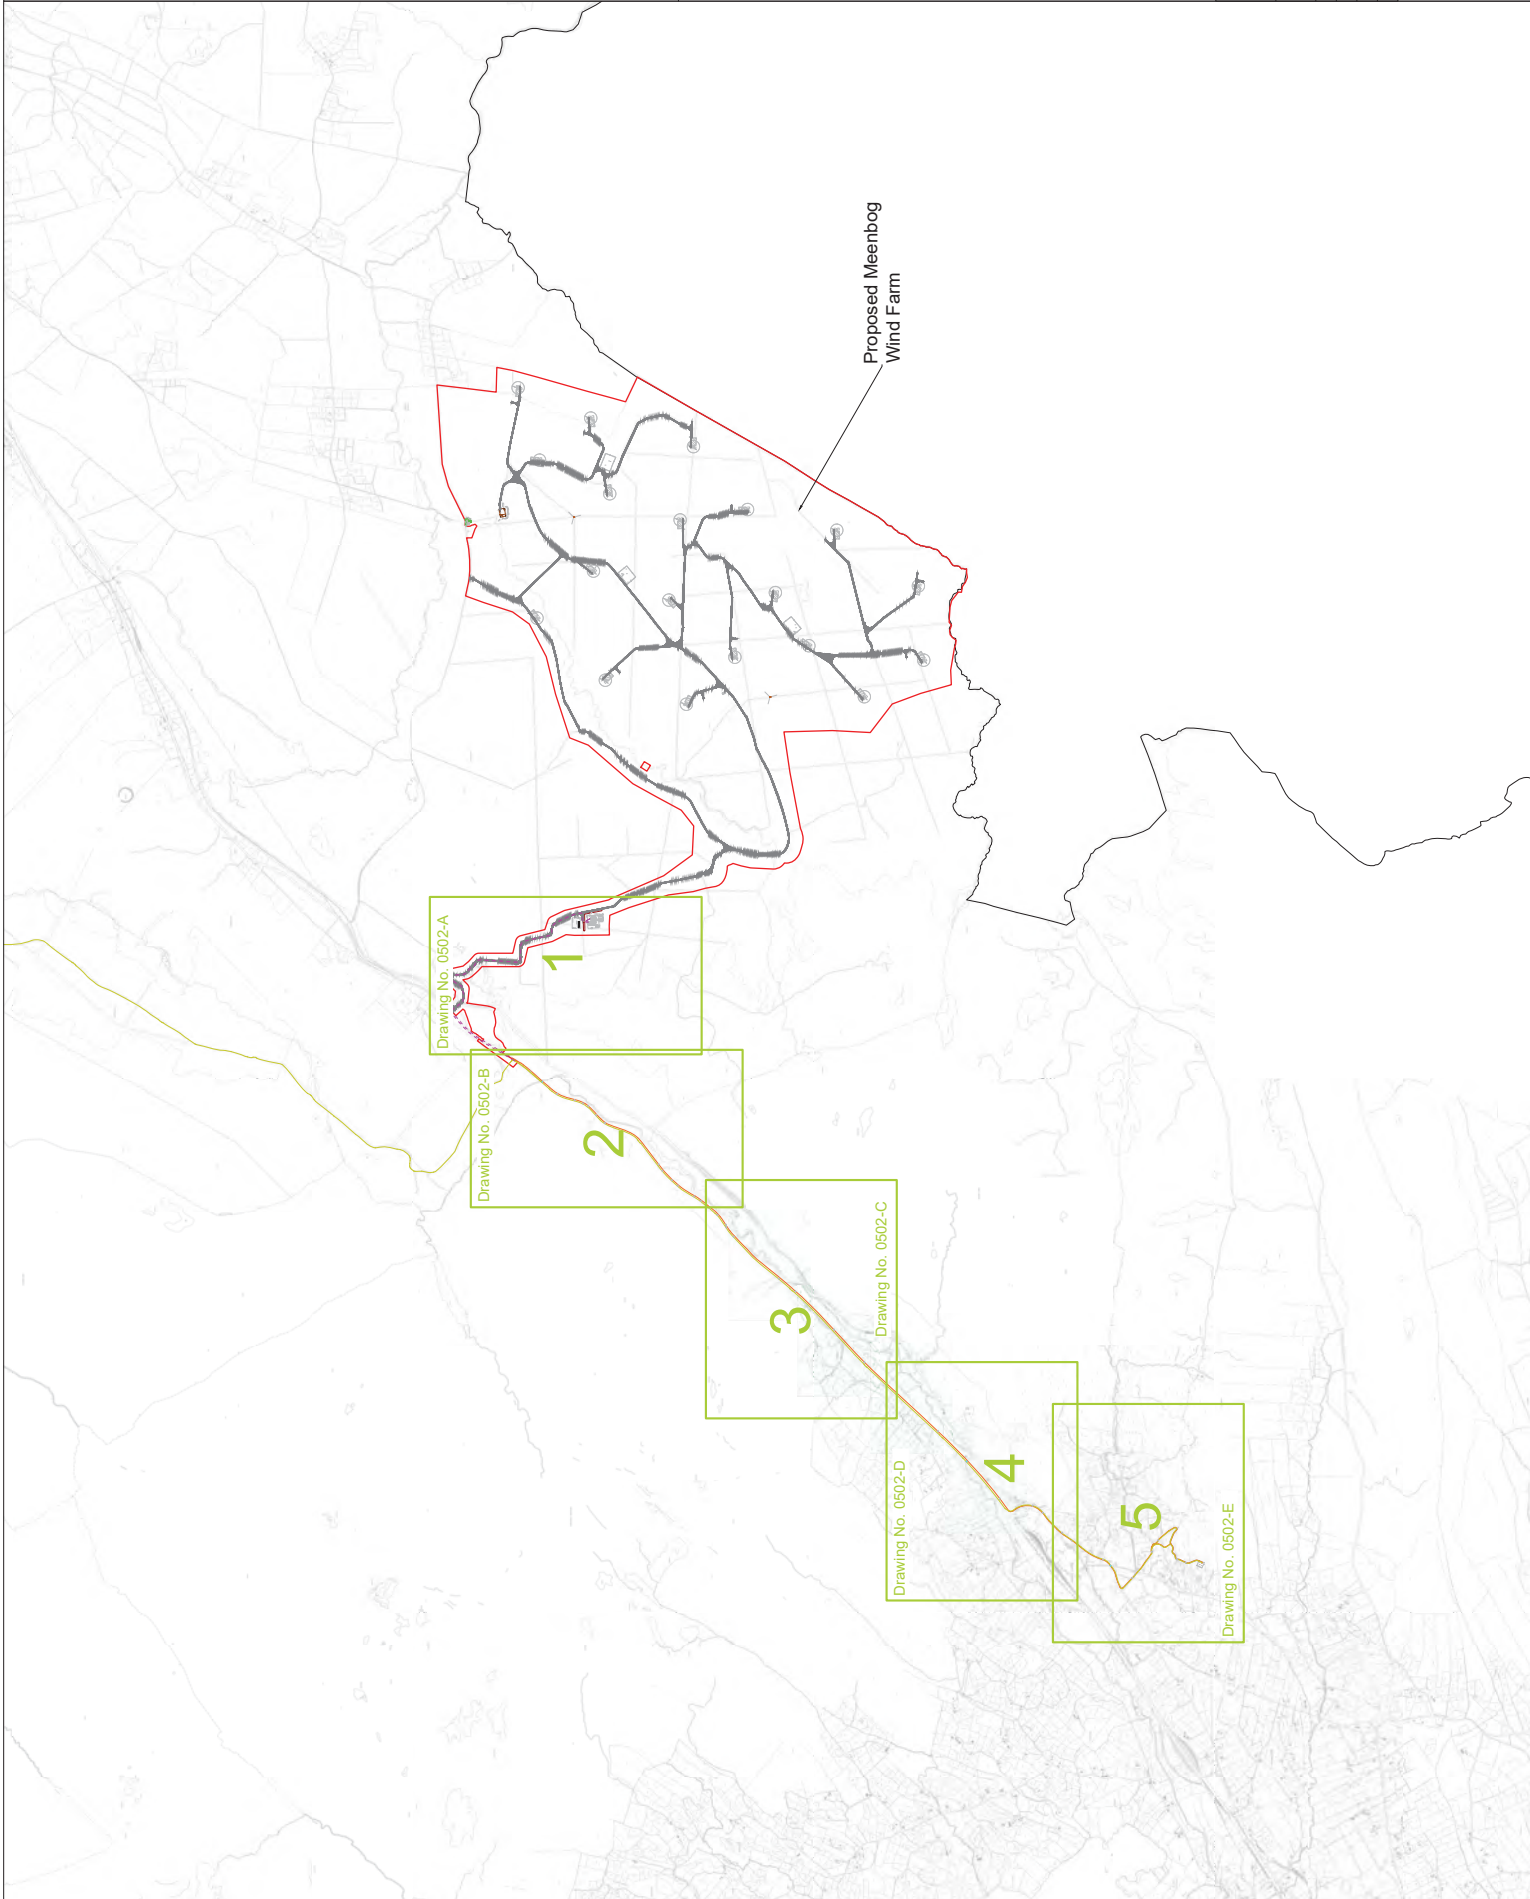
DRAWN BY Joseph O'Brien
DESIGNED BY Michael Watson

PROJECT NO. 160502
DRAWING NO. 0502 - A

SCALE 1:20,000 @ A1
DATE 20.12.2018

COPYRIGHT © 2018 McCarthy Keville O'Sullivan Ltd. All rights reserved. No part of this publication may be reproduced, stored in a retrieval system, or transmitted in any form or by any means, electronic, mechanical, photocopying, recording, or by any information storage and retrieval system, without the prior written permission of McCarthy Keville O'Sullivan Ltd.

McCarthy Keville O'Sullivan Ltd.
Planning & Environmental Consultants
Block 4, Financial Services Centre,
Monaghan Road,
Galway, Ireland.
email: info@mcCarthykeville.ie
www: www.mccarthykeville.ie
Tel: +353 91 733631
Fax: +353 91 771279

Project Design Drawing Notes

1. Drawings issued are for planning application purposes only.
2. Drawings not to be used for construction/contract conditions.
3. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior notice of the copyright owner McCarthy Keville O'Sullivan Ltd.
4. Do not scale off this drawing. Figured metric dimensions only should be taken off this drawing. All dimensions in millimeters unless otherwise stated.
5. All contractors, whether main or sub-contractors, must visit the site and are responsible for taking and checking any and all dimensions and levels that relate to the works.
6. The use of or reliance upon this drawing shall be deemed to be acceptance of these conditions of use unless otherwise agreed in writing, such written agreement to be sought from and issued by the copyright holder to the use or reliance upon this drawing.
7. Layout plans show typical Turbine rotor diameter as per turbine drawing.
8. Final levels may vary depending on local ground conditions.
9. Internal electrical cable trench may be installed on either side of site roads.



Drawing Legend

- Planning Application Site Boundary
- Existing Road to be Upgraded
- - - Existing Floating Road to be Upgraded
- Proposed Road
- - - Proposed Floating Road
- - - Internal Electrical Cable Trench
- / / / Berm
- - - Underground Cabling Routes



**Grid Connection Layout
Plan Sheet 1 of 5**

PROJECT TITLE: Meenbog Wind Farm, Co. Donegal

DRAWING BY: Joseph O'Brien	CHECKED BY: Michael Watson
PROJECT NO: 160502	DRAWING NO: 0502 - B
SCALE: 1:2,500 @ A1	DATE: 20.12.2018

OS SHEET No. 0027 0008 0009 0400 0401 0402 0403 0404 0405 0406 0407 0408 0409 0410 0411 0412 0413 0414 0415 0416 0417 0418 0419 0420 0500 0501 0502 0503 0504 0505 0506 0507 0508 0509 0510 0511




McCarthy Keville O'Sullivan Ltd.
 Planning & Environmental Consultants
 Block 1,
 Galway Financial Services Centre,
 Moneenageisha Road,
 Galway, Ireland.
 email: info@mccarthkyos.ie
 website: www.mccarthkyos.ie
 Tel: +353 91 735611
 Fax: +353 91 771279




Ordnance Survey Ireland License No. AR0021817 © Ordnance Survey Ireland/Government of Ireland

Project Design Drawing Notes

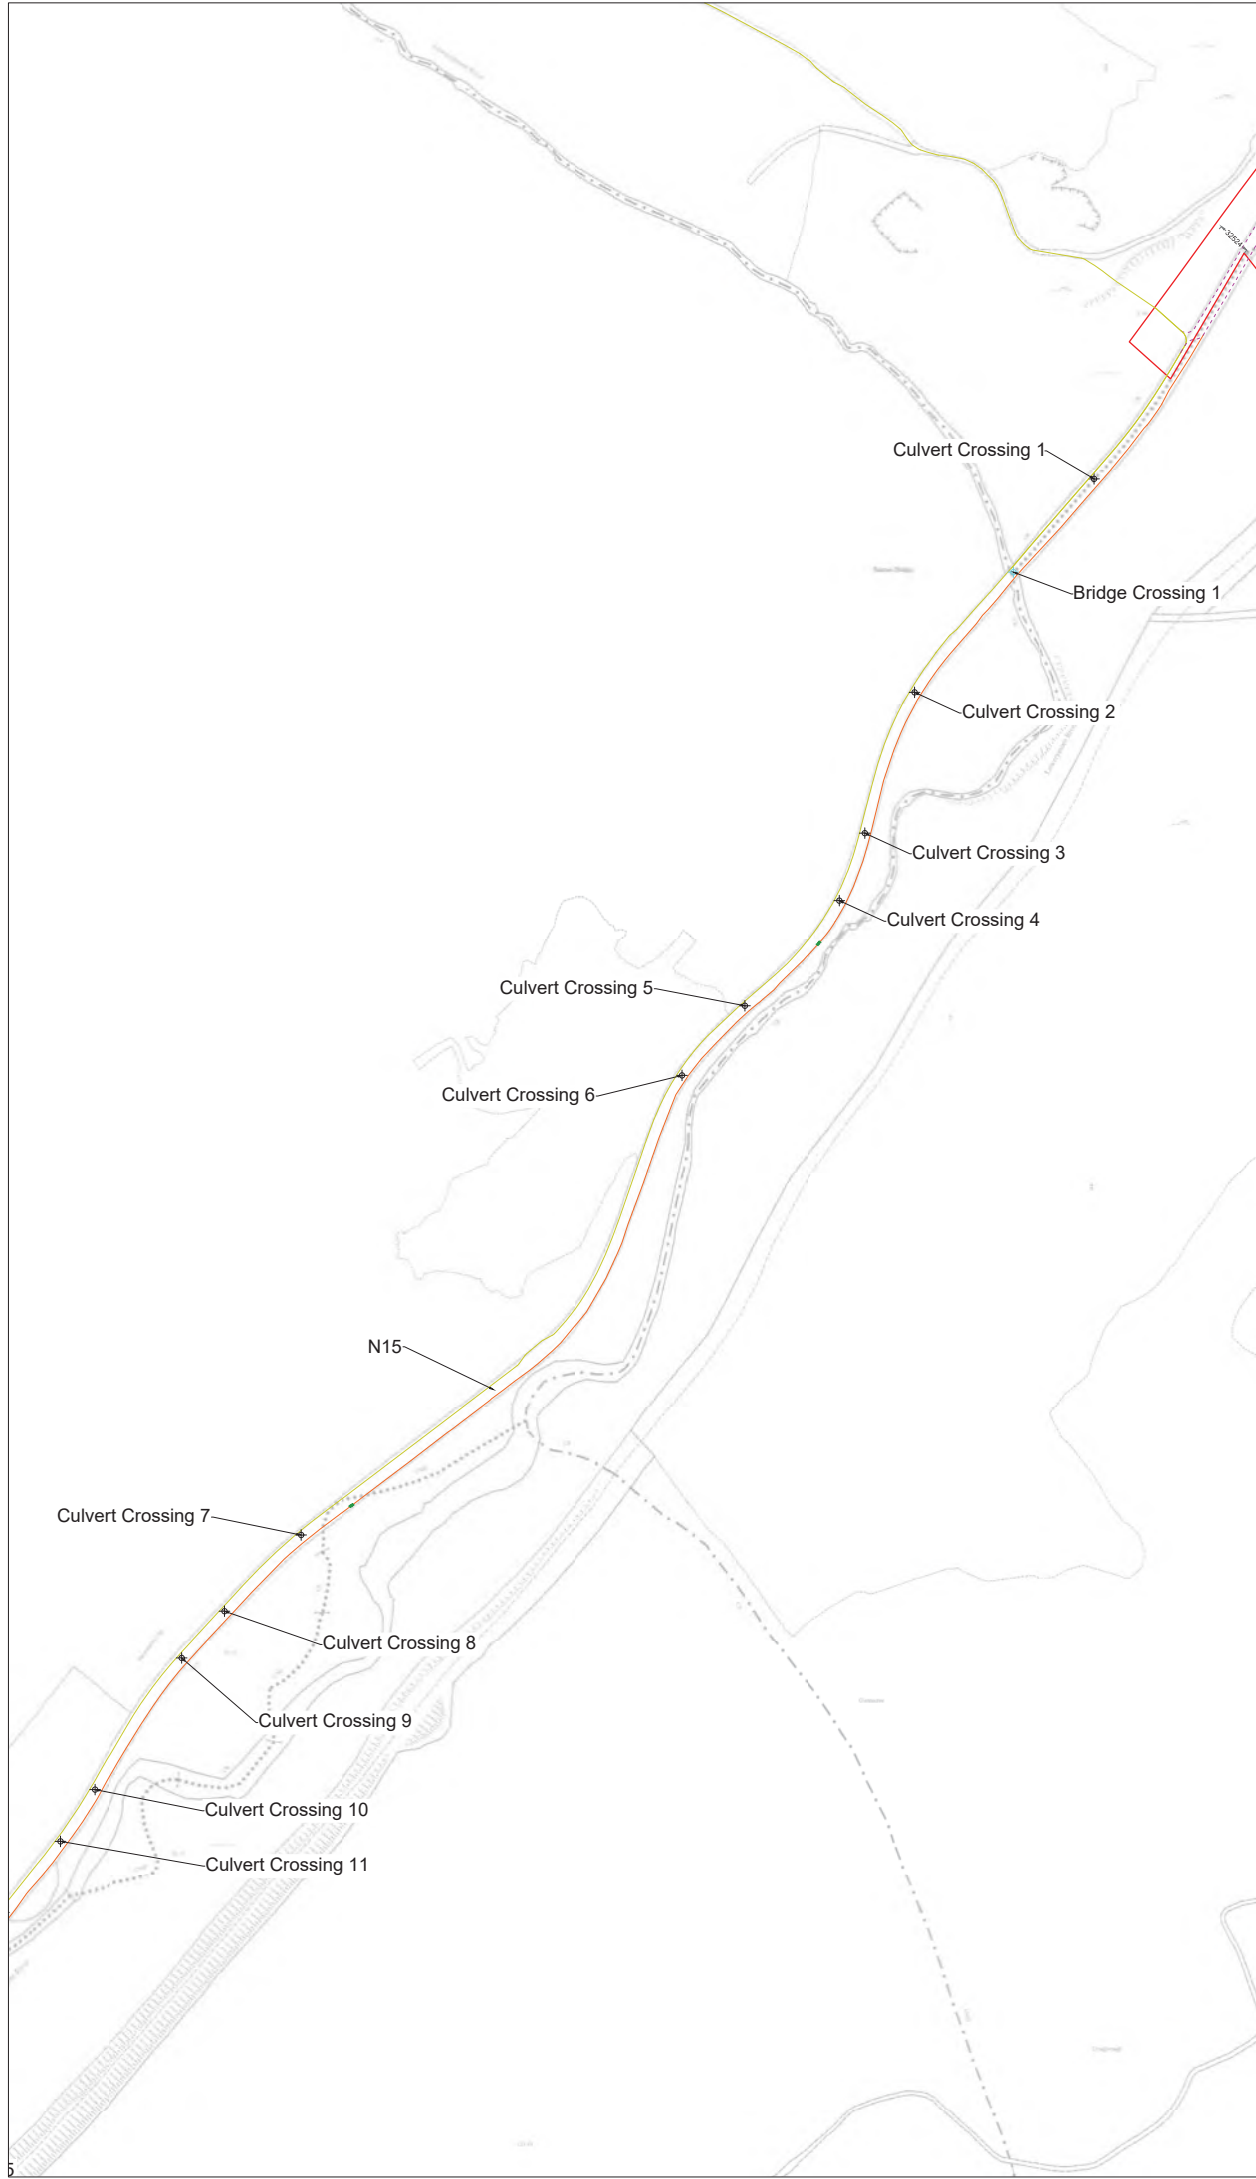1. Drawings issued are for planning application purposes only.
2. Drawings not to be used for construction/contract conditions.
3. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior notice of the copyright owner McCarthy Keville O'Sullivan Ltd.
4. Do not scale off this drawing. Figured metric dimensions only should be taken off this drawing. All dimensions in millimeters unless otherwise stated.
5. All contractors, whether main or sub-contractors, must visit the site and are responsible for taking and checking any and all dimensions and levels that relate to the works.
6. The use of or reliance upon this drawing shall be deemed to be acceptance of these conditions of use unless otherwise agreed in writing, such written agreement to be sought from and issued by the copyright holder to the use or reliance upon this drawing.
7. Layout plans show typical Turbine rotor diameter as per turbine drawing.
8. Final levels may vary depending on local ground conditions.
9. Internal electrical cable trench may be installed on either side of site roads.



Drawing Legend

- Planning Application Site Boundary
- - - Underground Cabling Routes
- Proposed Drumnahough & Lenalea Wind Farm Underground Grid Connection Cabling (On Access) (Pl. Ref. 17/50543 ABP Ref. PLOSE: 248796)
- Route of Meenbog Wind Farm Independent Grid Connection Cabling
-  Culvert Crossing
-  Bridge Crossing
-  Joint Bay

N
↑
Compass rose showing North direction.

DRAWING TITLE
Grid Connection Layout Plan Sheet 2 of 5


PROJECT TITLE
Meenbog Wind Farm, Co. Donegal

DRAWING BY Joseph O'Brien	CHECKED BY Michael Watson
PROJECT NO. 160502	DRAWING NO. 0502 - C
SCALE 1:2,500 @ A1	DATE 20.12.2018

CS SHEET No. 0007 0008 0009 0010 0011 0012 0013 0014 0015 0016 0017 0018 0019 0020 0021 0022 0023 0024 0025 0026 0027 0028 0029 0030 0031

 **McCarthy Keville O'Sullivan Ltd.**
Planning & Environmental Consultants
Block 1,
Galway Financial Services Centre,
Moneenageisha Road,
Galway, Ireland.
email: info@mccarthkyos.ie
website: www.mccarthkyos.ie
Tel: +353 91 735611
Fax: +353 91 771279

Ordnance Survey Ireland License No. AR0021817 © Ordnance Survey Ireland/Government of Ireland

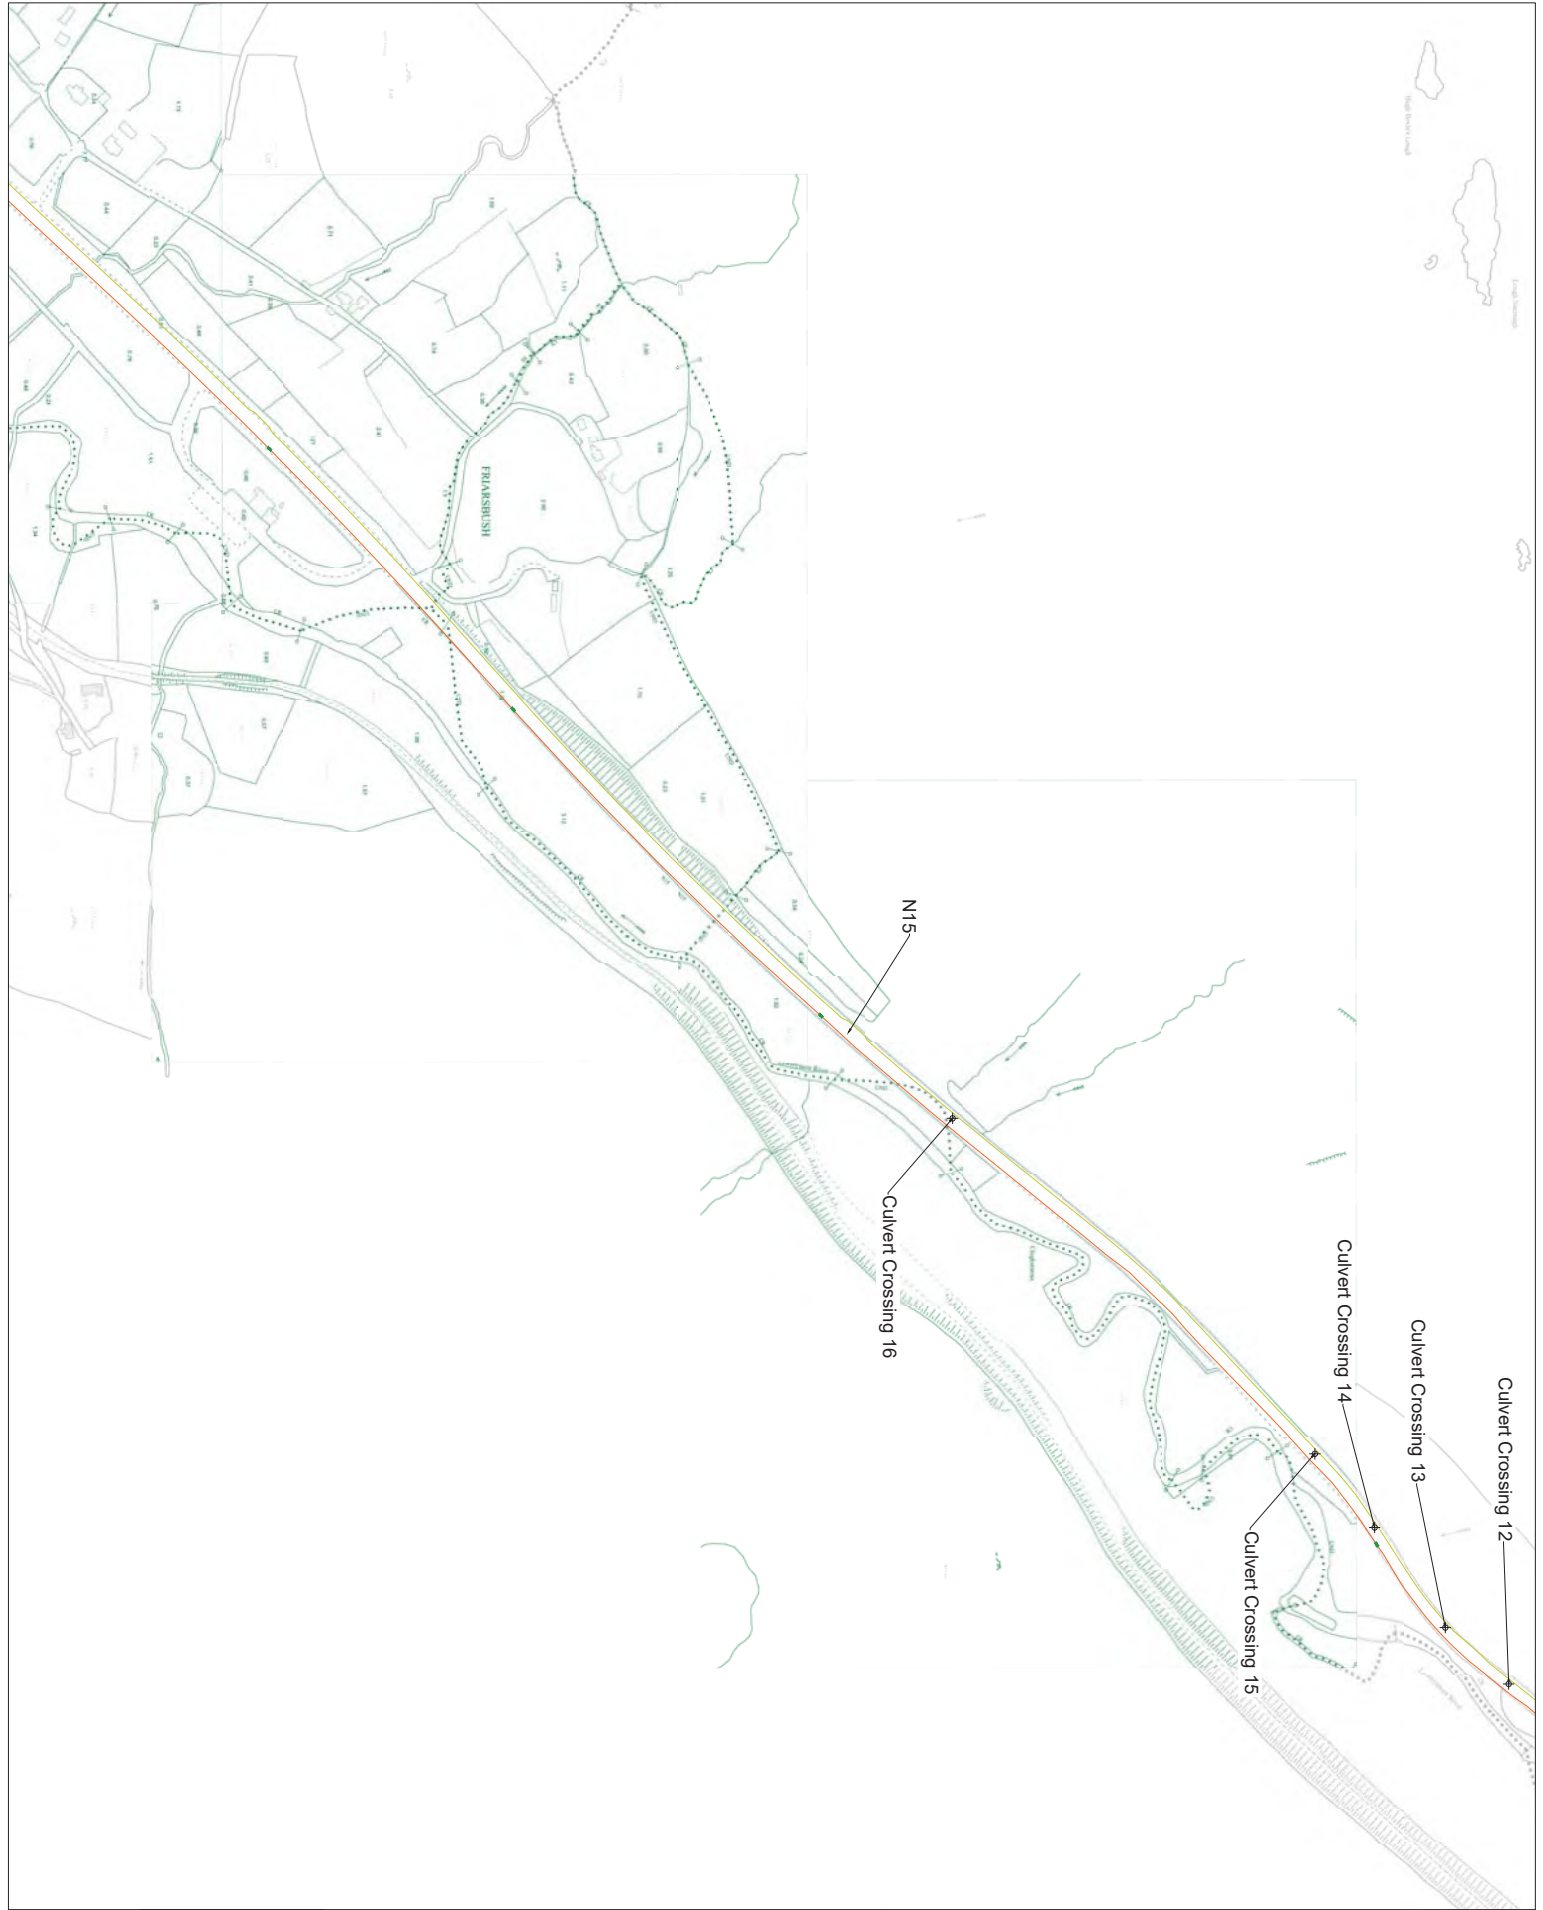

Project Design Drawing Notes

1. Drawings issued are for preparing applications purposes only.
2. All dimensions are in metres unless otherwise stated.
3. Copyright, all rights reserved. No part thereof may be copied or reproduced partially or wholly in any form whatsoever without the prior consent of the copyright owner, McCarthy Keville O'Sullivan Ltd.
4. The user of or reliance upon this drawing shall be deemed to be the user's responsibility for making and checking any and all dimensions and levels that relate to the works.
5. The user of or reliance upon this drawing shall be deemed to be the user's responsibility for making and checking any and all dimensions and levels that relate to the works.
6. The user of or reliance upon this drawing shall be deemed to be the user's responsibility for making and checking any and all dimensions and levels that relate to the works.
7. Final levels may vary depending on local ground conditions.

Drawing Legend

- Proposed Dunmoughagh & Lenealia Wind Farm Underground Grid Connection (PII Ref: 17/2643/ABP Ref: PI/DGE/248798)
- Route of Meenbog Wind Farm Independent Grid Connection Challenging
- Culvert Crossing
- Jarl Bay



Ordnance Survey Ireland Licence No. AR0021817 © Ordnance Survey Ireland/Government of Ireland

Grid Connection Layout
Plan Sheet 3 of 5

PROJECT TITLE: Meenbog Wind Farm, Co. Donegal

DESIGNED BY: Joseph O'Brien	CHECKED BY: Michael Wilson
PROJECT NO: 160502	DRAWING NO: 0502 - D
SCALE: 1:2,500 @A1	DATE: 20.12.2018

McCarthy Keville O'Sullivan Ltd.
Planning & Environmental Consultants
Block 1, Principal Services Centre,
Moontempah Road,
Galway, Ireland.
email: info@cmkyks.ie
Tel: +353 91 729611
Fax: +353 91 77279

Project Design Drawing Notes

- 1. Drawings are for planning application purposes only.
- 2. Copyright, all rights reserved. No part hereof may be copied or reproduced partially or wholly in any form whatsoever without the prior written consent of McCarthy Keville O'Sullivan Ltd.
- 3. The use of or reliance upon this drawing shall be deemed to be a warranty of accuracy by McCarthy Keville O'Sullivan Ltd. unless otherwise stated.
- 4. The use of or reliance upon this drawing shall be deemed to be a warranty of accuracy by McCarthy Keville O'Sullivan Ltd. unless otherwise stated.
- 5. The use of or reliance upon this drawing shall be deemed to be a warranty of accuracy by McCarthy Keville O'Sullivan Ltd. unless otherwise stated.
- 6. The use of or reliance upon this drawing shall be deemed to be a warranty of accuracy by McCarthy Keville O'Sullivan Ltd. unless otherwise stated.
- 7. The use of or reliance upon this drawing shall be deemed to be a warranty of accuracy by McCarthy Keville O'Sullivan Ltd. unless otherwise stated.
- 8. Final levels may vary depending on local ground conditions.

Drawing Legend

- Proposed Drumahaire & Lenalea Wind Farm Underground Grid Connection Cable Route (Pt. Ref. 1756343 ABP Ref. RL06E, 248796)
- Route of Meerabod Wind Farm Independent Grid Connection Cabling
- Culvert Crossing
- Bridge Crossing
- Joint Bay





DRAWING TITLE
Grid Connection Layout
Plan Sheet 4 of 5

PROJECT TITLE
Meerabod Wind Farm, Co. Donegal

DRAWN BY	Joseph O'Brien	CHECKED BY	Michael Watson
PROJECT NO.	160502	UNIVERSITY NO.	0502 - E
SCALE	1:2,500 @ A1	DATE	20.12.2018
COPY FILE NAME	C:\Users\joe\Documents\Projects\160502\160502_04.dwg		

McCarthy Keville O'Sullivan Ltd.
Planning & Environmental Consultants
Block 1 Financial Services Centre,
Monaghan Road,
Galway, Ireland.
email: info@mcortwo.ie
tel: +353 91 735611
fax: +353 91 771279

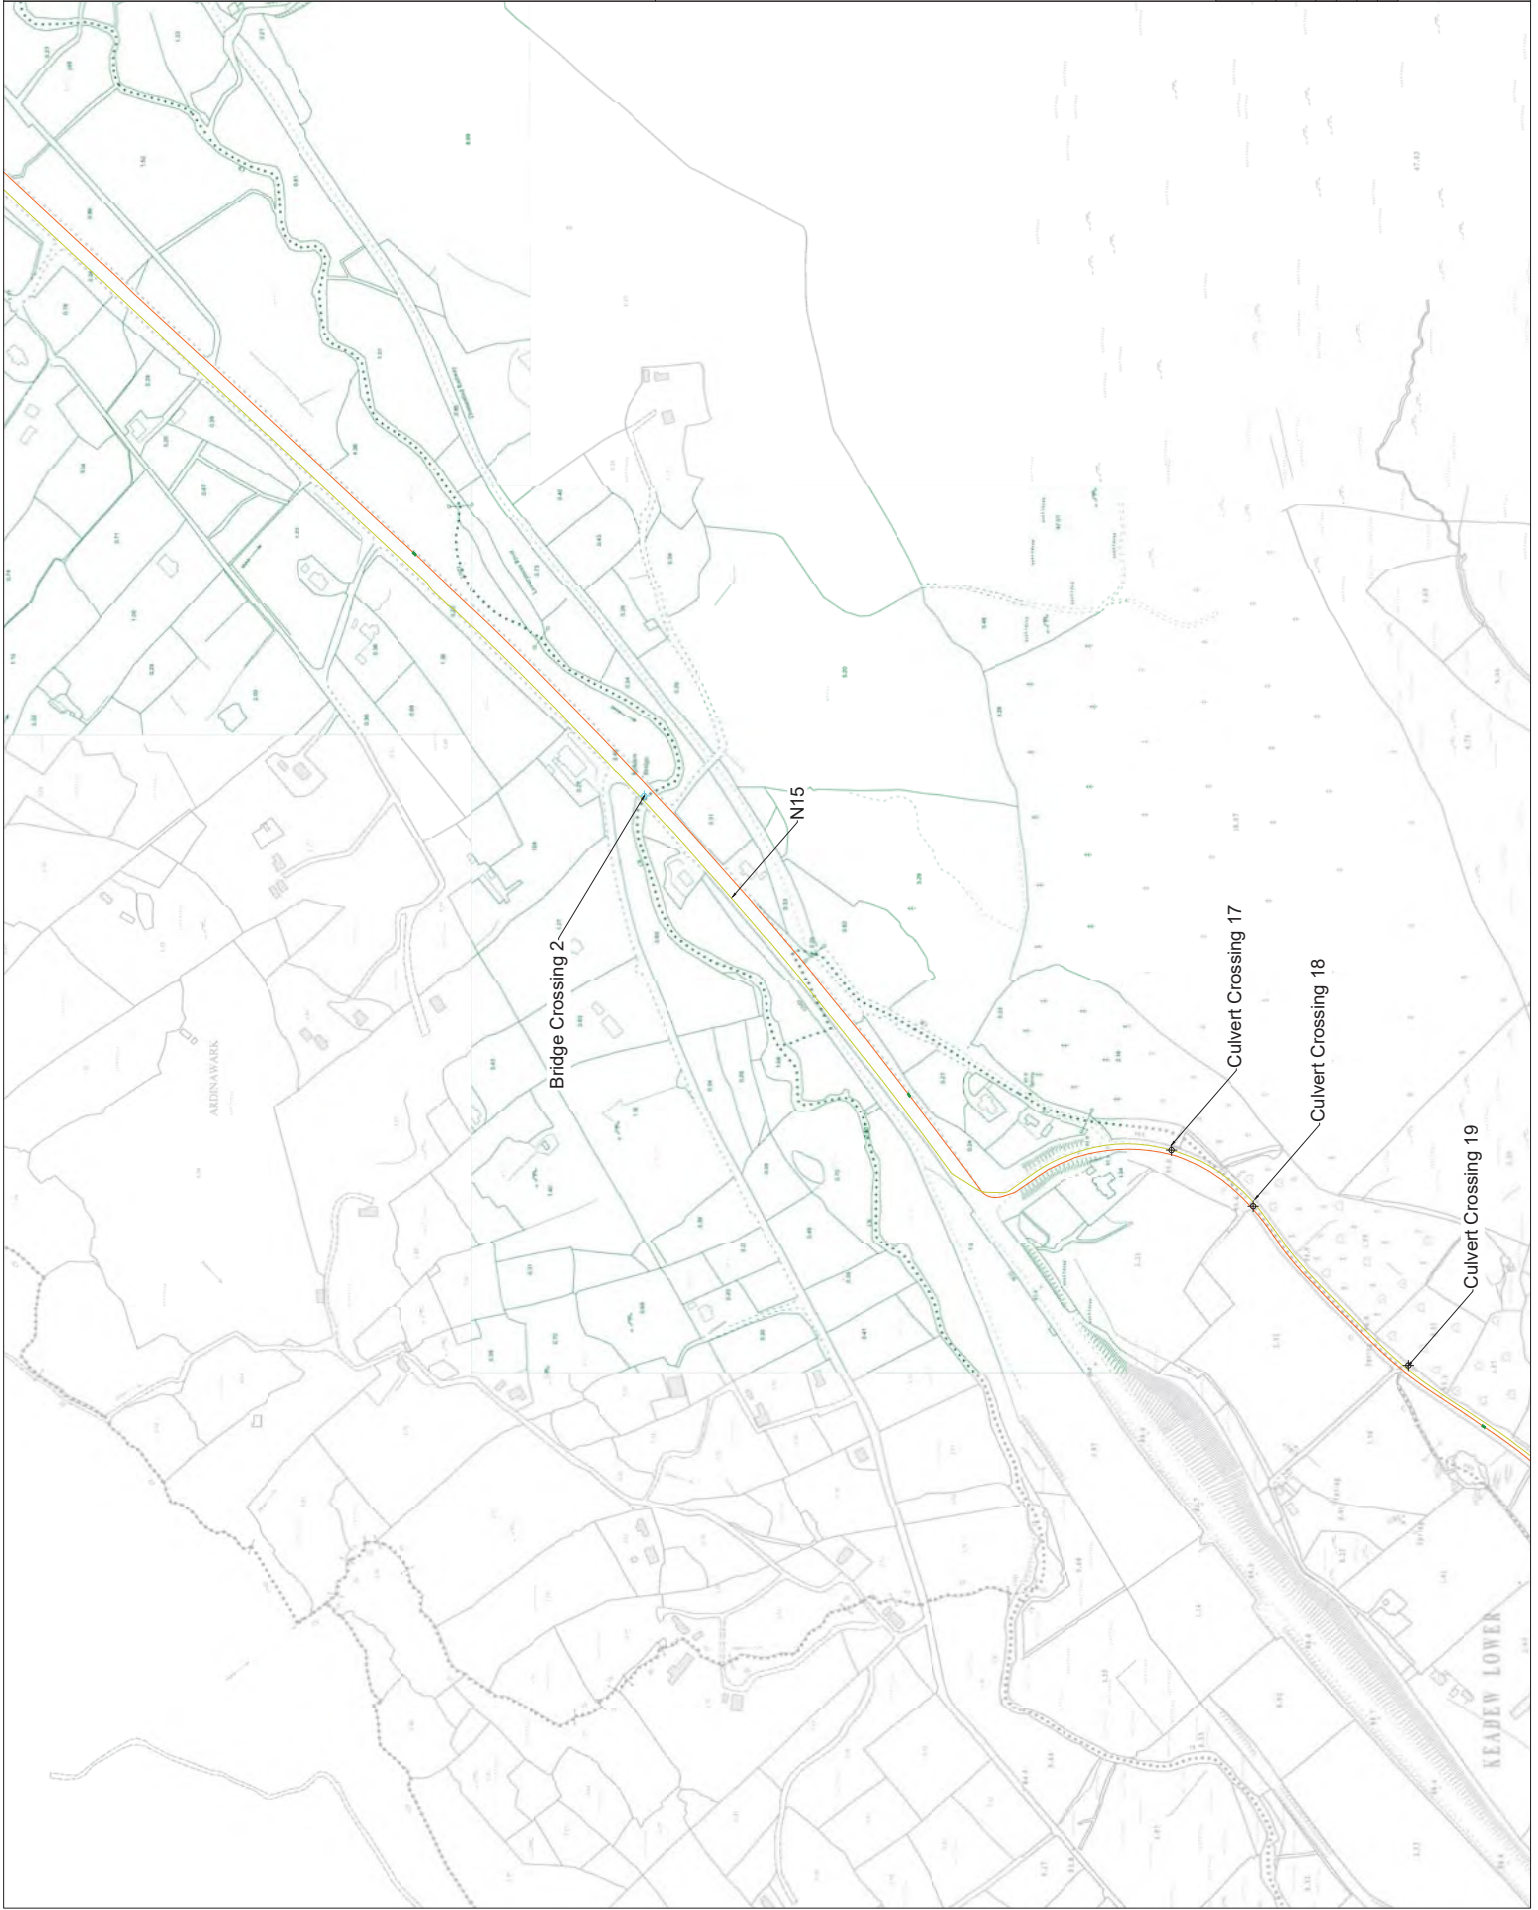

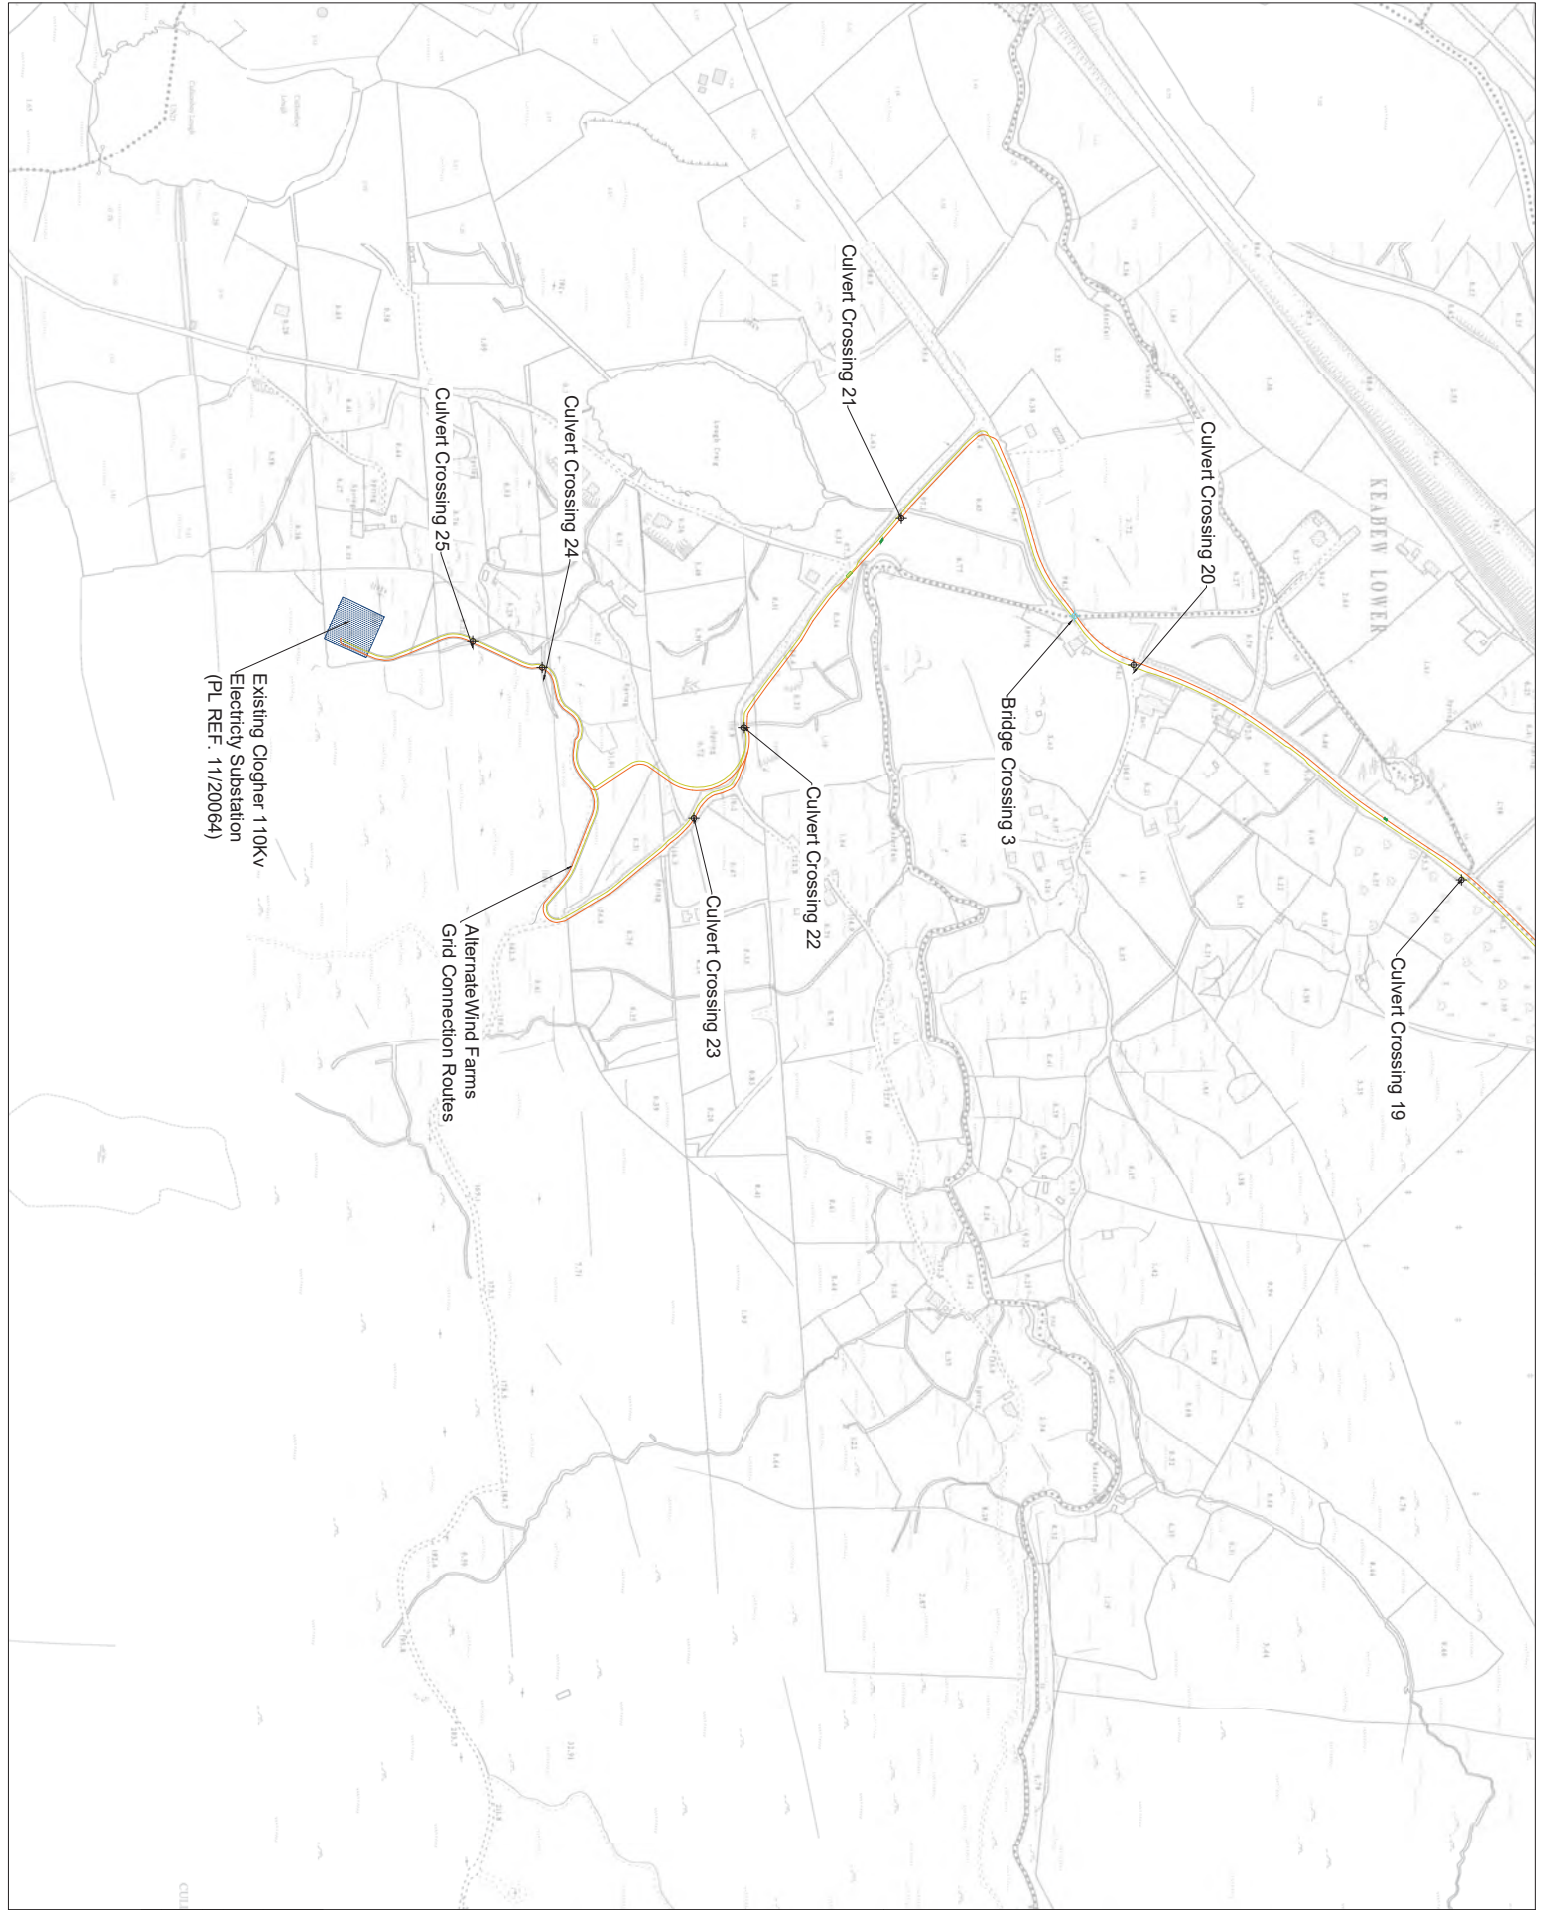

Proposed Design Drawing Notes

1. Drawings issued are for preparing applications purposes only.
2. All dimensions are in metres unless otherwise stated.
3. Copyright all rights reserved. No part thereof may be copied or reproduced partially or wholly in any form whatsoever without the prior consent of the copyright owner McCarthy Keville O'Sullivan Ltd. Any reproduction or use of the drawings without the prior consent of McCarthy Keville O'Sullivan Ltd. should be taken at the user's risk. All dimensions in millimetres unless otherwise stated.
4. The user of the drawings shall be deemed to be responsible for the design and construction of the works and shall be responsible for making and checking any and all dimensions and levels that relate to the works.
5. The user of the drawings shall be deemed to be responsible for the design and construction of the works and shall be responsible for making and checking any and all dimensions and levels that relate to the works.
6. The user of the drawings shall be deemed to be responsible for the design and construction of the works and shall be responsible for making and checking any and all dimensions and levels that relate to the works.
7. The user of the drawings shall be deemed to be responsible for the design and construction of the works and shall be responsible for making and checking any and all dimensions and levels that relate to the works.
8. Final levels may vary depending on local ground conditions.

- Drawing Legend**
- Proposed Dunmoughlin & Linnah Wind Farm Underground Grid Connection (PL Ref: 17/2043 ABP Ref: IN/DSE 248798)
 - Route of Meenbog Wind Farm Independent Grid Connection Channel
 - Culvert Crossing
 - Bridge Crossing
 - Joint Bay



Ordnance Survey Ireland Licence No. AR0021817 © Ordnance Survey Ireland/Government of Ireland

**Grid Connection Layout
Plan Sheet 5 of 5**

PROJECT TITLE: Meenbog Wind Farm, Co. Donegal

DESIGNED BY: Joseph O'Brien

CHECKED BY: Michael Wilson

SCALE: 1:2,500 @A1

DATE: 20.12.2018

PROJECT NO: 160502

CONTRACT NO: 0502 - F

McCarthy Keville O'Sullivan Ltd.
Planning & Environmental Consultants
Block 1, Principal Services Centre,
Moontaspeta Road,
Galway, Ireland.
email: info@cmkoyks.ie
Tel: +353 91 725611
Fax: +353 91 771279

Appendix 2

Schedule of Works Operation Record

Works item no.	Description	Estimated Duration of the works	Risk Schedule 1:very high risk Schedule 2:high risk Schedule 3:intermediate risk	Pre-commencement Triggers all four triggers should be met				Works Abandonment Triggers If any four triggers are met							
				Trigger 1	Trigger 2	Trigger 3	Trigger 4	Trigger 1	Trigger 2	Trigger 3	Trigger 4				
1	Enabling works including felling, site compound establishment welfare facilities, site office and fencing	2 months	Schedule 2	Drainage measures to be installed as per EIS & drainage management plan	Turbidity at baseline levels	Determined by the proximity of the planned sonde location to the works and if readings will be of benefit <i>i.e.</i> if sonde is upstream of the works.	Schedule 2 rainfall figures (see below) utilising reliable forecasting source	Drainage treatment infrastructure installed prior to works commencing And in good working order	River/watercourse turbidity	Turbidity measuring sonde installed prior to works commencing and operating correctly	Weather forecast: (a) during the planned works period (b) observed on site	Damage to silt fence/other drainage measure or drainage point close to capacity	River/watercourse turbidity	Alarm notification from sonde during the works activity. Immediate investigation	Weather forecast: (a) during the planned works period (b) observed on site
2	Borrow pit establishment. Preliminary enabling works and rock excavation operations	6 months	Schedule 1	Drainage measures to be installed as per EIS & drainage management plan	Turbidity at baseline levels	Sonde must be operational with alarm and data analysed before works commence	Schedule 1 rainfall figures (see below) utilising reliable forecasting source	Drainage measures to be installed as per EIS & drainage management plan	Turbidity at baseline levels	Sonde must be operational with alarm and data analysed before works commence	Schedule 1 rainfall figures (see below)	Works cease and emergency response procedure activated including the use and installation of additional pumping equipment, sediments, siltbags and silt fencing	Turbidity 20% above baseline conditions or > 15ntu – subject to baseline data analysis	Works cease and investigation conducted.	Schedule 1 rainfall figures (see below)

Works item no.	Description	Estimated Duration of the works	Risk Schedule 1:very high risk Schedule 2:high risk Schedule 3:intermediate risk	Pre-commencement Triggers all four triggers should be met				Works Abandonment Triggers If any four triggers are met			
				Trigger 1	Trigger 2	Trigger 3	Trigger 4	Trigger 1	Trigger 2	Trigger 3	Trigger 4
3	Site Roads (Stage 1). Excavate new roads, upgrade/widen existing	3-4 months	Schedule 1	Drainage measures to be installed as per EIS & drainage management plan	Turbidity at baseline levels	Sondes in-situ and operational	Schedule 1 rainfall figures (See below) utilising reliable forecasting source	Works cease and emergency response procedure activated including the use and installation of additional pumping equipment, sedimats, siltbags and silt fencing	Turbidity 20% above baseline conditions or >15ntu – subject to baseline data analysis	Works cease and investigation conducted.	Schedule 1 rainfall figures (see below)
4	Turbine foundation excavation and installation	6 months	Schedule 1	Drainage measures to be installed as per EIS & drainage management plan	Turbidity at baseline levels	Sondes in-situ and operational	Schedule 1 rainfall figures (See below) utilising reliable forecasting source	Works cease and emergency response procedure activated including the use and installation of additional pumping equipment, sedimats, siltbags and silt fencing	Turbidity 20% above baseline conditions or >15ntu – subject to baseline data analysis	Works cease and investigation conducted.	Schedule 1 rainfall figures (see below)

Works item no.	Description	Estimated Duration of the works	Risk Schedule 1:very high risk Schedule 2:high risk Schedule 3:intermediate risk	Pre-commencement Triggers all four triggers should be met				Works Abandonment Triggers If any four triggers are met							
				Trigger 1	Trigger 2	Trigger 3	Trigger 4	Trigger 1	Trigger 2	Trigger 3	Trigger 4				
5	Substation construction and connection to the grid	6 months	Schedule 2	Drainage measures to be installed as per EIS & drainage management plan	Turbidity at baseline levels	Sondes in-situ and operational	Schedule 2 rainfall figures (see below) utilising reliable forecasting source	Drainage treatment infrastructure installed prior to works commencing And in good working order	River/watercourse turbidity	Turbidity measuring sonde installed prior to works commencing and operating correctly	Weather forecast: (a) during the planned works period (b) observed on site	Damage to silt fence/other drainage measure or drainage point close to capacity	River/watercourse turbidity	Alarm notification from sonde during the works activity. Immediate investigation	Weather forecast: (a) during the planned works period (b) observed on site
6	Duct installation between turbines and substation and cabling	4 months	Schedule 1	Drainage measures to be installed as per EIS & drainage management plan	Turbidity at baseline levels	Sondes in-situ and operational	Schedule 1 rainfall figures (see below) utilising reliable forecasting source	Drainage treatment infrastructure installed prior to works commencing And in good working order	River/watercourse turbidity	Turbidity measuring sonde installed prior to works commencing and operating correctly	Weather forecast: (a) during the planned works period (b) observed on site	Works cease and emergency response procedure activated including the use and installation of additional pumping equipment, sediments, siltbags and silt fencing	Turbidity 20% above baseline conditions or > 15ntu – subject to baseline data analysis	Works cease and investigation conducted.	Schedule 1 rainfall figures (see below)

Works item no.	Description	Estimated Duration of the works	Risk Schedule 1:very high risk Schedule 2:high risk Schedule 3:intermediate risk	Pre-commencement Triggers all four triggers should be met				Works Abandonment Triggers If any four triggers are met			
				Trigger 1	Trigger 2	Trigger 3	Trigger 4	Trigger 1	Trigger 2	Trigger 3	Trigger 4
7	Site Roads (Stage 2). Further upgrade/maintenace and final surfacing prior to turbine delivery	4 months	Schedule 1	Drainage measures to be installed as per EIS & drainage management plan	Turbidity at baseline levels	Sondes in-situ and operational	Schedule 1 rainfall figures (See below) utilising reliable forecasting source	Works cease and emergency response procedure activated including the use and installation of additional pumping equipment, sedimats, siltbags and silt fencing	Turbidity 20% above baseline conditions or >15ntu – subject to baseline data analysis	Works cease and investigation conducted.	Schedule 1 rainfall figures (see below)
8	Crane delivery and mobilisation	1 month	Schedule 3	Activity not dependent on drainage treatment infrastructure	Turbidity at baseline levels	Sondes in-situ and operational	Schedule 3 rainfall figures (See below) utilising reliable forecasting source	Activity not dependent on drainage treatment infrastructure	Activity not anticipated to effect turbidity	Activity not dependent on sonde data	Activity not weather dependent
9	Turbine delivery	3 months	Schedule 3	Activity not dependent on drainage treatment infrastructure	Activity not anticipated to effect turbidity	Activity not dependent on sonde data	Activity not weather dependent	Activity not dependent on drainage treatment infrastructure	Activity not anticipated to effect turbidity	Activity not dependent on sonde data	Activity not weather dependent

Works item no.	Description	Estimated Duration of the works	Risk Schedule 1:very high risk Schedule 2:high risk Schedule 3:intermediate risk	Pre-commencement Triggers all four triggers should be met				Works Abandonment Triggers If any four triggers are met			
				Trigger 1	Trigger 2	Trigger 3	Trigger 4	Trigger 1	Trigger 2	Trigger 3	Trigger 4
10	Turbine erection	2-3 months	Schedule 3	Drainage treatment infrastructure installed prior to works commencing And in good working order	River/watercourse turbidity	Turbidity measuring sonde installed prior to works commencing and operating correctly	Weather forecast: (a) during the planned works period (b) observed on site	Damage to silt fence/other drainage measure or drainage point close to capacity	River/watercourse turbidity	Alarm notification from sonde during the works activity. Immediate investigation	Weather forecast: (a) during the planned works period (b) observed on site
11	Commissioning and testing of operational turbines	2 months	Schedule 3	Activity not dependent on drainage treatment infrastructure	Activity not anticipated to effect turbidity	Activity not dependent on sonde data	Activity not determined by rainfall	Activity not dependent on drainage treatment infrastructure	Activity not anticipated to effect turbidity	Activity not dependent on sonde data	Activity not weather dependent
				Activity not dependent on drainage treatment infrastructure	Activity not anticipated to effect turbidity	Activity not dependent on sonde data	Activity not weather dependent	Activity not dependent on drainage treatment infrastructure	Activity not anticipated to effect turbidity	Activity not dependent on sonde data	Activity not weather dependent

Trigger 4: activities should not begin or should cease if the following rainfall amounts are forecasted:	
Schedule 1 – Very high-risk activities	>10 mm/hr (i.e. high intensity local rainfall events) >25 mm in a 24-hour period (heavy frontal rainfall lasting most of the day); or, > half monthly average rainfall in any 7 days. No overland flow or pathway for water movement Conditions on the ground match the forecast
Schedule 2 – High risk activities	>10 mm/hr (i.e. high intensity local rainfall events) >25 mm in a 24-hour period (heavy frontal rainfall lasting most of the day); or, > half monthly average rainfall in any 7 days. Conditions on the ground match the forecast
Schedule 3 – Intermediate risk	>10 mm/hr (i.e. high intensity local rainfall events) >25 mm in a 24-hour period (heavy frontal rainfall lasting most of the day); or, > half monthly average rainfall in any 7 days. Conditions on the ground match the forecast

Appendix 3

Wind Farm Site Culvert Assessment

Crossing ID	Location Description	Easting	Northing	Culvert Type	Culvert Dimensions (m)			Channel Dimensions			Water Depth (m)	Catchment Area (km ²)	Existing Culvert Capacity (m ³ /s)	100 Year Flow (m ³ /s)	Hydraulic Status of Existing Crossing	Minimum Pipe Culvert Diameter Required (mm)
					Diameter	Width	Height	Bottom Width	Top Width	Depth						
EC1	Road between T15 and T17	208169	387078	Pipe	600	-	-	0.7	1	1.5	0.2	0.083	0.54	0.171	Adequate	-
EC2	Road between T15 and T17	208130	387062	Pipe	400	-	-	1.5	2	1.5	0.15	0.083	0.165	0.171	Upgrade Required	900
EC3	Road between T15 and T17	208038	387003	Pipe	600	-	-	2	3	2	0.2	0.083	0.54	0.171	Adequate	-
EC4	Southwest of Borrow Pit 1	207640	386362	Pipe	600	-	-	1.5	1.5	0.7	0.3	0.448	0.54	0.767	Upgrade Required	900
EC5	Southwest of proposed met mast	205684	385277	Box	-	2.5	1.5	2.5	2.5	1.2	0.2	2.58	26.005	3.644	Adequate	-
EC6	Southwest of proposed met mast	205791	385190	Pipe	900	-	-	1	1	1.3	0.1	0.9	1.66	1.427	Adequate	-
EC7	Southeast of T10	207012	385739	Pipe	500	-	-	0.5	1	1.5	0.2	0.16	0.32	0.307	Adequate	-
EC8	South of T10	206862	385608	Pipe	400	-	-	0.5	1.5	1	0.15	0.15	0.165	0.290	Upgrade Required	900
EC9	Southwest of T12	207461	385985	Pipe	900	-	-	0.5	1	1	0.2	0.2	1.66	0.374	Adequate	-
EC10	Southeast of T12	207708	385973	Pipe	900	-	-	1.5	1.5	1	0.1	0.189	1.66	0.356	Adequate	-
EC11	East of T8	207843	385627	Pipe	600	-	-	0.5	0.5	1	0.25	0.136	0.54	0.266	Adequate	-
EC12	Northwest of T14	206593	384481	Pipe	600	-	-	1.5	1.5	1	0.15	0.192	0.54	0.361	Adequate	-
EC13	South of substation	205692	385486	Pipe	600	-	-	1.5	2	2.5	0.1	0.1	0.54	0.202	Adequate	-
EC14	Just north of proposed substation	205314	386479	Pipe	750	-	-	1.5	1.5	1	0.2	0.3	1	0.537	Adequate	-
EC15	Southwest of Borrow Pit 1	207480	386240	n/a	-	-	-	-	1.2	0.7	0.25	0.24	-	0.440	Not determined	900
EC16	Furthest west along the site entrance road	205040	387030	-	-	-	-	-	-	-	-	-	-	-	Not determined	-
EC17	South of T10	206862	385608	Pipe	400	-	-	0.5	1.5	1	0.15	0.15	9.2	0.000	Upgrade Required	900
EC18	West of T10	206135	386006	Pipe	300	-	-	1	1.5	1	0.1	0.164	0.066	0.314	Upgrade Required	900
EC19	North of T14	206804	386851	Pipe	900	-	-	1.5	2	1.5	0.2	0.57	1.66	0.951	Adequate	-

Appendix 4

Traffic Management Plan



Civil Engineering

Traffic Management Plan Meenbog WF – Construction Stage



January 2019

Telephone: +353 (0) 21 733 6034, Fax: +353 (0) 21 733 6145
Web: www.mceengineering.ie, Email: office@mceengineering.ie
Lissarda Industrial Estate, Lissarda, Cork, Ireland.

MCE – Meenbog WF's Traffic Management Plan

Contractor: MCE ltd.

Project name: Meenbog Wind Farm

Address: Croaghonagh & Meenbog, Co. Donegal.

Name : Thomas Scanlan – Tel: 021-2066910
Chris Murnane – Tel: 086 -7955083

Email: thomas.scanlan@turnkeydev.com
chris.murnane@gmail.com

Site supervisor: TBC

Safety officer: TBC

Description of task: Traffic Management Plan for Meenbog WF Construction Stage

Key plant: Construction Traffic e.g.
Lorries,
Excavator transport vehicles
Site vehicles
Tractors & trailers

Specific Training: FAS safe pass
CSCS plant ticket
Site induction

MCE – Meenbog WF's Traffic Management Plan

Introduction:

This traffic management plan outlines the traffic calming measures along the N15 and the L-6554 local road around the wind farm entrances for the construction stage process. The entrance (Location 1 on Drg. No. 614) on the N15, is the main entrance in which turbines will be delivered into the site. All traffic management will comply with guidance given in Chapter 8, Traffic Signs Manual, Department of Transport November 2006 and Control and management of Traffic at Road Work October 2007.

Local Access for Residents

As part of the traffic management plan local residents will be alerted to the works through the use of letter drops and prior consultation, if required.

Every effort will be made to limit the effect on local residents and any residents who require special provisions to be made will be accommodated (i.e. Home carer, etc.). Traffic management plans will be reviewed on a daily basis and take into account all local parameters in the area. All required Roadwork Temporary Traffic Management Design Sheets will be completed and kept on site.

Pedestrian & Cyclist Management

Construction traffic & operatives will be made aware to watch out for oncoming pedestrians / cyclists.

MCE – Meenbog WF's Traffic Management Plan

Dealing With Emergency Services

Gardaí will be advised of the intended works prior to commencement on the Gardaí Consultation form. Emergency services using the local roads will be given priority.

Signage Plan

All works will be signed in accordance with the “Guidance for the Control and Management of Traffic at Road Works” (Second Edition 2010). The Routine Works Traffic Management Design, including the layout parameters is illustrated on attachment.

A fully certified and competent ‘Signing Lighting & Guarding’ officer will sign off on the works before commencement and carry out routine monitoring. A qualified supervisor will be on site at all times.

- ✓ See attached traffic management design sheet for signage etc.
- ✓ The entire traffic management system will be set up prior to any works commencing.
- ✓ Only approved signs will be used on approach to the wind farm entrances.
- ✓ All signs will be clean and clearly visible.
- ✓ Once signs are in place the route will be assessed to ensure adequate visibility for drivers and pedestrians.
- ✓ All signs will be secured and weighted down where appropriate.
- ✓ Contractor vehicles will be parked with consideration given to traffic management plan.

MCE – Meenbog WF's Traffic Management Plan

Overview Drawings:

The following drawings are included at the end of this document:

- ✓Drg. No. 614 – Construction Stage Overall Layout View
- ✓Drg. No. 615-1 – Sheet 1 of 2 – Location 1 Layout
- ✓Drg. No. 615-2 – Sheet 2 of 2 – Location 2 Layout

Signage Layout On Approach To The Wind Farm Entrances

The following is the layout for signage that will be in place on the approach to the wind farm entrances. See attached Drg. No. 615-1 showing signage layout entering the wind farm from the N15 and Drg. No. 615-2 showing signage layout entering the wind farm from the L-6554:

- ✓Sign no 1: WK001 / P011D indicates sign 600m before entrance “Man with Shovel”
 - ✓Sign no 2: RUS014 indicates sign 400m before entrance “No Overtaking”.
 - ✓Sign no 6: CON039 indicates sign 200m before entrance “Caution Construction Site Entrance 200m”
 - ✓Signage after road works will indicate 'No Overtaking Ends' and 'End of Road Works'.
- Traffic entering and exiting existing secondary road will continue as normal with construction traffic kept to a minimum.

ROUTINE WORKS TRAFFIC MANAGEMENT DESIGN

SHUTTLE CONTROL SELECTION

Method	Max Speed Limit (km/h)	Length of Works (m)	Max Traffic (veh/hr)	3 Min Count	Notes
All Stop	100	n/a	300	15	15-10 mins max.
Give and Take	50	50	400	20	Clear Visibility required from both directions
Priority	100	80	840	42	Speed Limit 50 km/h distance from before an obstruction to a point an equal distance beyond the obstruction. If used at night, will require a warning beacon.
Stop/Go	100	20	500	25	Can be Single Man/Single Sign 100 Can be single Man-Auto Sign 100 Can be single Man-Auto Sign 100 Can be single Man-Two Sign 100 Can be single Man-Two Sign 100 Has to be Two Man-Two Sign 100 Has to be Two Man-Two Sign 100 Has to be Two Man-Two Sign
Traffic Lights	100	500/n/a	n/a	n/a	Vehicle Actuated

NOTE: WHEN USING SHUTTLE CONTROL, TAPERS ARE AT 45 DEGREES

LAYOUT PARAMETER SELECTION SHEET

Type of Road	Advance Sign Distance (D) (m)	Min No. & Type Of Advance Signs In Sequence	Min clear visibility of Signs (m)	Min size of signs (mm)	Min height of cones (mm)	Long. Safety Zone (L) (m)	Side. Safety Zone (S) (m)	Long. Cone Space (m)	Long. Lamp Space (m)	Lane Taper Multiply factor	Taper Cone Spacing (m)	Taper Lamp Spacing (m)	Lead-in cone tapers (See Notes below)	Recommended lengths	Width of hazard (including safety zone) NOTE: TAPERS ARE ONLY WHERE TWO WAY TRAFFIC MAINTAINED	Hard Shoulder Taper Multiply factor
Single carriageway road, 30km/h	50	1 (r.w.a.) 1 (t.m.)	50	600	450	5	0.5	6	12	8	3	9	Length of taper (T) in (m) Minimum No. of Cones	1 m 2 m 3 m 4 m	32 12	4
Single carriageway, 60km/h	50	1 (r.w.a.) 1 (t.m.)	50	600	450	5	0.5	6	12	8	3	9	Length of taper (T) in (m) Minimum No. of Cones	1 m 2 m 3 m 4 m	32 12	4
Single Carriageway 80km/h	600	1 (r.w.a.) 1 (n.o.) 1 (t.m.)	90	750* 900*	750	45	1.2	12	24	35	2.5	9	Length of taper (T) in (m) Minimum No. of Cones	1 m 2 m 3 m 4 m	140 58 17	20
Single Carriageway 100 km/h	800	1 (r.w.a.) 1 (n.o.) 2 (t.m.)	120	750* 900*	750	60	1.2	12	24	40	1	9	Length of taper (T) in (m) Minimum No. of Cones	1 m 2 m 3 m 4 m	160 162 19	20
Dual Carriageway 60 km/h	600	1 (r.w.a.) 2 (t.m.) X 2	50	900	450	5	0.5	6	12	8	3	9	Length of taper (T) in (m) Minimum No. of Cones	1 m 2 m 3 m 4 m	32 12 5	4
Dual Carriageway 80 km/h	600	1 (r.w.a.) 2 (t.m.) X 2	90	900	750	45	0.75	12	24	35	3	9	Length of taper (T) in (m) Minimum No. of Cones	1 m 2 m 3 m 4 m	140 48 17	10
Dual Carriageway 100 km/h	1000	2 (r.w.a.) 3 (t.m.) X 2	120	1200	750	45	1.2	12	24	40	1	9	Length of taper (T) in (m) Minimum No. of Cones	1 m 2 m 3 m 4 m	160 162 19	20

* Use 750mm signs where Vehicles Per Day < 5,000. Use 900mm signs where Vehicles Per Day > 5,000

Warm	r.w.a.	Priority	road works ahead
inform	t.m.	1	traffic management
		2	
		3	
		4	
Direct	n.o.		no overtaking

For Advance Signs Space Signs evenly through the advance sign distance

select appropriate

End

Works Signs

End

Signs

End

Signs

End

Signs

End

Signs

End

Signs

End

Signs

End

Signs

End

Signs

End

Signs

End

Signs

End

Signs

End

Signs

End

Signs

End

Signs

End

Signs

End

Signs


End

Signs

End

TRAFFIC MANAGEMENT PLAN FOR ROUTINE WORKS


















5) Road Schematic



6) Traffic Management Selection

6.1) Classification	Road Type	Road Width	Speed Limit	Urban/Rural	Traffic Heavy/ Light	
6.2) Selection	All Stop	Give & Take	Priority	Stop/ Go	Lights	Tapers
6.3) Semi-Static	Will Semi-Static Management be used?				Yes	No

7) Signage (Warn / Inform / Direct / End)

No	Sign	Dir	No	Sign	Dir	No	Sign	Dir	No	Sign	Dir
1 + 2 ARE SEMI-STATIC	 SELECT PLATE BELOW	A	6		A	11		A	16	 Pedestrian Barrier	A
		B			B			B			
		C			C			C			
		D			D			D			
	 Deisiú Bóthair ROAD REPAIRS Oibreache DRAINAGE WORKS Bearradh Fíil HEDGE CUTTING	A	7		A	12		A	17		A
		B			B			B			
		C			C			C			
		D			D			D			
	 2 km ar fad FOR 2 km	A	8		A	13		A	18		A
		B			B			B			
		C			C			C			
		D			D			D			
3		A	9	 YIELD (Priority)	A	14	 Barrier Board	A	19	 Críoach END	A
		B			B			B			
		C			C			C			
		D			D			D			
5		A	10		A	15		A	20	 Críoach END	A
		B			B			B			
		C			C			C			
		D			D			D			
If Using Traffic Lights/ Stop-Go, Have Gardai Been Notified?										YES	NO
Are All Required Cones /(Lamps & Beacons) In Place (and operating)?										YES	NO

8) Workforce Induction & Communication

8.1) Has this Plan been Communicated to the workforce and does everyone know their role? Operatives to Sign Below	Yes	No
8.2) Supervisor		

NOTIFICATION OF POSITIVE TRAFFIC CONTROL

Under the following Road Traffic Acts/Regulations

- Section 37 of the Road Traffic Act, 1994
- Road Traffic (Signs) Regulations 2006 (S.I. No. 637 of 2006)
- Road Traffic (Control of Traffic) Regulations 2006 (S.I. No. 638 of 2006)

The Roads Authority of

Hereby notifies

Of the use of

TEMPORARY TRAFFIC LIGHTS

STOP-GO BOARD(s)

at the following location:

Road

From a point

To a point

ON/ BETWEEN (delete as appropriate) the following dates

and

Observations (if any) should be faxed to:

Signed: _____

On behalf of the Roads Authority

PLANNED WORKS TRAFFIC MANAGEMENT SITE INSPECTION SHEET					
PROJECT NAME:				Phase:	
Date:		Time:	1).		2).
1) TRAFFIC MANAGEMENT SET-UP/ MODIFICATION, INSPECTIONS					
1-1) Installation Checks					
Does the Traffic Management conform to the Design Layout and Parameters?					
Have all hazards been addressed in the Traffic Management Plan?					
Has allowance been made for the delivery and removal of materials?					
Have Gardaí been informed of any Traffic Lights/ Stop-Go Boards in use?					
Have Gardaí been informed of Roadworks Speed limits being introduced?					
2) TRAFFIC MANAGEMENT OPERATION INSPECTIONS					
2-1) Operation Checks					
			1	2	
Are Safety Zones being kept clear of operatives, plant and materials?					
Are all the signs in good condition/ are all cones in good condition with sleeves?					
Are sign vision lines free from bends, hills/dips in the road, parked vehicles, hedges etc?					
Will the site be safe at night or in wind, fog, snow or rain? (delete as appropriate)					
Are all misleading permanent signs and road markings covered?					
Is the carriageway/footway being kept clear of mud and surplus equipment?					
Are materials/ plant that are left on verges or lay-bys being properly guarded and lit?					
2-2) Traffic Checks					
Is there safe access to adjacent premises?					
Does Signing and Guarding meet the (changing) conditions?					
Are traffic control arrangements working at the optimum level to reduce traffic delays?					
If present, are the needs of cyclists or horse riders incorporated into the layout?					
2-3) Pedestrian & Vulnerable Road User Checks					
Have the needs of pedestrians & vulnerable road users been addressed in the layout?					
If pedestrian route blocked, has a suitable alternative route been provided?					
Are pedestrian routes clearly evident/ indicated?					
If a footway in the road is to be used, are ramps to the kerb provided?					
Are pedestrian hazards sufficiently GUARDED at night?					
3) TRAFFIC MANAGEMENT CESSATION INSPECTIONS					
3-1) Works Complete Checks					
Have all signs, cones, barriers, and lamps been removed?					
Have any covered permanent signs been restored?					
Have Gardaí been informed that Speedlimits/ Traffic Signals/ Stop-Go removed?					
4) EXCEPTIONS REPORT					
(Append attachments as necessary)					
Check Completed By:					

PROJECT CLOSEOUT SHEET	
PROJECT NAME:	

1) Procedures	
The extents of construction have been completed per the plans	
Pavement Surface has been visually inspected and deemed satisfactory (incl. sweeping of surfaces that have been surface dressed)	
Temporary Traffic Management arrangements (incl. Orders) have been removed	
Any Permanent Road Markings, Road Studs, and Signs have been installed	
2) Works Extents	
The length of work completed was (m)	
The average width of work completed was (m)	
3) Appointments	
PSDP appointment terminated	
Designer appointment terminated	
PSCS appointment terminated	
Contractor given completion certificate	
4) Records	
The safety file is complete and will be stored	
5) Site Inspection	
The site has been inspected by (print name) and deemed to be satisfactory:	
Signature:	
Date of inspection:	
6) Procedure Monitoring (to be completed by supervisor of person listed in 5 above)	
I recommend that the Project be deemed complete (print name)	
Signature:	
Date:	

INCIDENT/ ACCIDENT REPORT FORM

1) Job Details

1.1) Job Name	
1.2) Job Location	

2) Incident

2.1) Date of Incident		2.2) Time of Incident	
------------------------------	--	------------------------------	--

2.3) Incident Involves	Public	Layout	Operatives	Plant	Materials	Hired	Contractor	Environment

2.4) Incident Classification	Class 1		Class 2		Class 3	Class 4	
	Long Traffic Delays	Pedestrian Danger	Near Miss	Minor Injury	3 Day Injury	Road Traffic Accident	Serious Injury or Death

2.5) Weather Conditions	Light:	Sunny	Cloudy	Fog	Dawn/Dusk	Night	Floodlit
	Rain:	Dry	Light Rain	Heavy Rain	Hailstones	Snow	
	Wind:	No Wind	Breeze	Windy	Gale		
	Temperature:	Warm		Cold		Freezing	

2.6) Locus	Carriageway	Footpath	Safety Zone	Working Space

2.7) Pavement Condition	Clean	Dirty	Dry	Wet	Granular	Wearing	Base	Chips	Markings

2.8) Number involved (Class 2 or greater)	
--	--

3) Traffic Management

N/A Yes No

3.1) Were the appropriate signs in their correct place?			
3.2) Were the signs in a good condition?			
3.3) Were all cones in place and in good condition?			
3.4) Were all TM Lamps in place and operating?			
3.5) Were all TM Beacons in place and operating?			
3.6) Were Plant Hazard Beacons operating?			

4) Site Health and Safety

N/A Yes No

4.1) Had operative appropriate CSCS card?			
4.2) Had plant/ equipment been checked for suitability?			
4.3) Were Safety Guards in place and in good condition?			
4.4) Were correct operating procedures/ guidelines used?			
4.5) Were operatives wearing appropriate PPE?			
4.6) Was there good housekeeping on site?			

5) Emergency Procedure

5.1) Services	None	First Aid	Driven to Aid	Ambulance	Fire Brigade	Gardaí

5.2) Procedure		Good	Bad	None
	Training			
	Equipment			

6) Operatives (List operatives on site at time of incident)

7) Incident Description

8) Suggested Control Measures to Prevent Re-Occurance

9) Incident Sketch

**10) Report
Completed By:**

**11) Report
Noted By:**




MCE – Meenbog WF’s Traffic Management Plan

	Name (Print)	Signature	I understand the details in the traffic management plan and agree to sign off (tick)	Date
1				
2				
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				

Location 1
See Drg. No. 615-1


Location 2
See Drg. No. 615-2

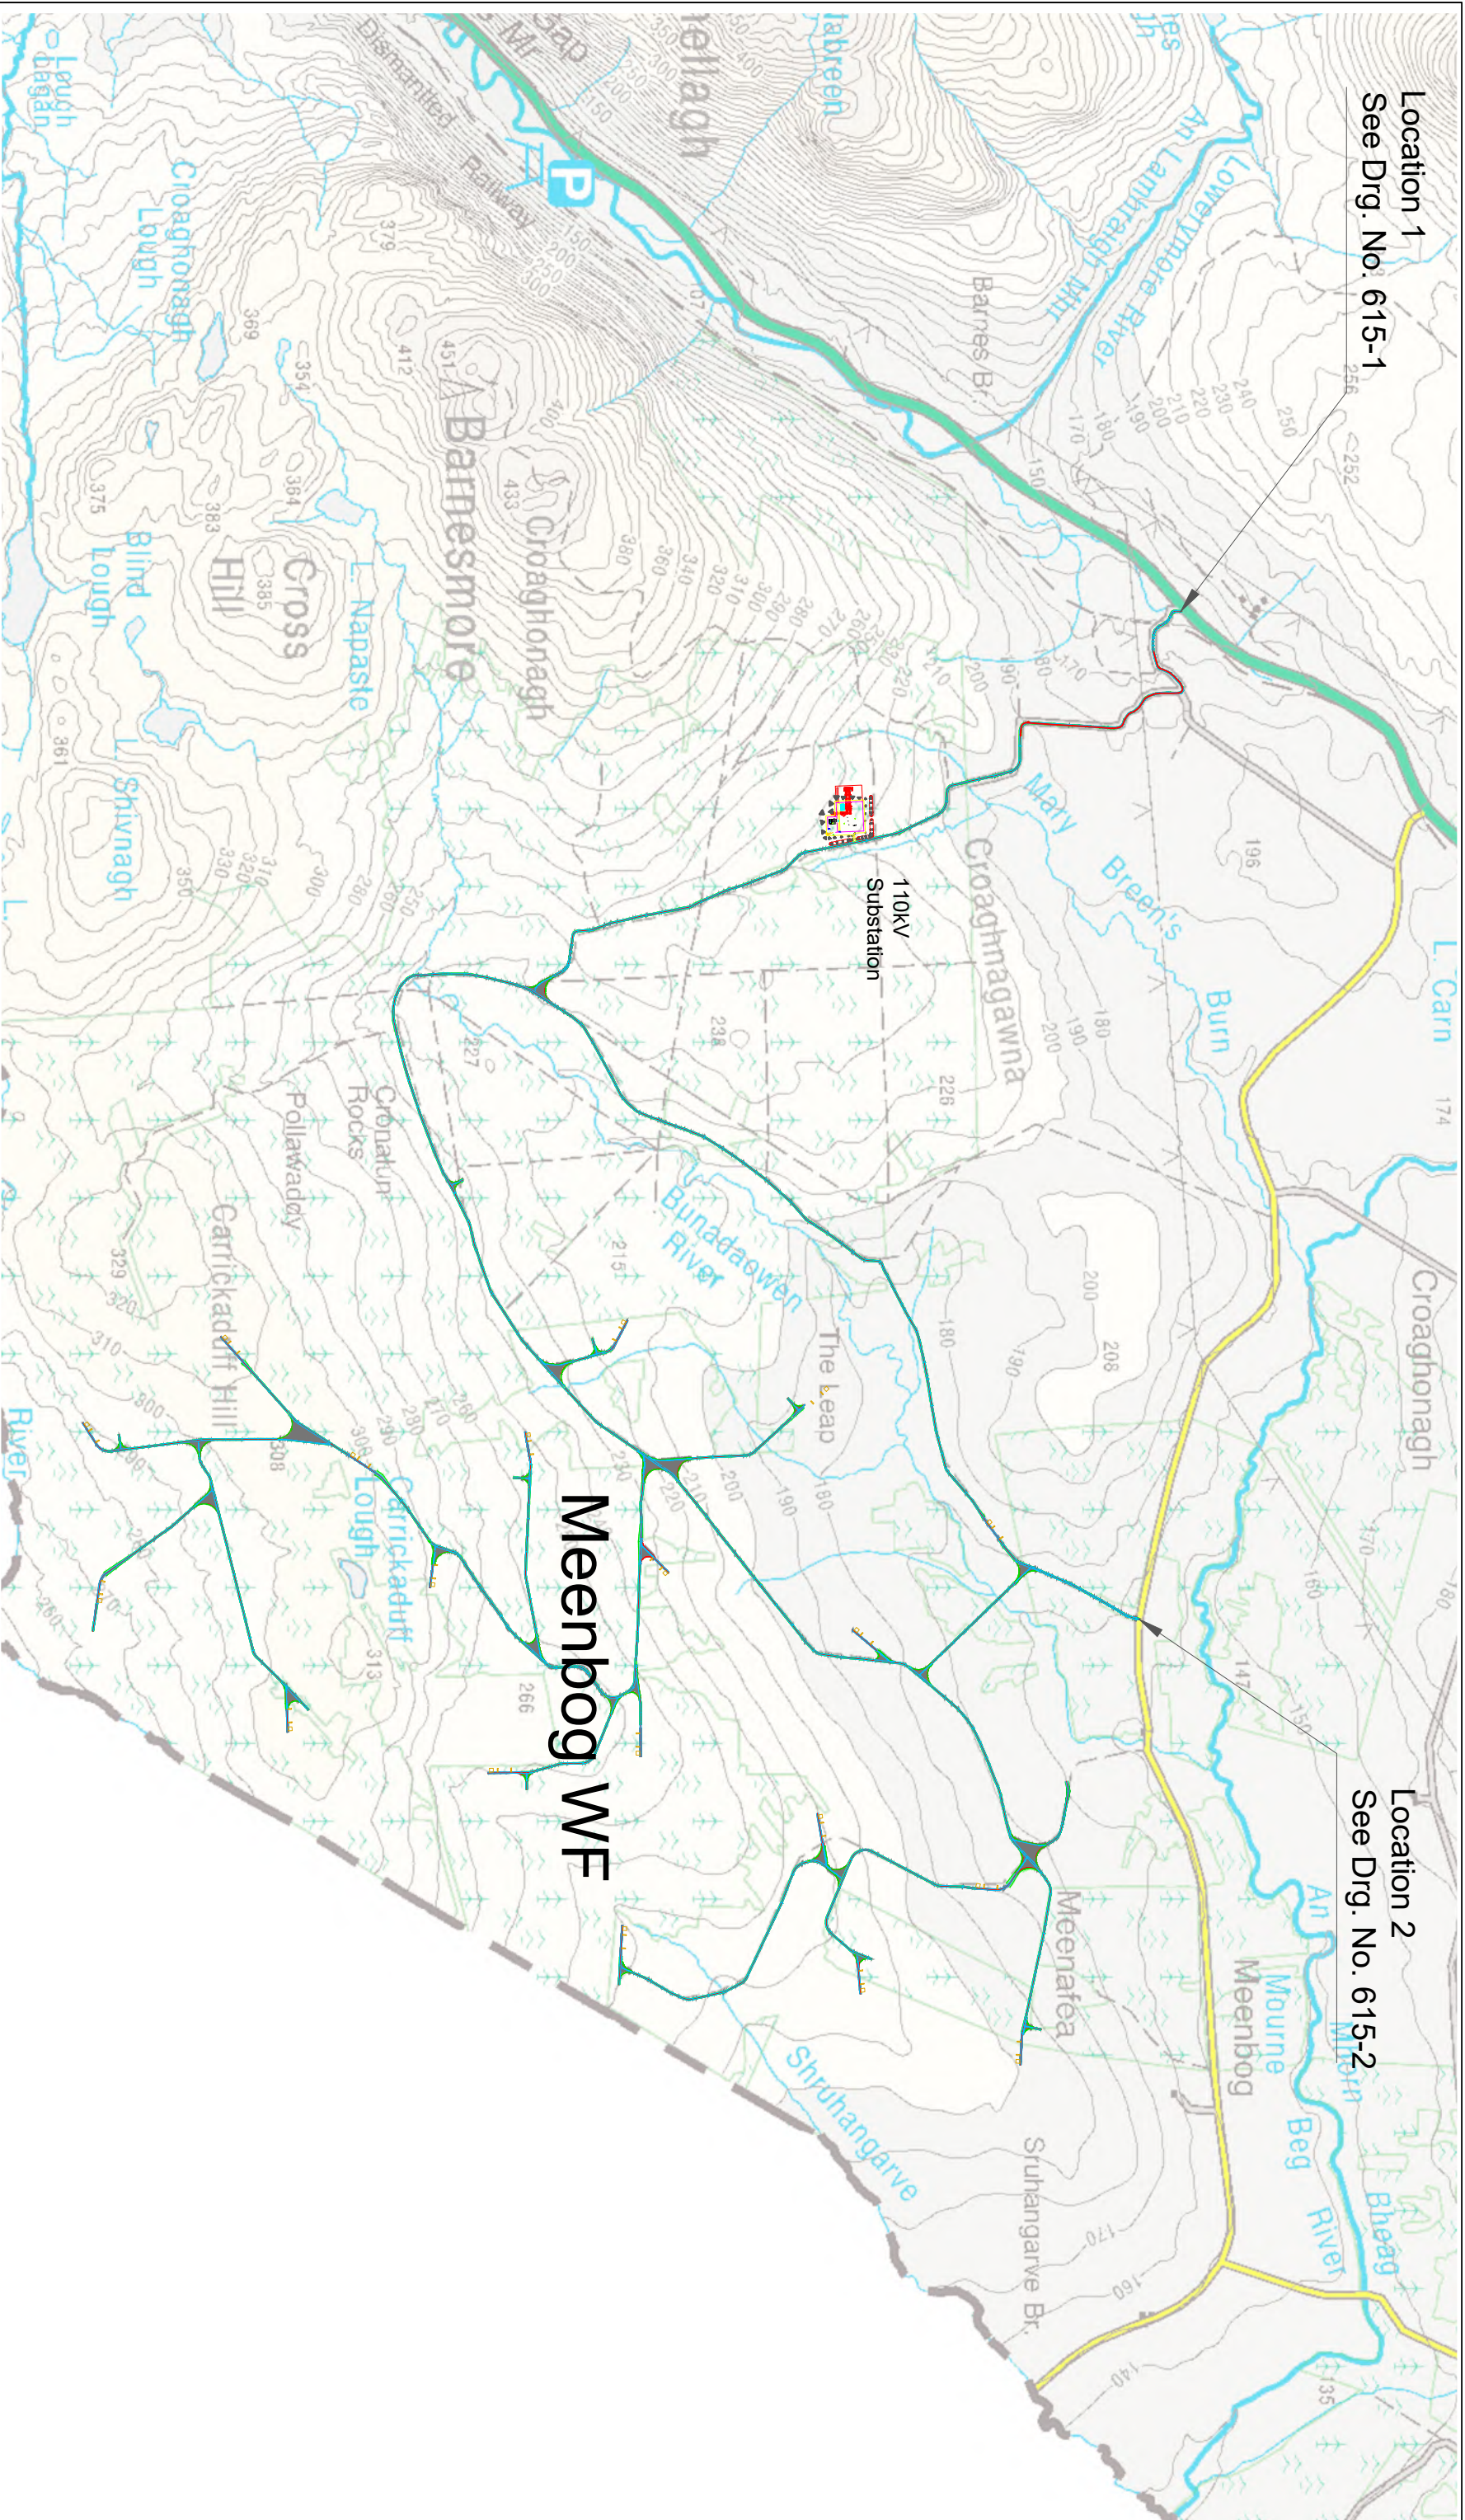

Meenbog WF


Project Title:	Meenbog WF		
	Construction Stage TMP		



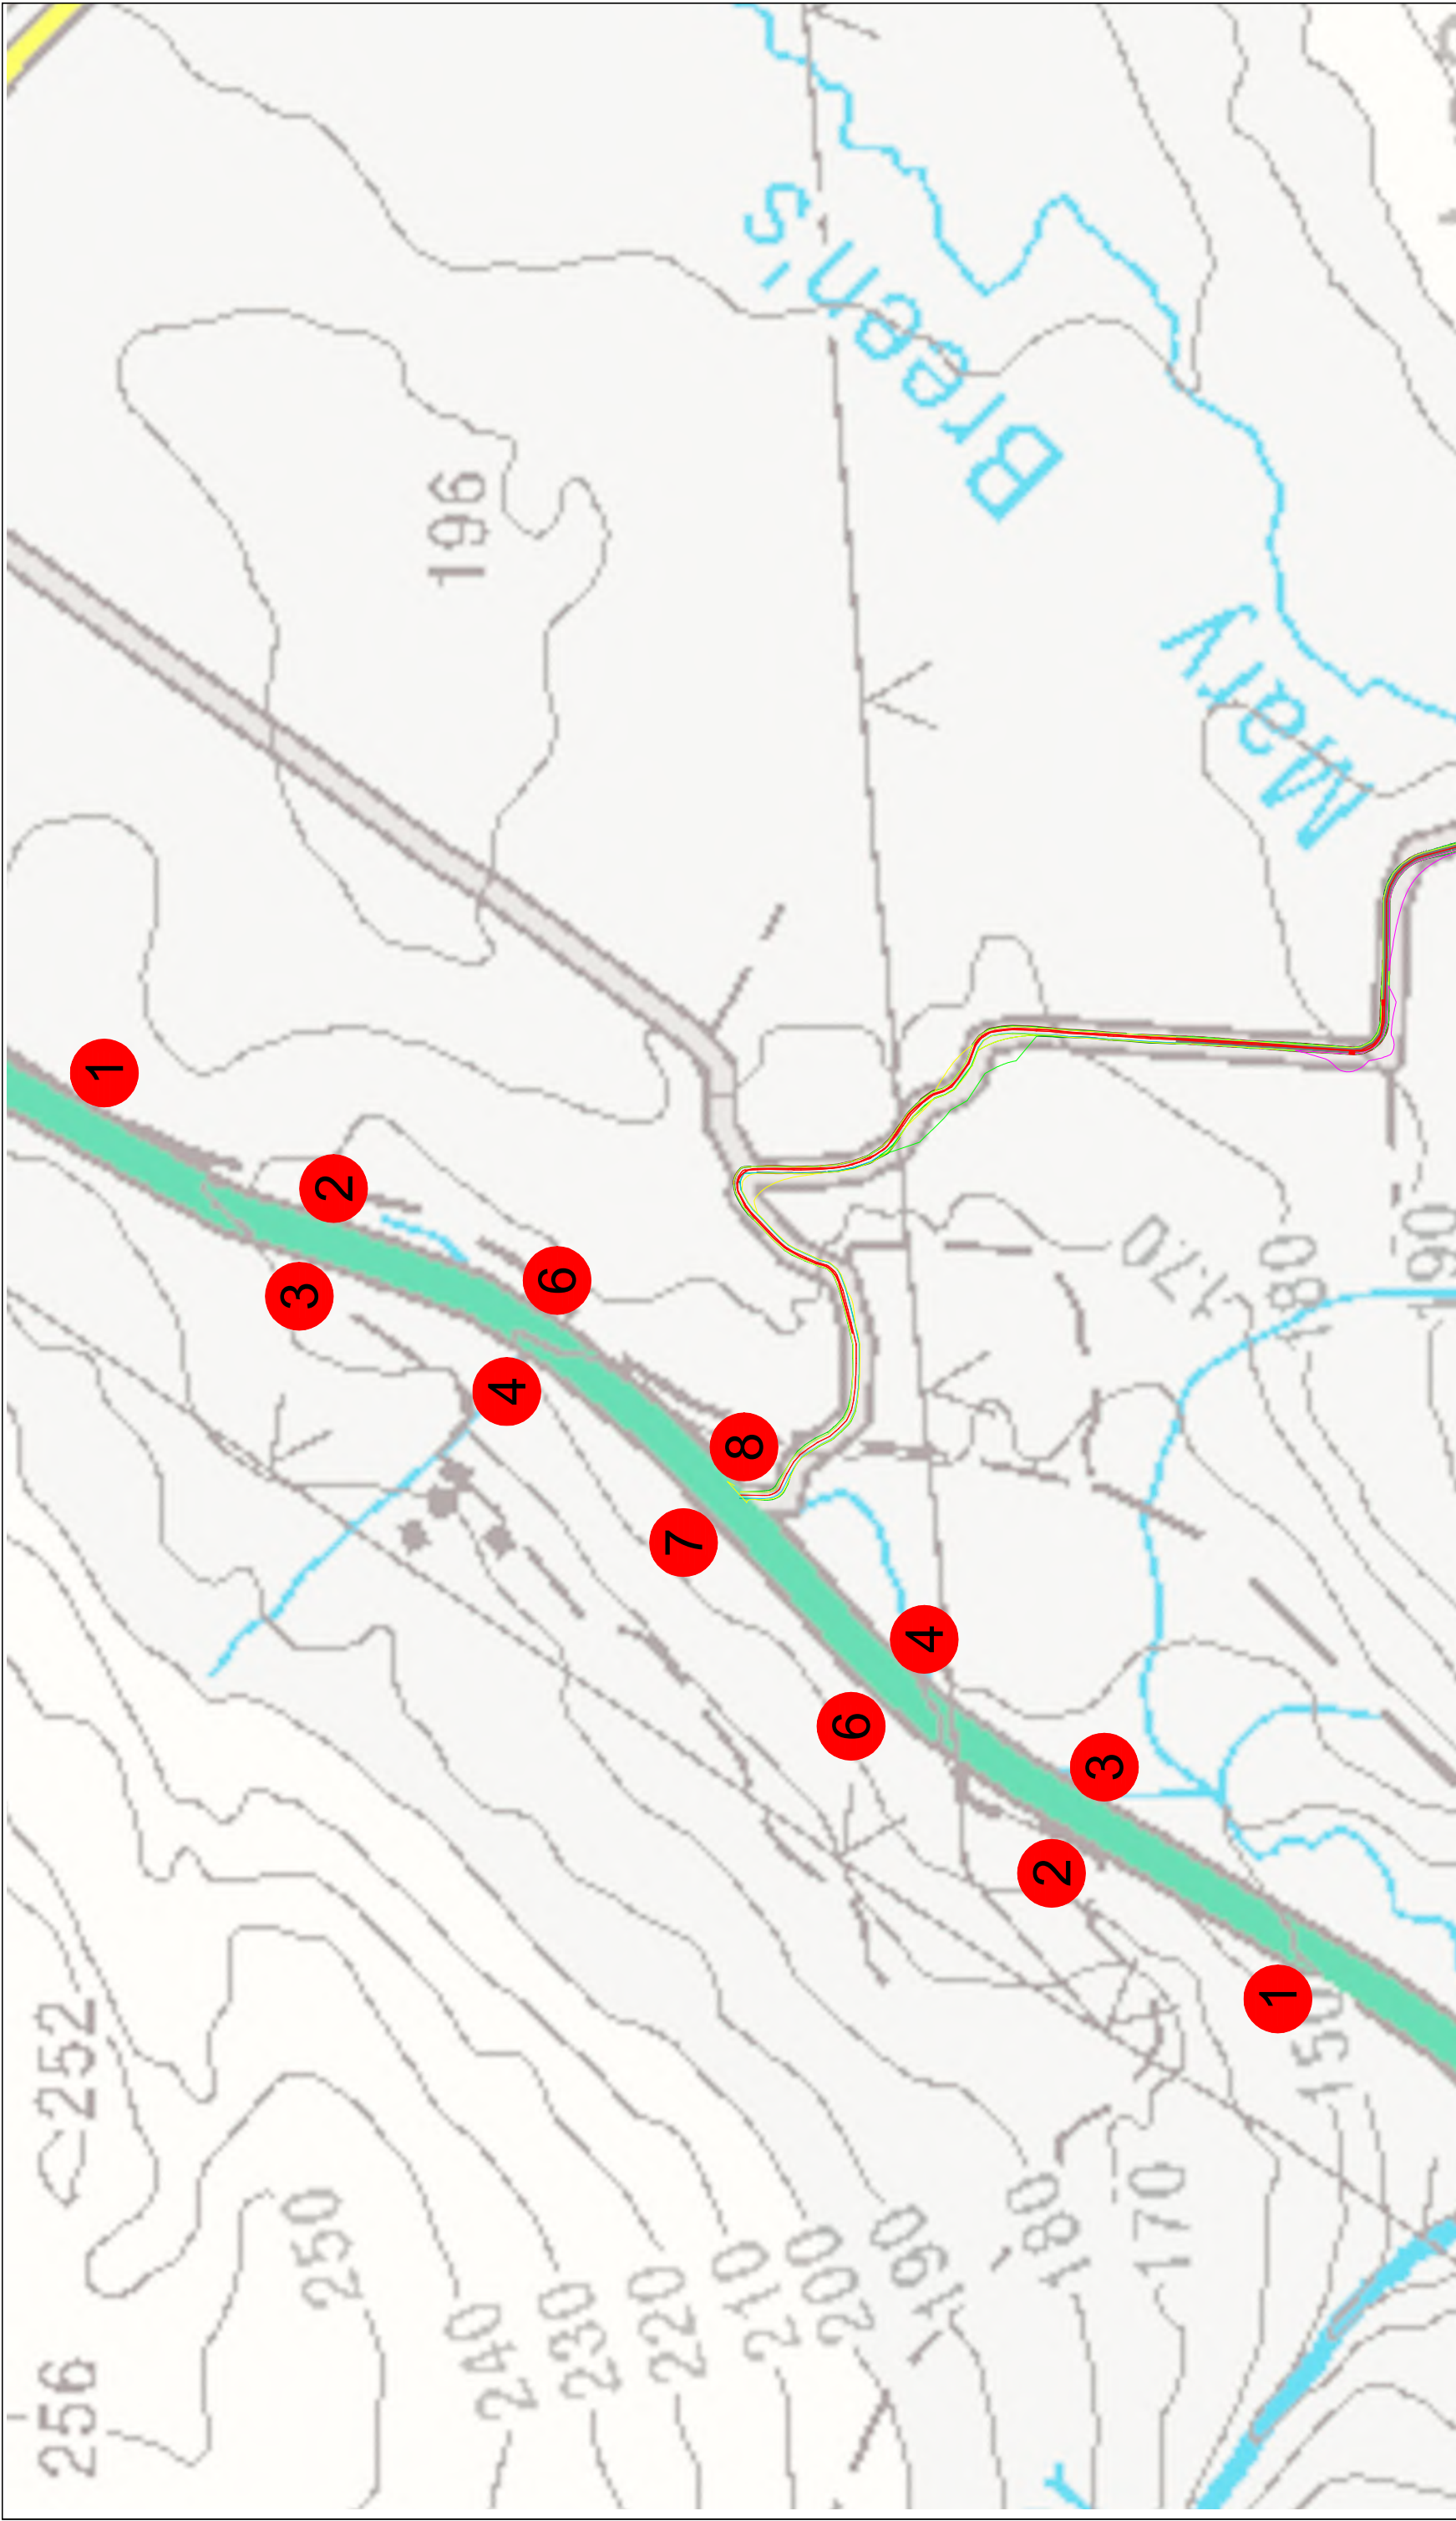



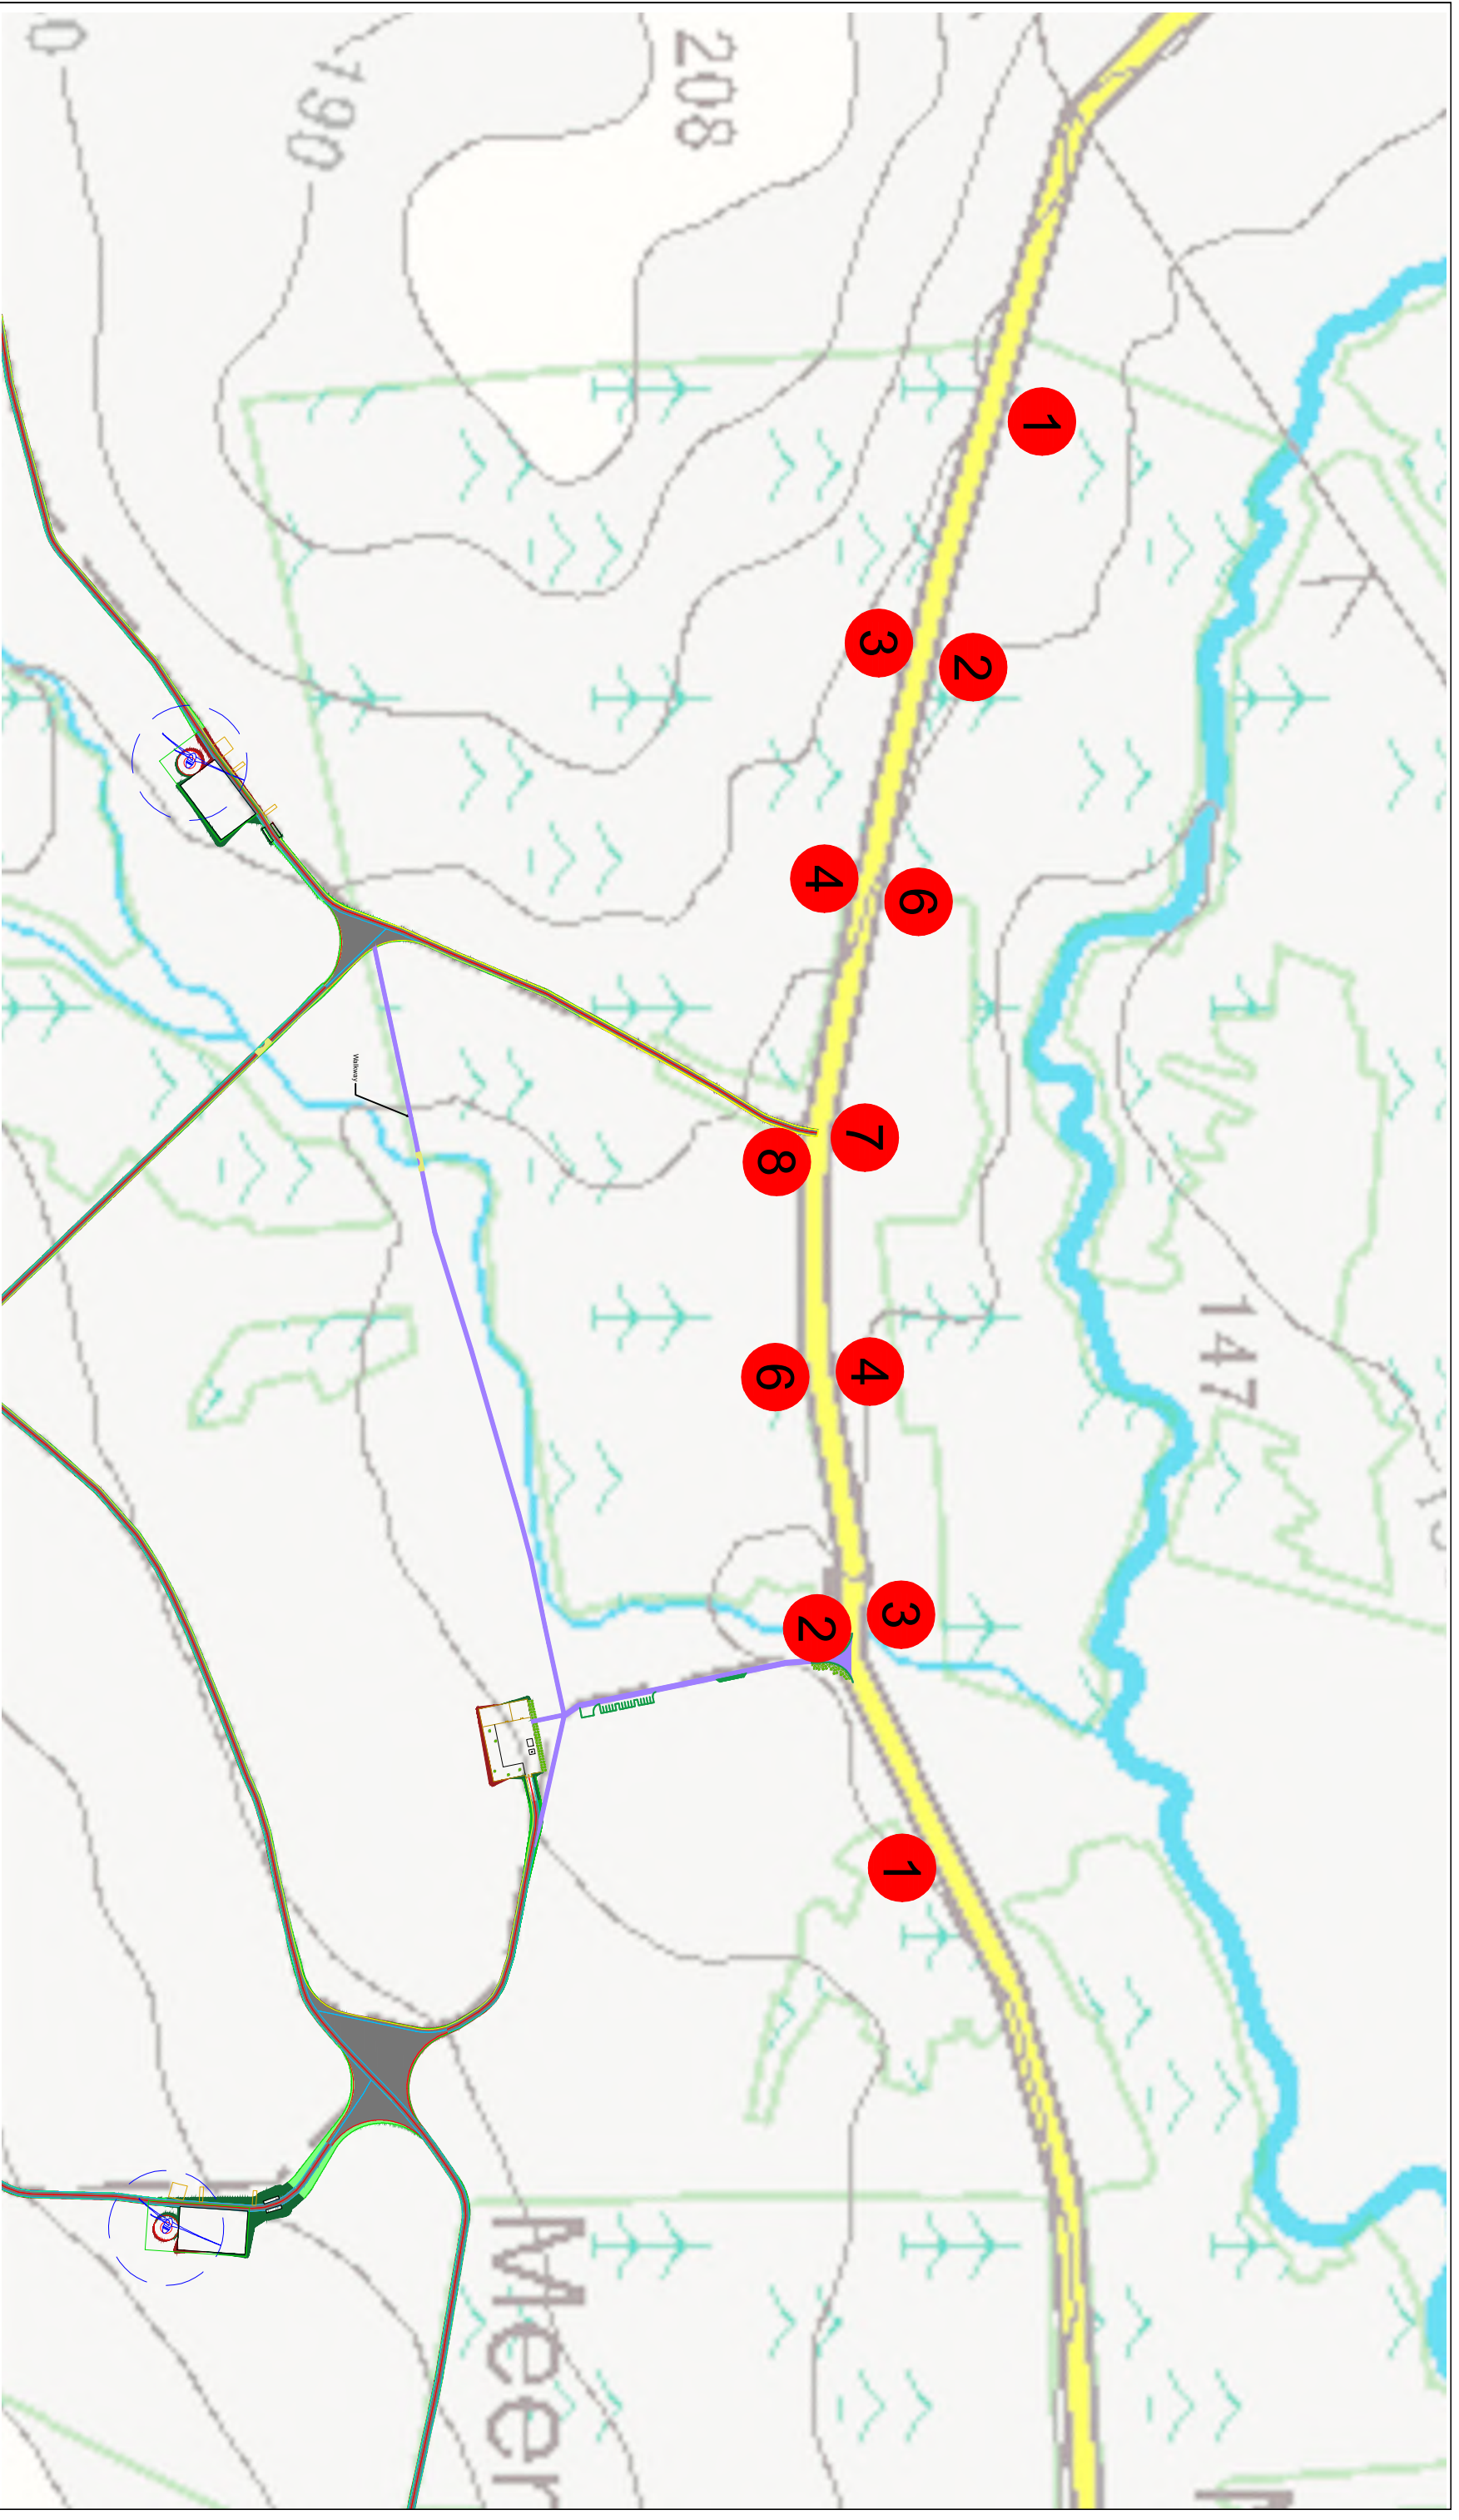

Drawing Title:	Overview Sheet		
Date:	15.01.19	Prepared by:	T.Scantlan
Scale:	1:20000@A3	Rev:	000
		DRG No.:	614
		Job Ref:	0059



1		3		5			
2		4		6			

Project Title: Meenbog WF Construction Stage TMP	
Drawing Title: Location 1 - Sheet 1 of 2	
Date: 15.01.19	Prepared by: T.Scanlan
Scale: 1:5000@A3	Rev: 000
DRG No. 615-1	Job Ref: 0059



- 1 
- 2 
- 3 
- 4 
- 5 
- 6 
- 7 
- 8 

Project Title: Meenbog WF Construction Stage TMP			
Drawing Title: Location 2 - Sheet 2 of 2			
Date: 15.01.19	Prepared by: T.Scannlan	DRG No. 615-2	Job Ref. 0059
Scale: 1:5000@A3	Rev. 000		



Civil Engineering

Traffic Management Plan: MCE – Duct Installation along Local Road L-2595-1.



November 2015

Telephone: +353 (0) 21 733 6034, Fax: +353 (0) 21 733 6145
Web: www.mceengineering.ie, Email: office@mceengineering.ie
Lissarda Industrial Estate, Lissarda, Cork, Ireland.

MCE – Grid Connection Duct Installation Traffic Management Plan

Contractor: MCE ltd.

Project name: Meenbog Windfarm

Address: Carrickalangan, Meenbog & Cullionboy, Co. Donegal.

Name : Sean Driscoll - Tel:086-8528329
Chris Murnane – Tel: 086-7955083

Email: sean.odriscoll@turnkeydev.com
chris.murnane@gmail.com

Site supervisor: Sean Driscoll / Chris Murnane








































Safety officer: Chris Murnane

Description of task: Traffic Management Plan for Meenbog Wind Farm along local road L2595-1.

Key plant: 360 excavators
8 tonne dumper
Lorries
Roller
Submersible Pumps
Plate compactor
Generator
Spill Kit
Diesel Bouser
Drip Trays
Directional Drilling Rig
Auger Boring Machine

Specific Training: FAS safe pass
CSCS plant ticket
Site induction

MCE – Grid Connection Duct Installation Traffic Management Plan

<p>Method of Access and Egress to the work Area</p>	<p>All operatives must complete pre works MCE Ltd. site induction before commencing work on the ducting route.</p>														
<p>Fall Protection Measures: (Where work at height cannot be eliminated)</p>	<p>No persons are permitted within 2 meters of excavation. Trench support will be utilized if required. Open trenches will be fenced off or backfilled every evening to ensure the areas are safe for workers and local traffic.</p>														
<p>Hazardous Substances: Applicable:</p>	<table border="1" style="width: 100%; text-align: center;"> <tr> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>No</td> <td>No</td> <td>No</td> <td>No</td> <td>No</td> <td>Yes</td> <td>No</td> </tr> </table>								No	No	No	No	No	Yes	No
															
No	No	No	No	No	Yes	No									
<p>Storage Arrangements:</p>	<p>No material will be used or generated during the course of this task</p>														
<p>Mandatory and Additional PPE as Required:</p>	<table border="1" style="width: 100%; text-align: center;"> <tr> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>Other: 1. Hi-Vis</td> </tr> <tr> <td>Safety Boots Yes</td> <td>Hard Hats Yes</td> <td>Kevlar Yes</td> <td>Hearing Protection When required</td> <td>Eye Protection Yes</td> <td>Respiratory Protection N/A</td> <td></td> </tr> </table>							Other: 1. Hi-Vis	Safety Boots Yes	Hard Hats Yes	Kevlar Yes	Hearing Protection When required	Eye Protection Yes	Respiratory Protection N/A	
						Other: 1. Hi-Vis									
Safety Boots Yes	Hard Hats Yes	Kevlar Yes	Hearing Protection When required	Eye Protection Yes	Respiratory Protection N/A										
<p>Emergency Procedures:</p>	<p>MCE Emergency Procedures (All employees informed at site inductions) All employees to be made aware of the nearest exit routes from site.. All personnel to be in possession of the site coordinates at all times in case of need to contact emergency services for any reasons.</p>														
<p>First Aid Facilities:</p>	<p>On-Site First Aider: Sean O’Driscoll / Chris Murnane First Aid Box Location: MCE Site Vehicle & Site Office Nearest Hospital: Letterkenny General Hospital – (074) 9125888 HSE Community Care Centre, Ballybofey (074 9131391)</p>														
<p>Welfare Facilities:</p>	<p>Site office, canteen and toilet supplied by Mid Cork Electrical at site compound across from substation and assembly point.</p>														

MCE – Grid Connection Duct Installation Traffic Management Plan

Introduction:

This traffic management plan outlines the affected roadways for the 110 kV ducting installation of an underground cable grid connection between Meenbog WF's 110kV Substation (Croaghonagh) and Clogher 110kV substation (Cullionboy). This is to be read in conjunction with the works method statement in order to provide a safe system of work.

The total length of roadway affected is 1,166 metres along the L-2595-1 and it is proposed that the road be closed during the works, (See Drawing No.612). Access will be limited to emergency vehicles and to local householders who are unable otherwise to access their homes. Traffic calming measures will be utilized to slow down vehicles and ensure ducting can be carried out safely.

Prior to any works commencing a dilapidation survey will be completed of the entire route, photographing and noting any existing damage or defects to property or road surfaces. A copy of this will be submitted to the Donegal County Council prior to work commencing.

Local Access for Residents

As part of the management plan local residents affected by the road closure will be alerted to the works through the use of letter drops and prior consultation. Every effort will be made to limit the effect on local residents and any residents who require special provisions to be made will be accommodated (i.e. Home carer, etc.). Traffic management plans will be reviewed on a daily basis and take into account all local parameter in the area where work is being carried out. All required traffic management calculation forms will be completed and kept on site.

MCE – Grid Connection Duct Installation Traffic Management Plan

Pedestrian & Cyclist Management

Pedestrians and cyclist will be accommodated along the primary and secondary diversion routes. Operatives will be made aware to watch out for oncoming pedestrians / cyclists and to advise them accordingly.

Dealing With Emergency Services

Gardai will be advised of the intended works to be carried out prior to commencement on the Gardai Consultation form. Emergency services using the local roads will be made priority and areas where the works are being carried out will be covered immediately with road plates so as to allow access.

Signage Plan

All works will be signed in accordance with the “Guidance for the Control and Management of Traffic at Road Works” (Second Edition 2010). The Routine Works Traffic Management Design, including the layout parameters is illustrated on attachment.

MCE – Grid Connection Duct Installation Traffic Management Plan

All traffic management will comply with guidance given in Chapter 8, Traffic Signs Manual, Department of Transport November 2006 and Control and management of Traffic at Road Work October 2007.

A fully certified and competent ‘Signing Lighting & Guarding’ officer will sign off on the works before commencement and carry out routine monitoring. A qualified supervisor will be onsite at all times.

- ✓ See attached traffic management design sheet for signage etc.
- ✓ The entire traffic management system will be set up prior to any works commencing.
- ✓ Only approved signs will be used along the works area.
- ✓ All signs will be clean and clearly visible.
- ✓ Once signs are in place the route will be assessed to ensure adequate visibility for drivers and pedestrians.
- ✓ All signs will be secured and weighted down where appropriate.
- ✓ Traffic will be reduced to single flow during all excavations on the roadside along sections which do not require a closure.
- ✓ At the end of each day the excavation is back filled and all materials will be removed from the roadside.
- ✓ Contractor vehicles will be parked with consideration given to traffic management plan.
- ✓ Where flag men are required, both flag men, the foreman and guarding officer will all communicate via two-way radios.

MCE – Grid Connection Duct Installation Traffic Management Plan

Road Closure / Road Opening Licence Drawings:

The following drawings are included at the end of this document:


- ✓0059 – 612 – Road Closure – Section 1 – Overall Layout View
- ✓0059 – 613-1 – Sheet 1 of 4 – Location 1 Layout
- ✓0059 – 613-2 – Sheet 2 of 4 – Location 2 Works Area Layout
- ✓0059 – 613-3 – Sheet 3 of 4 – Location 3 & 4 Layout
- ✓0059 – 613-4 – Sheet 4 of 4 – Location 5 Layout

MCE – Grid Connection Duct Installation Traffic Management Plan

Signage Layout

The following is the layout for signage that will be in place on the approach to the works area in the closed sections of road which will be occurring on the L-2595-1. See attached drawings showing signage layout for the alterations to the road layout which will be occurring .

- ✓ Sign no 1: WK 001 (man with shovel) 600m before road works
- ✓ Sign no 2: (do not pass) 400m before road works
- ✓ Sign no 3: WK 032 or WK 033 (road narrows ahead) 200m before road works
- ✓ Cones with reflectors start 50m before works location.
- ✓ Statutory sign no 6 : (blue arrow) at start of cones.
- ✓ Signage after road works will indicate 'No Overtaking Ends' and 'End of Road Works'.
- ✓ Traffic entering and exiting existing secondary road will continue as normal with construction traffic kept to a minimum.
- ✓ See attached generic shuttle layout system for one-way stop and go. This shuttle layout will be set up onsite by the qualified signing lighting and guarding officer.

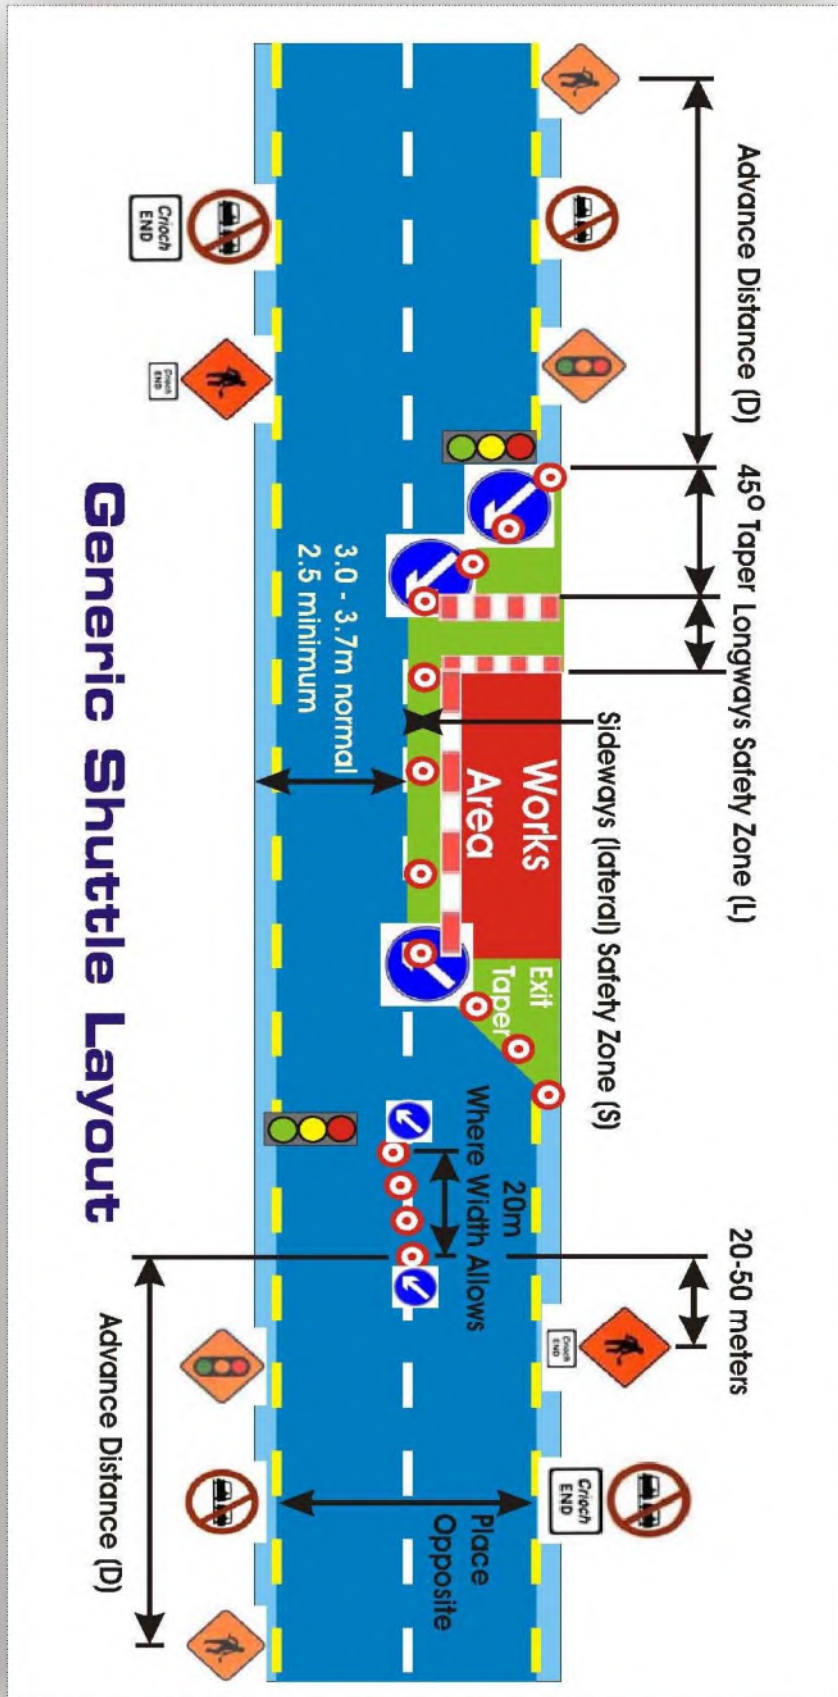

Generic Shuttle Layout

ROUTINE WORKS TRAFFIC MANAGEMENT DESIGN

SHUTTLE CONTROL SELECTION

Method	Max Speed Limit (km/h)	Length of Works (m)	Max Traffic (veh/hr)	3 Min Count	Notes
All Stop	100	n/a	300	15	5-10 mins max.
Give and Take	50	50	400	20	Clear Visibility required from both directions
Priority	100	80	840	42	Speed Limit 50 km/h Clear Visibility required from 60 km/h 80 km/h 80m 100m
Stop/Go	100	20	500	25	Can be Single Man/Single Sign 100 Can be single Man-Auto Sign 100 1250 Can be single Man-Auto Sign 100 200 63 Has to be Two Man-Two Sign 100 300 1050 53 Has to be Two Man-Two Sign 100 400 950 48 Has to be Two Man-Two Sign 100 500 850 43 Has to be Two Man-Two Sign
Traffic Lights	100	500	n/a	n/a	Vehicle Actuated

NOTE: WHEN USING SHUTTLE CONTROL, TAPERS ARE AT 45 DEGREES

LAYOUT PARAMETER SELECTION SHEET

Type of Road	Advance Sign Distance (D) (m)	Min No. & Type Of Advance Signs in Sequence	Min clear visibility of Signs (m)	Min size of signs (mm)	Min height of cones (mm)	Long. Safety Zone (L) (m)	Side. Safety Zone (S) (m)	Long. Cone Space	Long. Lamp Spacing	Lane Taper Multiply	Taper Cone Spacing	Taper Lamp Spacing	Lead-in cone tapers (See Notes below) Recommended lengths	Width of hazard (including safety zone) NOTE: TAPERS ARE ONLY WHERE TWO WAY TRAFFIC MAINTAINED	Hard Shoulder Taper Multiply
Single carriageway road, 30km/h	50	1 (r.w.a.) 1 (l.m.)	50	600	450	5	0.5	6	12	8	3	9	Length of taper (T) in (m) Minimum No. of Cones Minimum No. of Lamps	1m 8 2m 16 3m 24 4m 32	4
Single carriageway, 60km/h	50	1 (r.w.a.) 1 (l.m.)	50	600	450	5	0.5	6	12	8	3	9	Length of taper (T) in (m) Minimum No. of Cones Minimum No. of Lamps	1m 8 2m 16 3m 24 4m 32	4
Single Carriageway 80km/h	600	1 (r.w.a.) 1 (n.o.) 1 (l.m.)	90	750*	750	45	1.2	12	24	35	2.5	9	Length of taper (T) in (m) Minimum No. of Cones Minimum No. of Lamps	1m 35 2m 70 3m 105 4m 140	20
Single Carriageway 100 km/h	800	1 (r.w.a.) 1 (n.o.) 2 (l.m.)	120	750* 900*	750	60	1.2	12	24	40	1	9	Length of taper (T) in (m) Minimum No. of Cones Minimum No. of Lamps	1m 40 2m 80 3m 120 4m 160	20
Dual Carriageway 60 km/h	600	1 (r.w.a.) 2 (l.m.) X 2	50	900	450	5	0.5	6	12	8	3	9	Length of taper (T) in (m) Minimum No. of Cones Minimum No. of Lamps	1m 8 2m 16 3m 24 4m 32	4
Dual Carriageway 80 km/h	600	1 (r.w.a.) 2 (l.m.) X 2	90	900	750	45	0.75	12	24	35	3	9	Length of taper (T) in (m) Minimum No. of Cones Minimum No. of Lamps	1m 35 2m 70 3m 105 4m 140	10
Dual Carriageway 100 km/h	1000	2 (r.w.a.) 3 (l.m.) X 2	120	1200	750	45	1.2	12	24	40	1	9	Length of taper (T) in (m) Minimum No. of Cones Minimum No. of Lamps	1m 40 2m 80 3m 120 4m 160	20

* Use 750mm signs where Vehicles Per Day < 5,000. Use 900mm signs where Vehicles Per Day > 5,000

Warn	r.w.a.	Priority	Advance Signs	Works Signs	End Signs
		1			
		2			
		3			
		4			


For Advance Signs Space Signs evenly through the advance sign distance

Direct n.o.

select appropriate

TRAFFIC MANAGEMENT PLAN FOR ROUTINE WORKS


















5) Road Schematic



6) Traffic Management Selection

6.1) Classification	Road Type	Road Width	Speed Limit	Urban/Rural	Traffic Heavy/ Light	
6.2) Selection	All Stop	Give & Take	Priority	Stop/ Go	Lights	Tapers
6.3) Semi-Static	Will Semi-Static Management be used?				Yes	No

7) Signage (Warn / Inform / Direct / End)

No	Sign	Dir	No	Sign	Dir	No	Sign	Dir	No	Sign	Dir
1 + 2 ARE SEMI-STATIC	 SELECT PLATE BELOW	A	6		A	11		A	16		A
		B			B			B			
		C			C			C			
		D			D			D			
	 Deisiú Bóthair ROAD REPAIRS Oibreache DRAINAGE WORKS Bearradh Fíil HEDGE CUTTING	A	7		A	12		A	17		A
		B			B			B			
		C			C			C			
		D			D			D			
	 2 km ar fad FOR 2 km	A	8		A	13		A	18		A
		B			B			B			
		C			C			C			
		D			D			D			
3		A	9	 YIELD (Priority)	A	14	 Barrier Board	A	19	 Críoach END	A
		B			B			B			
		C			C			C			
		D			D			D			
5		A	10		A	15		A	20	 Críoach END	A
		B			B			B			
		C			C			C			
		D			D			D			
If Using Traffic Lights/ Stop-Go, Have Gardai Been Notified?										YES	NO
Are All Required Cones /(Lamps & Beacons) In Place (and operating)?										YES	NO

8) Workforce Induction & Communication

8.1) Has this Plan been Communicated to the workforce and does everyone know their role? Operatives to Sign Below	Yes	No
8.2) Supervisor		

NOTIFICATION OF POSITIVE TRAFFIC CONTROL

Under the following Road Traffic Acts/Regulations

- Section 37 of the Road Traffic Act, 1994
- Road Traffic (Signs) Regulations 2006 (S.I. No. 637 of 2006)
- Road Traffic (Control of Traffic) Regulations 2006 (S.I. No. 638 of 2006)

The Roads Authority of

Hereby notifies

Of the use of

TEMPORARY TRAFFIC LIGHTS

STOP-GO BOARD(s)

at the following location:

Road

From a point

To a point

ON/ BETWEEN (delete as appropriate) the following dates

and

Observations (if any) should be faxed to:

Signed: _____

On behalf of the Roads Authority

PLANNED WORKS TRAFFIC MANAGEMENT SITE INSPECTION SHEET					
PROJECT NAME:				Phase:	
Date:		Time:	1).		2).
1) TRAFFIC MANAGEMENT SET-UP/ MODIFICATION, INSPECTIONS					
1-1) Installation Checks					
Does the Traffic Management conform to the Design Layout and Parameters?					
Have all hazards been addressed in the Traffic Management Plan?					
Has allowance been made for the delivery and removal of materials?					
Have Gardaí been informed of any Traffic Lights/ Stop-Go Boards in use?					
Have Gardaí been informed of Roadworks Speed limits being introduced?					
2) TRAFFIC MANAGEMENT OPERATION INSPECTIONS					
2-1) Operation Checks				1	2
Are Safety Zones being kept clear of operatives, plant and materials?					
Are all the signs in good condition/ are all cones in good condition with sleeves?					
Are sign vision lines free from bends, hills/dips in the road, parked vehicles, hedges etc?					
Will the site be safe at night or in wind, fog, snow or rain? (delete as appropriate)					
Are all misleading permanent signs and road markings covered?					
Is the carriageway/footway being kept clear of mud and surplus equipment?					
Are materials/ plant that are left on verges or lay-bys being properly guarded and lit?					
2-2) Traffic Checks					
Is there safe access to adjacent premises?					
Does Signing and Guarding meet the (changing) conditions?					
Are traffic control arrangements working at the optimum level to reduce traffic delays?					
If present, are the needs of cyclists or horse riders incorporated into the layout?					
2-3) Pedestrian & Vulnerable Road User Checks					
Have the needs of pedestrians & vulnerable road users been addressed in the layout?					
If pedestrian route blocked, has a suitable alternative route been provided?					
Are pedestrian routes clearly evident/ indicated?					
If a footway in the road is to be used, are ramps to the kerb provided?					
Are pedestrian hazards sufficiently GUARDED at night?					
3) TRAFFIC MANAGEMENT CESSATION INSPECTIONS					
3-1) Works Complete Checks					
Have all signs, cones, barriers, and lamps been removed?					
Have any covered permanent signs been restored?					
Have Gardaí been informed that Speedlimits/ Traffic Signals/ Stop-Go removed?					
4) EXCEPTIONS REPORT (Append attachments as necessary)					
Check Completed By:					

PROJECT CLOSEOUT SHEET	
PROJECT NAME:	

1) Procedures	
The extents of construction have been completed per the plans	
Pavement Surface has been visually inspected and deemed satisfactory (incl. sweeping of surfaces that have been surface dressed)	
Temporary Traffic Management arrangements (incl. Orders) have been removed	
Any Permanent Road Markings, Road Studs, and Signs have been installed	
2) Works Extents	
The length of work completed was (m)	
The average width of work completed was (m)	
3) Appointments	
PSDP appointment terminated	
Designer appointment terminated	
PSCS appointment terminated	
Contractor given completion certificate	
4) Records	
The safety file is complete and will be stored	
5) Site Inspection	
The site has been inspected by (print name) and deemed to be satisfactory:	
Signature:	
Date of inspection:	
6) Procedure Monitoring (to be completed by supervisor of person listed in 5 above)	
I recommend that the Project be deemed complete (print name)	
Signature:	
Date:	

INCIDENT/ ACCIDENT REPORT FORM

1) Job Details

1.1) Job Name	
1.2) Job Location	

2) Incident

2.1) Date of Incident								2.2) Time of Incident			
2.3) Incident Involves	Public	Layout	Operatives	Plant	Materials	Hired	Contractor	Environment			
2.4) Incident Classification	Class 1		Class 2		Class 3	Class 4					
	Long Traffic Delays	Pedestrian Danger	Near Miss	Minor Injury	3 Day Injury	Road Traffic Accident	Serious Injury or Death				
2.5) Weather Conditions	Light:	Sunny	Cloudy	Fog	Dawn/Dusk	Night	Floodlit				
	Rain:	Dry	Light Rain	Heavy Rain	Hailstones	Snow					
	Wind:	No Wind	Breeze	Windy	Gale						
	Temperature:	Warm		Cold		Freezing					
2.6) Locus	Carriageway	Footpath	Safety Zone	Working Space							
2.7) Pavement Condition	Clean	Dirty	Dry	Wet	Granular	Wearing	Base	Chips	Markings		
2.8) Number involved (Class 2 or greater)											

3) Traffic Management

	N/A	Yes	No
3.1) Were the appropriate signs in their correct place?			
3.2) Were the signs in a good condition?			
3.3) Were all cones in place and in good condition?			
3.4) Were all TM Lamps in place and operating?			
3.5) Were all TM Beacons in place and operating?			
3.6) Were Plant Hazard Beacons operating?			

4) Site Health and Safety

	N/A	Yes	No
4.1) Had operative appropriate CSCS card?			
4.2) Had plant/ equipment been checked for suitability?			
4.3) Were Safety Guards in place and in good condition?			
4.4) Were correct operating procedures/ guidelines used?			
4.5) Were operatives wearing appropriate PPE?			
4.6) Was there good housekeeping on site?			

5) Emergency Procedure

5.1) Services	None	First Aid	Driven to Aid	Ambulance	Fire Brigade	Gardaí
5.2) Procedure		Good	Bad	None		
	Training					
	Equipment					

6) Operatives (List operatives on site at time of incident)

7) Incident Description

8) Suggested Control Measures to Prevent Re-Occurance

9) Incident Sketch


**10) Report
Completed By:**

**11) Report
Noted By:**



MCE – Grid Connection Duct Installation Traffic Management Plan

	Name (Print)	Signature	I understand the details in the traffic management plan and agree to sign off (tick)	Date
1				
2				
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				

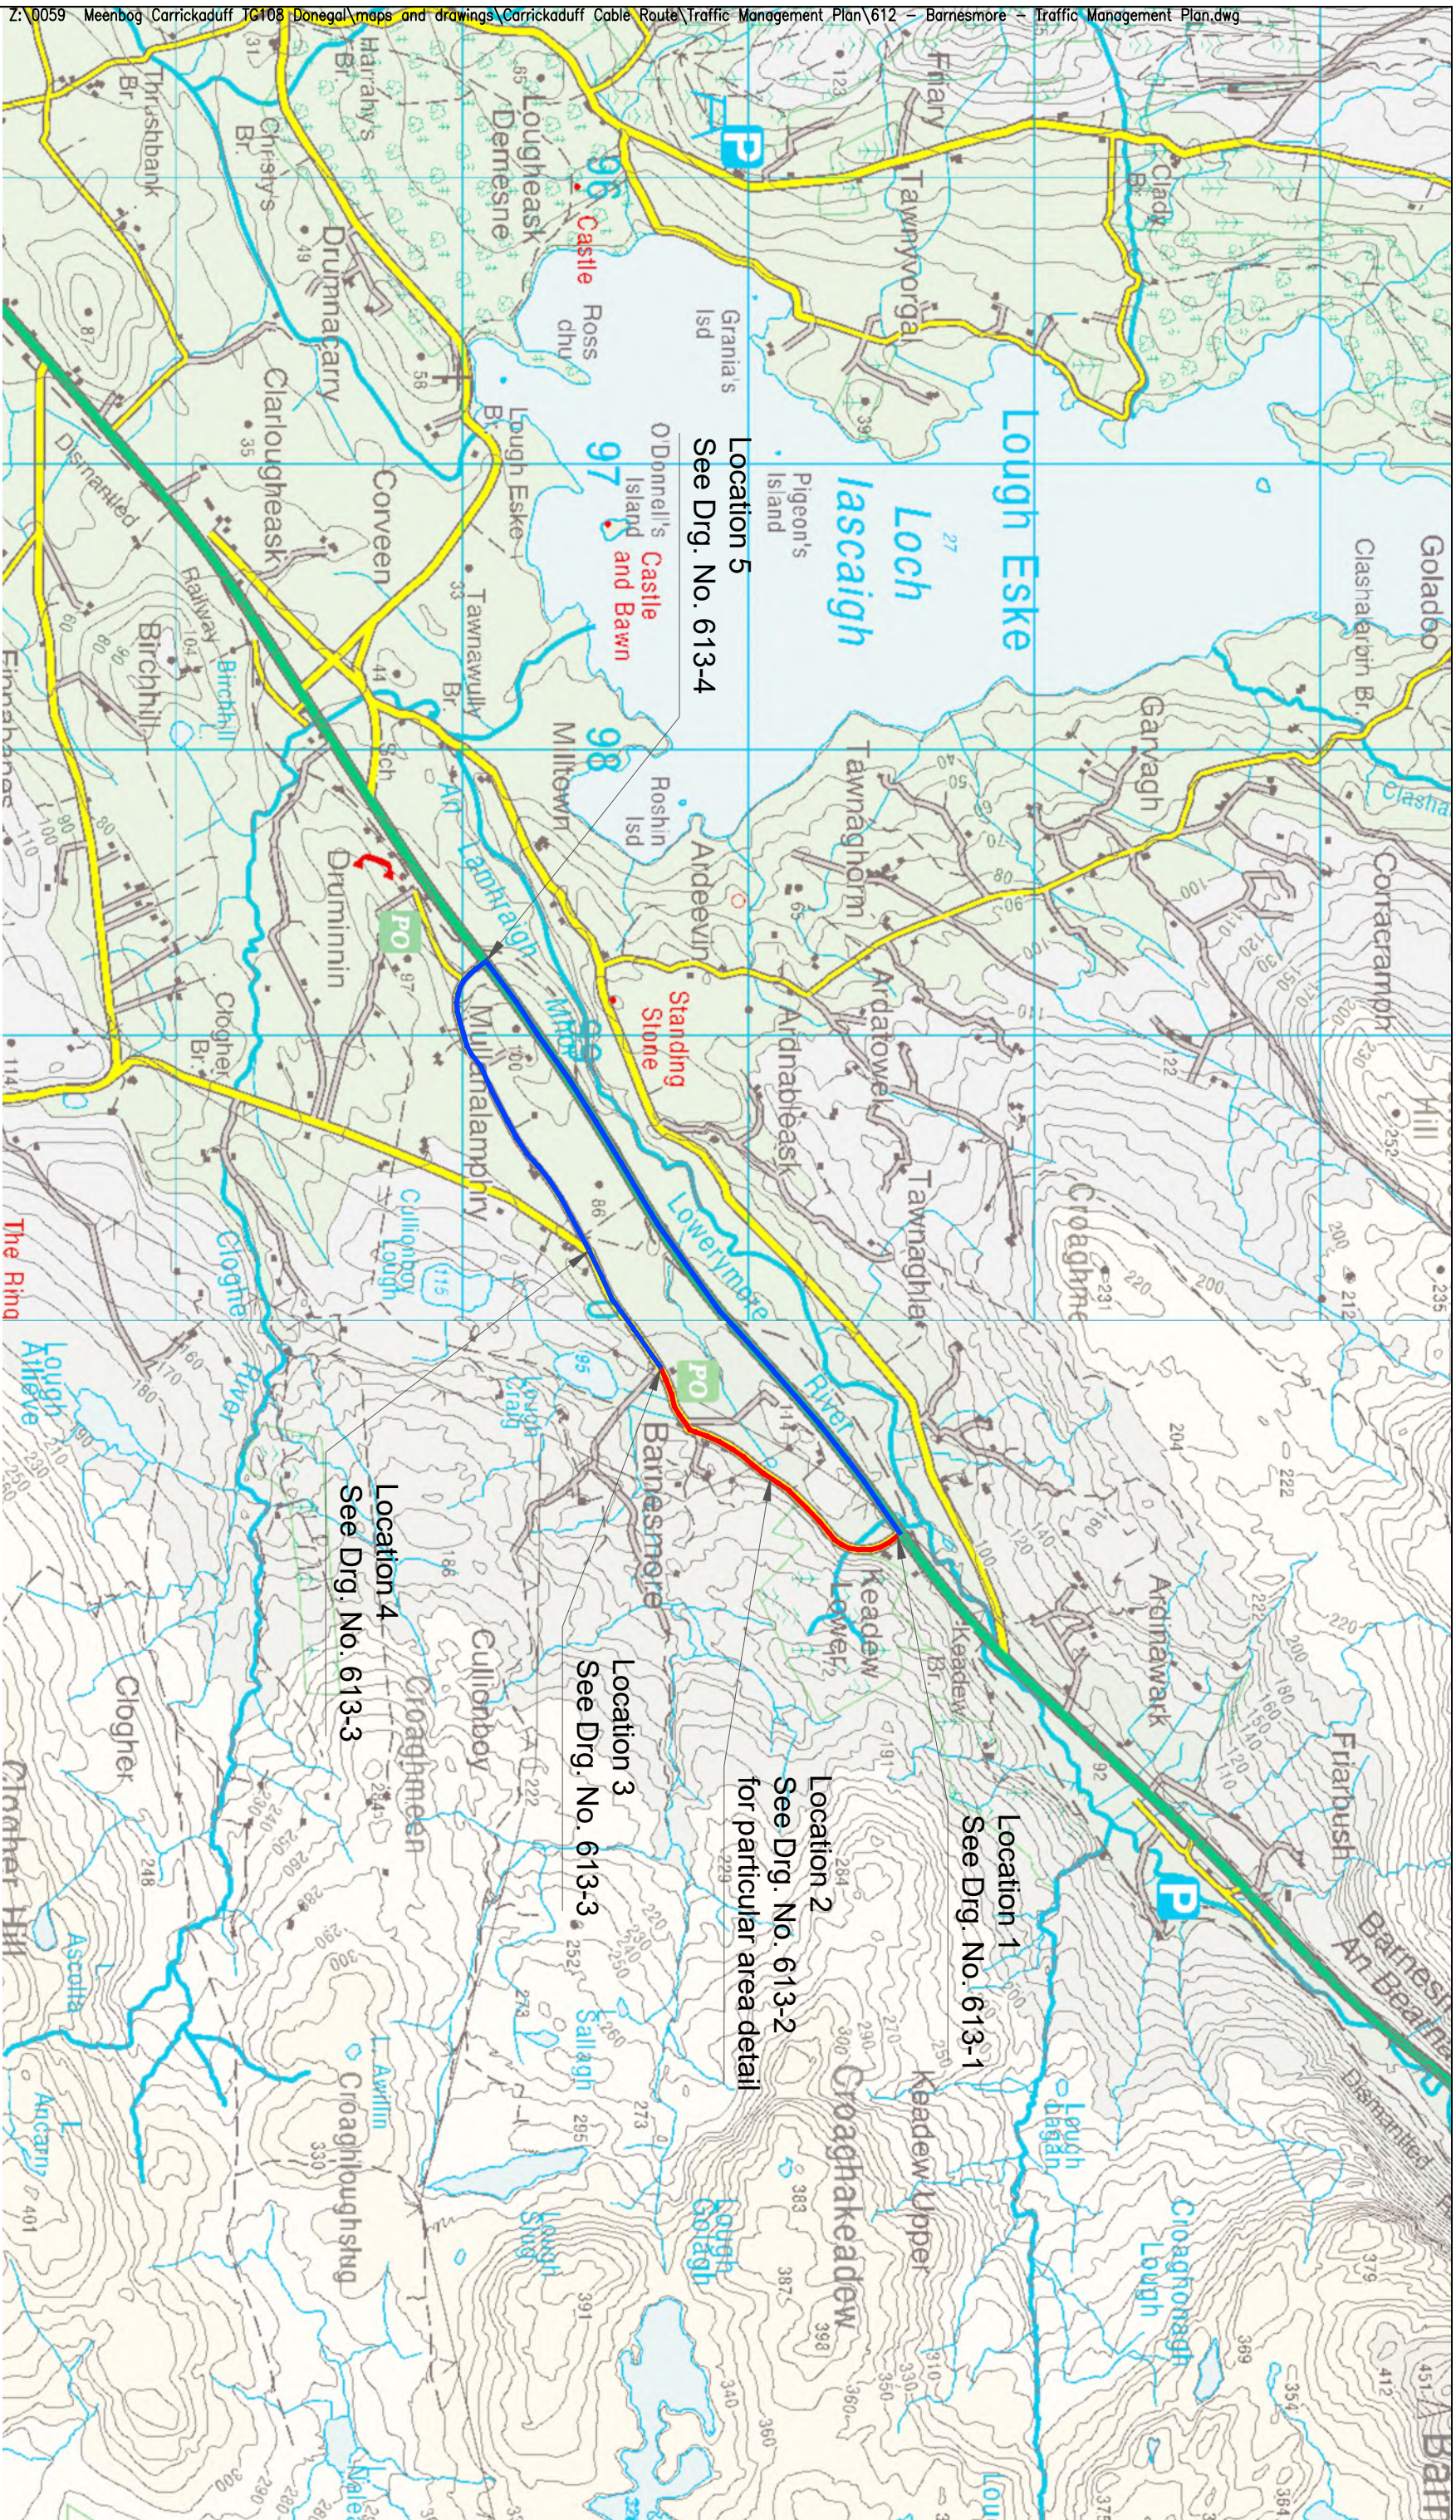

N



LEGEND:

1166m ROAD CLOSURE




4142m PRIMARY DIVERSION ROUTE



Project
Title: **Meenbog WF**
Underground Cable


Drawing
Title: **Barnesmore Section**
Overall Layout View

Date: 11.01.19	Prepared by: T.Scannlan	DRG No. 612
Scale: NTS@A3	Rev: 000	Job Ref: 0059

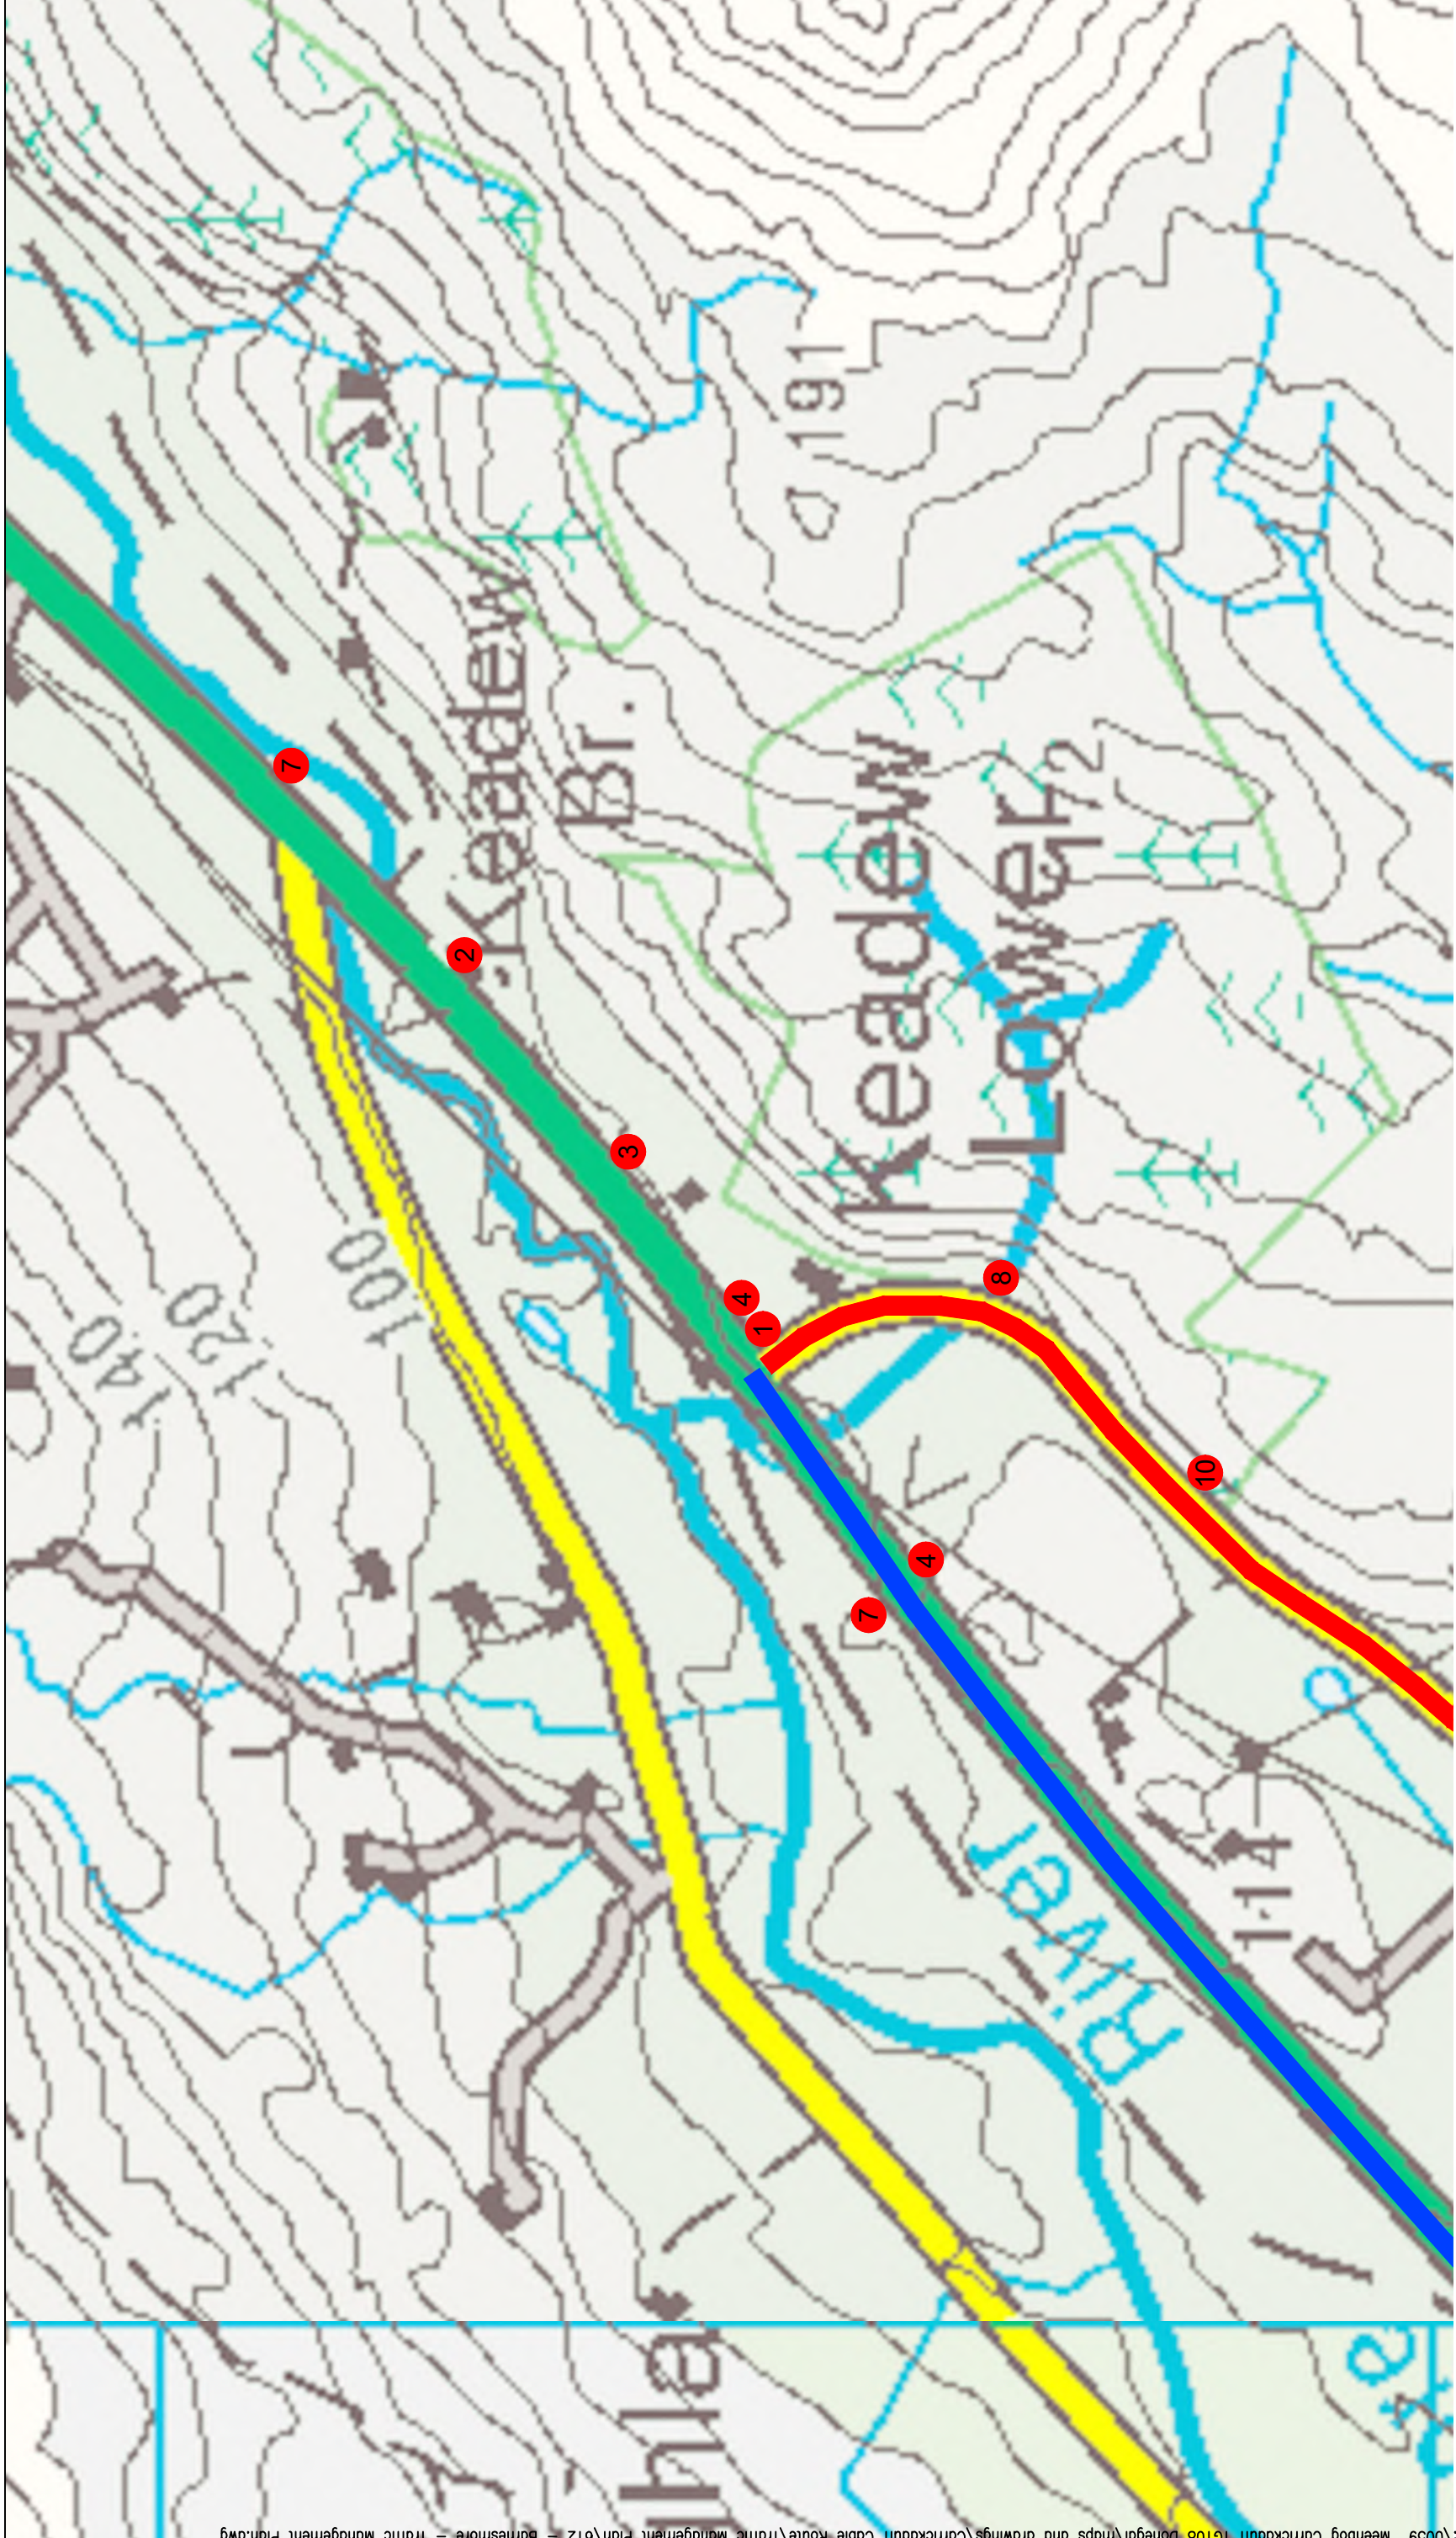


Z:\0059 Meenbog Carrickduff\6108 Donegal\maps and drawings\Carrickduff\Cable Route\Traffic Management Plan\612 - Barnesmore - Traffic Management Plan.dwg


- 1
- 2
- 3
- 4
- 5
- 6
- 7
- 8
- 9
- 10




LEGEND:
 1166m ROAD CLOSURE
 4142m PRIMARY DIVERSION ROUTE



Project Title: Meenbog WF Underground Cable	
Drawing Title: Barnesmore Section Location 1 - Sheet 1 of 4	
Date: 11.01.19	Prepared by: T.Scannlan
Scale: 1:5000@A3	Rev: 000
DRG.No: 613-1	Job Ref: 0059

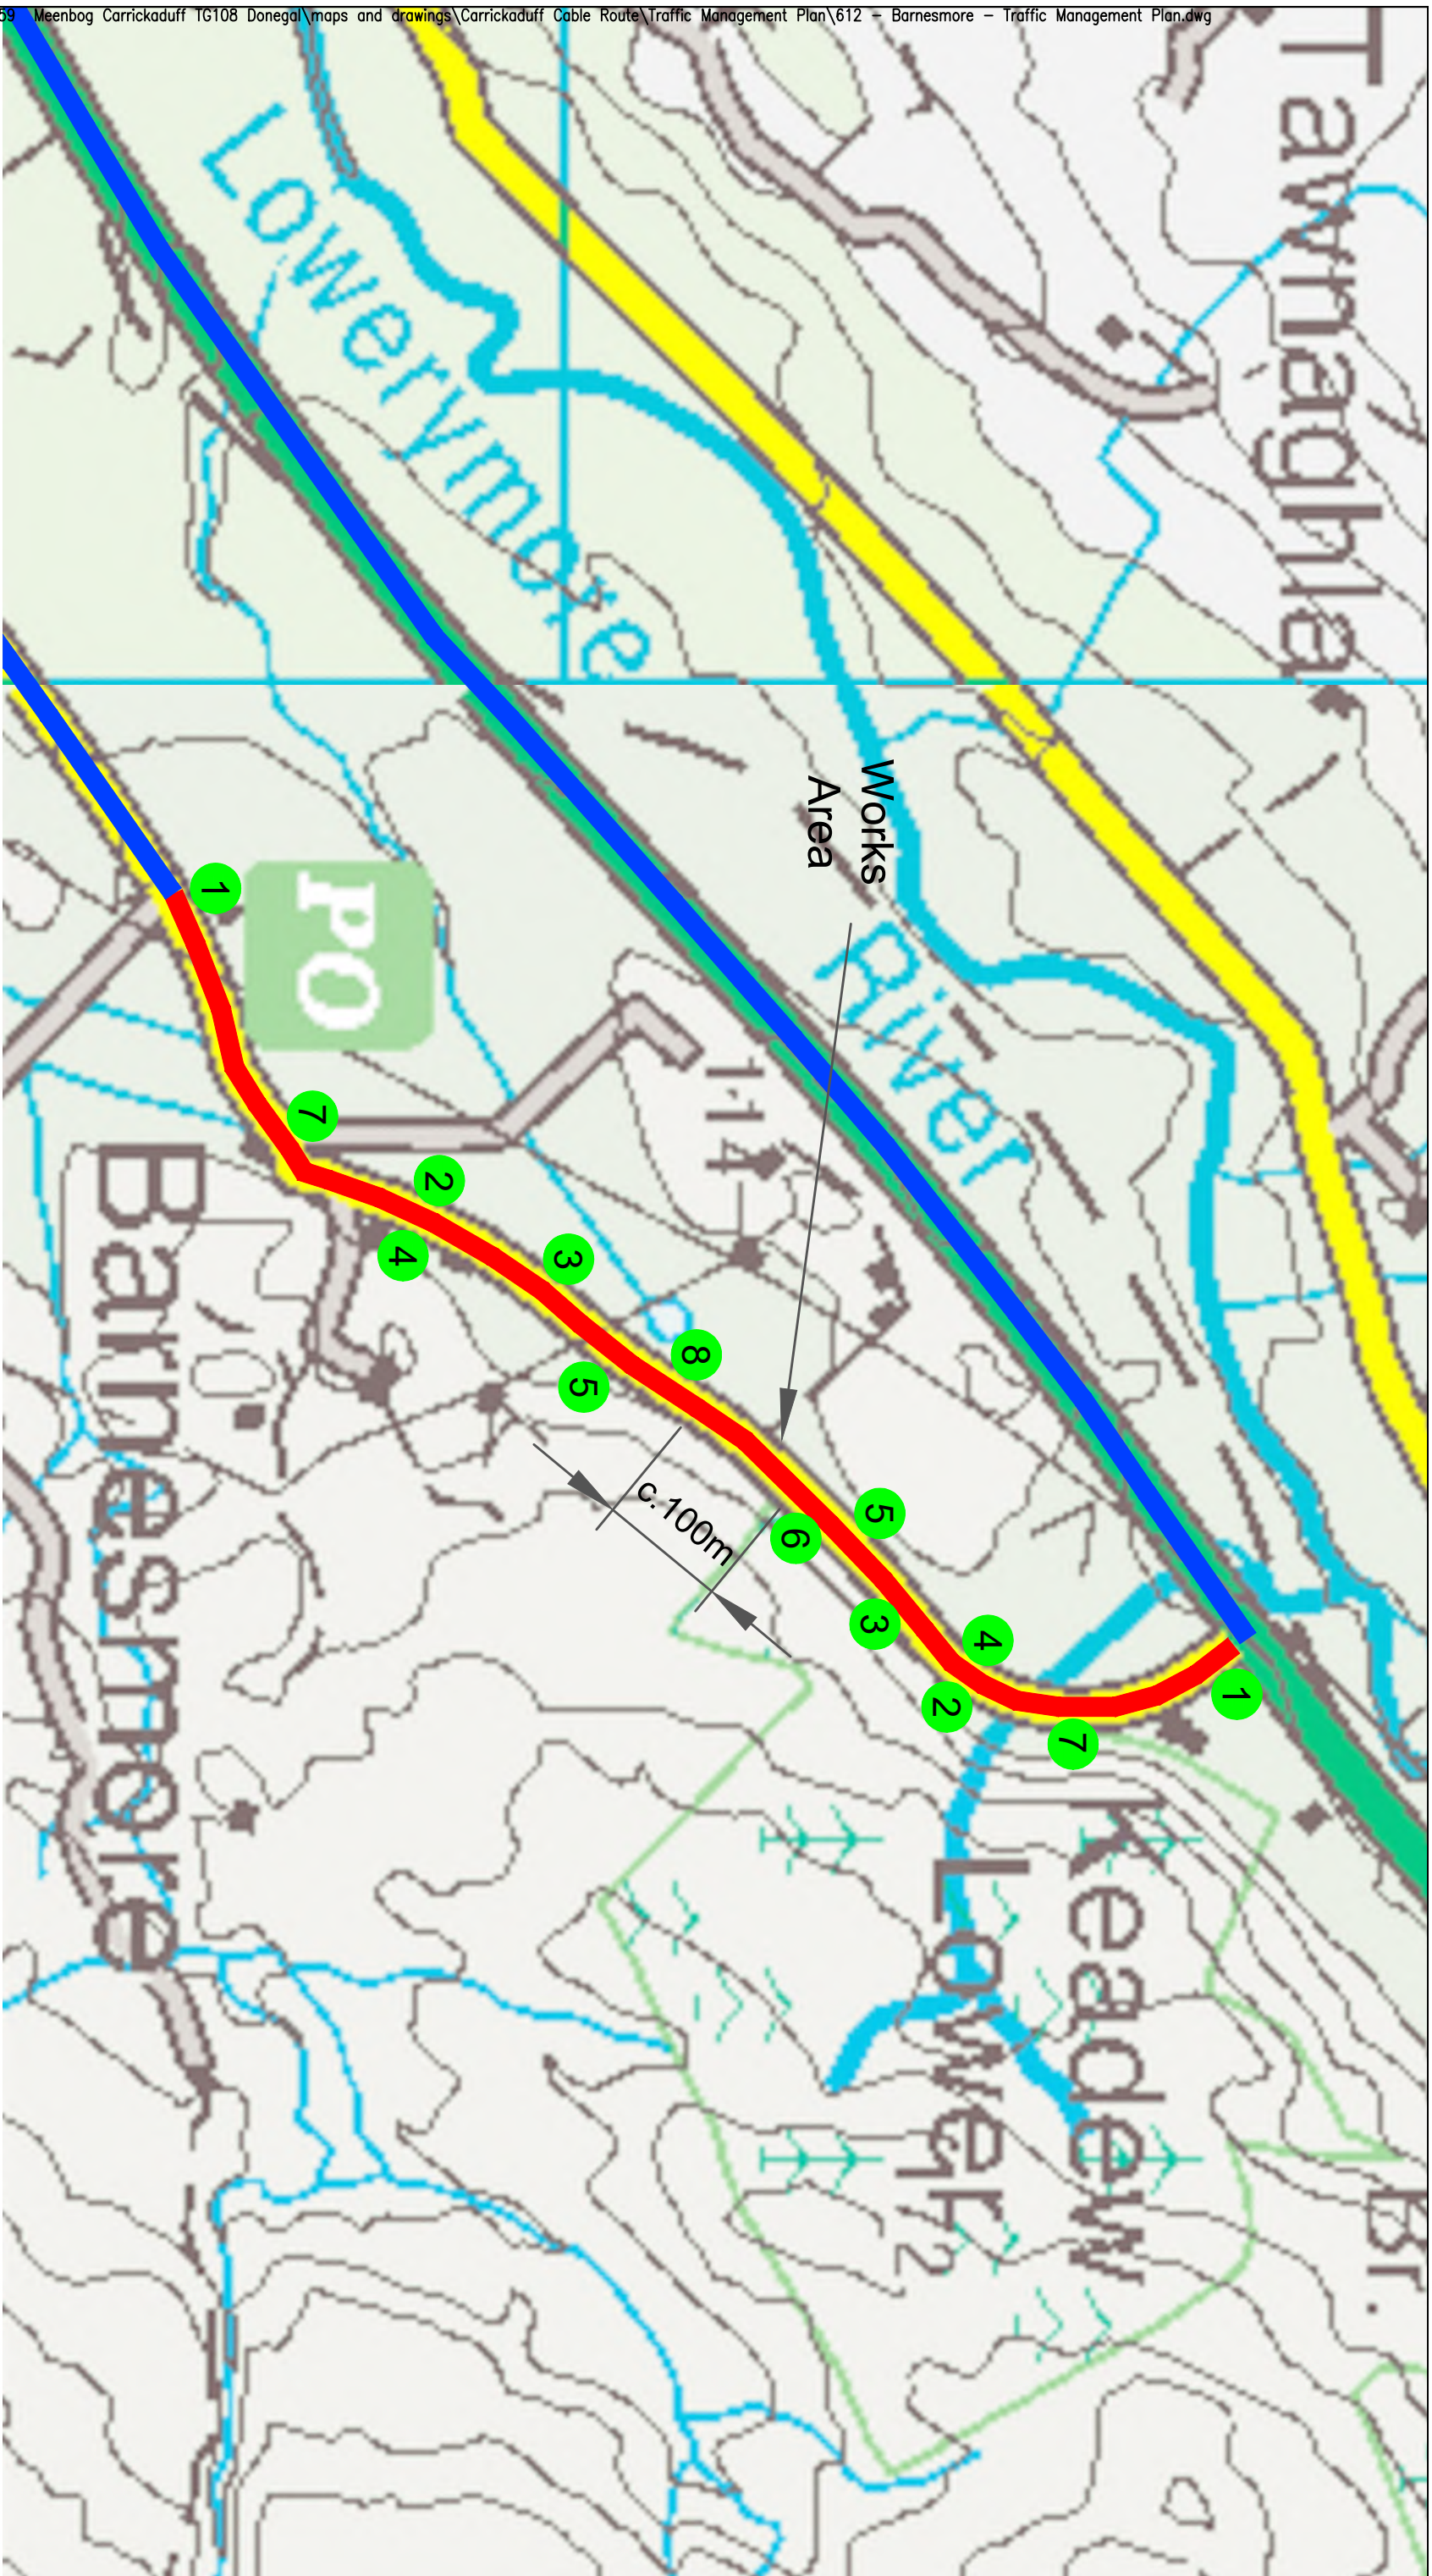

- | | | | |
|--|--|--|--|
| | | | |
| | | | |
| | | | |
| | | | |
| | | | |



LEGEND:

1166m ROAD CLOSURE —

4142m PRIMARY DIVERSION ROUTE —

Project Title:		Meenbog WF	
Title:		Underground Cable	
Drawing Title:		Barnesmore Section	
Location:		Location 2 - Sheet 2 of 4	
Date:	11.01.19	Prepared by:	T. Scallan
Scale:	1:5000@A3	Rev:	000
DRG No.:	613-2	Job Ref.:	0059




Project Title: Meenbog WF Underground Cable	
Drawing Title: Barmesmore Section Location 3 & 4 - Sheet 3 of 4	
Date: 11.01.19	Prepared by: T.Scannlan
Scale: 1:5000@A3	Rev: 000
DRG No. 613-3	Job Ref. 0059


LEGEND:

1166m ROAD CLOSURE —


4142m PRIMARY DIVERSION ROUTE —



1	2	3	4	5	6	7	8	9	10

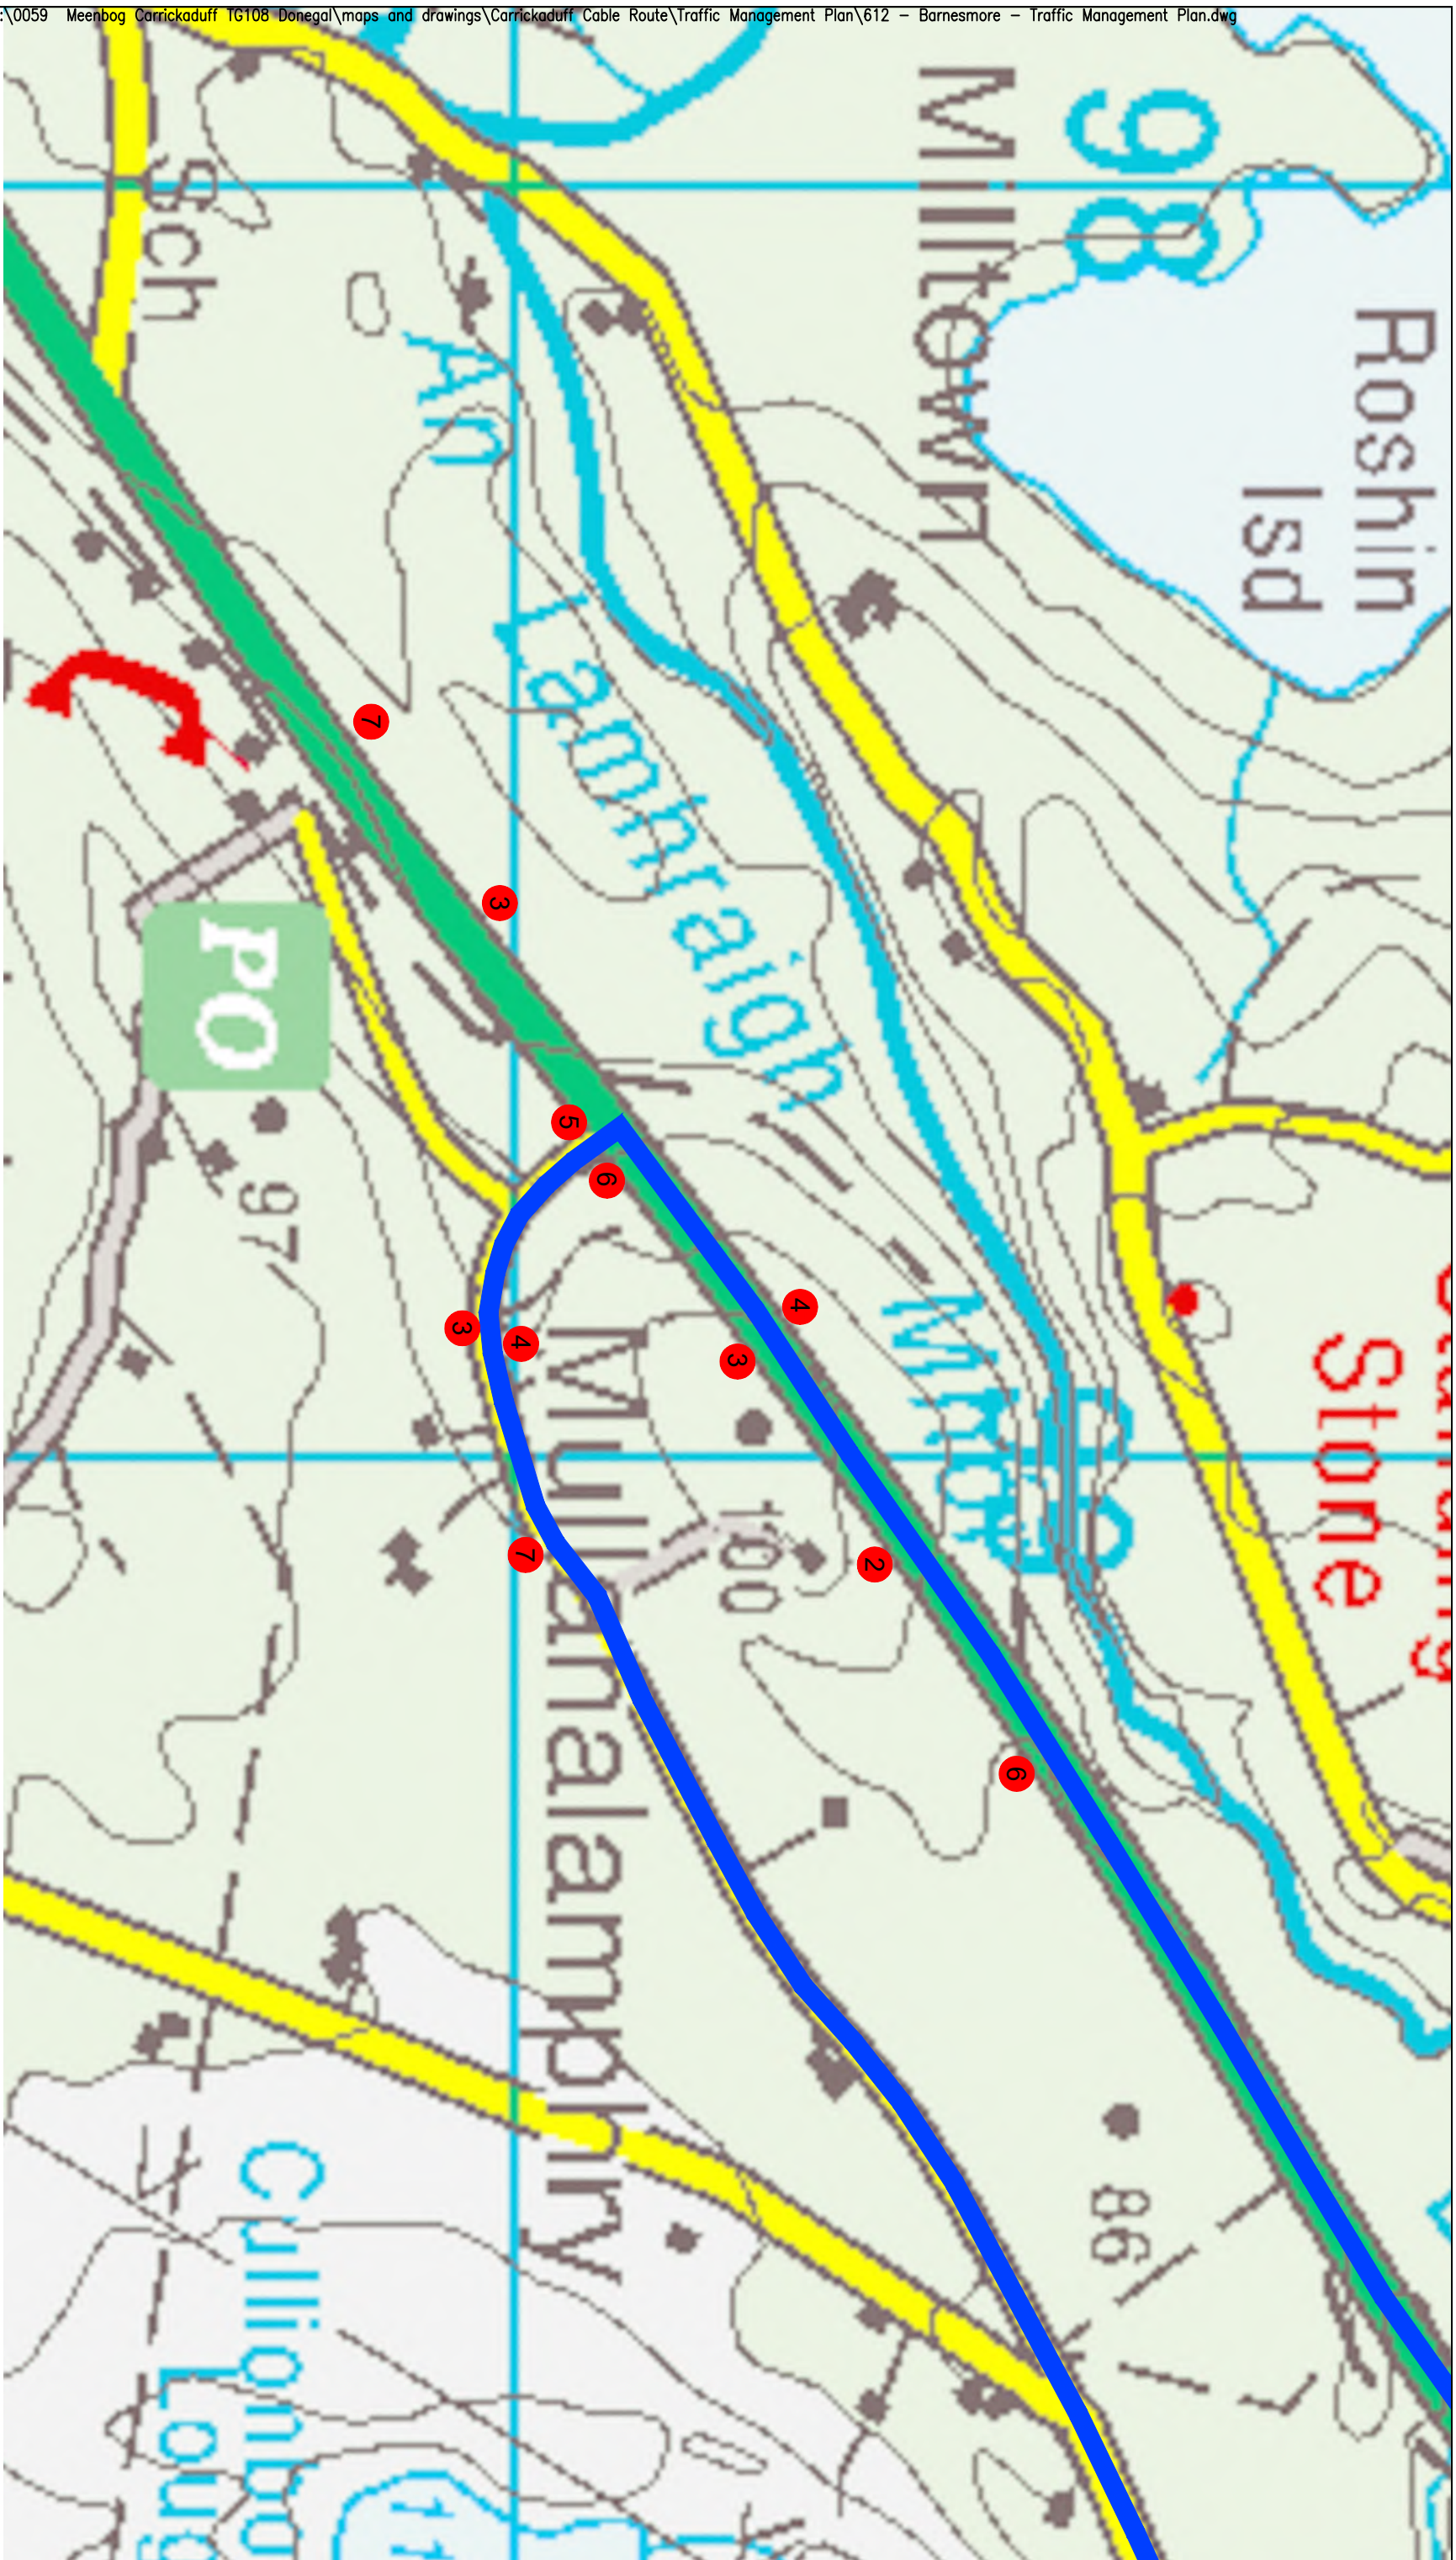

- 1 **1** **Boithar Dúnta**
ROAD CLOSED
LOCAL ACCESS ONLY
- 2 **2** **Malaírt S/I**
DETOUR
400m
- 3 **3** **Malaírt S/I**
DETOUR
200m
- 4 **4** **Traocht ar**
DIVERITED
TRAFFIC
- 5 **5** **Traocht ar**
DIVERITED
TRAFFIC
- 6 **6** **Traocht ar**
DIVERITED
TRAFFIC
- 7 **7** **Boithar dúnta L-2395-1**
Dúnta Kombair -
Traigh ar Mhalaírt S/I
LOCAL ROAD L-2395-1
CLOSED AHEAD
FOLLOW DIVERSIONS
- 8 **8** **Go Moll**
SLOW
- 9 **9** **Crioch**
END
- 10 **10** **No Trucks**



LEGEND:
 1166m ROAD CLOSURE
 4142m PRIMARY DIVERSION ROUTE

Project Title: Meenbog WF	
Underground Cable	
Drawing Title: Barnesmore Section	
Location 5 - Sheet 4 of 4	
Date: 11.01.19	Prepared by: T.Scannlan
Scale: 1:5000@A3	Rev: 000
DRG No. 613-4	Job Ref: 0059



Civil Engineering

Traffic Management Plan: MCE – N-15 Duct Installation along National Primary Roads N-15-25, N-15-24, N-15-23, N-15-22 & N-15-21.



January 2019

Telephone: +353 (0) 21 733 6034, Fax: +353 (0) 21 733 6145
Web: www.mceengineering.ie, Email: office@mceengineering.ie
Lissarda Industrial Estate, Lissarda, Cork, Ireland.

MCE – N-15 Duct Installation Traffic Management Plan

Contractor: MCE ltd.

Project name: Meenbog Wind Farm

Address: Carrickalangan, Meenbog & Cullionboy, Co. Donegal.

Name : Sean Driscoll - Tel:086-8528329
Chris Murnane – Tel: 086-7955083

Email: sean.odriscoll@turnkeydev.com
chris.murnane@gmail.com

Site supervisor: Sean Driscoll / Chris Murnane








































Safety officer: Chris Murnane

Description of task: Traffic Management Plan for Meenbog Wind Farm for the grid connection cable on road numbers N-15-25, N-15-24, N-15-23, N-15-22 & N-15-21.

Key plant: 360 excavators
8 tonne dumper
Lorries
Roller
Submersible Pumps
Plate compactor
Generator
Spill Kit
Diesel Bouser
Drip Trays
Directional Drilling Rig
Auger Boring Machine

Specific Training: FAS safe pass
CSCS plant ticket
Site induction

MCE – N-15 Duct Installation Traffic Management Plan

<p>Method of Access and Egress to the work Area</p>	<p>All operatives must complete pre works MCE Ltd. site induction before commencing work on the ducting route.</p>														
<p>Fall Protection Measures: (Where work at height cannot be eliminated)</p>	<p>No persons are permitted within 2 meters of excavation. Trench support will be utilized if required. Open trenches will be fenced off or backfilled every evening to ensure the areas are safe for workers and local traffic.</p>														
<p>Hazardous Substances: Applicable:</p>	<table border="1" style="width: 100%; text-align: center;"> <tr> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>No</td> <td>No</td> <td>No</td> <td>No</td> <td>No</td> <td>Yes</td> <td>No</td> </tr> </table>								No	No	No	No	No	Yes	No
															
No	No	No	No	No	Yes	No									
<p>Storage Arrangements:</p>	<p>No material will be used or generated during the course of this task</p>														
<p>Mandatory and Additional PPE as Required:</p>	<table border="1" style="width: 100%; text-align: center;"> <tr> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>Other: 1. Hi-Vis</td> </tr> <tr> <td>Safety Boots Yes</td> <td>Hard Hats Yes</td> <td>Kevlar Yes</td> <td>Hearing Protection When required</td> <td>Eye Protection Yes</td> <td>Respiratory Protection N/A</td> <td></td> </tr> </table>							Other: 1. Hi-Vis	Safety Boots Yes	Hard Hats Yes	Kevlar Yes	Hearing Protection When required	Eye Protection Yes	Respiratory Protection N/A	
						Other: 1. Hi-Vis									
Safety Boots Yes	Hard Hats Yes	Kevlar Yes	Hearing Protection When required	Eye Protection Yes	Respiratory Protection N/A										
<p>Emergency Procedures:</p>	<p>MCE Emergency Procedures (All employees informed at site inductions) All employees to be made aware of the nearest exit routes from site.. All personnel to be in possession of the site coordinates at all times in case of need to contact emergency services for any reasons.</p>														
<p>First Aid Facilities:</p>	<p>On-Site First Aider: Sean O’Driscoll / Chris Murnane First Aid Box Location: MCE Site Vehicle & Site Office Nearest Hospital: Letterkenny General Hospital – (074) 9125888 HSE Community Care Centre, Ballybofey (074 9131391)</p>														
<p>Welfare Facilities:</p>	<p>Site office, canteen and toilet supplied by Mid Cork Electrical at site compound across from substation and assembly point.</p>														

MCE – N-15 Duct Installation Traffic Management Plan

Introduction:

This traffic management plan outlines the affected roadways for the 110 kV ducting installation for the underground cable grid connection between Meenbog WF 110kV Substation (Croaghonagh) and Clogher 110kV substation (Cullionboy). This is to be read in conjunction with the works method statement in order to provide a safe system of work.

The length of roadway affected is 5,748 metres along the N-15-25, N-15-24, N-15-23, N-15-22 & N-15-21. There will not be a requirement to close the road at any time during the works and access will be granted at all times to all vehicles. Traffic calming measures will be utilized to slow down vehicles and ensure ducting can be carried out safely.

Prior to any works commencing a dilapidation survey will be completed of the entire route, photographing and noting any existing damage or defects to property or road surfaces. A copy of this will be submitted to the Donegal County Council prior to work commencing.

Local Access for Residents

As part of the management plan local residents affected by the road closure will be alerted to the works through the use of letter drops and prior consultation.

Every effort will be made to limit the effect on local residents and any residents who require special provisions to be made will be accommodated (i.e. Home carer, etc.). Traffic manage plans will be reviewed on a daily basis and take into account all local parameter in the area where work is being carried out. All required traffic management calculation forms will be completed and kept on site.

MCE – N-15 Duct Installation Traffic Management Plan

Pedestrian & Cyclist Management

Pedestrians and cyclist will be accommodated along the primary and secondary diversion routes. Operatives will be made aware to watch out for oncoming pedestrians / cyclists and to advise them accordingly.

Dealing With Emergency Services

Gardai will be advised of the intended works to be carried out prior to commencement on the Gardai Consultation form. Emergency services using the local roads will be made priority and areas where the works are being carried out will be covered immediately with road plates so as to allow access.

Signage Plan

All works will be signed in accordance with the “Guidance for the Control and Management of Traffic at Road Works” (Second Edition 2010). The Routine Works Traffic Management Design, including the layout parameters is illustrated on attachment.

MCE – N-15 Duct Installation Traffic Management Plan

All traffic management will comply with guidance given in Chapter 8, Traffic Signs Manual, Department of Transport November 2006 and Control and management of Traffic at Road Work October 2007.

A fully certified and competent ‘Signing Lighting & Guarding’ officer will sign off on the works before commencement and carry out routine monitoring. A qualified supervisor will be onsite at all times.

- ✓ See attached traffic management design sheet for signage etc.
- ✓ The entire traffic management system will be set up prior to any works commencing.
- ✓ Only approved signs will be used along the works area.
- ✓ All signs will be clean and clearly visible.
- ✓ Once signs are in place the route will be assessed to ensure adequate visibility for drivers and pedestrians.
- ✓ All signs will be secured and weighted down where appropriate.
- ✓ Lane width will be reduced and a two-way layout flow during all ducting installation with the north bound hard shoulder closed.
- ✓ At the end of each day the excavation is back filled and all materials will be removed from the roadside.
- ✓ Contractor vehicles will be parked with consideration given to traffic management plan.
- ✓ Where flag men are required, both flag men, the foreman and guarding officer will all communicate via two-way radios.

MCE – N-15 Duct Installation Traffic Management Plan

Road Closure / Road Opening Licence Drawings:

The following drawings are included at the end of this document:


- ✓0059 – 610 – Traffic Calming Measures– Overall Layout View
- ✓0059 – 611-1 – Sheet 1 of 4 – Location 1 Layout
- ✓0059 – 611-2 – Sheet 2 of 4 – Location 2 Layout
- ✓0059 – 611-3 – Sheet 3 of 4 – Location 3 & 4 Layout
- ✓0059 – 611-4 – Sheet 4 of 4 – Location 5 Works Area Layout

MCE – N-15 Duct Installation Traffic Management Plan

Signage Layout

The following is the layout for signage that will be in place on the approach to the road works which will be occurring on the N-15-25, N-15-24, N-15-23 N-15-22 & N-15-21. See attached drawings showing signage layout for the alterations to the road layout which will be occurring .

- ✓ Sign no.1: WK 001 (man with shovel) 1000m before road works
- ✓ Sign no.2: (do not pass) 800m before road works
- ✓ Sign no.3: P 011 (Cautionary Speed limit 60 km/h) 600m before road works
- ✓ Sign no.4: WK 032 (road narrows ahead) 400m before road works
- ✓ Sign no.5: P 083 (end of hard shoulder) & WK 013 (divert to right) 200m before road works
- ✓ Cones with reflectors start to taper 200m before works location begin.
- ✓ Sign no.6: WK 052 (site entrance on left) 100m before entrance to works
- ✓ Sign no.7: WK 052 (site entrance on left) at entrance to works
- ✓ Statutory sign no 6 : (blue arrow) at start of cones.
- ✓ Signage after road words will indicate 'No Overtaking Ends' and 'End of Road Works'.
- ✓ Traffic entering and exiting existing secondary road will continue as normal with construction traffic kept to a minimum.
- ✓ See attached generic shuttle layout system for one-way stop and go. This shuttle layout will be set up onsite by the qualified signing lighting and guarding officer.

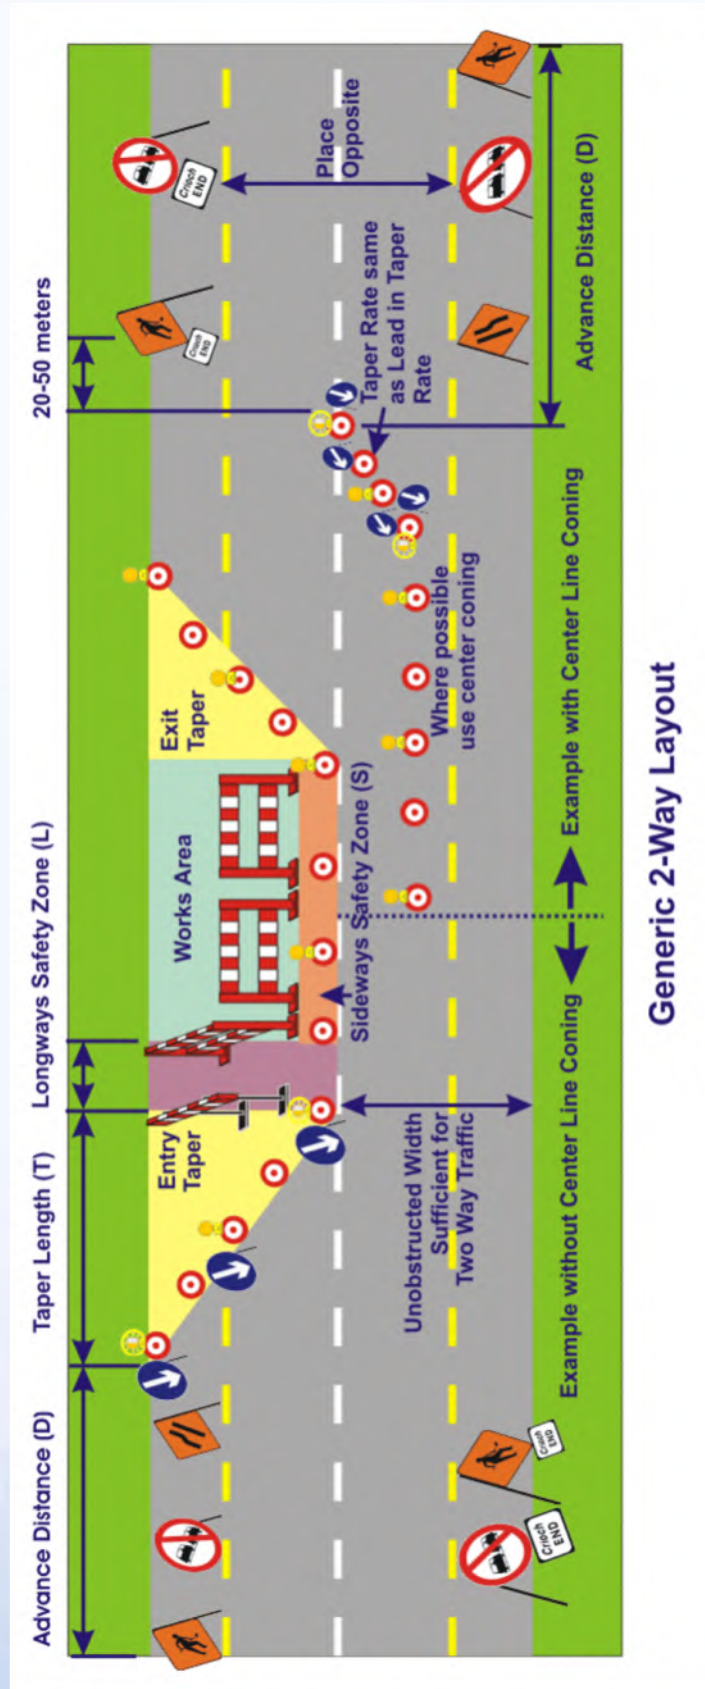

Generic 2-Way Layout

ROUTINE WORKS TRAFFIC MANAGEMENT DESIGN

SHUTTLE CONTROL SELECTION

Method	Max Speed Limit (km/h)	Length of Works (m)	Max Traffic (veh/hr)	3 Min Count	Notes
All Stop	100	n/a	300	15	5-10 mins max.
Give and Take	50	50	400	20	Clear Visibility required from both directions
Priority	100	80	840	42	Speed Limit 50 km/h Clear Visibility required from 60 km/h 80 km/h 80m 100m
Stop/Go	100	20	500	25	Can be Single Man/Single Sign 100 100 1400 70 Can be single Man-Auto Sign 100 200 1250 63 Can be single Man-Auto Sign 100 300 1050 53 Has to be Two Man-Two Sign 100 400 950 48 Has to be Two Man-Two Sign 100 500 850 43 Has to be Two Man-Two Sign
Traffic Lights	100	500	n/a	n/a	Vehicle Actuated

NOTE: WHEN USING SHUTTLE CONTROL, TAPERS ARE AT 45 DEGREES

LAYOUT PARAMETER SELECTION SHEET

Type of Road	Advance Sign Distance (D) (m)	Min No. & Type Of Advance Signs in Sequence	Min clear visibility of Signs (m)	Min size of signs (mm)	Min height of cones (mm)	Long. Safety Zone (L) (m)	Side. Safety Zone (S) (m)	Long. Cone Space	Long. Lamp Spacing	Lane Taper Multiply	Taper Cone Spacing	Taper Lamp Spacing	Lead-in cone tapers (See Notes below) Recommended lengths	Width of hazard (including safety zone) NOTE: TAPERS ARE ONLY WHERE TWO WAY TRAFFIC MAINTAINED	Hard Shoulder Taper Multiply
Single carriageway road, 30km/h	50	1 (r.w.a.) 1 (l.m.)	50	600	450	5	0.5	6	12	8	3	9	Length of taper (T) in (m) Minimum No. of Cones Minimum No. of Lamps	1m 8 2m 16 3m 24 4m 32	4
Single carriageway, 60km/h	50	1 (r.w.a.) 1 (l.m.)	50	600	450	5	0.5	6	12	8	3	9	Length of taper (T) in (m) Minimum No. of Cones Minimum No. of Lamps	1m 8 2m 16 3m 24 4m 32	4
Single Carriageway 80km/h	600	1 (r.w.a.) 1 (n.o.) 1 (l.m.)	90	750*	750	45	1.2	12	24	35	2.5	9	Length of taper (T) in (m) Minimum No. of Cones Minimum No. of Lamps	1m 35 2m 70 3m 105 4m 140	20
Single Carriageway 100 km/h	800	1 (r.w.a.) 1 (n.o.) 2 (l.m.)	120	750* 900*	750	60	1.2	12	24	40	1	9	Length of taper (T) in (m) Minimum No. of Cones Minimum No. of Lamps	1m 40 2m 80 3m 120 4m 160	20
Dual Carriageway 60 km/h	600	1 (r.w.a.) 2 (l.m.) X 2	50	900	450	5	0.5	6	12	8	3	9	Length of taper (T) in (m) Minimum No. of Cones Minimum No. of Lamps	1m 8 2m 16 3m 24 4m 32	4
Dual Carriageway 80 km/h	600	1 (r.w.a.) 2 (l.m.) X 2	90	900	750	45	0.75	12	24	35	3	9	Length of taper (T) in (m) Minimum No. of Cones Minimum No. of Lamps	1m 35 2m 70 3m 105 4m 140	10
Dual Carriageway 100 km/h	1000	2 (r.w.a.) 3 (l.m.) X 2	120	1200	750	45	1.2	12	24	40	1	9	Length of taper (T) in (m) Minimum No. of Cones Minimum No. of Lamps	1m 40 2m 80 3m 120 4m 160	20

* Use 750mm signs where Vehicles Per Day < 5,000. Use 900mm signs where Vehicles Per Day > 5,000

Warn	r.w.a	Priority	Advance Signs	Works Signs	End Signs
		1			
		2			
		3			
		4			

For Advance Signs Space Signs evenly through the advance sign distance

Direct select appropriate


road works ahead

traffic management

no overtaking

TRAFFIC MANAGEMENT PLAN FOR ROUTINE WORKS


















5) Road Schematic



6) Traffic Management Selection

6.1) Classification	Road Type	Road Width	Speed Limit	Urban/Rural	Traffic Heavy/ Light	
6.2) Selection	All Stop	Give & Take	Priority	Stop/ Go	Lights	Tapers
6.3) Semi-Static	Will Semi-Static Management be used?				Yes	No

7) Signage (Warn / Inform / Direct / End)

No	Sign	Dir	No	Sign	Dir	No	Sign	Dir	No	Sign	Dir
1 + 2 ARE SEMI-STATIC	 SELECT PLATE BELOW	A	6		A	11		A	16		A
		B			B			B			
		C			C			C			
		D			D			D			
		A	7		A	12		A	17		A
		B			B			B			
		C			C			C			
		D			D			D			
	 2 km ar fad FOR 2 km	A	8		A	13		A	18		A
		B			B			B			
		C			C			C			
		D			D			D			
3		A	9		A	14		A	19		A
		B			B			B			
		C			C			C			
		D			D			D			
5		A	10		A	15		A	20		A
		B			B			B			
		C			C			C			
		D			D			D			
If Using Traffic Lights/ Stop-Go, Have Gardai Been Notified?										YES	NO
Are All Required Cones /(Lamps & Beacons) In Place (and operating)?										YES	NO

8) Workforce Induction & Communication

8.1) Has this Plan been Communicated to the workforce and does everyone know their role? Operatives to Sign Below	Yes	No
8.2) Supervisor		

NOTIFICATION OF POSITIVE TRAFFIC CONTROL

Under the following Road Traffic Acts/Regulations

- Section 37 of the Road Traffic Act, 1994
- Road Traffic (Signs) Regulations 2006 (S.I. No. 637 of 2006)
- Road Traffic (Control of Traffic) Regulations 2006 (S.I. No. 638 of 2006)

The Roads Authority of

Hereby notifies

Of the use of

TEMPORARY TRAFFIC LIGHTS

STOP-GO BOARD(s)

at the following location:

Road

From a point

To a point

ON/ BETWEEN (delete as appropriate) the following dates

and

Observations (if any) should be faxed to:

Signed: _____

On behalf of the Roads Authority

PLANNED WORKS TRAFFIC MANAGEMENT SITE INSPECTION SHEET					
PROJECT NAME:				Phase:	
Date:		Time:	1).	2).	
1) TRAFFIC MANAGEMENT SET-UP/ MODIFICATION, INSPECTIONS					
1-1) Installation Checks					
Does the Traffic Management conform to the Design Layout and Parameters?					
Have all hazards been addressed in the Traffic Management Plan?					
Has allowance been made for the delivery and removal of materials?					
Have Gardaí been informed of any Traffic Lights/ Stop-Go Boards in use?					
Have Gardaí been informed of Roadworks Speed limits being introduced?					
2) TRAFFIC MANAGEMENT OPERATION INSPECTIONS					
2-1) Operation Checks					
Are Safety Zones being kept clear of operatives, plant and materials?			1	2	
Are all the signs in good condition/ are all cones in good condition with sleeves?					
Are sign vision lines free from bends, hills/dips in the road, parked vehicles, hedges etc?					
Will the site be safe at night or in wind, fog, snow or rain? (delete as appropriate)					
Are all misleading permanent signs and road markings covered?					
Is the carriageway/footway being kept clear of mud and surplus equipment?					
Are materials/ plant that are left on verges or lay-bys being properly guarded and lit?					
2-2) Traffic Checks					
Is there safe access to adjacent premises?					
Does Signing and Guarding meet the (changing) conditions?					
Are traffic control arrangements working at the optimum level to reduce traffic delays?					
If present, are the needs of cyclists or horse riders incorporated into the layout?					
2-3) Pedestrian & Vulnerable Road User Checks					
Have the needs of pedestrians & vulnerable road users been addressed in the layout?					
If pedestrian route blocked, has a suitable alternative route been provided?					
Are pedestrian routes clearly evident/ indicated?					
If a footway in the road is to be used, are ramps to the kerb provided?					
Are pedestrian hazards sufficiently GUARDED at night?					
3) TRAFFIC MANAGEMENT CESSATION INSPECTIONS					
3-1) Works Complete Checks					
Have all signs, cones, barriers, and lamps been removed?					
Have any covered permanent signs been restored?					
Have Gardaí been informed that Speedlimits/ Traffic Signals/ Stop-Go removed?					
4) EXCEPTIONS REPORT					
(Append attachments as necessary)					
Check Completed By:					

PROJECT CLOSEOUT SHEET	
PROJECT NAME:	

1) Procedures	
The extents of construction have been completed per the plans	
Pavement Surface has been visually inspected and deemed satisfactory (incl. sweeping of surfaces that have been surface dressed)	
Temporary Traffic Management arrangements (incl. Orders) have been removed	
Any Permanent Road Markings, Road Studs, and Signs have been installed	
2) Works Extents	
The length of work completed was (m)	
The average width of work completed was (m)	
3) Appointments	
PSDP appointment terminated	
Designer appointment terminated	
PSCS appointment terminated	
Contractor given completion certificate	
4) Records	
The safety file is complete and will be stored	
5) Site Inspection	
The site has been inspected by (print name) and deemed to be satisfactory:	
Signature:	
Date of inspection:	
6) Procedure Monitoring (to be completed by supervisor of person listed in 5 above)	
I recommend that the Project be deemed complete (print name)	
Signature:	
Date:	

INCIDENT/ ACCIDENT REPORT FORM

1) Job Details

1.1) Job Name	
1.2) Job Location	

2) Incident

2.1) Date of Incident								2.2) Time of Incident			
2.3) Incident Involves	Public	Layout	Operatives	Plant	Materials	Hired	Contractor	Environment			
2.4) Incident Classification	Class 1		Class 2		Class 3	Class 4					
	Long Traffic Delays	Pedestrian Danger	Near Miss	Minor Injury	3 Day Injury	Road Traffic Accident	Serious Injury or Death				
2.5) Weather Conditions	Light:	Sunny	Cloudy	Fog	Dawn/Dusk	Night	Floodlit				
	Rain:	Dry	Light Rain	Heavy Rain	Hailstones	Snow					
	Wind:	No Wind	Breeze	Windy	Gale						
	Temperature:	Warm		Cold		Freezing					
2.6) Locus	Carriageway	Footpath		Safety Zone		Working Space					
2.7) Pavement Condition	Clean	Dirty	Dry	Wet	Granular	Wearing	Base	Chips	Markings		
2.8) Number involved (Class 2 or greater)											

3) Traffic Management

	N/A	Yes	No
3.1) Were the appropriate signs in their correct place?			
3.2) Were the signs in a good condition?			
3.3) Were all cones in place and in good condition?			
3.4) Were all TM Lamps in place and operating?			
3.5) Were all TM Beacons in place and operating?			
3.6) Were Plant Hazard Beacons operating?			

4) Site Health and Safety

	N/A	Yes	No
4.1) Had operative appropriate CSCS card?			
4.2) Had plant/ equipment been checked for suitability?			
4.3) Were Safety Guards in place and in good condition?			
4.4) Were correct operating procedures/ guidelines used?			
4.5) Were operatives wearing appropriate PPE?			
4.6) Was there good housekeeping on site?			

5) Emergency Procedure

5.1) Services	None	First Aid	Driven to Aid	Ambulance	Fire Brigade	Gardaí
5.2) Procedure		Good	Bad	None		
	Training					
	Equipment					

6) Operatives (List operatives on site at time of incident)

7) Incident Description

8) Suggested Control Measures to Prevent Re-Occurance

9) Incident Sketch


**10) Report
Completed By:**

**11) Report
Noted By:**



MCE – N-15 Duct Installation Traffic Management Plan

	Name (Print)	Signature	I understand the details in the traffic management plan and agree to sign off (tick)	Date
1				
2				
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				

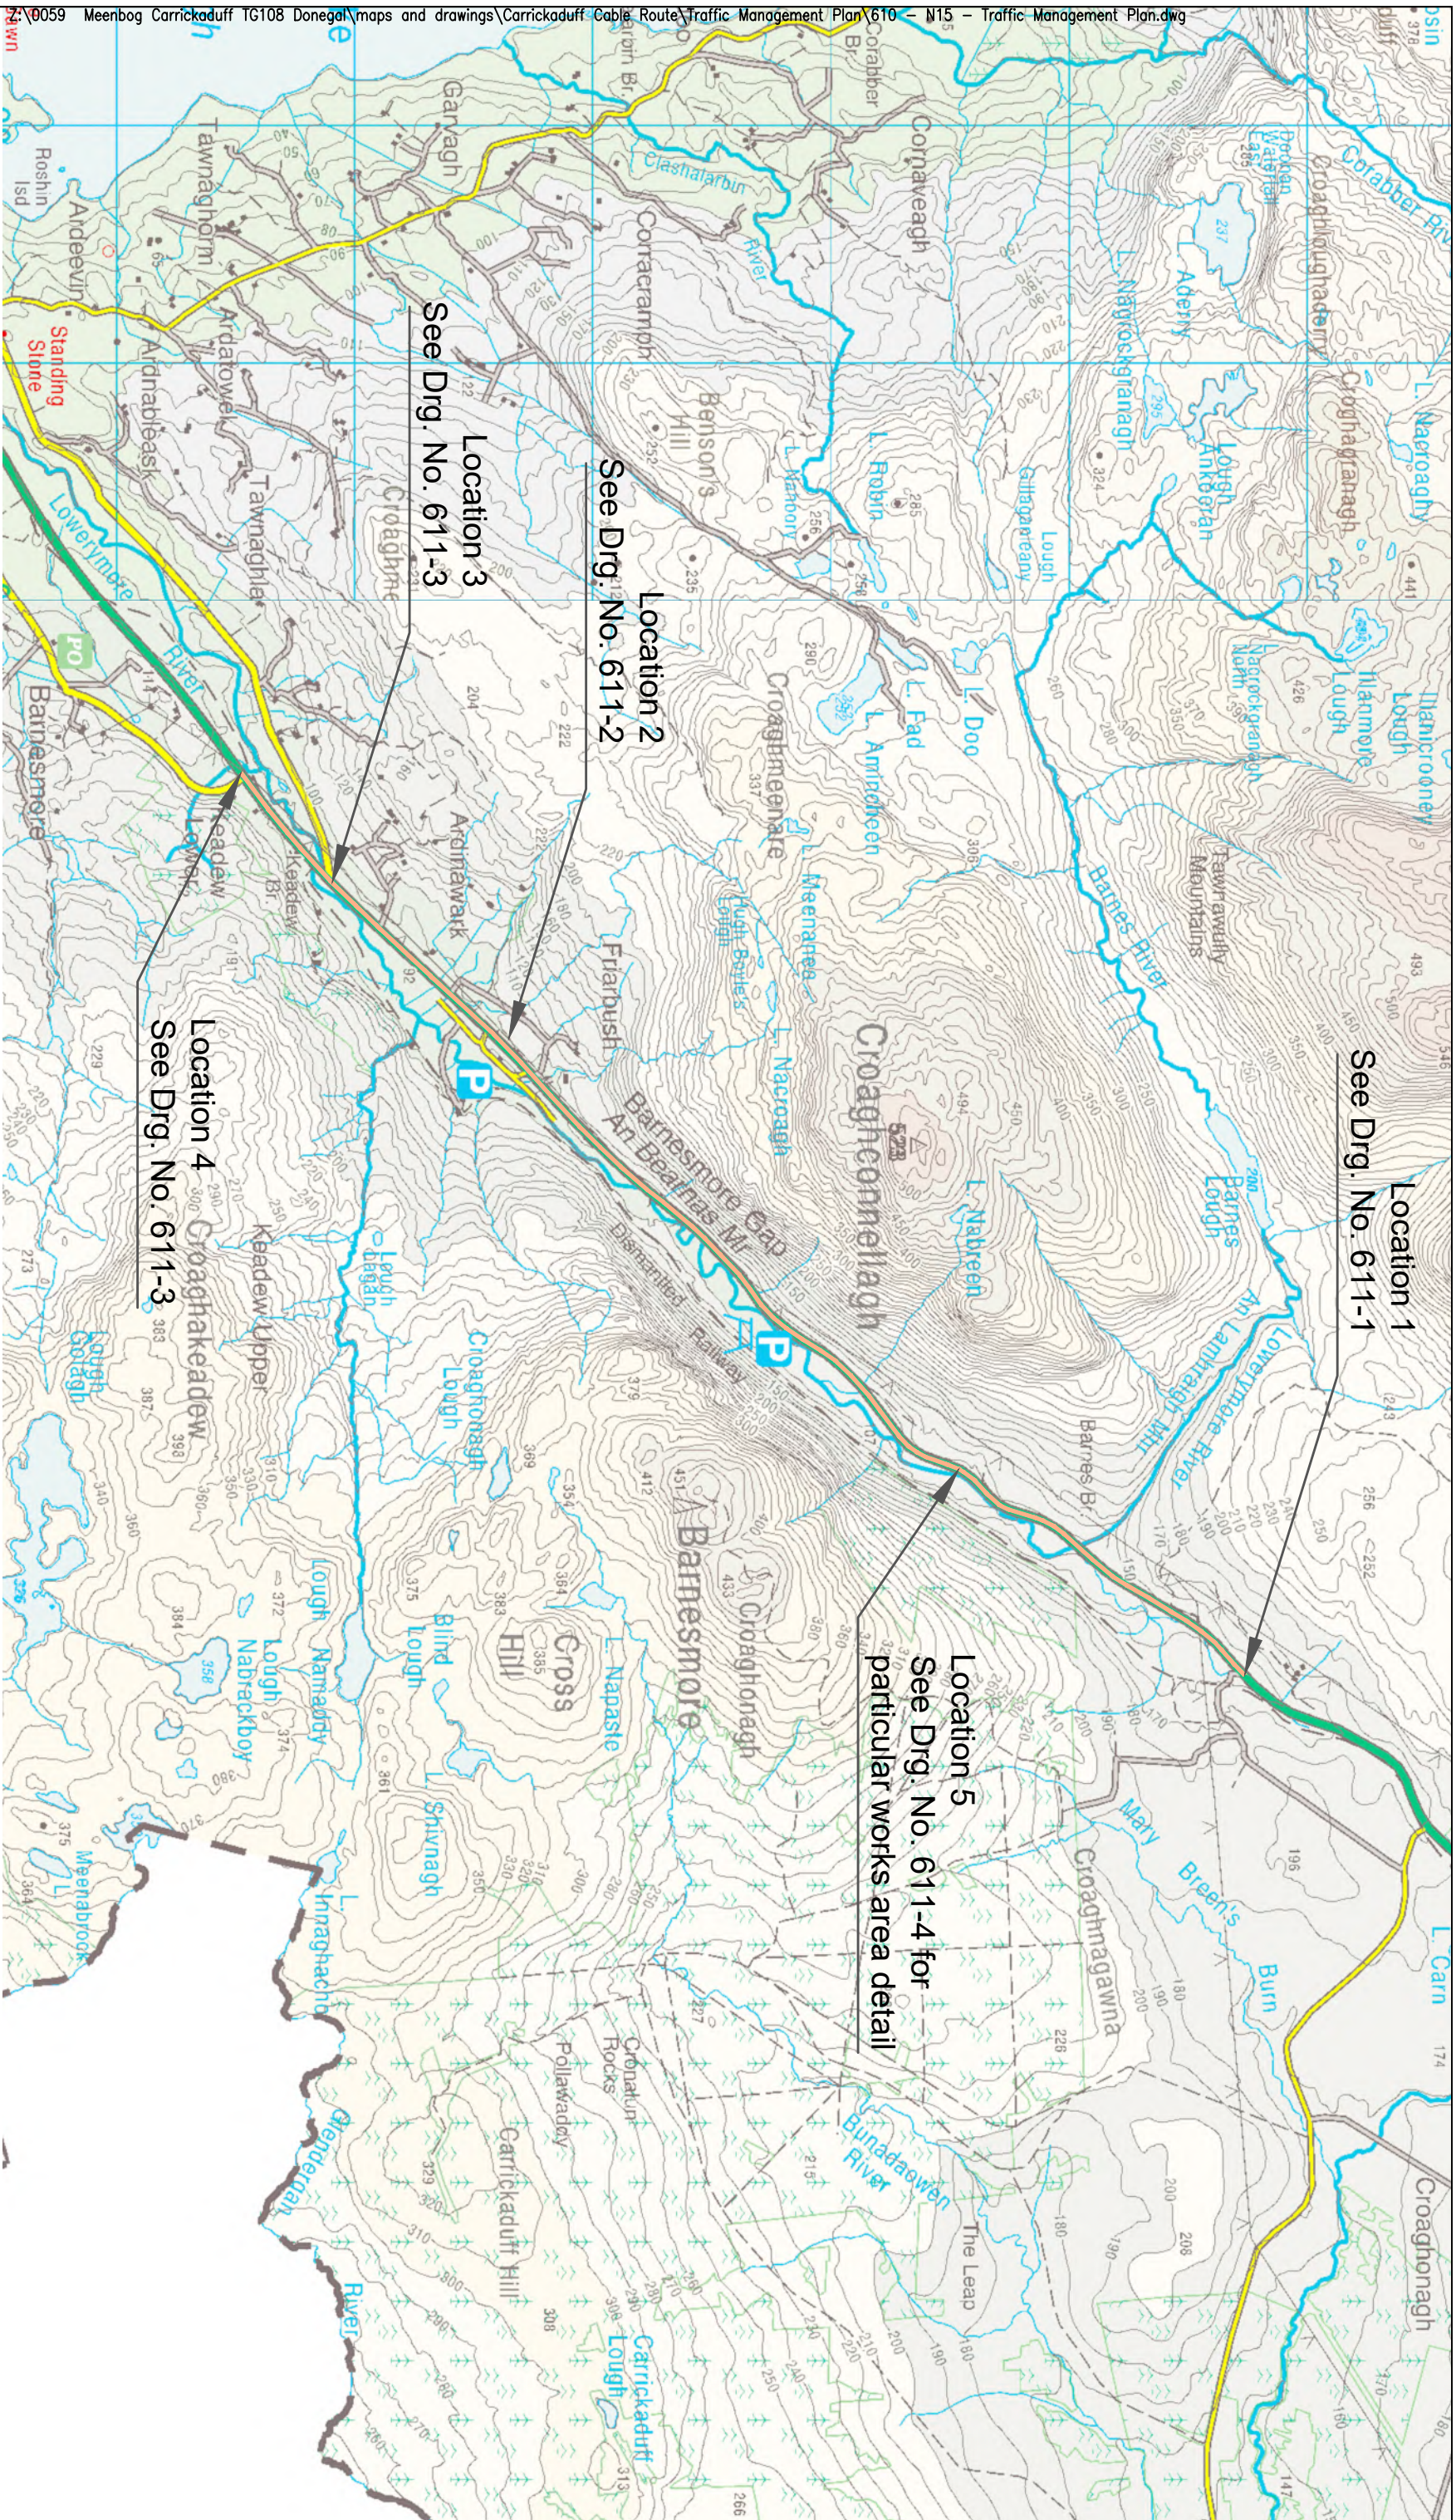

Location 1
See Drg. No. 611-1

Location 5
See Drg. No. 611-4 for
particular works area detail

Location 2
See Drg. No. 611-2

Location 3
See Drg. No. 611-3


Location 4
See Drg. No. 611-3



LEGEND:

5748m EXTENT OF WORKS —

Project		Title:	
Meenbog WF		Underground Cable	
Drawing			
Title: Traffic Calming Measures - N15 Overall Layout View			
Date: 11.01.19	Prepared by: T.Scannlan	DRG No. 610	
Scale: NTS	Rev: 000	Job Ref: 0059	



1




2



3



4



5




6




7



8



9



LEGEND:

5748m EXTENT OF WORKS



Project Title:

Meenbog WF
Underground Cable

Drawing Title:
Traffic Calming Measures - N15
Sheet 1 of 4
Location 1 - Layout

Date: 11.01.19 Prepared by: T.Scanlan DRG No. 611-1

Scale: 1:5000@A3 Rev: 000 Job Ref: 0059



- 1
- 2
- 3
- 4
- 5
- 6
- 7
- 8
- 9

↑ 5800 m ↓


Crioch
END

Crioch
END

←

→

N




LEGEND:

5748m EXTENT OF WORKS





Project Title: Meenbog WF	
Underground Cable	
Drawing Title: Traffic Calming Measures - N15	
Sheet 2 of 4	
Location 2 - Layout	
Date: 11.01.19	Prepared by: T. Scallan
Scale: 1:5000@A3	Rev: 000
DRG No. 611-2	Job Ref: 0059

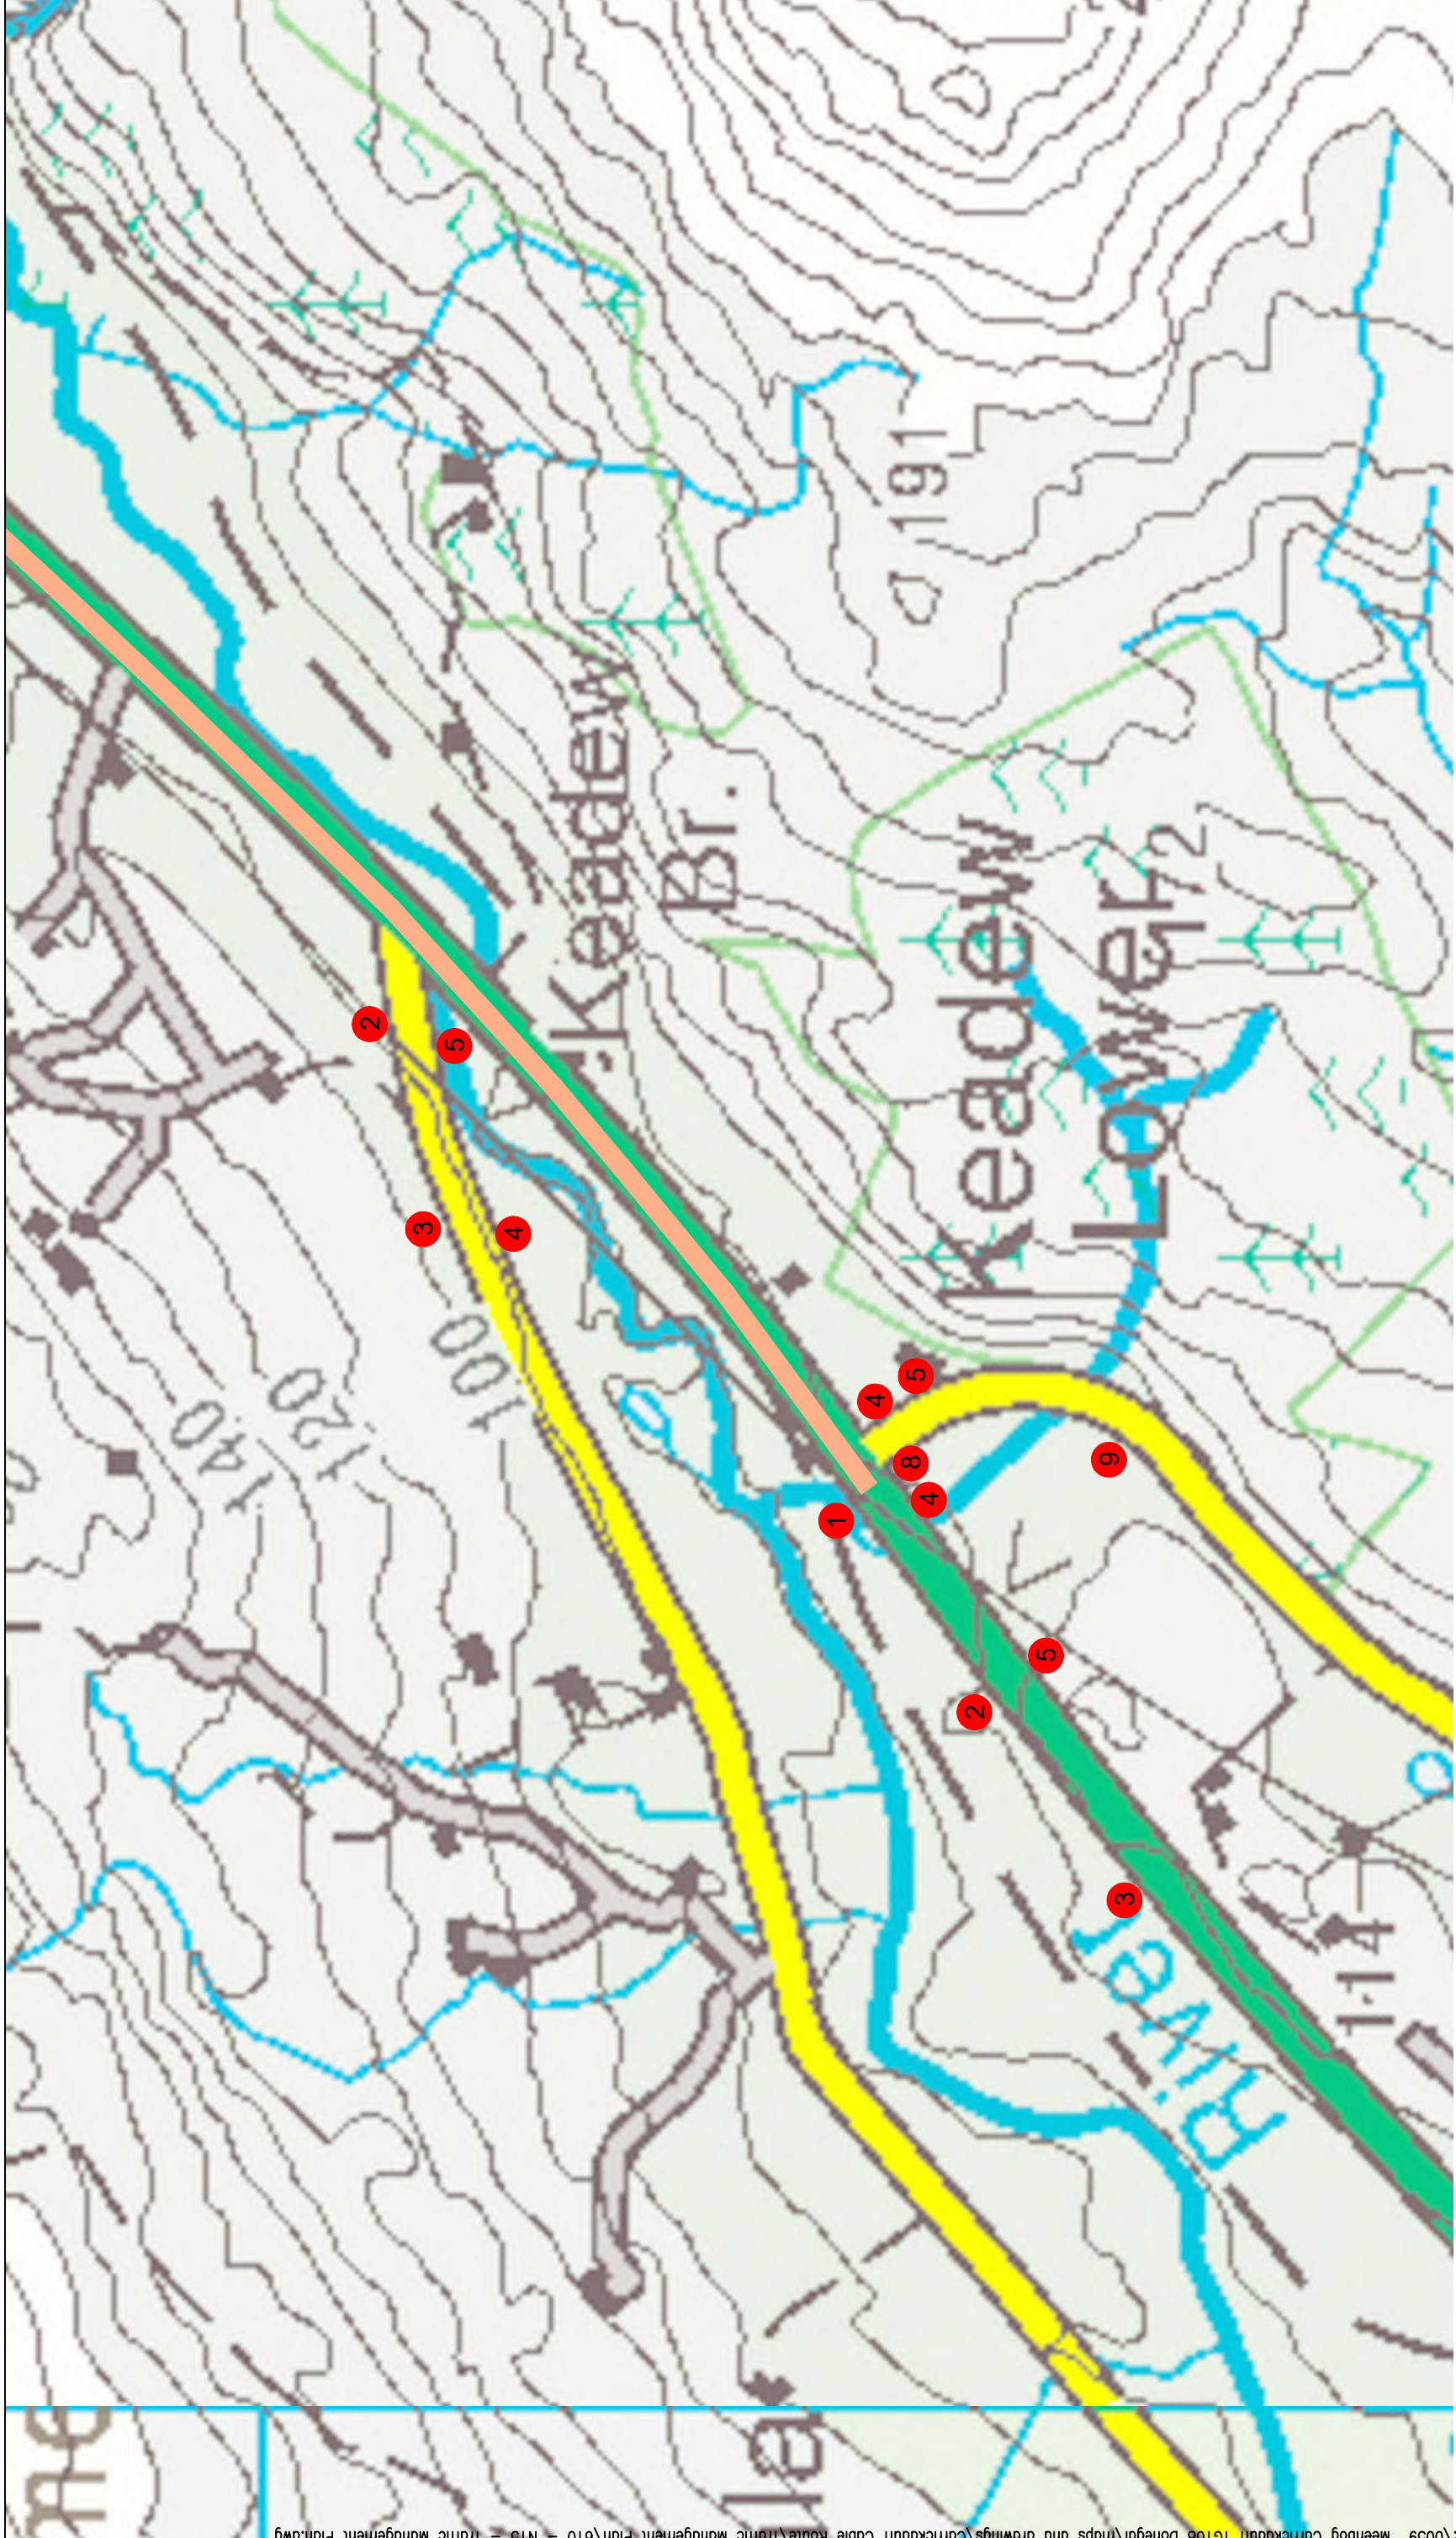

Project Title: Meenbog WF Underground Cable	
Drawing Title: Traffic Calming Measures - N15 Sheet 3 of 4 Locations 3 & 4 - Layout	
Date: 11.01.19	Prepared by: T.Scannlan
Scale: 1:5000@A3	Rev: 000
DRG No. 611-3	Job Ref. 0059

LEGEND:

5748m EXTENT OF WORKS

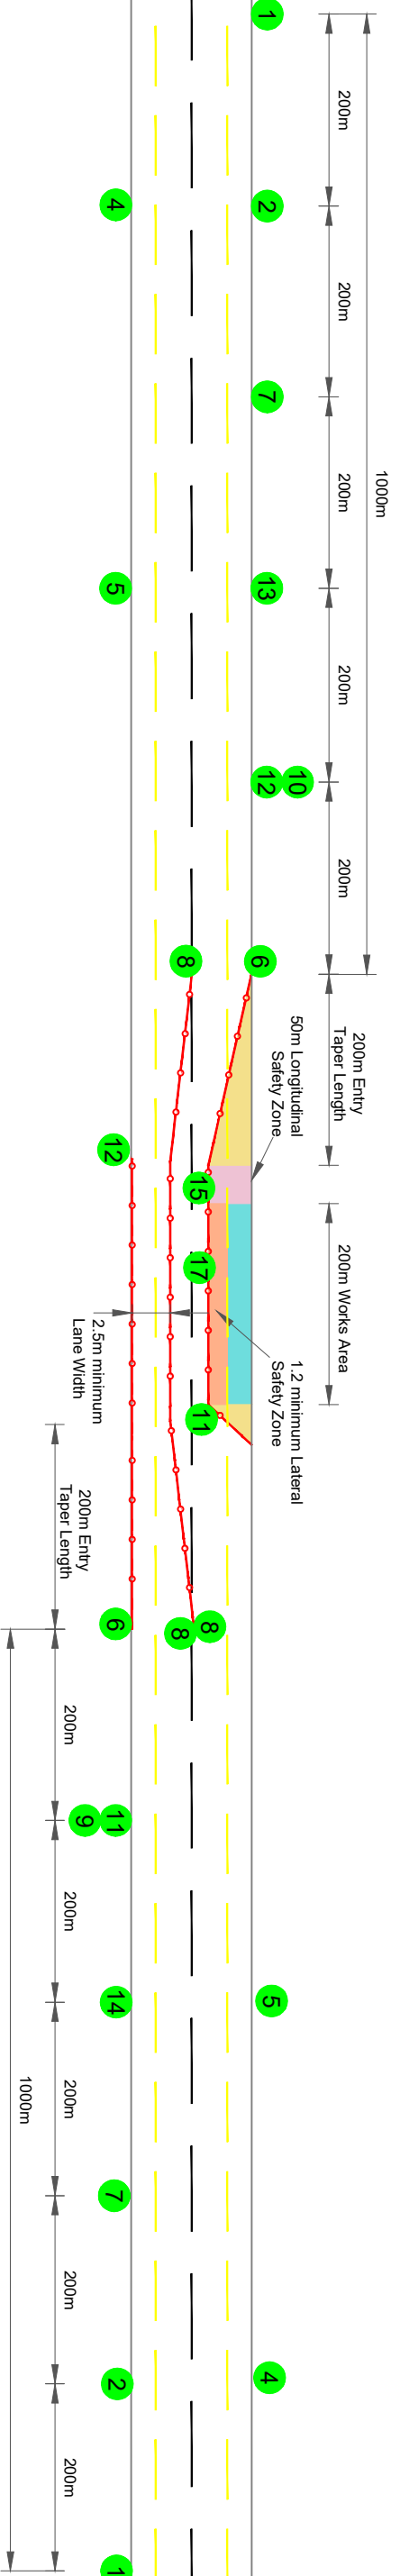

LEGEND:

- | | | | | | | | | | |
|---|--|------------|--|---|--|----|--|----|--|
| 1 | | 4 | | 7 | | 10 | | 13 | |
| 2 | | 5 | | 8 | | 11 | | 14 | |
| 3 | | 6 | | 9 | | 12 | | 15 | |
| | | Críoch END | | | | | | | |
| | | | | | | | | | |
| | | | | | | | | | |
| | | | | | | | | | |

CONING AT 12M MAXIMUM SPACING



Project Title: Meenbog WF Underground Cable	
Drawing Title: Section 4 - N15 Sheet 4 of 4 Location 5 - Works Area Layout	Prepared by: T. Scallan
Date: 11.01.19	Rev: 000
Scale: 1:5000@A3	Job Ref: 0059
