

# METROLINK

Integrated Transport. Integrated Life.



Oral Hearing  
AZ1 O'Scanails  
21 February 2024

# METROLINK

---



AZ1 O'Scanail's

## Outline Phasing of Works

Works adjacent to O'Scanail Veterinary Hospital

KEY ACTIVITES	Year 1	Year 2	Year 3	Year 4	Year 5	Year 6	Year 7	Year 8	Year 9
Notice to Treat	■								
Initial Works		■							
<b>Phase 1: Main Works</b>									
Structure: C&C 12 - CH 4491 to 4518			■						
PH1: Utility Diversion, Accesses & Reinstall			■						
<b>Phase 2: Main Works</b>									
Structure: Retained Cut - CH 4442 to 4491				■					
Structure: Retained Cut - CH 4518 to 4548				■					
PH2: Utility Diversion, Accesses & Reinstall				■					
<b>Phase 3: Main Works</b>									
Road Closure R125 - Structure: C&C 11 - CH4277 to 4442					■				
PH3: Utility Diversion, Accesses & Reinstall						■			
<b>Other Concurrent Works</b>									
<b>Transition into Fostertown Station</b>									
Structure: Retained Cut - CH 4548 to 4666			■						
Structure: C&C 13 - CH 4666 to 4736			■						
Fostertown Station: CH 4736 to 4831		■							
<b>BusConnects Scenario</b>									
Works at Pinnock Hill Junction (Except R125 Arm)				■					
R125 Arm modifications						■			

### Assumptions:

- The phasing of the works programmes includes the completion of either MetroLink alone or the combine MetroLink/BusConnect works as detailed.
- Based on current working assumptions of MetroLink commencing before BusConnects, the BusConnects works will only complete on the opening of the closed arm of the R125.







# Pinnock Hill Junction

## Outline Construction Phases: O'Scanaill Veterinary Hospital (Metrolink before BusConnects)

### Initial Works:

1. Current points of Access/Egress to O'Scanaill's from R132 are maintained.
2. Site clearance for Main Works:
  - Site Clearance within temporary hoarded site area.
  - Site testing, investigations and utility protection/diversions.
3. Access/Egress Works – R132:
  - Site Clearance within temporary hoarded site area.
  - Site testing, investigations and utility protection/diversions.
  - Create alternative access and egress provision from R132 and R125.
  - Temporary landscape and hoarding along new alignment of revised access/egress.
4. Onsite modifications – O'Scanaill's:
  - Access required to carry out clearance to hedgerows and installation of paving maintaining access for O'Scanaill as works progress.

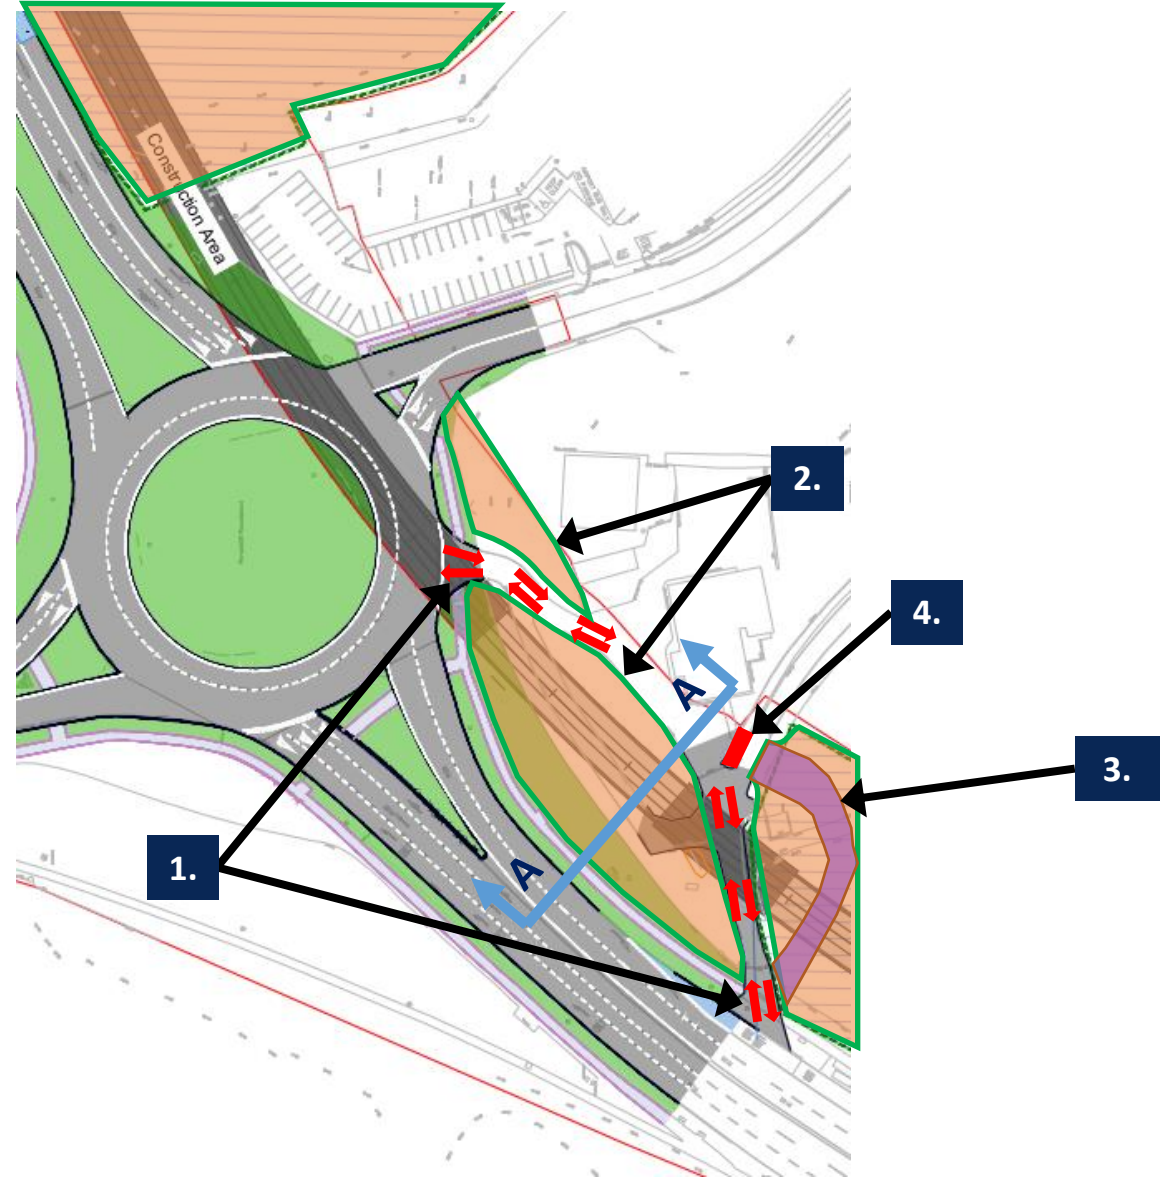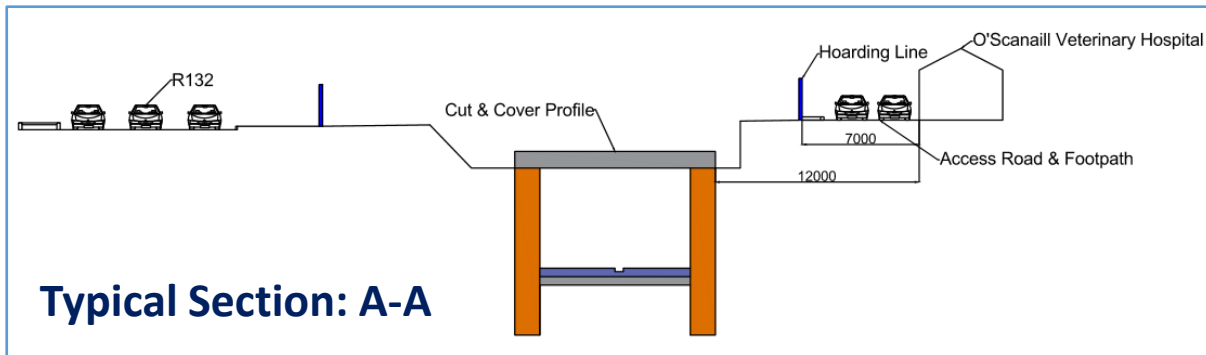


# Pinnock Hill Junction

## Outline Construction Phases: O'Scanail Veterinary Hospital (Metrolink before BusConnects)

### Main Works Phase 1:

1. **Access/Egress Works – R132:**
  - Maintain existing access/egress from R132 roundabout.
  - Open new access/egress from R132.
2. **Main Works – Cut and Cover:**
  - Site clearance and construction sites contained within hoarded fencing.
  - Site testing, investigations, utility protection/diversions.
  - Construct Cut and Cover structure.
  - Reinstate with utility diversions and reinstate access/egress road from R132, including landscaping and site hoarding.
3. **Other Main Works:**
  - Utility protection/diversions contained within hoarded fencing.
  - Construct open cut structures.
4. **Proposed MetroLink Site accesses.**

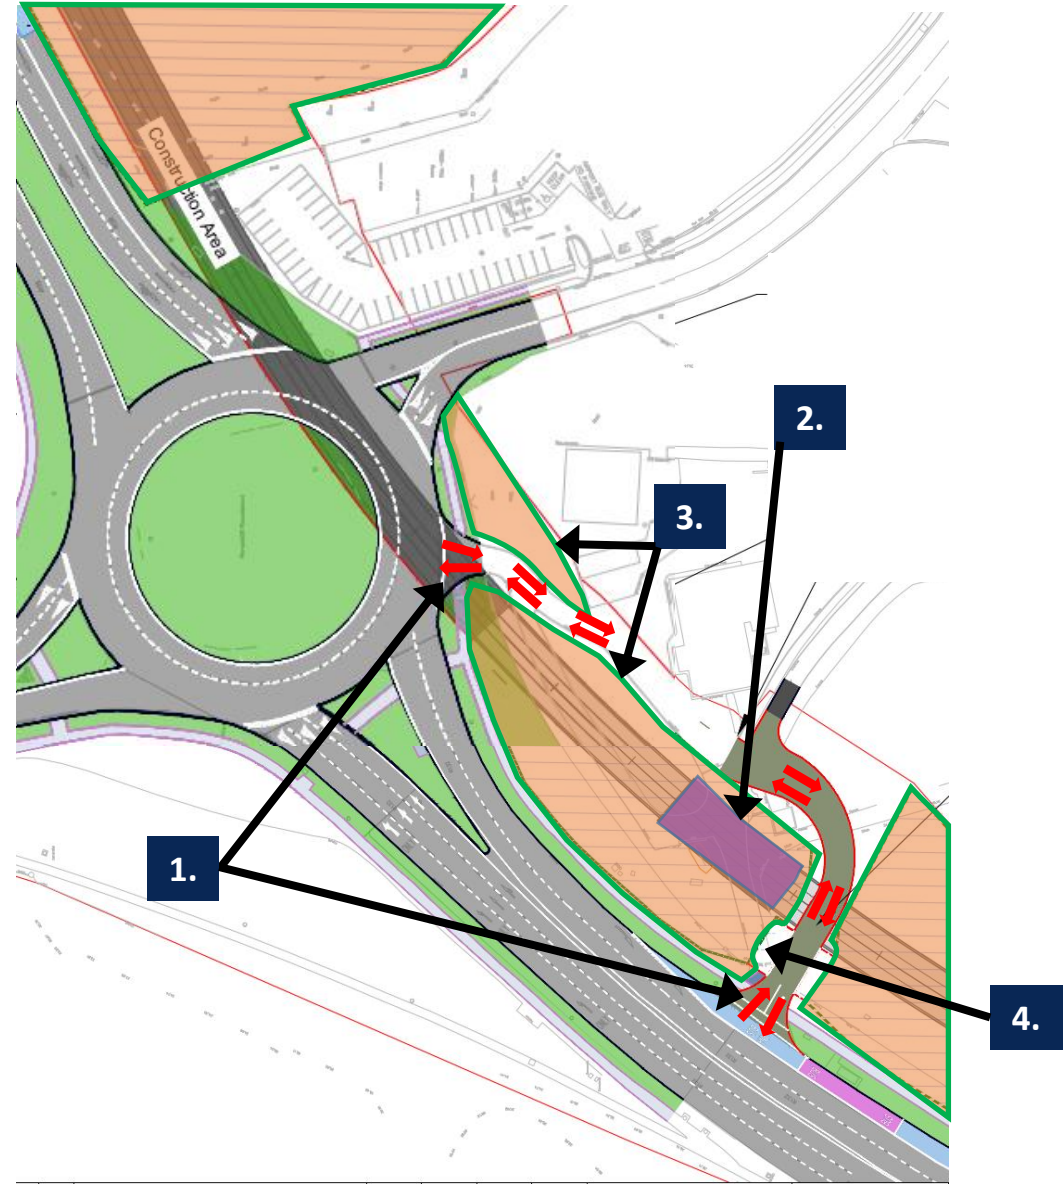



# Pinnock Hill Junction

## Outline Construction Phases: O'Scanail Veterinary Hospital (Metrolink before BusConnects)

### Main Works Phase 2:

#### 1. Access/Egress - R132:

- Maintain access/egress from R132 Roundabout and open reinstated access/egress from R132.
- Construction sites 2 and 4 contained within hoarded fencing.


#### 2. Main Works – Open Cut

- Complete final utility protection/diversions.
- Complete Construct Open Cut structure.
- Reinstall and commence landscaping.

#### 3. Proposed MetroLink Site accesses.

#### 4. Access/Egress Works – R125:

- Create alternative access and egress provision from R125.
- Landscape along new boundary for O'Scanails.
- Install site boundary/hoarding along alignment of MetroLink.

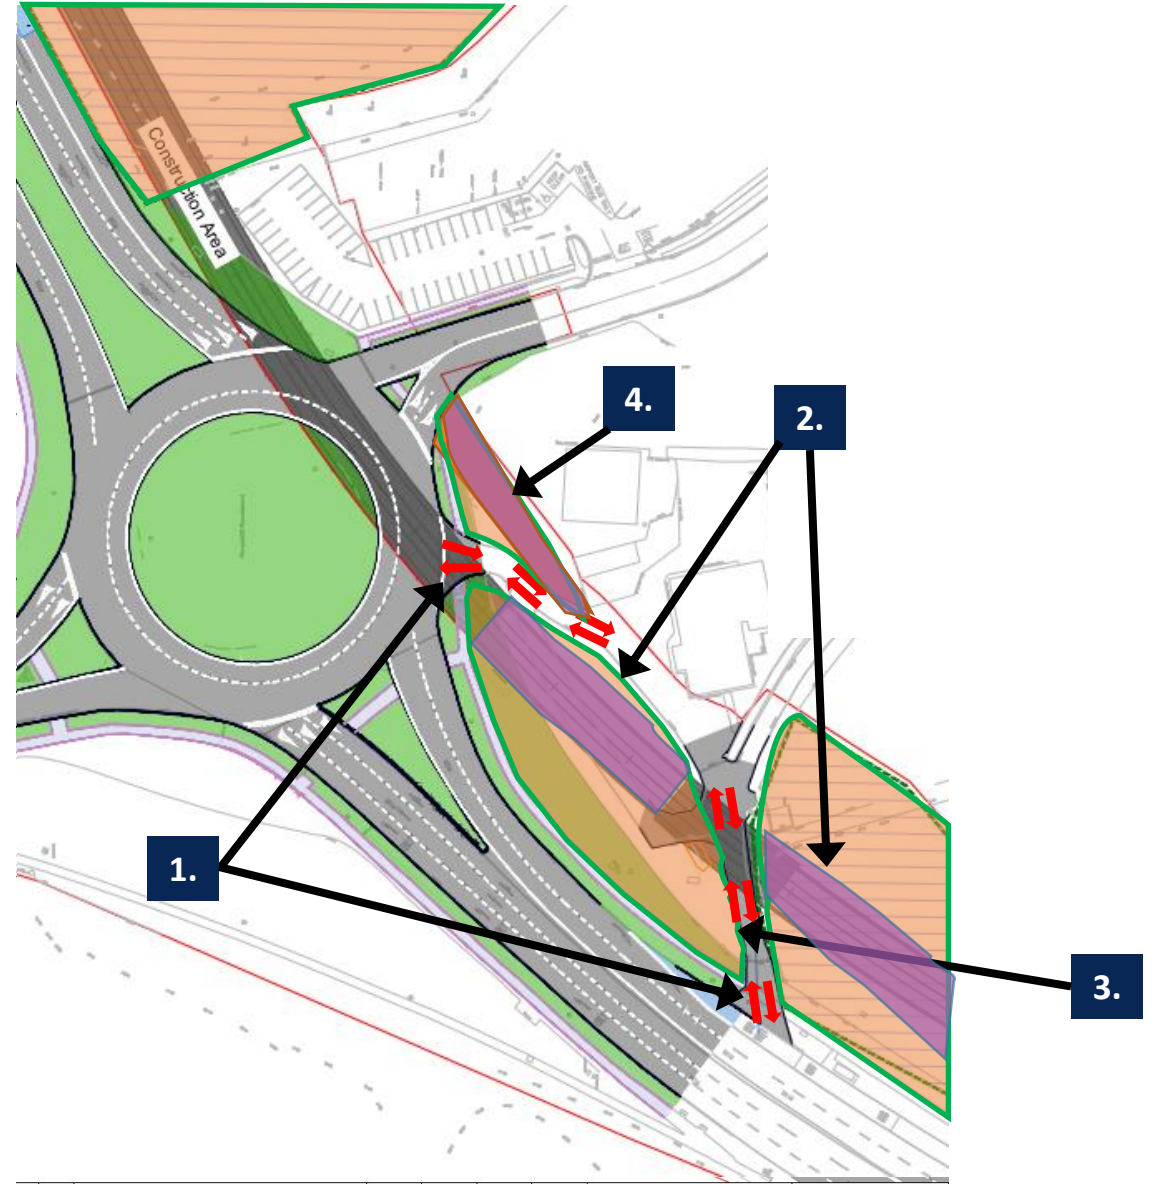


# Pinnock Hill Junction

Outline Construction Phases: O'Scanail Veterinary Hospital (Metrolink before BusConnects)

## Main Works Phase 3: R125 Closed at Pinnock Hill – Cut & Cover Crossing

1. **Access/Egress Works – R125 & R132:**
  - Open and maintain access/egress from R125 and the maintain R132 access.
2. **Main Works – Completed and Reinstated**
  - Complete, reinstated and landscape.
  - Construction Hoarding removed.
3. **Main Works – Cut and Cover under R125 (Continued):**
  - Works within hoarded areas.
  - Site testing, investigations, utility protection/diversions.
  - Construct Cut and Cover structure.
  - Reinststate with utility reinstated and reopen R125.
  - Complete reinstatement of access/egress from R132 roundabout.
  - Complete landscape to R125 and surroundings.

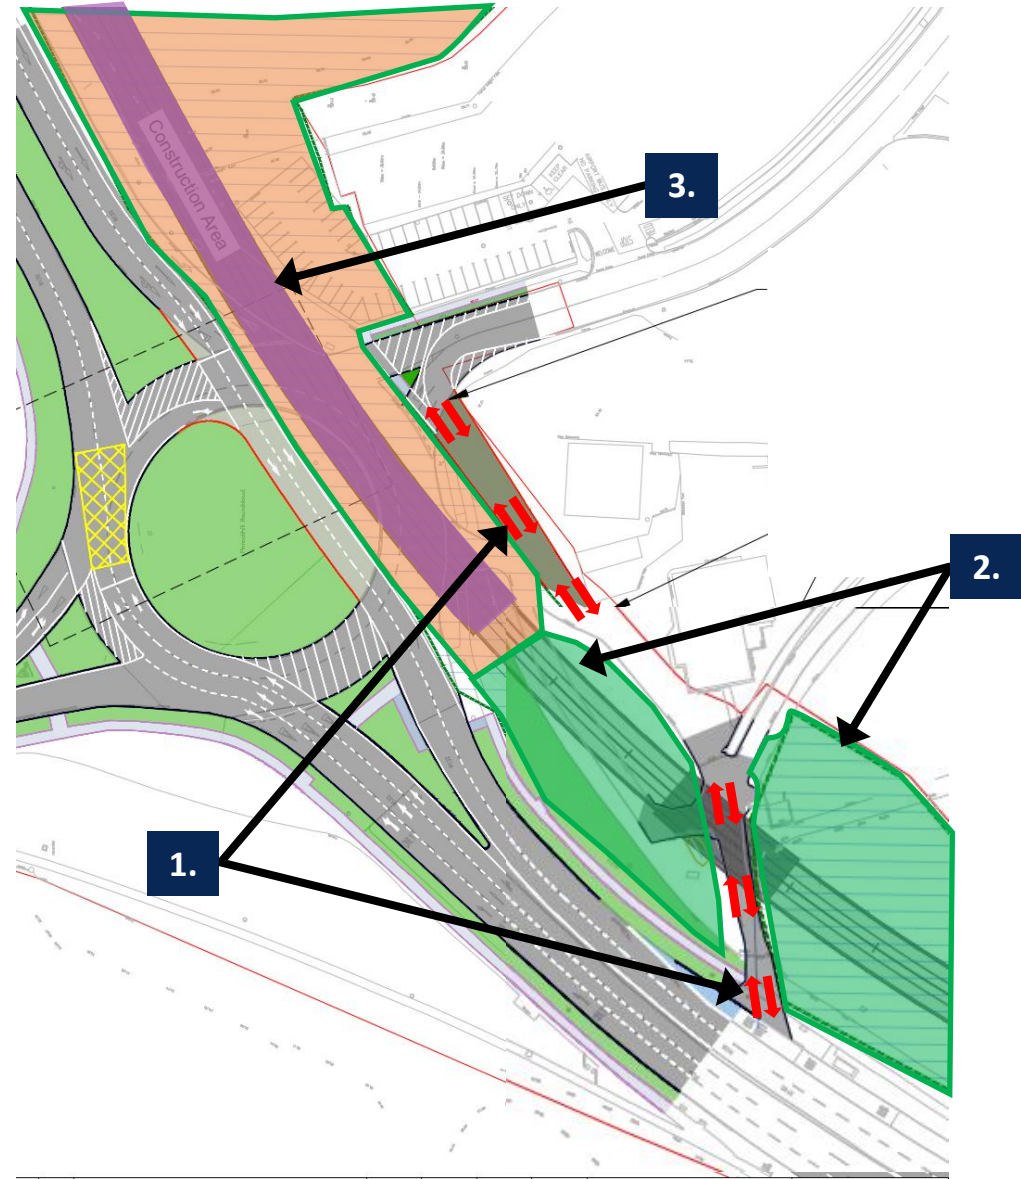




# Pinnock Hill Junction


## Outline Construction Phases: O'Scanail Veterinary Hospital (Metrolink before BusConnects)

### Completion:

1. **Access/Egress R132:**
  - Open the reinstated access/egress from R132.
2. **Landscape – Completed and Reinstated**
  - Remove access/egress from R125, reinstated and landscape.
  - Construction Hoarding removed.
3. **Access/Egress to R132:**
  - Reinstale existing access/egress from R132.

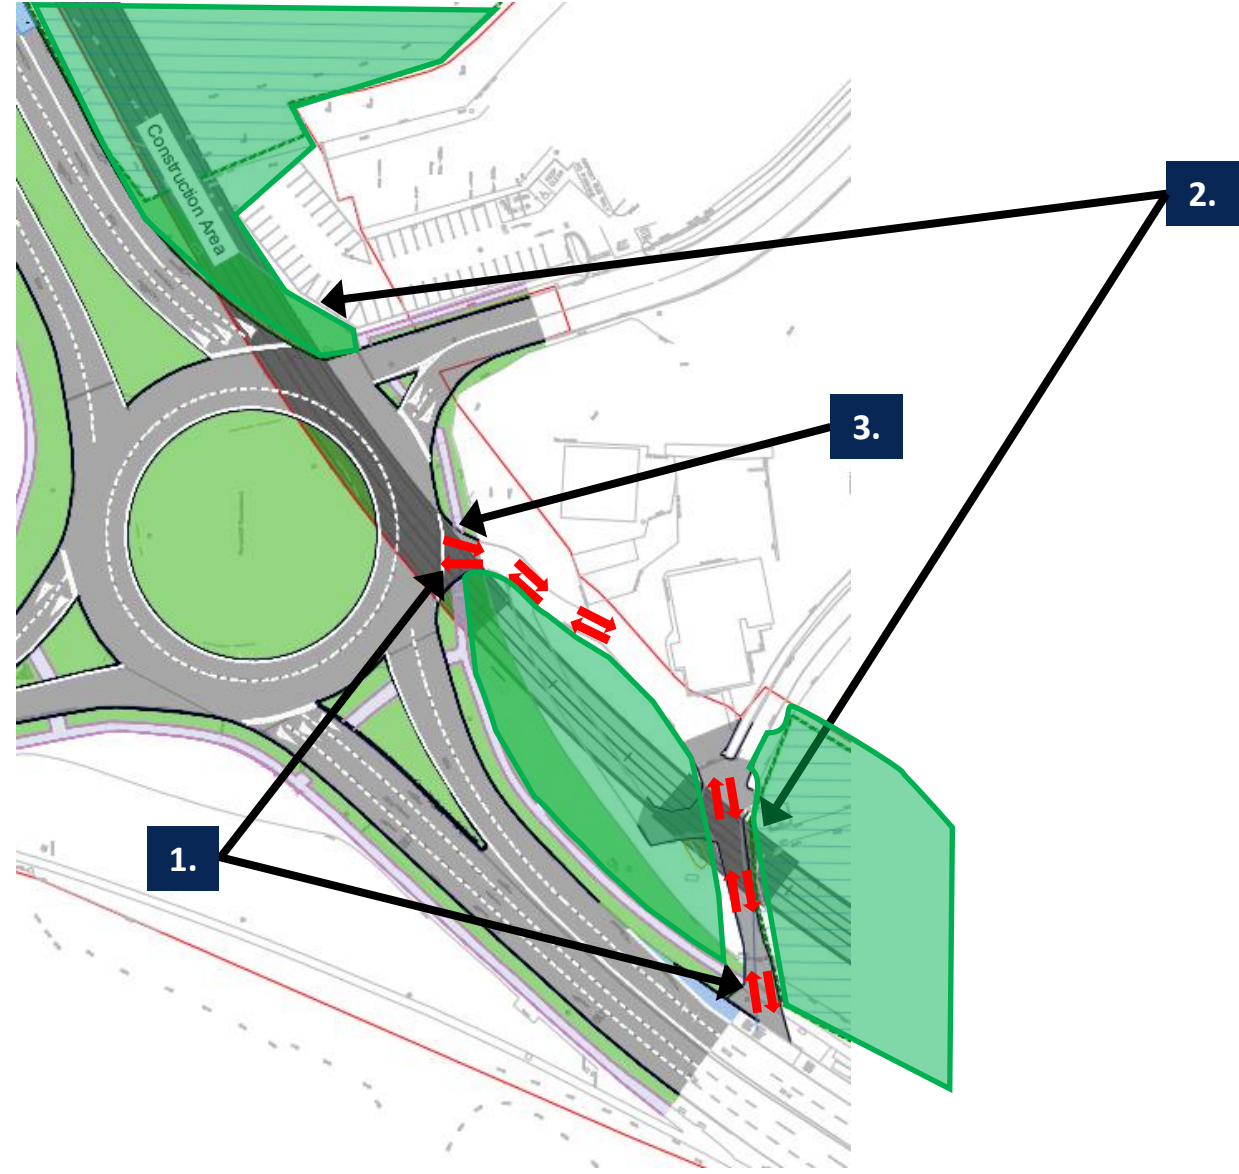

## With BusConnects Design Pinnock Hill Junction

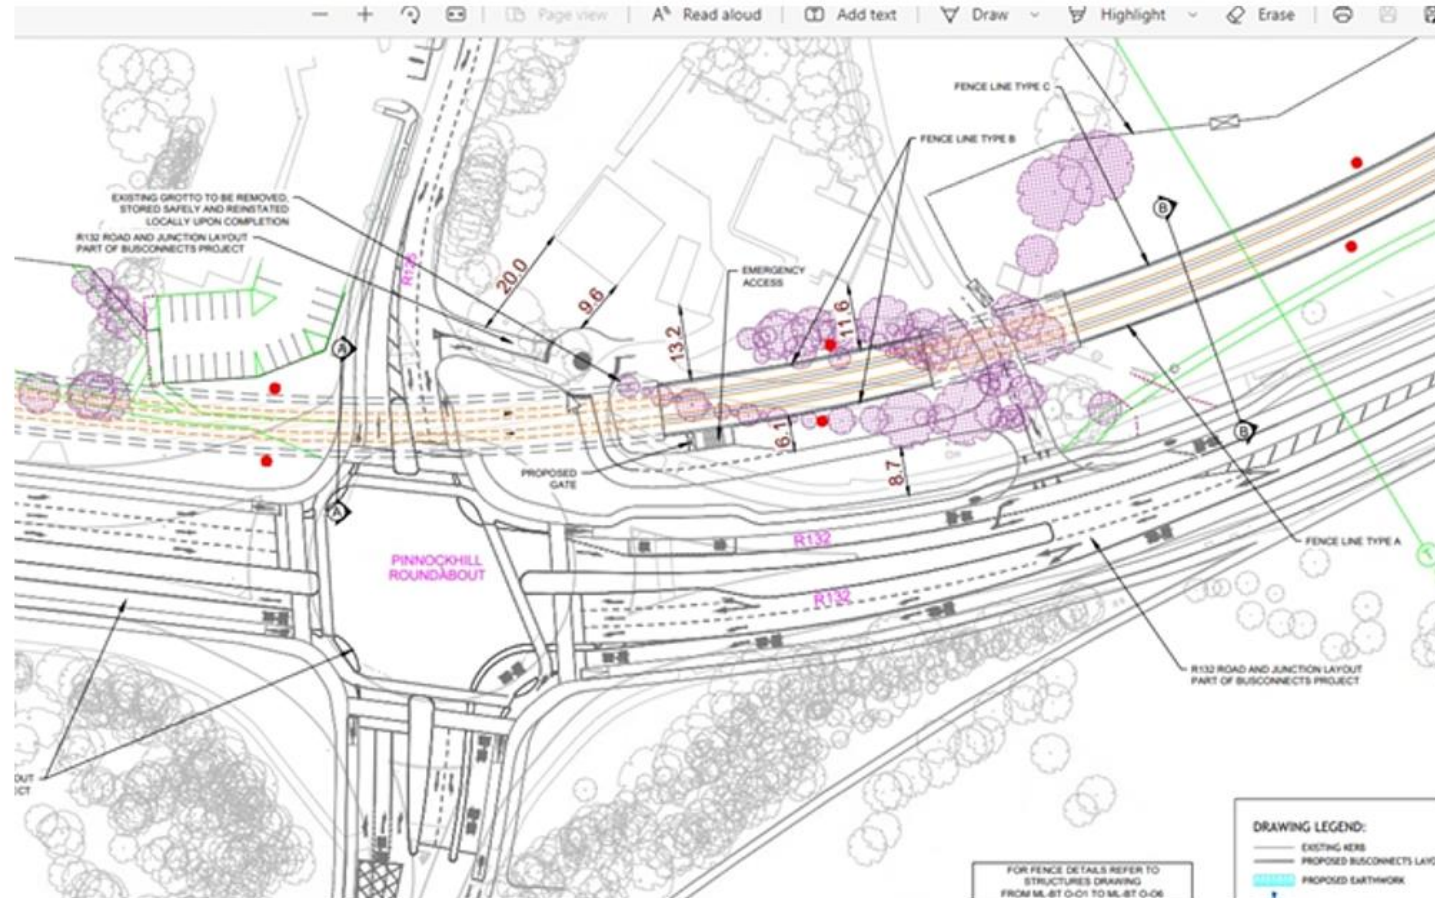


# Pinnock Hill Junction

## Outline Construction Phases: O'Scanail Veterinary Hospital (Metrolink with BusConnects)

### Initial Works:

1. **Current points of Access/Egress to O'Scanail's from R132 are maintained.**
2. **Site clearance for Main Works:**
  - Site Clearance within temporary hoarded site area.
  - Site testing, investigations and utility protection/diversions.
3. **Access/Egress Works – R132:**
  - Site Clearance within temporary hoarded site area.
  - Site testing, investigations and utility protection/diversions.
  - Create alternative access and egress provision from R132 and R125.
  - Temporary landscape and hoarding along new alignment of revised access/egress.
4. **Onsite modifications – O'Scanail's:**
  - Access required to carry out clearance to hedgerows and installation of paving maintaining access for O'Scanail as works progress.

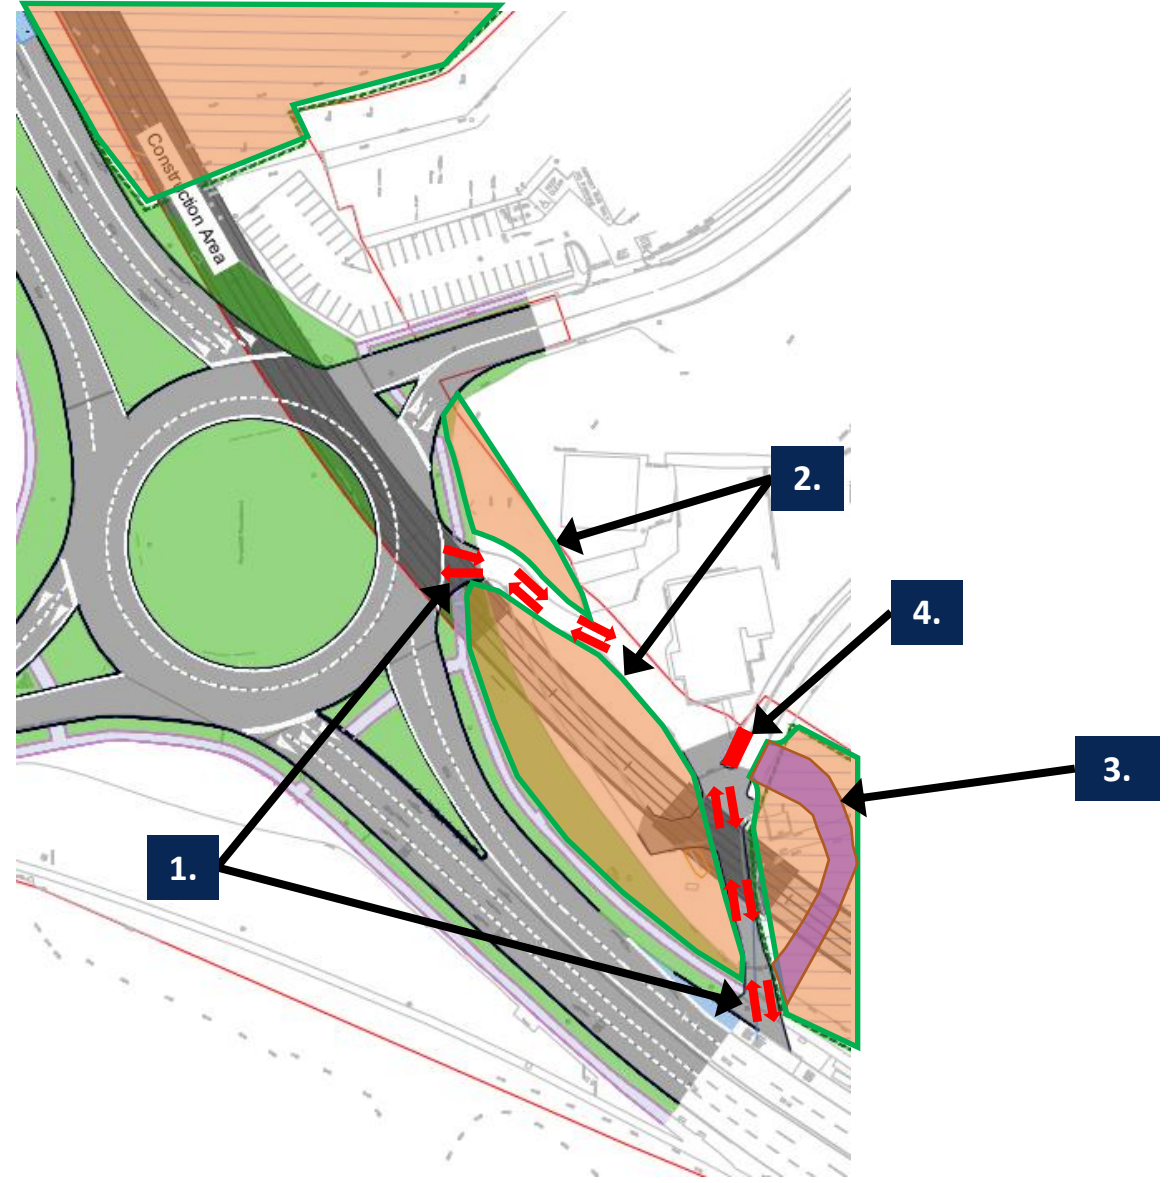




# Pinnock Hill Junction

## Outline Construction Phases: O'Scanail Veterinary Hospital (Metrolink with BusConnects)

### Main Works Phase 1:

1. **Access/Egress Works – R132:**
  - Maintain existing access/egress from R132 roundabout.
  - Open new access/egress from R132.
2. **Main Works – Cut and Cover:**
  - Site clearance and construction sites contained within hoarded fencing.
  - Site testing, investigations, utility protection/diversions.
  - Construct Cut and Cover structure.
  - Reinstate with utility diversions and reinstate access/egress road from R132, including landscaping and site hoarding.
3. **Other Main Works:**
  - Utility protection/diversions contained within hoarded fencing.
  - Construct open cut structures.
4. **Proposed MetroLink Site accesses.**

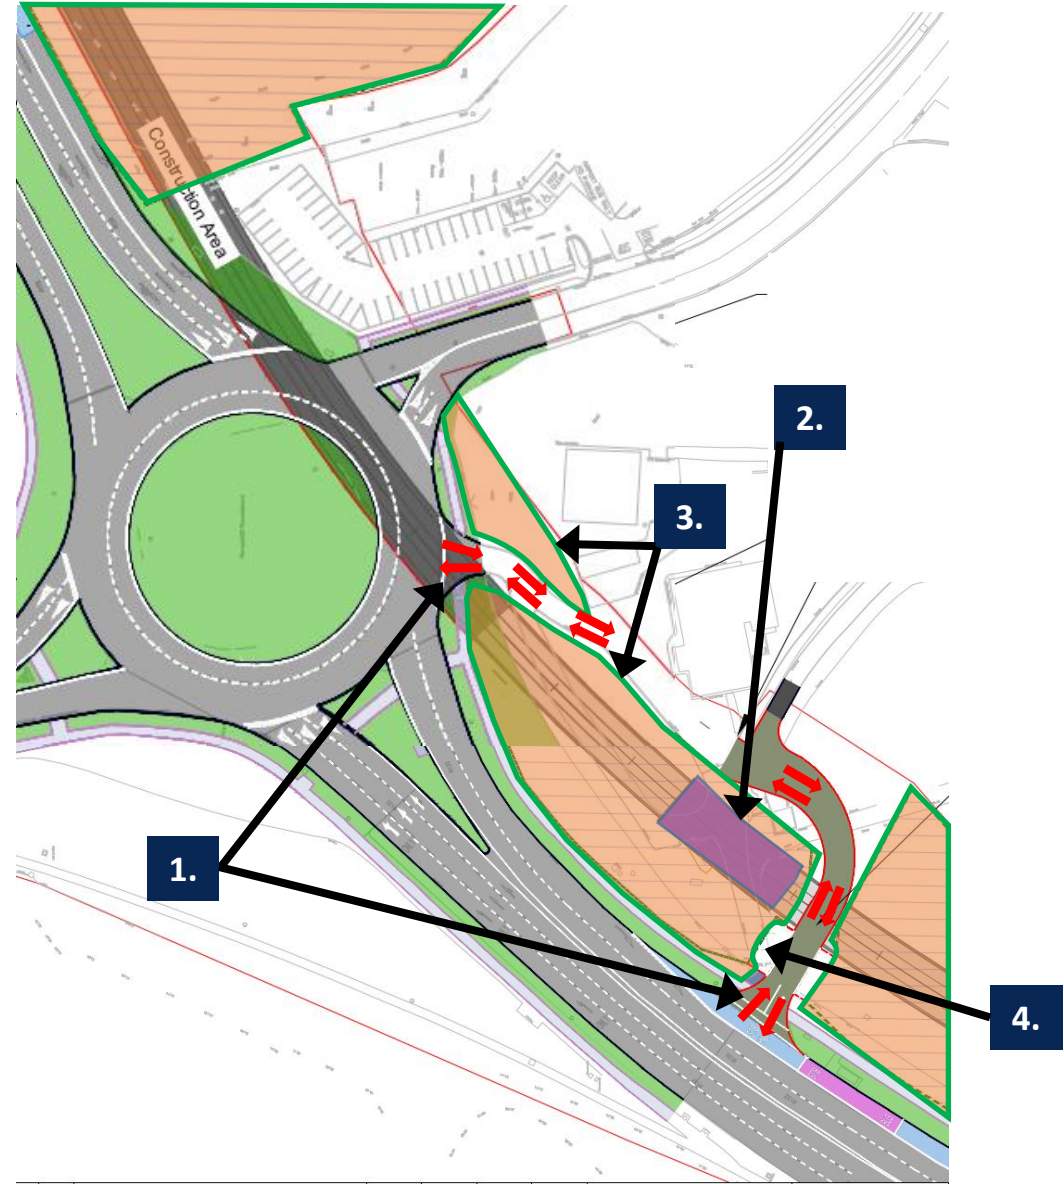

# Pinnock Hill Junction

## Outline Construction Phases: O'Scanail Veterinary Hospital (Metrolink with BusConnects)

### Main Works Phase 2:

#### 1. Access/Egress - R132:

- Maintain access/egress from R132 Roundabout and open reinstated access/egress from R132.
- Construction sites 2 and 4 contained within hoarded fencing.


#### 2. Main Works – Open Cut

- Complete final utility protection/diversions.
- Complete Construct Open Cut structure.
- Reinstall and commence landscaping.

#### 3. Proposed MetroLink Site accesses.

#### 4. Access/Egress Works – R125:

- Create alternative access and egress provision from R125.
- Landscape along new boundary for O'Scanails.
- Install site boundary/hoarding along alignment of MetroLink.

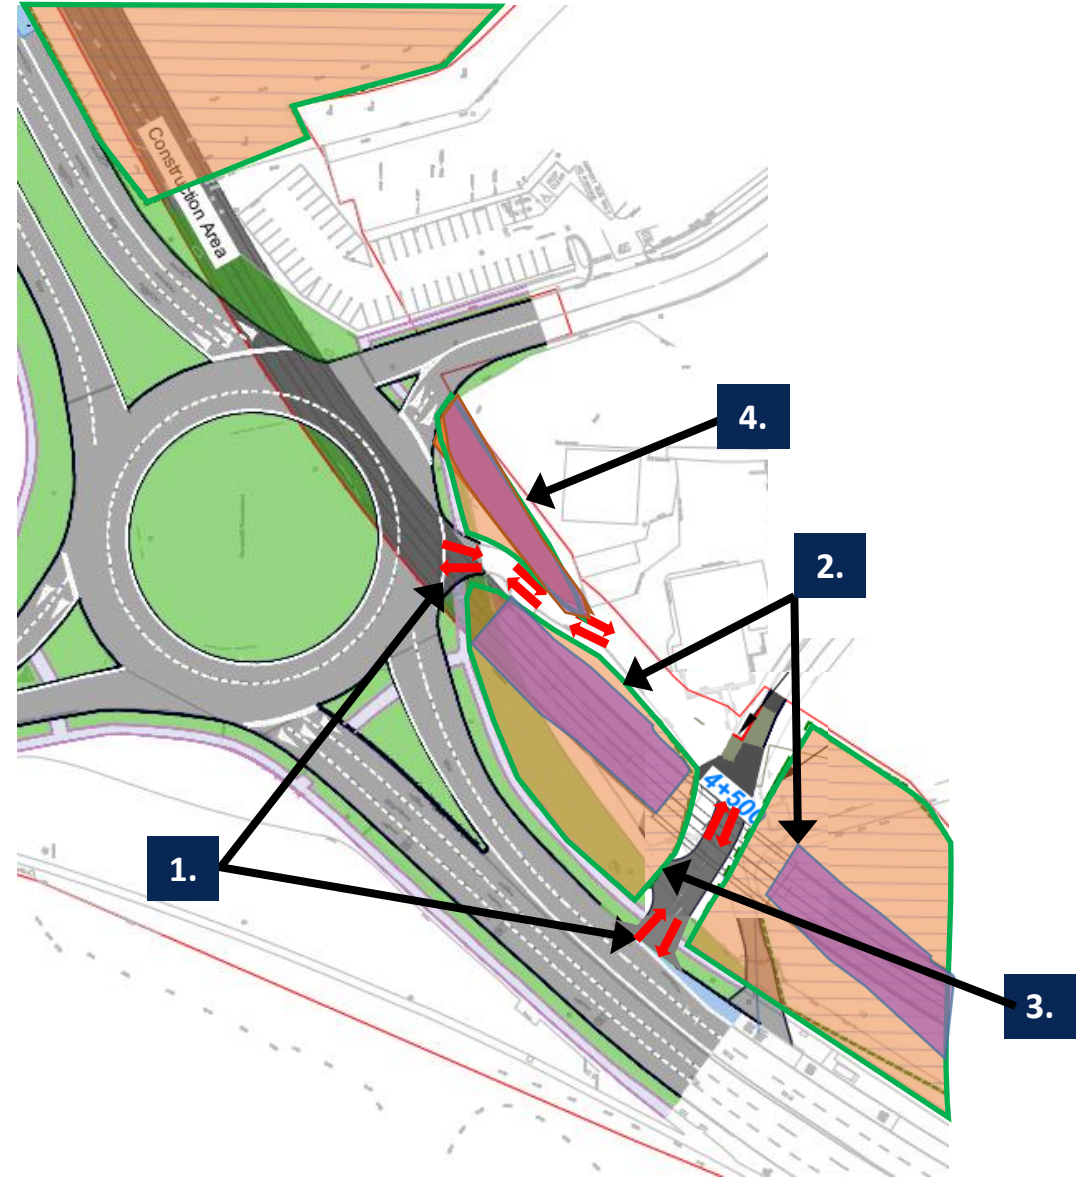


# Pinnock Hill Junction

## Outline Construction Phases: O'Scanail Veterinary Hospital (Metrolink with BusConnects)

### Main Works Phase 3 (BusConnects): R125 Closed at Pinnock Hill – Cut & Cover Crossing

1. **Access/Egress Works – R125 & R132:**
  - Open and maintain access/egress from R125 and R132.
  - Construction site 3 contained within hoarded fencing.
2. **Main Works – Completed and Reinstated**
  - Complete, including BusConnects works, reinstated and landscape.
  - Construction Hoarding removed.
3. **Main Works – Cut and Cover under R125:**
  - Site Clearance within temporary hoarded site area.
  - Site testing, investigations, utility protection/diversions.
  - Construct Cut and Cover structure.
  - Reinstatement with utility reinstated and reopen R125.
  - Complete reinstatement of access/egress from R132.
  - Complete landscape to R125 and surroundings.
  - Other junction modifications BusConnects\*.
4. **Proposed MetroLink Site accesses.**

**Note:** \* Assumes that BusConnects junction modifications will commence on or around the closure of the R125 for MetroLink Works (TBC).

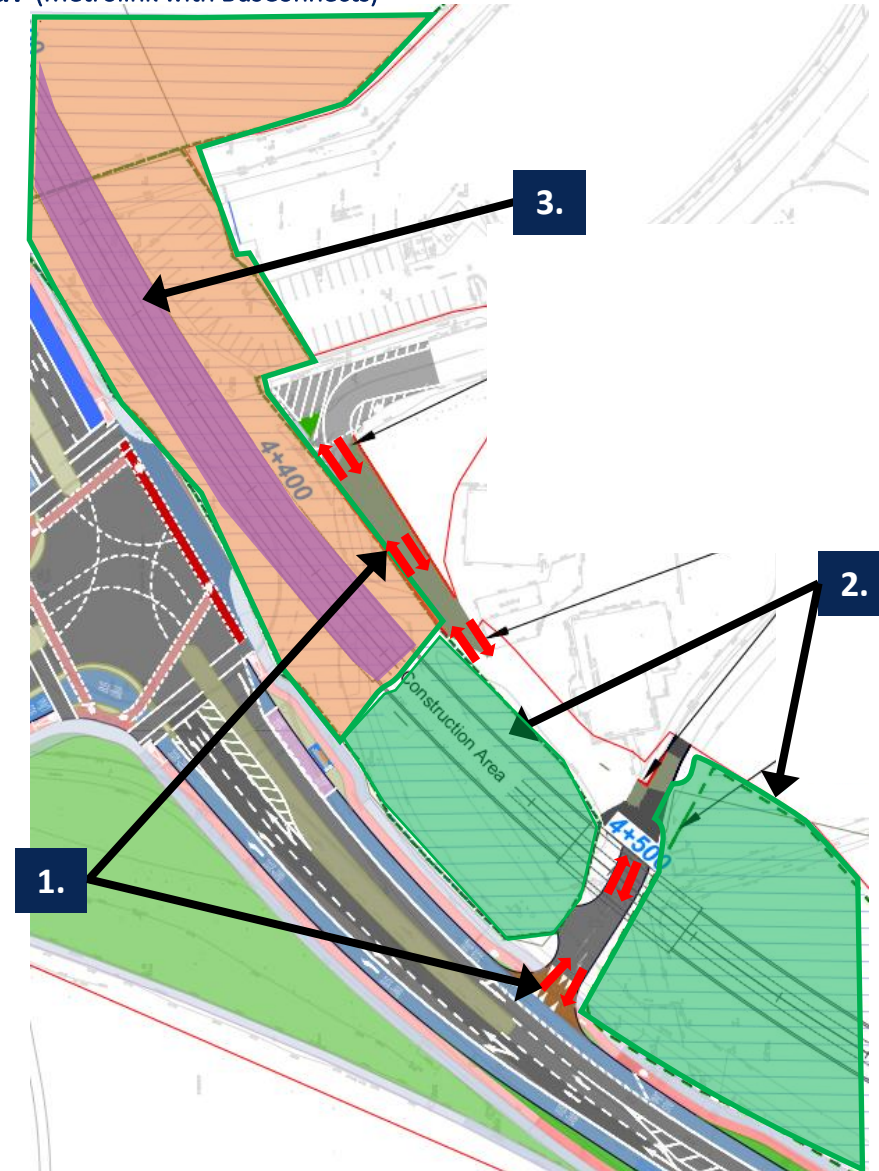




# Pinnock Hill Junction

## Outline Construction Phases: O'Scanail Veterinary Hospital (Metrolink with BusConnects)

### Completion:

1. **Access/Egress R132:**
  - Open the reinstated access/egress from R132 and R125.
2. **Landscape – Completed and Reinstated**
  - Remove access/egress from R125, reinstated and landscape.
  - Construction Hoarding removed.

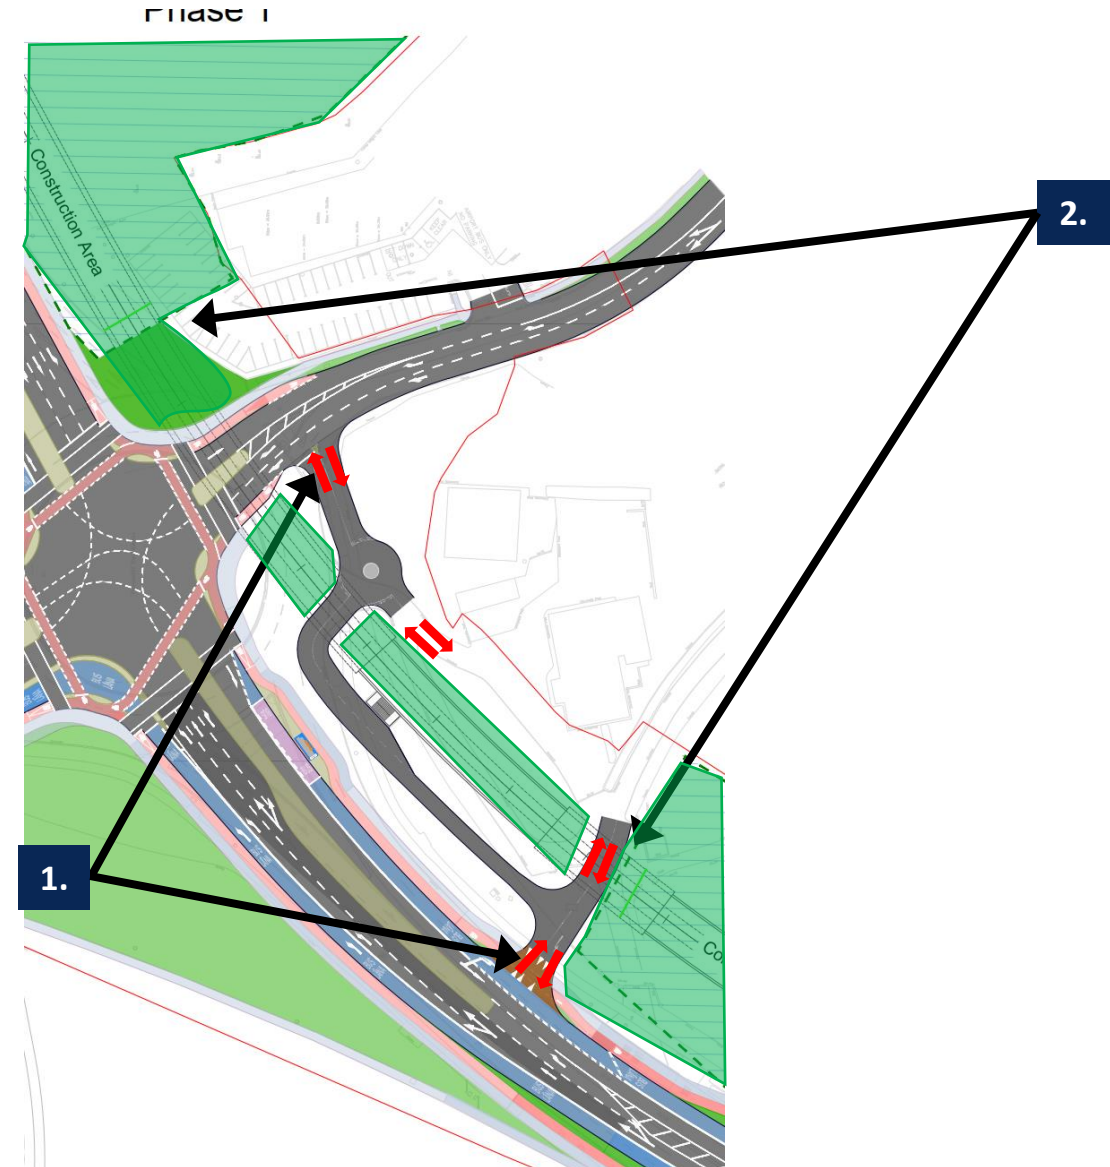



# METROLINK

 [info@metrolink.ie](mailto:info@metrolink.ie)

 [www.metrolink.ie](http://www.metrolink.ie)

 1800 333 777

 @metrolink\_ie
