

Tree Experts in the  
Built Environment



**John Morris Arboricultural Consultancy**

Tree Risk Management

Trees, Planning & Development

Expert Witness

Arboricultural Clerk of Works

Government Support

**Client:** South Dublin County Council  
**Site:** Kishoge Sites 3, 4, 5a & 5b  
Dublin 22

**Date:** 5<sup>th</sup> April 2025  
**Ref:** 24-075-04  
**Version:** 1

## ARBORICULTURAL IMPACT ASSESSMENT & METHOD STATEMENTS



## DOCUMENT CONTROL SHEET

| Originating Author:    | Date:    | Version | Notes:                    |
|------------------------|----------|---------|---------------------------|
| JM                     | 05.04.25 | 1       | Original Document         |
| Reviewed By:           |          |         |                           |
| RC                     | 07.04.25 | 1       | Quality Control           |
| Approved for Issue By: |          |         |                           |
| JM                     | 07.04.25 | 2       | Final Document for Client |

### Prepared by:

#### John Morris Arboricultural Consultancy Ltd

Executive Suites  
Weavers Court  
Belfast  
BT12 5SH



+44 (0) 7830 793 487



info@johnmorristrees.com



www.johnmorristrees.com



### Prepared for:

#### South Dublin County Council

County Hall  
Tallaght  
Dublin 24  
D24 A3XC

## COPYRIGHT ©

The copyright of this document remains with John Morris Arboricultural Consultancy Ltd. Its contents must not be copied or reproduced in whole or in part for any purpose without the written consent of John Morris Arboricultural Consultancy Ltd.

## Purpose of Document

This report provides an assessment of trees on land at Kishoge Sites 3, 4, 5a & 5b in Dublin 22, in accordance with BS5837:2012 *Trees in relation to design, demolition and construction – Recommendations*.

It provides an overview of the constraints posed by trees on or within influencing distance of the site, and assesses the impacts of the development proposal to those trees.

It includes:

- A **Tree Schedule** that provides information for each tree;
- A **Tree Constraints Plan** that illustrates the location and constraints posed by trees;
- An **Arboricultural Impact Assessment** that considers the impacts of the development proposal to those trees, including proposals for arboricultural mitigation and improvements;
- An **Arboricultural Method Statement** that outlines how retained trees will be protected during construction, and;
- A **Tree Impact & Protection Plan** that illustrates the impact of the proposal upon trees and protection measures that should be adopted during construction.

The information contained within this report is provided to allow South Dublin County Council to assess tree related issues associated with the development proposal.

## Executive Summary

The proposed development is for new residential schemes and all associated works at Sites 3, 4, 5a & 5b in Kishoge, Dublin 22.

Sites 3, 5a & 5b comprise derelict land and fields with self-sown naturally regenerating scrub and pioneer tree species such as ash and willow, which are growing from rubble, old hard standings and rank grass across the sites. Site 4 includes part of the South Dublin County Council Parks Depot and lands to the west including a woodland, old tree nursery and fields adjoining construction sites.

The proposed works will require removal of all trees and hedgerows within Sites 3, 5a & 5b. It is proposed to retain some trees within the woodland in Site 4 by incorporating them into a gated access wildlife and aquatic habitat in the south east corner of the site.

It is proposed to plant new trees and hedgerows across each of the sites within the new built environment and areas of public open space in streets, car parking areas, gardens and parks. The aim of this new planting should be to increase species diversity and canopy cover in the local landscape to provide a future net gain in canopy cover and improvement on the pre-development baseline.

The following tree protection measures are required on site:

- Tree Protection Fencing
- Construction Exclusion Zones

## CONTENTS

|  |           |
|--|-----------|
| <b>1. INTRODUCTION .....</b>   | <b>6</b>  |
| INSTRUCTION .....  | 6         |
| SCOPE .....  | 6         |
| SITE.....  | 6         |
| <b>2. TREE SURVEY .....</b>  | <b>6</b>  |
| SITE VISIT .....   | 6         |
| DESCRIPTION OF TREES.....  | 7         |
| SITE 3 .....   | 7         |
| SITE 4 .....   | 7         |
| SITE 5A & 5B.....  | 7         |
| <b>3. ARBORICULTURAL PRINCIPLES .....</b>  | <b>9</b>  |
| TREES AND DEVELOPMENT .....  | 9         |
| BELOW GROUND CONSTRAINTS .....   | 9         |
| IMPACTS OF CONSTRUCTION & DEVELOPMENT .....                                      | 9         |
| ROOT PROTECTION AREAS .....  | 9         |
| ABOVE GROUND CONSTRAINTS .....   | 10        |
| <b>4. PLANNING POLICY, STATUTORY CONSIDERATIONS &amp; TREE LEGISLATION .....</b> | <b>10</b> |
| PLANNING POLICY .....  | 10        |
| SOUTH DUBLIN COUNTY DEVELOPMENT PLAN (2022-2028).....                            | 10        |
| CLONBURRIS STRATEGIC DEVELOPMENT ZONE PLANNING SCHEME (2019).....                | 12        |
| TREE PRESERVATION ORDERS & CONSERVATION AREAS .....                              | 13        |
| FELLING LICENCES.....  | 14        |
| WILDLIFE .....   | 14        |
| <b>5. ARBORICULTURAL IMPACT ASSESSMENT .....</b>                                 | <b>15</b> |
| DEVELOPMENT PROPOSAL .....   | 15        |
| TREE REMOVALS & PRUNING .....  | 15        |
| THE IMPACT .....   | 15        |
| MITIGATION & IMPROVEMENTS.....   | 16        |
| <b>6. ARBORICULTURAL METHOD STATEMENTS .....</b>                                 | <b>16</b> |
| PURPOSE.....   | 16        |
| PRE COMMENCEMENT MEETING .....   | 16        |
| KEY RESPONSIBILITIES.....  | 17        |
| TREE PROTECTIVE FENCING .....  | 17        |
| SITE COMPOUNDS & FACILITIES .....  | 17        |
| SITE CRANES, PILING RIGS AND MACHINERY .....                                     | 17        |
| POLLUTION CONTROL.....   | 18        |
| TEMPORARY GROUND PROTECTION.....   | 18        |
| EXCAVATIONS AND REMOVAL OF EXISTING SURFACES.....                                | 18        |

|   |           |
|---|-----------|
| UPGRADING EXISTING SURFACES.....                                    | 19        |
| INSTALLATION OF SERVICES .....                                      | 19        |
| INSTALLATION OF RAILINGS, LIGHTING COLUMNS OR STREET FURNITURE..... | 20        |
| SOFT LANDSCAPING .....  | 20        |
| <b>7. ABOUT THE AUTHOR &amp; LIMITATIONS.....</b>                   | <b>20</b> |
| AUTHORS QUALIFICATIONS & EXPERIENCE.....                            | 20        |
| LIMITATIONS.....  | 21        |

## APPENDICIES

|  |    |
|--|----|
| APPENDIX 1: TREE SURVEY CRITERIA (BS5837:2012) .....       | 22 |
| BS5837:2012 ASSESSMENT CRITERIA & CASCADE CHART .....      | 23 |
| APPENDIX 2 – CALCULATION OF THE ROOT PROTECTION AREA ..... | 24 |
| APPENDIX 3 – EXAMPLE OF TREE PROTECTIVE FENCING.....       | 26 |
| APPENDIX 4 – EXAMPLE OF TREE PROTECTIVE SIGNS.....         | 28 |
| APPENDIX 5 – EXAMPLE OF TEMPORARY GROUND PROTECTION .....  | 29 |

## ATTACHMENTS

| DOCUMENT TITLE                | DOCUMENT REFERENCE |
|-------------------------------|--------------------|
| TREE SCHEDULE                 | 24-075-01          |
| TREE CONSTRAINTS PLAN         | 24-075-02          |
| TREE IMPACT & PROTECTION PLAN | 24-075-03          |



## 1. INTRODUCTION

### Instruction


- 1.1. Instruction was received from South Dublin County Council on 8<sup>th</sup> March 2024 to undertake a tree survey and prepare an arboricultural report to in connection with a planning application for proposed works at Kishoge Sites 3, 4, 5a & 5b in Dublin 22.

### Scope

- 1.2. The survey has been carried out in accordance with BS5837:2012 *Trees in relation to design, demolition and construction – Recommendations*.
- 1.3. The information collected during the survey has been used to prepare a report in connection with a planning application.

### Site

- 1.4. The sites include 3, 4, 5a & 5b at Kishoge, Dublin 22 (Figure 1).

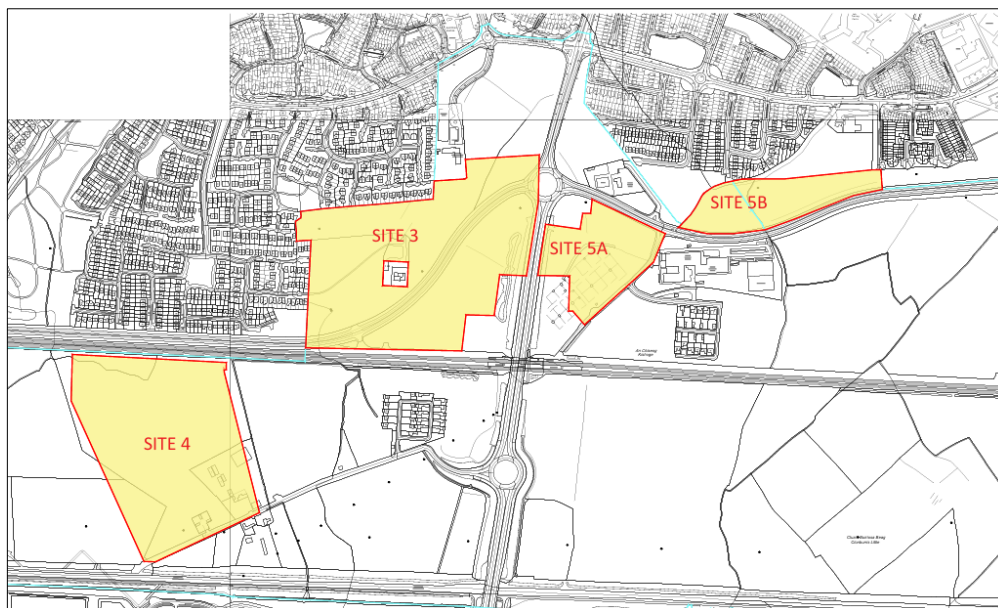

**Figure 1.** Sites 3, 4, 5a & 5b at Kishoge, Dublin 22.

## 2. TREE SURVEY

### Site Visit

- 2.1. The tree survey was undertaken between Monday 8<sup>th</sup> and Friday 12<sup>th</sup> April 2024.
- 2.2. Details of the survey methodology and assessment criteria can be found in Appendix 1.
- 2.3. The survey data is contained in the Tree Schedule (Ref: 24-075-01) and illustrated on the Tree Constraints Plan (Ref: 24-075-02) attached to this report.
- 2.4. The tree survey considered all trees that have the potential to be impacted by the proposal including those outside the application area, but within influencing distance.

- 2.5. On the Tree Constraints Plan, The above ground constraints posed by canopy spread are plotted as a continuous line around the tree and shaded in the corresponding BS5837 retention category colour, whilst the below ground constraints posed by the Root Protection Area (RPA) have been plotted as a continuous magenta line with the text RPA inscribed.

#### **Description of Trees**

- 2.6. The trees are spread across four parcels of land, known as Site 3, 4, 5a & 5b.

#### **Site 3**

- 2.7. Site 3 comprises 2 areas of derelict land separated by Adamstown Avenue. There are few trees on these sites apart from sporadic self-sown natural regeneration of ash and hawthorn and two hybrid poplar.

#### **Site 4**

- 2.8. Site 4 comprises the western part of the South Dublin County Council Parks Depot, a single residential dwelling, an area of woodland and fields and an old tree nursery. There are three mature sycamores growing within a grass verge in the Park Depot. To the immediate west of the Parks Depot and residential dwelling beyond a steel palisade fence is a mature line of beech growing from the top of a bank, followed by a row of Monterey cypress further north and dense mixed species woodland extending to the west. The eastern part of the woodland contains staggered rows and sporadic planting of lime, Norway maple, hornbeam and sycamore but becomes less formal with sporadic natural regeneration comprising willows and ash. Within the central area of woodland is a group of larger mature trees including flowering cherry, crack willow, birch, beech, horse chestnut and more poplar. The woodland is enclosed along the southern and western boundary by dense rows of evenly spaced hybrid poplar. The old tree nursery in the northern part of the site comprises rows of sycamore, silver birch, alder, beech, Norway maple, oak, field maple, horse chestnut and alder. A group of dense trees consisting of pioneer species such as ash and willow covers much of the north west corner of the site beyond the tree nursery, with more hybrid poplar extending along the boundary.

#### **Site 5a & 5b**

- 2.9. Site 5a consists of a derelict piece of land with sporadic self-sown natural regenerating ash, hawthorn, elder and willows arising from around old hard standings, concrete and rubble, and a mixed species shelterbelt along the western boundary with the R136 and part of the Thomas Omer Way comprising hawthorn, birch, Scots pine, blackthorn, alder, hazel, ash and willows. Site 5b includes an area of land accessible via a construction site to the immediate north leading from Omer Walk. In the south wester corner of this site are some ash and a mixed species group of hawthorn hazel and willow. There have been extensive ground works around all trees with rubble and earth leading to root suffocation, and all trees within this site are recommended for removal due to decline.



**Figure 2.** Row of hybrid poplar along boundary of Site 4.



**Figure 3.** Edge of tree nursery in northern part of Site 4.



**Figure 4.** Ash with increased ground levels on Site 5b.

2.10. A summary assessment of the tree quality is contained in Table 1.

**Table 1.** Overview assessment of tree quality by BS5837 retention category.

|              | Category A | Category B | Category C | Category U | Total      |
|--------------|------------|------------|------------|------------|------------|
| <b>Trees</b> | 1          | 61         | 464        | 111        | <b>637</b> |

2.11. A summary of the tree population age classification is contained in Table 2.

**Table 2.** Summary of age class.

|              | Young | Semi-mature | Early mature | Mature | Over Mature | Ancient or Veteran | Dead |
|--------------|-------|-------------|--------------|--------|-------------|--------------------|------|
| <b>Trees</b> | 6     | 136         | 441          | 27     | 0           | 0                  | 27   |



### **3. ARBORICULTURAL PRINCIPLES**

#### **Trees and Development**

- 3.1. Trees provide a multitude of economic, environmental and social benefits to individuals and communities including (but not limited) to visual amenity and landscape value, ecosystem services and habitats for local wildlife. Trees can also hold historic and cultural importance by providing links to the past that create a sense of place and belonging.
- 3.2. They are living, self-optimising, mechanical organisms that grow in and react to the environment in which they are located and are capable of being wounded or infected by objects or other organisms that can cause a decline in health or result in death.
- 3.3. Development proposals that will impact trees should consider the value and contribution made by those trees, the impacts of development activity upon their health and an assessment of future conflicts that may arise between trees and the development proposal.

#### **Below Ground Constraints**

- 3.4. Soils contain organic and mineral material, air and water that provides a medium essential for root growth. The physical properties of soils including texture, porosity and bulk density can greatly impact the availability of water, nutrients and oxygen in the soil available to support the function and growth of tree roots. Protection of the soil environment in which trees grow is therefore essential to ensure tree vitality.
- 3.5. Tree roots provide support and anchorage and allow the uptake and transport of water, nutrients and oxygen for tree function and growth. Roots are commonly found in the upper 600-1000mm of soil, however depth can vary significantly depending on soil and local site conditions. Typically, tree root systems comprise a network of lateral roots that provide structural support and smaller fibrous roots that function in the uptake of water, nutrients and oxygen. Protection of the tree roots is therefore essential to ensure tree vitality.

#### **Impacts of Construction & Development**

- 3.6. The processes of construction including the movement of machinery and equipment near trees can cause soil compaction that can starve roots of oxygen and water, resulting in tree decline or death. Increasing ground levels near trees can cause similar impacts, whilst belowground soil excavations can damage root bark or lead to root severance and impair structural stability. Further impacts include (but are not limited to) contamination of soils by toxic substances such as cement or chemicals and root desiccation due to inadequate protection during exposure.

#### **Root Protection Areas**

- 3.7. In accordance with BS5837, the Root Protection Area (RPA) indicates the notional minimum area of ground around a tree deemed to contain sufficient roots and rooting volume to avoid adverse physiological or structural impairment and to support future tree function, growth and health.
- 3.8. The RPA is calculated in accordance with Section 4.6 of BS5837 and is summarised in Appendix 2.
- 3.9. The RPA is plotted as a continuous circle centred on the base of the stem, however where pre-

existing site conditions such as the presence of built structures, changes in topography, soil type and structure or past management are likely to act as barriers, or alter normal distribution, BS5837 allows modifications to the shape of the RPA can be made based upon sound arboricultural assessment.

- 3.10. The default position should be that no development works occur inside RPAs, however in accordance with BS5837 when there is an overriding justification, it may be appropriate to implement specialist methods of construction or technical solutions that will reduce or eliminate the impact to roots and soil environments.
- 3.11. Additionally, where an area of RPA is lost, it should be demonstrated that the tree can remain viable with the area lost from encroachment compensated elsewhere contiguous with its RPA, based on the species, age, condition and past management of the tree, pre-existing site conditions and nature of operations proposed is undertaken.

#### **Above Ground Constraints**

- 3.12. Tree stems and crowns can restrict the availability of space on a development site that may result in conflicts between trees and the new built environment. The design and layout of a site should take into consideration the presence of tree canopies, as well as individual species characteristics and future growth requirements to create a harmonious relationship between trees and the new built environment.

## **4. PLANNING POLICY, STATUTORY CONSIDERATIONS & TREE LEGISLATION**

### **Planning Policy**

- 4.1. The National Planning Framework 'Project Ireland 2040' and National Development Plan (2021-2030) underpin planning policy across Ireland. These documents recognise the need to manage future growth in a planned, productive and sustainable way.
- 4.2. At the heart of Green Infrastructure Planning is to protect, preserve and enhance national capital by:

*“protecting and valuing important and vulnerable habitats, landscapes, natural heritage and green spaces”.*

- 4.3. The Site falls within the jurisdiction of South Dublin County Council, which has a statutory obligation to ensure that provision is made for the protection of trees, woodlands and hedgerows under the Local Government Planning and Development Act (2000), through implementation of a Development Plan. The current plan for South Dublin County Council is the South Dublin County Development Plan (2022-2028).

### **South Dublin County Development Plan (2022-2028)**

- 4.4. The South Dublin County Development Plan contains various policies in relation to trees and proposals for development including (but not limited to):

**NCBH4 Objective 3:** To ensure that intact hedgerows/trees will be maintained above the 120m contour line within the County ensuring that the strong rural character will not be diluted and that important heritage features & potential wildlife corridors are protected.

**NCB9 Objective 4:** To ensure that development along and adjacent to the Grand Canal protects and incorporates natural heritage features including watercourses, wetlands, grasslands, woodlands, mature trees, hedgerows and ditches and includes an appropriate set-back distance or buffer area from the pNHA boundary to facilitate protected species and biodiversity and a fully functioning Green Infrastructure network.

**Policy NCBH11:** Tree Preservation Orders and Other Tree Protections Review Tree Preservation Orders (TPO) within the County and maintain the conservation value of trees and groups of trees that are the subject of a Tree Preservation Order while also recognising the value of and protecting trees and hedgerows which are not subject to a TPO.

**NCBH11 Objective 1:** To review Tree Preservation Orders within the County and maintain the conservation value of trees and groups of trees that are the subject of any Tree Preservation Order.

**NCBH11 Objective 2:** To regularly evaluate and identify trees of amenity value within the County with a view to making them the subject of Tree Preservation Orders or otherwise protecting them and further, to furnish information to the public in this regard.

**NCBH11 Objective 3:** To protect and retain existing trees, hedgerows, and woodlands which are of amenity and/or biodiversity and/or carbon sequestration value and/or contribute to landscape character and ensure that proper provision is made for their protection and management taking into account Living with Trees: South Dublin County Council's Tree Management Policy (2015-2020) or any superseding document and to ensure that where retention is not possible that a high value biodiversity provision is secured as part of the phasing of any development to protect the amenity of the area.

**GI1 Objective 1:** To establish a coherent, integrated and evolving GI Network across South Dublin County with parks, open spaces, hedgerows, trees including public street trees and native mini woodlands (Miyawaki-Style), grasslands, protected areas and rivers and streams and other green and blue assets forming strategic links and to integrate and incorporate the objectives of the GI Strategy throughout all relevant land use plans and development in the County.

**GI2 Objective 7:** To enhance the biodiversity value of publicly owned hard infrastructure areas by incorporating the planting of new trees, grasses and other species, thereby integrating this infrastructure into the overall GI network.

**GI5 Objective 3:** To ensure compliance with the South Dublin Climate Change Action Plan and the provisions of the Council's Tree Management Strategy. Green Infrastructure (GI) à Increase the County's tree canopy cover by promoting annual planting, maintenance preservation and enhancement of trees, woodlands and hedgerows within the County using locally native species and supporting their integration into new development. à Identify suitable sites for new urban trees including Miyawaki style mini woodlands, where feasible. à Support the implementation of a co-ordinated regional approach to the maintenance of trees and support the work of the Regional Steering Group on Tree Management to which South Dublin County Council is a participant. à Promote the establishment of tree trails in public parks across the County.

Promote the planting of new woodlands and forestry within appropriate open space and park locations within the County. à To plant “pocket forests” in tracts of open grassland to act as an oasis for biodiversity. à The Council recognises the value of mature trees in terms of carbon sequestration and amenity over saplings.

**GI5 Objective 6:** To provide more tree cover across the county, in particular to areas that are lacking trees.

**SM5 Objective 4:** To prioritise safety on rural roads and junctions, while considering the protection of biodiversity, green infrastructure and rural character present in roadside trees, hedgerows and banks, etc.

**SM5 Objective 5:** To design new roads and streets to incorporate green infrastructure elements such as planting of native trees, hedgerows and pollinator species in medians and on roadside verges, as appropriate to the location.

**SM7 Objective 9:** To ensure that car parking is designed in such a manner as to promote visual amenity, green infrastructure, carbon sequestration and sustainable drainage (SuDS) by applying the following requirements: à Provision of landscaping integrated into the design of all car parking, to include planting of native trees and pollinator species; à Provision of not more than two parallel or five perpendicular spaces between trees/planting bays; à Use of permeable paving, where appropriate.

**COS5 Objective 8:** To ensure the design of parks and public open space areas is of high quality; to provide a pleasant setting, accommodate use by people of all ages and abilities, to support life-long activity and good health and well-being by the provision of a balanced mix of active and passive recreation and access to, or view of, nature, ensuring that the design considers: à provision of an appropriate mix of hard and soft surfaced areas; à enhancement of biodiversity and existing trees and hedgerows; à incorporation of water courses, other natural features and existing built heritage into the design of parks and open spaces as appropriate; à provision of new planting, landscape features and appropriate site furniture including a variety of accessible, well located and designed seating.

**E11 Objective 1:** To ensure the implementation of policy and objectives on tree planting, protection of trees on site and development management standards in relation to new development as set out in the Green Infrastructure, Heritage and Implementation Chapters of this plan.

**NCB9 Objective 4:** To ensure that development along and adjacent to the Grand Canal protects and incorporates natural heritage features including watercourses, wetlands, grasslands, woodlands, mature trees, hedgerows and ditches and includes an appropriate set-back distance or buffer area from the pNHA boundary to facilitate protected species and biodiversity and a fully functioning Green Infrastructure network.

#### **Clonburris Strategic Development Zone Planning Scheme (2019)**

- 4.5. The sites are also within the Clonburris Strategic Development Zone (SDZ) and policies and objections relating to Green Infrastructure in the Clonburris SDZ Planning Scheme (May 2019)



will also apply to trees and development. These include:

- To protect, enhance and develop an interconnected green and blue infrastructure network of parks, open spaces, hedgerows, grasslands, protected areas, rivers and streams for amenity and recreation, biodiversity protection, flood management and adaptation to climate change;
- To retain and improve key landscape and ecological features such as hedgerows, the Grand Canal and the Griffeen River; To incorporate new elements of Green and Blue Infrastructure such as tree planting, parks and natural open spaces and sustainable urban drainage systems;
- To reduce fragmentation and strengthen ecological links through the retrofitting and or upgrading of the pedestrian bridge over the railway line to a 'green bridge';
- To connect parks and areas of open space with ecological and recreational corridors to aid the movement of biodiversity and people and to strengthen the overall Green Infrastructure network;
- To support native plant and animal species and encourage corridors for their movement; and To seek to retain hedgerows, aquatic habitats and established tree lines wherever possible.

#### Tree Preservation Orders & Conservation Areas

- 4.6. Tree Preservation Orders (TPOs) may be made under Section 45 of the Local Government (Planning and Development) Act, 1963 and subsequent acts. Part XIII of the Planning and Development Act 2000 sets out the provisions for TPOs. A TPO can be made if it appears to the planning authority to be desirable and appropriate in the interest of amenity or the environment. A TPO can apply to a tree, trees, group of trees or woodland.
- 4.7. The principal effect of a TPO is to prohibit the cutting down, topping, lopping or wilful destruction of trees without the planning authority's consent. The order can also require the owner and occupier of the land subject to the order to enter into an agreement with the planning authority to ensure the proper management of the tree, trees or woodland. A review of the South Dublin County Development Plan (2022-2028) indicates that at the time of the development plan, there were no TPO's in place upon the Site (Table 3.3).

**Table 3.3:** Tree Preservation Orders

| Tree Preservation Order   | Location   |
|---|--|
| Dublin County Council Tree Preservation Order (St Brigid's Clondalkin) Order 1973                     | St Brigid's (now Newlands Garden Centre), New Road, Clondalkin, Dublin 22. |
| Dublin County Council Tree Preservation Order (Beaufort Downs, Rathfarnham) Order 1987                | Beaufort Downs, Rathfarnham, Dublin 14.                                    |
| Dublin County Council Tree Preservation Order (Quarryvale, Brooklawn) (Liffey Valley No.1) Order 1990 | Townland of Quarryvale and Brooklawn, Palmerstown, Dublin 20.              |
| South Dublin County Council Tree Preservation Order (Coolamber Site) Order 2015                       | Newcastle Road, Lucan.   |

### **Felling Licences**

- 4.8. It is an offence for any person to uproot or cut down any tree unless the owner has obtained permission in the form of a felling licence from the Forest Service, with the exception of the following scenarios (under section 19 of the Forestry Act 2014):
- A tree in an urban area. (An urban area is an area that is comprised of a city, town or borough specified in Part 2 of Schedule 5 and in Schedule 6 of the Local Government Act 2001, before the enactment of the Local Government Reform Act 2014 (this act dissolved Town Councils, however, the old boundaries of these areas are still considered as urban for the purpose of the Forestry Act 2014).
  - A tree within 30 metres of a building (other than a wall or temporary structure) but excluding any building built after the trees were planted.
  - A tree less than 5 years of age that came about through natural regeneration and removed from a field as part of the normal maintenance of agricultural land (but not where the tree is standing in a hedgerow).
  - A tree uprooted in a nursery for the purpose of transplantation.
  - A tree of the willow or poplar species planted and maintained solely for fuel under a short rotation coppice.
  - A tree outside a forest within 10 metres of a public road and which, in the opinion of the owner (being an opinion formed on reasonable grounds), is dangerous to persons using the public road on account of its age or condition.
  - A tree outside a forest, the removal of which is specified in a grant of planning permission, providing it was indicated on the lodged plans as being planned for removal as part of the application.
  - A tree outside a forest of the hawthorn or blackthorn species growing in a hedge.
  - A tree outside a forest in a hedgerow and felled for the purposes of its trimming the hedge providing that the tree does not exceed 20 centimetres diameter at 1.3 metres above ground level.
  - Agricultural holdings can fell a limited small number of trees not exceeding 3 cubic metres.
  - The maximum number of trees permitted to be felled under that exemption per year is 4 trees (12 cubic metres)
  - Outside a forest, apple, pear, plum, or damson species are exempt from the need for a felling license.

### **Wildlife**

- 4.9. The cutting of hedges is prohibited during the period 1st April to 31st August every year with limited exceptions under the Wildlife Acts 1976-2008.

## **5. ARBORICULTURAL IMPACT ASSESSMENT**

### **Development Proposal - Site 3**

- 5.1. The proposed development comprises 580no. residential units in a mix of house, apartment, duplex and triplex units comprising 1-bedroom, 2-bedroom and 3-bedroom typologies; 2-storey childcare facility; All associated and ancillary site development and infrastructural works including surface level car parking, bicycle parking, hard and soft landscaping and boundary treatment works, including public, communal and private open space, public lighting, bin stores and foul and water services. Vehicular access to the site will be from Adamstown Avenue and the Northern Link Street, permitted under Reg. Ref. SDZ24A/0033W.

### **Development Proposal – Site 4**

- 5.2. The proposed development comprises 436no. residential units in a mix of house, apartment, duplex and triplex units comprising 1-bedroom, 2-bedroom, 3-bedroom and 4-bedroom typologies; a childcare facility on the ground floor of Block F; retail unit; community building; employment uses and All associated and ancillary site development and infrastructural works including surface level car parking, bicycle parking, hard and soft landscaping and boundary treatment works, including public, communal and private open space, public lighting, bin stores and foul and water services. Vehicular access to the site will be via the Southern Link Road permitted under SDZ20A/0021

### **Development Proposal – Site 5a & 5b**

- 5.3. The proposed development comprises 236 no. residential units including 55 no. social housing units, 113 no. affordable purchase units and 68 no. cost rental units. The scheme provides for a mix of 1, 2 and 3-bedroom units in a range of dwelling typologies, as follows: 35 no. houses; 110 no. duplex units; 33 no. triplex units, and 58 no. apartments. The proposal also includes all associated and ancillary site development and infrastructural works including a total of 219 no. car parking spaces at undercroft and surface level, bicycle parking, hard and soft landscaping and boundary treatment works, public, communal and private open space, public lighting, waste storage areas and foul and water services. Vehicular access to the site will be from Thoms Omer Way and the Northern Link Street (NLS) proposed under concurrent application Reg. Ref. SDZ24A/0033W.

### **Tree Removals & Pruning**

- 5.4. Tree removals and pruning have been limited to that which is necessary and unavoidable to allow the development proposal to be implemented, with consideration given to species attributes, the tolerance of individual trees to disturbance, and to the presence of surrounding trees and features of the site which may have an influence on retained trees.
- 5.5. The pruning of trees may be required for reasons of good arboricultural practice or management to promote tree health and longevity, to remove hazards for reasons of health and safety, or to limit the impacts of the development proposal upon trees where incursions into RPAs are unavoidable.

### **The Impact**

- 5.6. The proposed works will require the removal of all trees from Sites 3, 5a & 5b.

- 5.7. The reason for these removals is to facilitate new buildings, roads, car parking, landscaping, services and all other associated works on site.
- 5.8. It is proposed to retain some trees within the woodland in Site 4 within a gated access wildlife and aquatic habitat in the south east corner of the site, including trees 91, 92, 93, 94, 95, 96, 97, 98, 104, 105, 116 and part of woodland W117.

### **Mitigation & Improvements**

- 5.9. It is proposed to plant new trees and hedgerows across each of the sites within the new built environment and areas of public open space in streets, car parking areas, gardens and parks. The aim of this new planting should be to increase species diversity and canopy cover in the local landscape to provide a future net gain in canopy cover and improvement on the pre-development baseline.

## **6. ARBORICULTURAL METHOD STATEMENTS**

### **Purpose**

- 6.1. The purpose of this statement is to provide a system of working to ensure retained trees are protected at all times during construction. It should be read in conjunction with the Tree Impact & Protection Plan (Ref: 24-803-03) attached to this report.
- 6.2. A copy of this report must be made permanently available for the duration of the development.

It can be:

- Included in tender documents to identify and quantify tree protection and management requirements;
  - Used to plan timing of site operations to minimise the impact upon trees, and;
  - Referenced on site for practical guidance on how to protect trees.
- 6.3. The compliance of arboricultural method statements is recommended as a condition of planning and is necessary to ensure the protection and vitality of retained trees.

### **Pre Commencement Meeting**

- 6.4. A pre-commencement meeting will be held prior to commencement of any demolition or construction works on site. The pre-commencement meeting may require the attendance of:
- The Main Works Contractor;
  - Landscape Architect;
  - Structural/Civil Engineer;
  - Project Arboriculturist; and
  - Any other parties as required.
- 6.5. The purpose of this meeting will be to agree the details of the tree protection measures and ensure that all aspects of tree protection are understood. The Project Arboriculturist and Main



Works Contractor will agree and mark the location of the tree protective fencing and temporary ground protection and any other specific tree protection measures, as required.

### **Key Responsibilities**

- 6.6. It is the responsibility of the main contractor to ensure that all site personnel fully understand the protection measures on the site, that tree protection measures are adhered to at all times, and that the project arboriculturist is contacted if there are any issues related to trees.

### **Tree Protective Fencing**

- 6.7. A protective fence will be erected around retained trees, prior to the commencement of materials or machinery being brought onto site, removal of soil or any form of construction. The area within this fencing will form the construction exclusion zone (CEZ) and it will be afforded protection at all times. No works will be undertaken within this zone that causes compaction to the soil, severance of tree roots or damage to tree canopies.
- 6.8. The fence is to be sited in accordance with the TIPP attached to this report.
- 6.9. Details of the minimum distance for fencing from trees can be found in the Tree Schedule attached to this report.
- 6.10. The precise form of fencing can vary provided it is fit for purpose and prevents damaging activities within the CEZ. For a proposal of this nature the Heras 151 system of fencing will afford the necessary level of protection (Appendix 3).
- 6.11. The fence will have signs attached to it stating that it defines a CEZ and that no works are permitted beyond it.
- 6.12. An example of a tree protection sign is provided in Appendix 4.
- 6.13. The protective fencing may only be removed following completion of all construction works.
- 6.14. The following principles will be adopted by site personnel within the CEZ during construction, to ensure protection of retained trees:
- No level changes.
  - No excavations.
  - No fires.
  - No use of herbicides.
  - No storage of materials, machinery or access for construction workers.

### **Site Compounds & Facilities**

- 6.15. Site compounds and facilities will be located outside of all RPAs and CEZs as identified on the TIPP.

### **Site Cranes, Piling Rigs and Machinery**

- 6.16. The location of all site cranes, piling rigs and other machinery should be sited outside of RPAs to avoid soil compaction.

### **Pollution Control**

- 6.17. Any storage or mixing station located outside of the construction exclusion zone will be located in a place that minimises the risk of contaminated runoff entering to prevent adverse physiological impacts on trees that may result from contact with rooting environments. This may be achieved by using a non-permeable membrane on the ground, surrounded by sandbags or sawdust to contain any spillage.

### **Temporary Ground Protection**

- 6.18. Where it is not practical to protect RPAs by use of protective fencing, BS5837 allows for the fencing to be set back and the soil shielded by ground protection. A range of methods can be used including retaining existing hard surfaces or structures that already protect the soil, installing new temporary surfaces, or a combination of both. Whatever the choice of method, the end result must be that the underlying soil remains undisturbed and retains the capacity to support existing and new roots.
- 6.19. If fences are to be set back on a temporary the following specifications are recommended for use as temporary ground protection to protect roots and soil.
- 6.20. For pedestrian traffic, a plywood board with a minimum thickness of 40mm should be laid on a minimum of 100mm deep woodchip, with geotextile membrane beneath.
- 6.21. For small plant machinery with a gross weight of up to 2 tonne, interlinking aluminium or composite tracks with sufficient load bearing capacity should be laid on a minimum of 150mm deep woodchip, with geotextile membrane beneath.
- 6.22. For heavy machinery with a gross weight of up to 3.5tonne, interlinking aluminium or composite track with sufficient load bearing capacity should be laid over a minimum layer of 200mm deep woodchip, with a geotextile membrane beneath.
- 6.23. Any temporary protective surfaces must remain in place until all construction activity is finished.
- 6.24. Upon completion of construction works, the temporary ground protective measures should be removed working backwards from on top of the system. This will need to be done carefully ensure that there is no excavation or compaction of the original surface or change in ground levels.
- 6.25. Once this material has been removed vehicular access to this part of the site will not be permitted.
- 6.26. The location of where temporary ground protection is to be located and at what stage of development is illustrated on the TIPP attached to this report.

### **Excavations and Removal of Existing Surfaces**

- 6.27. All excavation must be carried out carefully using spades, forks and trowels, taking care not to damage the bark and wood of any roots. Specialist tools for removing soil around roots using compressed air such as an Air Spade may be an appropriate alternative to hand digging, if available.

- 6.28. All soil removal must be undertaken with care to minimise the disturbance of roots beyond the immediate area of excavation. Where possible, flexible clumps of small roots, including fibrous roots, should be retained if they can be displaced temporarily or permanently beyond the excavation without damage.
- 6.29. If digging by hand, a fork should be used to loosen the soil and help locate any substantial roots. Once the roots have been located the trowel should be used to clear the soil away from them without damaging the bark. Exposed roots that are to be removed should be cut cleanly with a sharp saw or secateurs 100-200mm behind the final face of the excavation.
- 6.30. Roots temporarily exposed must be protected from direct sunlight, drying out and extreme temperatures by appropriate covering. Roots greater than 25mm in diameter should only be cut in exceptional circumstances. Roots greater than 100mm in diameter should only be cut after consultation with the project arboriculturist.

#### **Upgrading Existing Surfaces**

- 6.31. Where upgrading of existing hard surfaces is required, the preferred option will be to leave the surface in place and install the new surface specification on top.
- 6.32. If the retained surface is impermeable, it may be appropriate to remove or puncture sections to create a more favourable environment for roots beneath, before the new surface is laid, through consultation with the project arboriculturist.
- 6.33. Where the existing surface is to be removed or upgraded, the surface layer should be excavated down the existing subbase and the new surface specification installed on top, to prevent any damage to roots beneath.
- 6.34. It is recommended that where possible, new and upgraded hard surfaces should be porous (e.g. permeable brick paving, porous resin bound aggregate or tarmac) to allow the flow of water and oxygen to roots. Wet concrete should only be poured if an impermeable geotextile fabric has first been installed to prevent soil contamination from toxic leachate.
- 6.35. New surfaces and upgraded surfaces should be set back from the base of stems by a minimum of 500mm to allow space for future growth and minimise the risk of distortion with new surface.

#### **Installation of Services**

- 6.36. All services and utilities should be installed within existing service routes and where possible outside of RPAs.
- 6.37. Where installation of utilities or services is required within RPAs, working practices will be adopted in accordance with the National Joint Utilities (NJUG) 10, Vol 4, Issue 2, 2007 'Guidelines for the Planning, Installation and Maintenance of Utility Apparatus in Proximity to Trees'.
- 6.38. In accordance with 4.1.3 of NJUG 10 2007, acceptable techniques in order of preference include:
- 6.39. Trenchless; b) Broken Trench; and c) Continuous Trench. Trenchless methods involve the use of thrust boring machinery, whilst broken and continuous trench methods require that excavations within RPAs are carried out using hand tools only.

- 6.40. For a proposal of this nature, broken or continuous trench methods are the most appropriate and should be undertaken as per NJUG 10, to prevent any damage to tree roots or disruption to soil rooting environments.

#### **Installation of Railings, Lighting Columns or Street Furniture**

- 6.41. The erection of a new railings, lighting columns or street furniture will require 'hand-digging' in the location where any foundations or posts are required within RPAs, to prevent damage to tree roots.
- 6.42. Any soil removal during excavations must be undertaken with care to minimise root disturbance and avoid any damage to root bark.
- 6.43. Exposed roots that are to be removed should be cut cleanly with a sharp saw or secateurs 10-20mm behind the final face of the excavation.
- 6.44. Roots greater than 25mm diameter should only be cut in exceptional circumstances and following approval by the project arboriculturist.
- 6.45. Fibrous clumps of roots must be retained where possible, with any exposed roots protected from desiccation by covering them with a damp hessian sack or damp sharp sand (**builders' sand must not be used**).
- 6.46. Prior to backfilling, roots must be surrounded with topsoil or sharp sand before the excavated earth is replaced. The soil must be free of contaminants and any foreign objects that may be potentially harmful to roots.

#### **Soft Landscaping**

- 6.47. To avoid damage to existing tree roots and prevent soil compact, any machinery used to remove existing surfaces and ground vegetation for purposes of soft landscaping (e.g. seeding new lawns or laying turf) should be sited outside of RPAs. If this is not possible, hand tools must be used.
- 6.48. The removal of the surface layer within RPAs must not exceed 50mm, to prevent exposure and damage of tree roots beneath.
- 6.49. Soft landscaping works must not involve raising or lowering of the existing ground level within any RPA as this can starve roots of oxygen and cause irreversible physiological damage to trees.
- 6.50. The use of rotavators within RPAs is prohibited.
- 6.51. Any level changes outside RPAs must be graded to marry existing soil levels within RPAs.

## **7. ABOUT THE AUTHOR & LIMITATIONS**

#### **Authors Qualifications & Experience**

- 7.1. This report has been written by John Morris, Director at John Morris Arboricultural Consultancy Ltd. John has a First Class BSc (Hons) in Housing (Ulster University) and a Post Graduate Diploma (UK NQF Level 7) in Arboriculture & Urban Forestry (Myerscough College & University of Central Lancashire). John regularly undertakes continuous professional development (CPD) in all areas of arboriculture and wider business administration. John is a Professional member of the



Arboricultural Association (AA) and Associate member of the Institute of Chartered Foresters (ICF).

### **Limitations**

- 7.2. This report is for planning purposes and is not a detailed assessment of the health and condition of trees, however where defects have been identified works have been recommended to ensure site safety.
- 7.3. This report does not take responsibility for the effects of extreme weather conditions, vandalism, accidents or any works to trees that occur without the authors knowledge, or that are not recommended within this report.
- 7.4. Tools used during the assessment have been limited to a sounding mallet, probe or binoculars. No invasive or diagnostic equipment has been used, nor have any aerial inspections, belowground root investigations, or soil, leaf or root samples been taken for further testing or analysis.
- 7.5. Trees were assessed between Monday 8<sup>th</sup> and Friday 12<sup>th</sup> April 2024 and the information gathered during the survey pertains to that moment in time. The observations within this report will remain valid for two years from the date of inspection. It is recommended that trees are inspected again within two years of the date of this report to assess what works are required for reasons of good arboricultural management and to enable the client to manage their legal reasonability in terms of tree risk management.
- 7.6. The location of trees places reliance on the accuracy of the topographical survey unless otherwise caveated within the report.
- 7.7. All works recommendation as a result of the survey should be undertaken by a suitably qualified and insured arborist in accordance with BS3998:2020 *Tree Works – Recommendations* to prevent any structural or physiological impairment to trees.

## Appendix 1: Tree Survey Criteria (BS5837:2012)

The assessment of the trees has been carried out in accordance with the guidance provided in Annexe C of BS5837, which requires that any tree on or influencing distance of the site with a stem diameter of over 75mm at 1.5m above ground level be recorded.

Stem diameter measurements were taken using a girthing tape or Biltmore stick, and in accordance with Annexe D of BS5837.

Height, crown spread, and canopy clearance measurements are recorded in accordance with the measurement convention detailed in paragraph 4.4.2.6 of BS5837.

The trees are categorised in an order defined in **Table 1** of BS5837, a copy of which can be seen below in **Figure 1**, but which can be summarised as:

- **Category A** Trees of high quality and value in such a condition as to be able to make a substantial contribution for a minimum of 40 years.
- **Category B** Trees of moderate quality and value in such a condition as to make a significant contribution for a minimum 20 years.
- **Category C** Trees of low quality and value currently in adequate condition and able to remain until new planting can be established with a minimum useful life expectancy of 10 years, and young trees with a stem diameter less than 150mm.
- **Category U** Trees in poor structural condition or physiological decline that cannot be realistically retained in the context of current land use for more than 10 years.





Further subcategories 1-3 indicate the area(s) in which a tree or group retention value lies.

- Mainly arboricultural.
- Mainly landscape.
- Mainly cultural, including conservation.



## BS5837:2012 Assessment Criteria & Cascade Chart

Table 1 Cascade chart for tree quality assessment

| Category and definition   | Criteria (including subcategories where appropriate)   | Identification on plan   |
|---|--|--|
| <b>Trees unsuitable for retention (see Note)</b>  |  |  |
| <b>Category U</b><br>Those in such a condition that they cannot realistically be retained as living trees in the context of the current land use for longer than 10 years | <ul style="list-style-type: none"> <li>Trees that have a serious, irremediable, structural defect, such that their early loss is expected due to collapse, including those that will become unviable after removal of other category U trees (e.g. where, for whatever reason, the loss of companion shelter cannot be mitigated by pruning)</li> <li>Trees that are dead or are showing signs of significant, immediate, and irreversible overall decline</li> <li>Trees infected with pathogens of significance to the health and/or safety of other trees nearby, or very low quality trees suppressing adjacent trees of better quality</li> </ul> <p><i>NOTE Category U trees can have existing or potential conservation value which it might be desirable to preserve; see 4.5.7.</i></p> | See Table 2<br>   |
| <b>Trees to be considered for retention</b>   |  |  |
| <b>Category A</b><br><b>Trees of high quality</b> with an estimated remaining life expectancy of at least 40 years  | <p><b>1 Mainly arboricultural qualities</b></p> <p>Trees that are particularly good examples of their species, especially if rare or unusual; or those that are essential components of groups or formal or semi-formal arboricultural features (e.g. the dominant and/or principal trees within an avenue)</p> <p><b>2 Mainly landscape qualities</b></p> <p>Trees, groups or woodlands of particular visual importance as arboricultural and/or landscape features</p> <p><b>3 Mainly cultural values, including conservation</b></p> <p>Trees, groups or woodlands of significant conservation, historical, commemorative or other value (e.g. veteran trees or wood-pasture)</p>   | See Table 2<br>   |
| <b>Category B</b><br><b>Trees of moderate quality</b> with an estimated remaining life expectancy of at least 20 years  | <p>Trees that might be included in category A, but are downgraded because of impaired condition (e.g. presence of significant though remediable defects, including unsympathetic past management and storm damage), such that they are unlikely to be suitable for retention for beyond 40 years; or trees lacking the special quality necessary to merit the category A designation</p> <p>Trees present in numbers, usually growing as groups or woodlands, such that they attract a higher collective rating than they might as individuals; or trees occurring as collectives but situated so as to make little visual contribution to the wider locality</p> <p>Trees with material conservation or other cultural value</p>  | See Table 2<br> |
| <b>Category C</b><br><b>Trees of low quality</b> with an estimated remaining life expectancy of at least 10 years, or young trees with a stem diameter below 150 mm       | <p>Unremarkable trees of very limited merit or such impaired condition that they do not qualify in higher categories</p> <p>Trees present in groups or woodlands, but without this conferring on them significantly greater collective landscape value; and/or trees offering low or only temporary/transient landscape benefits</p> <p>Trees with no material conservation or other cultural value</p>  | See Table 2<br> |

## Appendix 2 – Calculation of the Root Protection Area

### Circle Radius

The circle radius has been calculated by obtaining the stem diameter (measured at 1.5m above the ground) in millimetres and multiplying it by 12. Where the tree is multi-stemmed, an average stem diameter is calculated by the following formula specified in section 4.6.1 (a) & (b) of BS5837.

For trees with two to five stems, the combined stem diameter should be calculated as follows:

$$\sqrt{(\text{stem diameter } 1)^2 + (\text{stem diameter } 2)^2 \dots + (\text{stem diameter } 5)^2}$$

For trees with more than five stems (not illustrated in Annex C), the combined stem diameter should be calculated as follows:

$$\sqrt{(\text{mean stem diameter})^2 \times \text{number of stems}}$$

This total is then divided by 1000 to provide a circle radius in metres.

### RPA Areas


The RPA has been assessed according to the recommendations set out in section 4.6 of BS5837. It is calculated by multiplying the radius squared by 3.142 ( $\pi$ ).

### Length of sides of a square

Section 5.5.3 of BS5837 recommends that the ground protection and barriers should be shown as a polygon surrounding the stem of the tree. With a circle, the distance from the edge of the circle to the centre will remain constant, but with a square, the distance from the centre of the tree to the sides of the square is less than the distance to the corner of the square. The area of the square must remain the same as the area of the circle. In order to ensure that it is the case, the length of side of the square is calculated at the square root of the RPA area.

### Minimum barrier distance

This is the closest point that a side of the square can be to the centre of the tree.

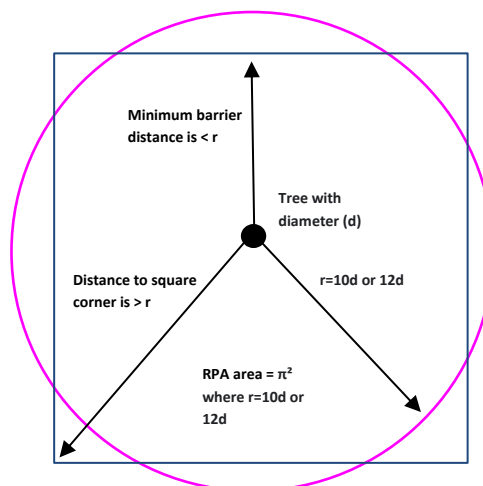

**Figure 1.** Illustration of area calculations and minimum barrier distances



Figure 1 illustrates the differences between a square and a circle in area. Where the distance from the centre of the tree to the corner of the square is greater than the radius of the circle ( $r$ ), but the distance from the centre of the tree to the side of the square is greater than the radius of the circle ( $r$ ), the total area will remain the same. The minimum barrier distance from the tree is calculated by taking the length of the side and dividing it by two.

#### **Clarification note on the RPA radius**

The RPA radius is not the automatic minimum distance of the tree protection. It is a notional figure for use as a means of calculating the actual area of the RPA. BS5837 clarifies this under *Section 3.7 Root Protection Area (RPA) – layout design tool indicating the minimum area around a tree deemed to contain sufficient roots and rooting volume to maintain the trees viability, and where the protection of the roots and soil structure is treated as a priority.*

# heras® 151 and 151steadfast system

round top panel with anti-climb mesh  
high visibility orange blocks  
steadfast strut  
anti-tamper coupler  
fully tested and certificated  
health and safety compliant (HSG 151)

Having invented the original concept of temporary fencing back in the 80s, Heras is proud of its reputation as a true innovator.

Our latest solution for securing site perimeters and protecting the public has been phenomenally successful since its launch, and offers the ultimate market leading temporary fencing system.

Our safest, most durable and most secure system ever offers you total peace of mind, and unrivalled performance.

You can be sure that by installing the Heras® 151 Steadfast System (patent pending), you are conforming fully to the latest HSE Guidelines on "Protecting the Public" from the dangers of construction sites.

Heras has campaigned widely over recent years against failing product standards, and has consulted closely with senior figures across the construction industry to ensure our products meet and exceed your expectations. This latest innovative system means you should never again need to compromise on:

- Value for money
- Quality
- Performance
- Design
- Ease of installation.

All backed up with unbeatable service from our nationwide branch network – deal direct with Heras – your safety first fencing supplier.

## Fully Tested and Certificated

Extensive independent testing by Sheffield Hallam University has proved the performance of the system, resisting wind speeds well in excess of gale force.

The HSE has confirmed that the system meets all of the guidelines in the HSG 151 Publication "Protecting the Public - 'Your next move'".

In turn, therefore, we can offer customers a certificate of compliance when they purchase this system from Heras.

It is your responsibility to ensure the system is correctly installed and fixed. For help and advice, contact your nearest branch.

## 151 system

The key components of the Heras 151 system are as listed.

### Round Top Panel with Anti-Climb Mesh

- The strongest panel on the market, with 3 sides formed from a continuous length of tube, eliminating the top corner weld, often the weakest point in traditional panel design.

### High Visibility Orange Block

- Permanently coloured with a durable UV stabilised "Haze" casing and filled with solid high density concrete.
- Effectively highlights any potential trip hazard.
- Resists all weather conditions – painted coatings will chip and peel.

### Heraslock® Anti-Tamper Coupler

- Providing additional security, these couplers can only be removed with the use of the specialist tool.

## 151 steadfast system

The Heras 151 steadfast system incorporates all the benefits of the 151 system, with the addition of the patented...

### Heras® Steadfast Strut

- The unique design of this clever strut dramatically increases the stability of the fence.
- The strut fits neatly within the high visibility block allowing a neat and compact solution, and acts as an integrated anti-fit device.
- 3 additional fixing holes incorporated into the design allow for soil pins and thunderbolts, dependent on ground conditions.

### Optional Extras


- Heras® Steadfast Safety Strips with reflective coating can be fitted in minutes to highlight site dangers.
- Front support brackets allow vastly improved performance on softer ground conditions and fit quickly and easily into the high visibility blocks.



ROUND TOP PANELS WITH ANTI-CLIMB MESH

Our latest solution for securing site perimeters and protecting the public has been phenomenally successful since its launch, and offers the ultimate market leading temporary fencing system.

Figure 2 Default specification for protective barrier

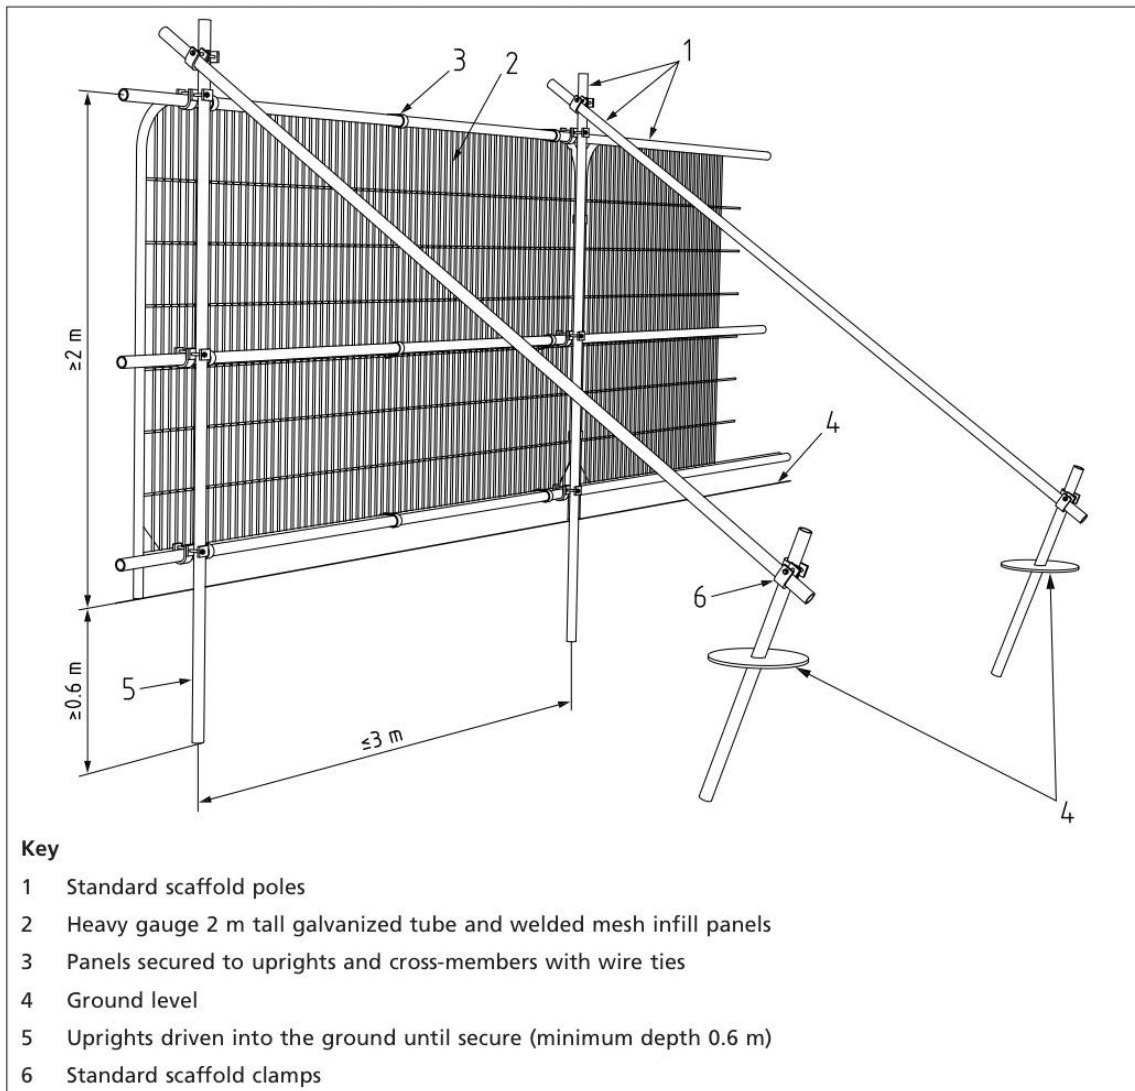

#### Appendix 4 – Example of Tree Protective Signs







## Appendix 5 – Example of Temporary Ground Protection

## DuraDeck

-|-|-|-|-|-|-|  
**PRODUCT SPECIFICATIONS**  
**DD1**

**Traction Surface:** Double-traction tread design includes two parallel traction treads positioned at 90 degrees to adjacent double traction tread sets.

**Module Size:**     **Length:** 8' / 2.44 m  
                           **Width:** 4' / 1.22 m  
                           **Module Size:** 32 sq/ft / 2.973 sq/meters  
                           **Thickness:** ½" thick mat + 3/8" cleat

**Module Weight:** 86 lbs. / 39.01 kg.  
                           **Per Square Foot:** 2.69 lbs. / 43 oz. / 1.22 kg. / 1219 grams  
                           **Per Square Meter:** 28.60 lbs. / 12.97 kg.

**Colors:**           Black, White.  
                           Custom colors available (minimum order required).

**Material:**       Black High-Density Polyethylene (HDPE) post-industrial recycled plastic, naturally UV resistant due to the carbon black used for color. White mats available.

| <b>Test Results:</b>            | <b>ASTM</b> | <b>Units</b>      | <b>Typical Values</b> |
|---------------------------------|-------------|-------------------|-----------------------|
| <b>Melt Index</b>               | D 1238      | g/10min           | 4.9                   |
| <b>Density</b>                  | D 792       | g/cm <sup>3</sup> | .960                  |
| <b>Tensile Strength</b>         | D 638       | mpa (psi)         | 30 (4,350)            |
| <b>@ Yield 50mm/min</b>         |             |                   |                       |
| <b>Elongation @ Break</b>       | D 638       | %                 | 1 500                 |
| <b>50mm/min</b>                 |             |                   |                       |
| <b>Flexural Modulus</b>         | D 790       | mpa (psi)         | 1 240 (180,000)       |
| <b>Hardness, Shore D</b>        | D 2240      | --                | 70                    |
| <b>Compressive Strength:</b>    |             | D695-02a          | psi   2,843           |
| <b>Flammability Resistance:</b> | UL-94 HB    |                   | Passed                |

**Tread Pattern:** **DD1:** Rugged double-traction tread on both sides

**Support Structure:** Matting incorporates multi-directional structural support (cleat design) allowing for distribution or dispersion of PSI weight factors. Not intended for bridging.

**Weight Loading:** Varies, depending on sub-surface, up to 80 tons capacity.

**Ground Surface:** DuraDeck mats are designed to be used with no ground preparation over grass, gravel, soil, concrete, asphalt, mud and sandy soil conditions.

**Connection System:** DuraDeck mats have eight holes: one in each corner and four in the center line (two on each 8ft side) to create multi-directional roadways of nearly any size or shape. Mats can be connected using metal DuraLink connectors. DuraLinks do not require tools to install.

**Shipping:**       Pallet maximum is 50 units (4' x 8')  
                           20' Ocean Container: 250 – 4' x 8' unit order and/or equal to 29,240 lbs.  
                           40' Ocean Container: 500 – 4' x 8' unit order and/or equal to 43,000 lbs.

**Warranty:**       7 years against cracking and breaking under normal use.



Signature Systems Group, LLC  
 12 N. W. 87th Street - 10th Floor  
 Miami, FL 33150  
 Tel: (305) 808-1201 • Fax: (305) 808-1114 • Email: info@signaturedecking.com  
 Website: www.signaturedecking.com • Photo: www.signaturedecking.com
