






Ashgrove House
 Kill Avenue
 Dun Laoghaire
 Co Dublin
 Tel. 01-2804839
 Mob. 086-3819011
 e-mail - thetreefile@eircom.net


Graphic Representation of Tree Form, Balance and Protection Zone

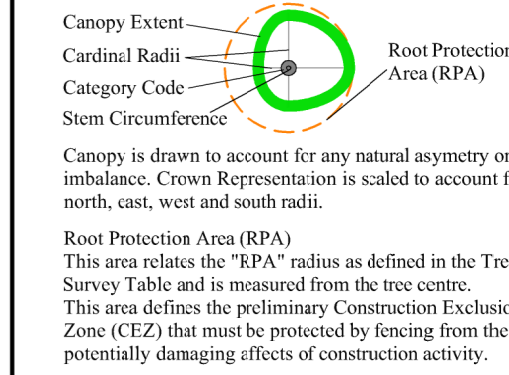


Tree Quality (Categorisation)

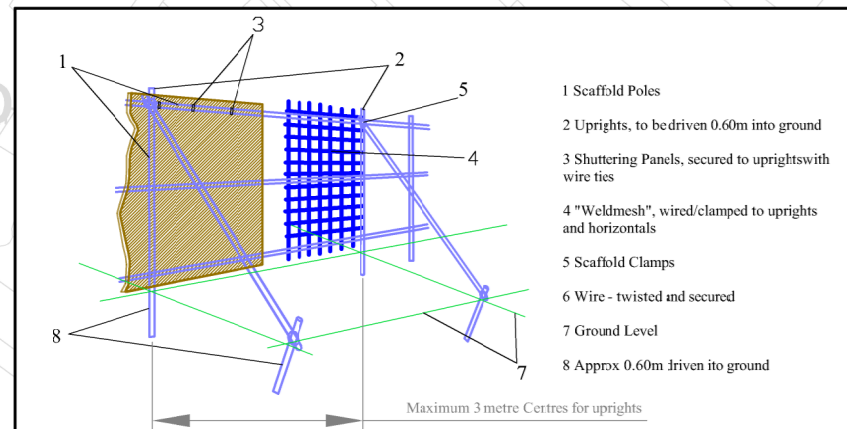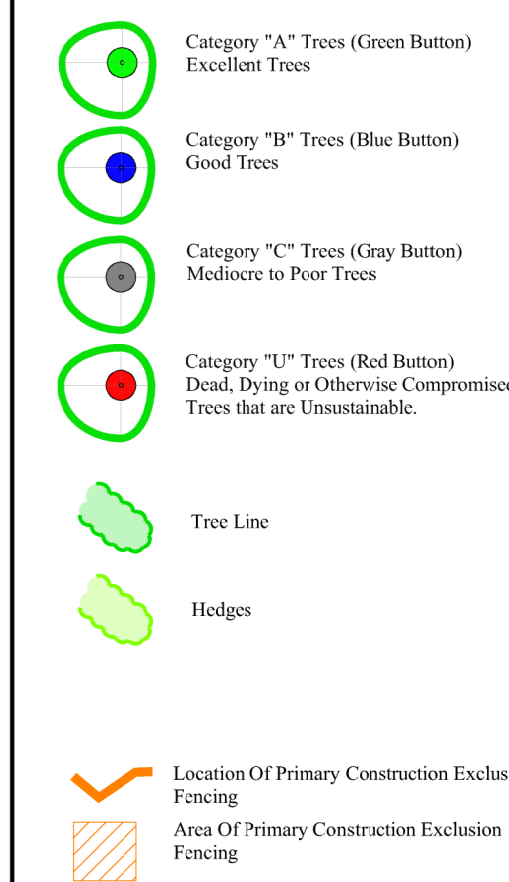

Example of Construction Methodology for "Construction Exclusion Fencing".

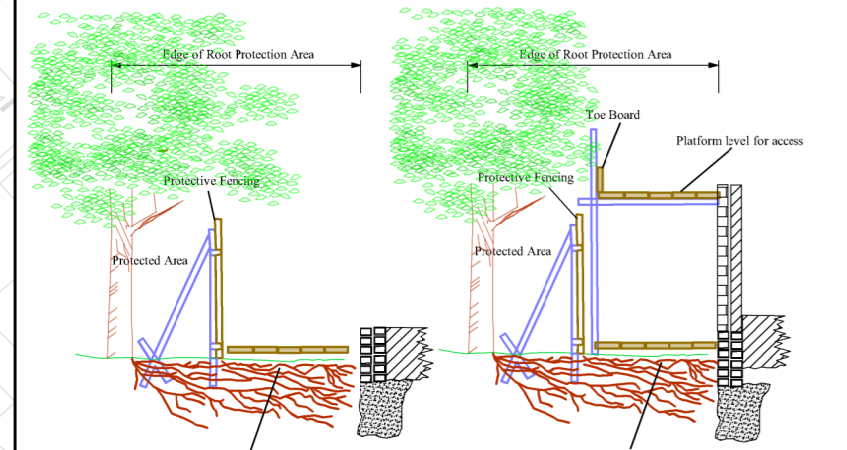


Cellular Confinement Systems can provide robust ground protection that can provide access for larger plant and machinery but must be installed in accordance with manufacturers specification and to engineers requirements.

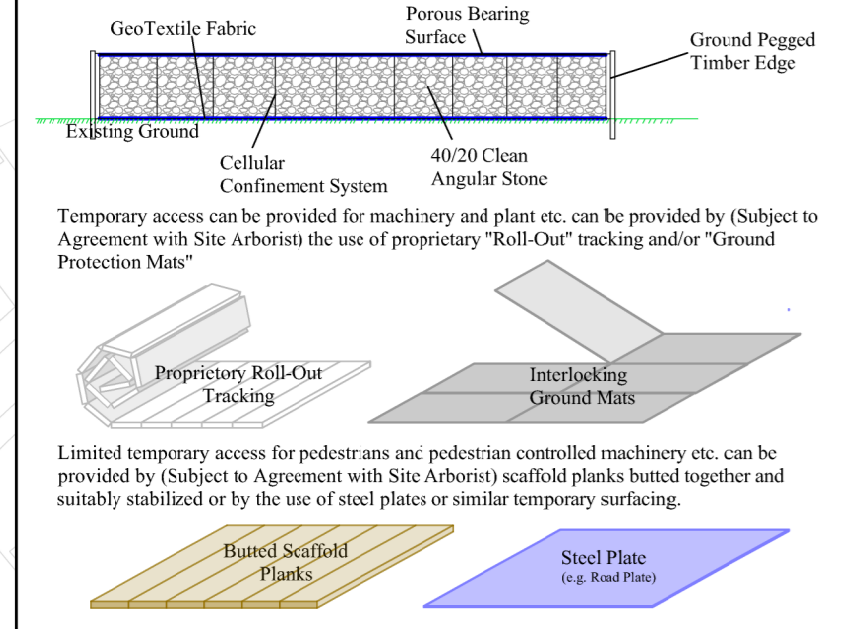


Each of the above must be installed on a progressive, rolling-out basis, with access only being gained from previously protected ground.
 The ground beneath such systems must be protected by the use of a "Geotextile" membrane and a layer of "Compression Resistant" material (e.g. wood chips).
 All above option must accord with the recommendations of Section 6.2.3 of BS5837:2012.

Examples of Ground Protection Systems

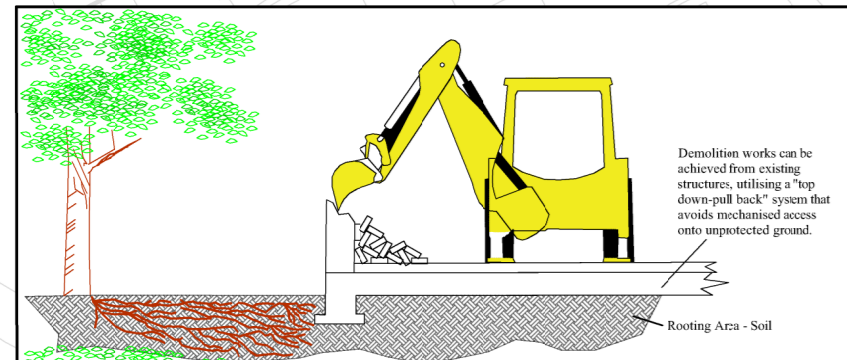

Any removal of existing surfaces must preserve ground space beneath surface without disturbance.
 Machinery must remain on protected ground (existing or provided) and must avoid moving onto unprotected (soft) ground

Mechanised Works Within Protection Zones



This Drawing Must Be Read in Conjunction with the "Arboricultural Method Statement" at "Appendix 1" of the Associated Arboricultural Report

Client: Westar Investments Ltd.
 Scale: 1:1000 Date: December 2020
 Project: Tree Survey, Capdoo, Clane, Co Kildare
 Description: Tree Protection Plan
 Drawing Title: Capdoo Tree Protection Plan
