


- Site Works:**
1. Site to be stripped of topsoil which will be temporarily stored on site.
 2. Terram 1000 and 300mm min. Clause 804 crushed stone laid at suitable falls.
 3. Ducts, fencing, portacabins etc. placed on site to be removed upon completion.
 4. Crushed stone and Terram to be removed, topsoil to be re-spread across site and seeded.

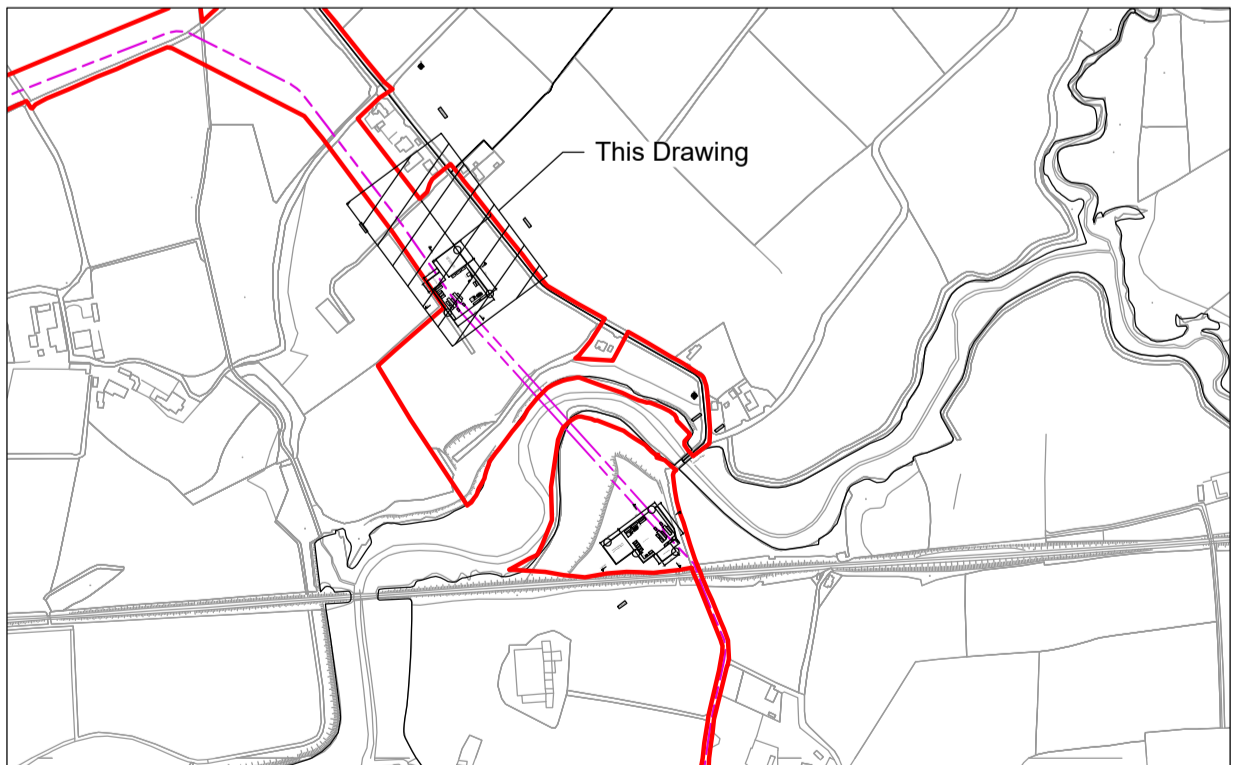


WORKING DRAFT ARUP

Ordnance Survey Ireland Licence No. EN 0002819 © Ordnance Survey Ireland/Government of Ireland

- Legend**
- Proposed Cable Route
 - Planning Corridor
 - Security Fencing (2.4m high)

- Notes**
1. All dimensions in metres unless noted otherwise.
 2. Do not scale, use figured dimensions only.
 3. Drawings for planning purposes only, not for bid or construction.
 4. Land levels shown relate to Ordnance Datum Malin Head unless otherwise noted.
 5. Coordinates shown are to Irish Transverse Mercator in metres.



PL2	10/06/20	EG	SOS	EJL
Issued for Planning				
PL1	13/03/20	SB	MM	EJL
Issued for Planning				
Rev	Date	By	Chkd	Appd

ARUP
One Albert Quay
Cork, Ireland
Tel +353 (0)21 422 3200
www.arup.com



Client
Greenlink Interconnector

Project Title
Campile Estuary Crossing
Temporary Construction Compound
for HDD Contractor
Site Layout Plan - Sheet 1 of 2

Scale at A1 1:500

Role	Civil
Suitability	Planning
Arup Job No	246369
Name	C-CAM-003
Rev	PL2
