

METROLINK
Integrated Transport. Integrated Life.

Oral Hearing
AZ1 Seatown West and Estuary Court
21 February 2024










METROLINK



AZ1 Seatown West & Estuary Court



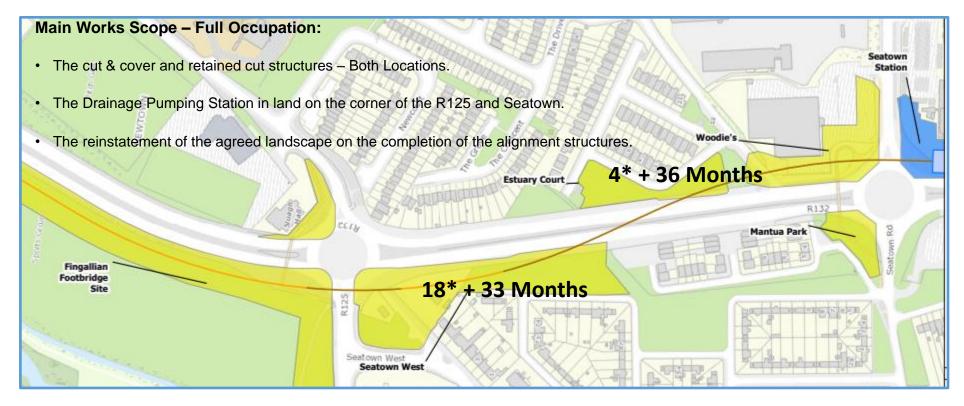

Advance Enabling Works* - Duration Before Main Worksites are established:

- Seatown West 18 months: Site Clearance, Surveys, Utility Diversions and Monitoring Work.
- Estuary Court 4 months: Site Clearance, Surveys, Utility Diversions and Monitoring Work.




Outline Construction Programme


Outline Construction Programme		Chainage				Year	Year 1					Year 2				Year 3				Year 4					Year 5				Year 6			
						Month	1 2 3	4 5	6 7 8	9 10	11 12 1	3 14 15 1	16 17 18	19 20 21	22 23 2			30 31 32	33 34 35	36 37 38		42 43 4		47 48	19 50 51 5	2 53 54	55 56 57	58 59	60 61 62	63 64 6	5 66 67	68 69 70 71
Location	Details	Start	Finish	Total LM	Start Month	Finish Month																		Ш			Т				\Box	
Seatown West	Seatown Satelitte Compound	2184.0	2450.0	266.0	0.3	49.8																		П			Ш	Ш			\Box	
	Reinstate Seatown Satelitte Compound				46.8	49.8																					Ш					
								Ш			Ш					Ш								Ш			Ш'		Ш	Ш	Ш	
	AEW & Utility Works	2184.0	2373.0	189.0	1.2	18.2								Ш	Ш	Ш					Ш		$\perp \perp$	Ш	$\perp \! \! \perp \! \! \perp$	Ш	Ш'	Ш	Ш	Ш	Ш	
								Ш		Ш	Ш	Ш				Ш				Ш	Ш	Ш		Ш	Ш	Ш	Щ'	Ш	Ш	Ш	Ш	
	R125 Crossing: Phase 1 (Seatown)	2184.0	2225.0	41.0	16.8	23.5	Ш	Ш		Ш	Ш	Ш								Ш		Ш		Ш	Ш	Ш	Щ'	Ш	Ш	Ш	Ш	
							Ш	Ш		Ш	Ш	Ш			Ш	Ш				Ш	Ш	Ш		Ш	Ш	Ш	Ш'	ш	Ш	ш	Ш	
	R125 Crossing: Phase 2 (Seatown)	2184.0	2274.0	90.0	24.4	30.6	Ш	Ш		Ш	Ш	Ш										Ш		Ш	$\perp \! \! \perp \! \! \perp$		Ш'	ш	Ш	Ш	Ш	ДШ.
							ш	Ш		Ш	ш					ш		Ш	\perp	\perp	ш	ш	\perp	ш	$\perp \! \! \! \! \! \! \! \! \! \! \! \! \! \! \! \! \! \! \!$	ш	Щ'	ш	Ш	Ш	Ш	
	R/C Seatown	2274.0	2373.0	99.0	3.1	49.7	Ш	Ш		Ш	Ш							Ш	$\perp \! \! \perp$		ш	ш		Ш	$+\!+\!+$	Ш.	Ш'	Ш	Ш.	Ш	Ш	444
							Ш	Ш	Ш	Ш	ш	Ш	Ш	Ш	Ш	Ш								ш	$\perp \! \! \! \! \! \! \! \! \! \! \! \! \! \! \! \! \! \! \!$	Ш	Ш'	Ш	Ш.	Ш	Ш	
	R132 Northbound Diverted: C/C with TTM Phase 1	2373.0	2450.0	77.0	27.6	45.8	ш	Ш	Ш	Ш	$\perp \! \! \! \! \! \! \! \! \! \! \! \! \! \! \! \! \! \! \!$	ш	\perp		Ш	ш								ш	$+\!+\!+$	Ш.	Ш'	ш	Ш.	ш	ДД.	
							ш	Ш		Ш	\perp					Ш								ш	$\perp \! \! \! \! \! \! \! \! \! \! \! \! \! \! \! \! \! \! \!$	Ш.	Ш'	ш	Ш	ш	Щ	
Seatown to Estua	ry R132: C/C under R132	2373.0	2627.0	254.0	12.5	45.8	ш	Ш		Ш														Ш	$\perp \! \! \perp \! \! \perp$	ш	Ш'	ш		ш	ш	+++
							$\sqcup \sqcup$	ш	\Box	Ш	++											+++	++	ш	+++	++-	Щ'	Ш		₩	444	+++
	R132 Southbound Diverted: C/C with TTM Phase 2	2450.0	2627.0	177.0	14.3	27.5	$\sqcup \sqcup$	Ш	\vdash	\sqcup	$+\!\!+\!\!\!+$										ш	+++		ш	+++	++-		Ш		+++	$+\!+\!\!+\!\!\!+$	
<u> </u>								ш		+	Ш	+				ш								Ш	+	Ш	ДΗ'	ш		НН-	ДД	
L							$\sqcup \sqcup$	ш	\vdash	Н						ш							-	ш	+	++-	Щ'	Ш		₩	444	+++
Estuary Court	Estuary Court Satelitte Compound	2482.0	2600.0	118.0	10.3	50.2	\vdash	ш		+			++-										++	ш	+++	++-		Ш			₩	+++
	D 5	-			40.0			ш		+	+	₩	++-	+++	+++	ш							-	ш	+++	++	ДΗ'	Ш	$+\!\!+\!\!-$	₩	#	+++
	Reinstate Estuary Court Satelitte Compound	-			48.2	50.2	\vdash	ш		Н	ш	+++	+		\Box	ш					+++	+++		ш	+++	+	ДΗ'	++	-	₩	##	
		-				44.2	\vdash	ш			ш		+		+++	ш				+	+++	+++		ш	+++	+	ДН'	++	$+\!\!+\!\!\!+$	₩	##	+++
	AEW & Utilities				9.9	14.3		ш					++-		ш	ш			+	-	+++	+++	-	ш	+++	++-	#	+++	$+\!\!+\!\!\!+$	+++	$+\!+\!+\!+$	+++
	Old Contains Bond TTM Consider Discouries	2500.0	2627.0	27.0	48.2	53.3	++	Н	\vdash	+++	++	+++	+	++	+++	+	++	++	++	+	+++	+++	+	++				+++	$+\!\!+\!\!-$	++	+++	+++
	Old Seatown Road TTM Crossing Diversion	2600.0	2627.0	27.0	48.2	53.3	++	+++	++	+++	++	+++	+	+++	++	++		++	++	+	++	+++	+	H			#	++	+	++	$+\!+\!\!+\!\!+$	+++
	Reinstate Old Seatown Road	 			53.4	55.4	++	Н	\vdash	+	++	+++	+	+++	++	+		\vdash	+	+	+++	+++	+	Н	+++			++	$+\!\!+$	++	+	+++
-	Neilistate Olu Seatowii Rodu	1		1	55.4	35.4	+++	Н	++	+++	++	+++	+	++	+++	++	++	++	++	+	++	+++	+	+++	+++			+++	+	++	+++	+++-
		<u> </u>	1	<u> </u>			ш	Ш	ш	Ш	ш	$\perp \perp \perp$		ш	ш	ш	шШ	$\sqcup \sqcup$	шШ	ш	ш	ш		\Box	ш			ш	ш	ш	Ш	




Typical Construction Sequence

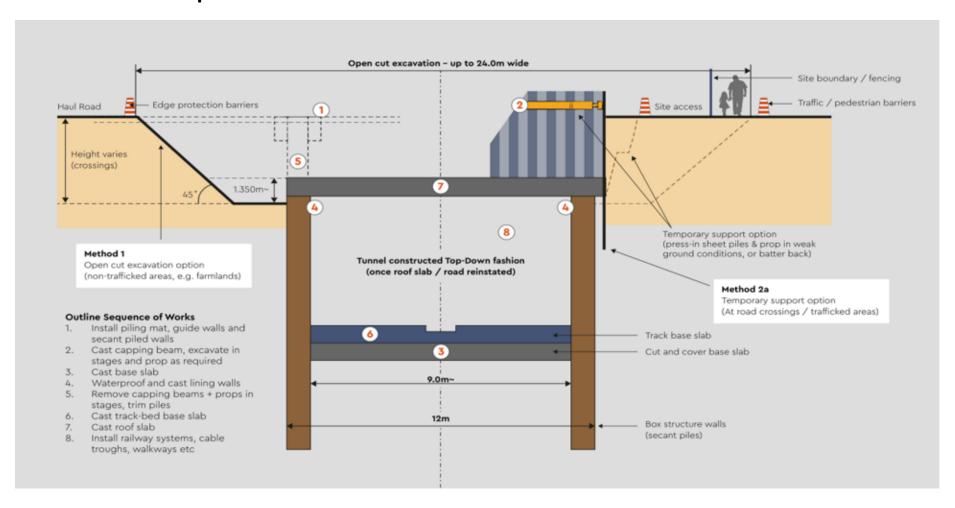




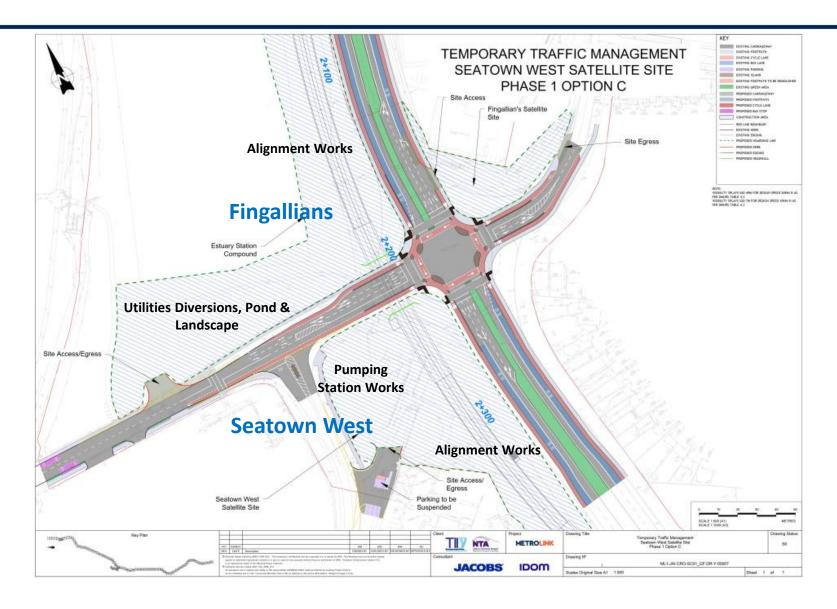




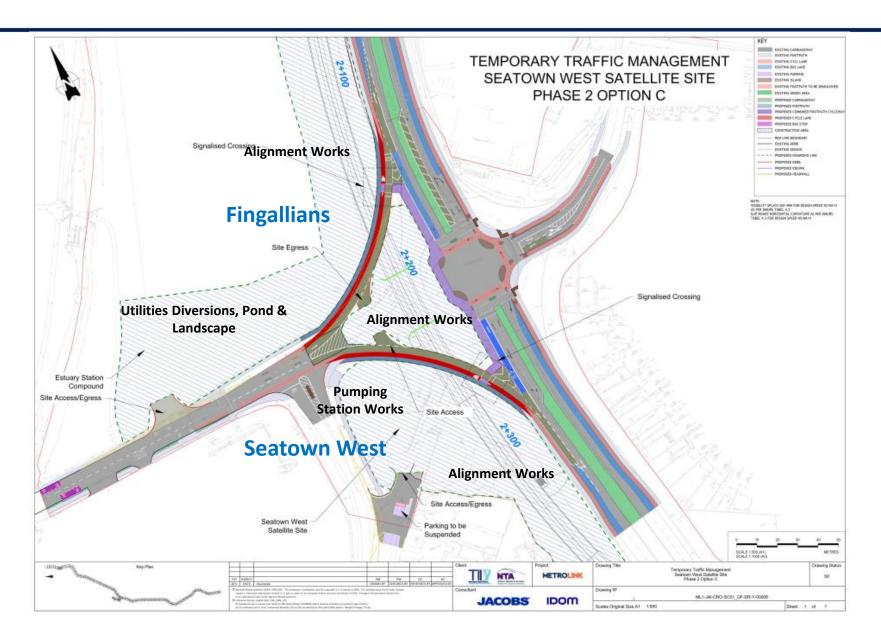




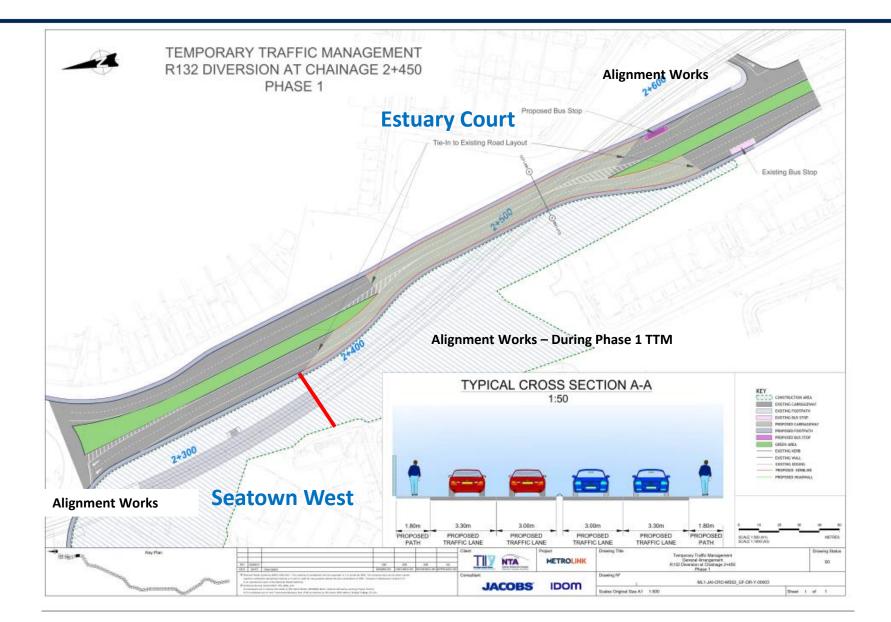



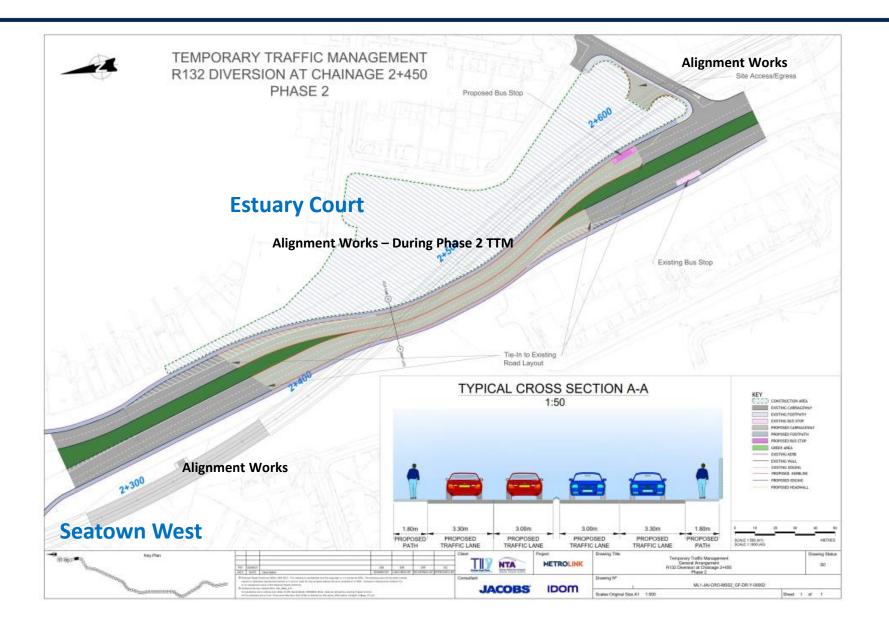



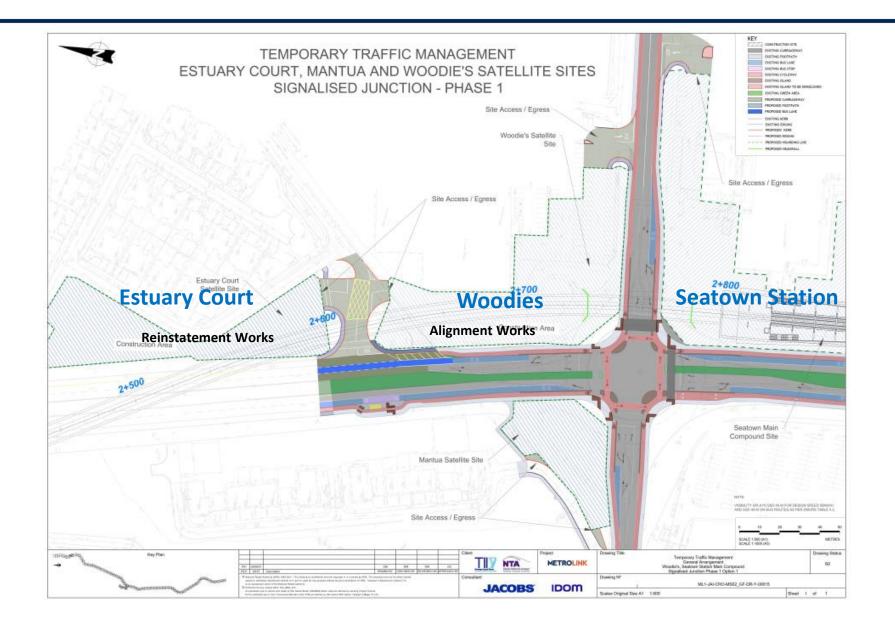



METROLINK

- info@metrolink.ie
- www.metrolink.ie
- **(** 1800 333 777
- **y** @metrolink_ie
